



## AGENDA

### COMMITTEE OF THE WHOLE WORKSHOP BOARD OF COUNTY COMMISSIONERS

Board Chambers  
Suite 100  
Ernie Lee Magaha Government Building - First Floor  
221 Palafox Place

January 17, 2019  
9:00 a.m.

Escambia County is committed to making our website accessible. If you use assistive technology, for example a screen reader, and have difficulty accessing information in this agenda online, please contact our ADA Coordinator at [ADA@myescambia.com](mailto:ADA@myescambia.com) or 850-595-1637.

**Notice: This meeting is televised live on ECTV and recorded for rebroadcast on the same channel. Refer to your cable provider's channel lineup to find ECTV.**

1. Call to Order  
  
(PLEASE TURN YOUR CELL PHONE TO THE SILENCE OR OFF SETTING.)
2. Was the meeting properly advertised?
3. OLF8 Land Offers  
(Amy Lovoy - 30 min)
  - A. Board Discussion
  - B. Board Direction
4. Lease Fees/Property Taxes on Pensacola Beach  
(Commissioner Bergosh - 15 min)
  - A. Board Discussion
  - B. Board Direction

5. Escambia County Housing Finance Authority (Multi-Family and Single-Family Revenue Bonds)  
(Patricia D. Lott, Executive Director and General Counsel, Escambia County Housing Authority - 15 min)
  - A. Board Discussion
  - B. Board Direction
  
6. New Escambia County Correctional Facility Progress Report  
(Steve Jernigan, Bay Design/Bob Dye, Facilities Management - 15 min)
  - A. Board Discussion
  - B. Board Direction
  
7. Design Standards Manual/Land Development Code (DSM/LDC) Modifications  
(Colby Brown - 30 min)
  - A. Board Discussion
  - B. Board Direction
  
8. Advanced Traffic Management System (ATMS)/Intelligent Transportation System (ITS) Signalization Upgrades - LOST IV  
(Colby Brown/David Forte - 15 min)
  - A. Board Discussion
  - B. Board Direction
  
9. Employee Engagement Survey/Performance Audit  
(Amy Lovoy/Eric Kleinert - 20 min)
  - A. Board Discussion
  - B. Board Direction
  
10. Public Forums/Agenda Reviews  
(Amy Lovoy - 10 min)
  - A. Board Discussion
  - B. Board Direction
  
11. Adjourn

**Committee of the Whole**

**3.**

**Meeting Date:** 01/17/2019

**Issue:** OLF8 Land Offers

**From:** Amy Lovoy, Assistant County Administrator

---

**Information**

**Recommendation:**

OLF8 Land Offers  
(Amy Lovoy - 30 min)

- A. Board Discussion
  - B. Board Direction
- 

**Attachments**

NFCU Offer

OLF8 Offer

---



ARMY  
MARINE CORPS  
NAVY  
AIR FORCE  
COAST GUARD  
VETERANS

December 19, 2018

Escambia County Board of County Commissioners  
221 Palafox Place  
Pensacola, FL 32502

**Re: Non-Binding Letter of Intent**

Honorable Commissioners:

This Letter of Intent (this “**Letter**”) indicates Navy Federal Credit Union’s interest in attempting to negotiate a written purchase contract (the “**Contract**”) for the property described below. The following are the non-binding principal terms and conditions which we propose as the basis for negotiations between the parties:

1. <b>Property:</b>	Approximately 100 acres of the property located in Escambia County, Florida and known as OLF 8. The Property is generally shown on Exhibit A. The actual location, dimensions and legal description of the Property would be determined by an ALTA survey which Navy Federal would commission.
2. <b>Seller:</b>	Escambia County (by and through the Escambia County Board of County Commissioners)
3. <b>Buyer:</b>	Navy Federal Credit Union
4. <b>Condition precedent:</b>	Seller must acquire title to the Property on or before February 28, 2019.
5. <b>Purchase Price:</b>	\$4,200,000. The Purchase Price is based on three use classifications of the Property: wetlands, commercial, and residential. The wetlands component of the Property equals 56% of the total Purchase Price; the commercial component of the Property equals 22% of the total Purchase Price; and the residential component of the Property equals 22% of the total Purchase Price. The Purchase Price will be adjusted to account for the final use classifications of the Property, on a percentage basis, according to Navy Federal’s survey of the Property. The Purchase Price will also be subject to customary prorations and closing adjustments.
6. <b>Deposit:</b>	\$100,000. If closing occurs, the Deposit will be applied to the Purchase Price at closing. If closing does not occur, the Deposit will be returned to Buyer unless Buyer is in default under the Contract.
7. <b>Study Period:</b>	Buyer will have 60 days to conduct its due diligence on the Property. During the Study Period, Buyer may perform a title search and conduct other customary inspections and environmental reviews of the Property. Prior to

	the end of the Study Period, Buyer may terminate the Contract for any reason and receive a full refund of the Deposit.
<b>8. Closing:</b>	Closing will occur 30 days after the end of the Study Period if all conditions precedent in the Contract have been satisfied.
<b>9. Costs:</b>	At closing, Seller will pay for the full release of any and all liens on the Property. All other closing costs will be prorated between Seller and Buyer in accordance with customary practices in Escambia County, Florida.
<b>10. Representations and closing conditions:</b>	To be negotiated between Buyer and Seller. The parties anticipate incorporating provisions comparable to those used in similar transactions in Escambia County, Florida including that (i) each party must obtain all required approvals necessary to consummate the purchase of the Property, and (ii) the Property must be legally subdivided to the extent required by law.
<b>11. Recreational facilities:</b>	Navy Federal would agree to use a portion for the Property, as designated by Navy Federal, for the construction of recreational facilities. The design and construction of these facilities would be paid for by Navy Federal. Navy Federal is willing to allow these facilities to be accessible to the public subject to Navy Federal's reasonable conditions and limitations. Exhibit A to this Letter shows a depiction of certain recreation facilities which has been included for initial planning and discussion purposes only. Navy Federal may adjust the location or design of these facilities during its design process.
<b>12. Expiration:</b>	If not accepted by Seller, the non-binding terms proposed in this Letter will expire on January 31, 2019.

Please note that this Letter is not binding on either Buyer or Seller, and no binding agreement will exist between Buyer and Seller until the Contract is fully executed and delivered by both parties. Until the Contract is fully executed and delivered by both parties, either Buyer or Seller may, without any liability to the other, terminate negotiations with respect to the Contract and the purchase of the Property at any time and for any reason whatsoever. This Letter is subject to modification or withdrawal by either party until the Contract is fully executed and delivered by both parties.

If the terms of this Letter are acceptable to you, please execute a copy of this Letter where indicated below. We will then prepare a draft Contract for your review. In the meantime, if you have any questions or require additional information, please feel free to contact me at either [george\\_eichert@navyfederal.org](mailto:george_eichert@navyfederal.org) or 703.255.8509.

Sincerely,




George E. Eichert  
 Senior Vice President, Administrative Services  
 Navy Federal Credit Union

**Agreed and Accepted:**

**Escambia County Board of County Commissioners**

By: \_\_\_\_\_  
Name: \_\_\_\_\_  
Title: \_\_\_\_\_

Exhibit A

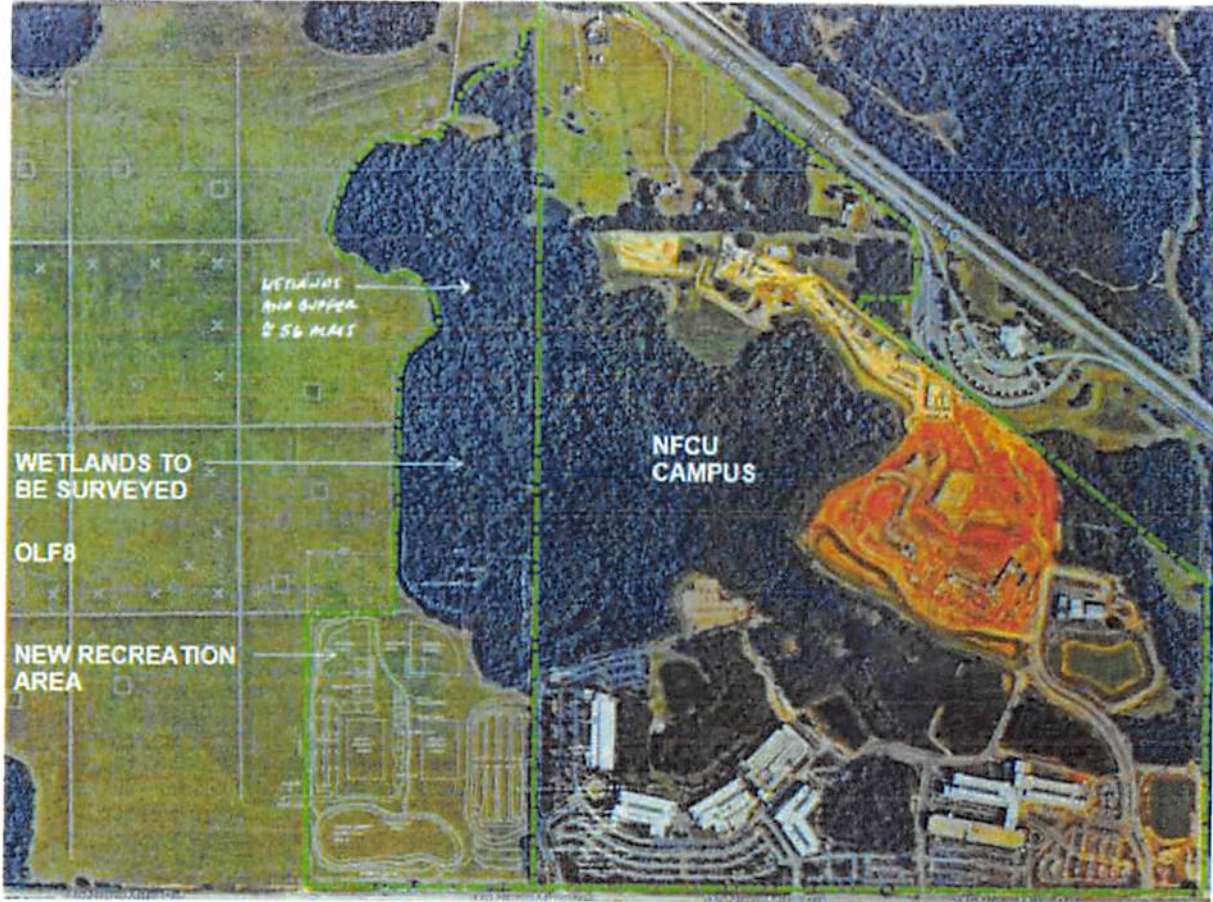


The Property is the area outlined in green and located adjacent to the NFCU Campus. The location and depiction of the facilities shown in the "New Recreation Area" above are included for the purposes described in Section 11 of the Letter only.


**To:** ESCAMBIA COUNTY BOARD OF COUNTY COMMISSIONERS

**Re:** Purchase Offer for the OLAF-8 Parcel presently owned by the U.S. Government and under option to the Escambia County Government of approximately 530 acres located in Escambia County, Florida, (hereby referred to as the "Property")

This Letter of Intent (LOI) outlines the interest of our group comprised of Hemmer Consulting, LLC, and its affiliates; AND 68 Ventures, LLC, and its affiliates (collectively the "Buyer"), to purchase the Fee Simple Title to the Property from Escambia County Government ("Seller") on the basic terms set forth herein, subject to the execution of a binding Purchase and Sale Agreement ("Purchase Agreement") between Buyer and Seller.

- Purchase Price:** \$18,000,000
- Terms:** \$18,000,000 CASH at closing.
- Deposit:** A refundable deposit of \$100,000 shall be paid when the Purchase Agreement is executed.
- Assignment:** This contract shall be assignable to a special purpose entity (SPE) specifically set-up to develop this project.
- Condition:** Buyer agrees to place covenants of the property controlling design aspects including but not limited to: signage, streetscaping, landscaping, maintenance of structures and the grounds.
- Zoning:** Seller shall facilitate the zoning approvals necessary to accommodate the Development Plan.
- Development Plan:** Buyer intends to develop a mixed-use site that will be mutually agreed upon by both parties.
- Tax Assessment:** Seller agrees to set property tax values at agricultural levels until each parcel is platted.
- Due Diligence:** The "Due Diligence Period" shall be nine (9) months from the date the Seller acquires the Property from the U.S. Government.
- Closing Period:** The Closing will take place 30 days after the later of: (i) the completion of zoning; or (ii) the end of the Due Diligence period. At any time during the Closing Period, the Buyer may provide an additional deposit of \$100,000 to extend the Closing Period by another ninety (90) days. The Buyer shall be permitted to pay for said extension up to two (2) times.
- Representation:** There are no licensed brokers representing either party in this transaction.
- Contract:** A bona fide Purchase Agreement shall be submitted by Buyer to the Seller within thirty (30) days following the execution of this Letter of Intent. The Buyer and Seller shall use good faith efforts to negotiate and execute a Purchase Agreement within twenty-one (21) days from the time the Buyer sends the initial draft of the Purchase Agreement to the Seller. Buyer understands that the Purchase Agreement must be approved by majority vote of the Seller's commission during normal government meetings and process.
- Non-Binding:** This Letter of Intent is not intended to be a binding contract. This Letter of Intent is an expression of mutual intent to proceed to a Purchase Agreement.

Offered by BUYER:  Fred Hemmer, President  
Hemmer Consulting, LLC

 Nathan Cox, CEO  
68 Ventures, LLC

Accepted by SELLER: \_\_\_\_\_ Title: \_\_\_\_\_ Date: \_\_\_\_\_



**Committee of the Whole**

**4.**

**Meeting Date:** 01/17/2019

**Issue:** Lease Fees/Property Taxes on Pensacola Beach

**From:** Jeff Bergosh, Commissioner, District 1

---

**Information**

**Recommendation:**

Lease Fees/Property Taxes on Pensacola Beach  
(Commissioner Bergosh - 15 min)

- A. Board Discussion
  - B. Board Direction
- 

**Attachments**

*No file(s) attached.*

---

**Committee of the Whole**

**5.**

**Meeting Date:** 01/17/2019

**Issue:** Escambia County Housing Finance Authority (Multi-Family and Single-Family Revenue Bonds)

**From:** Amy Lovoy, Assistant County Administrator

---

**Information**

**Recommendation:**

Escambia County Housing Finance Authority (Multi-Family and Single-Family Revenue Bonds)

(Patricia D. Lott, Executive Director and General Counsel, Escambia County Housing Authority - 15 min)

A. Board Discussion

B. Board Direction

---

**Attachments**

*No file(s) attached.*

---

**Committee of the Whole**

6.

**Meeting Date:** 01/17/2019

**Issue:** Progress Report on New Correctional Facility

**From:** Robert Dye, Division Manager

---

**Information**

**Recommendation:**

New Escambia County Correctional Facility Progress Report  
(Steve Jernigan, Bay Design/Bob Dye, Facilities Management - 15 min)

- A. Board Discussion
  - B. Board Direction
- 

**Attachments**

presentation

DBE progress report

---

# New Escambia County Correctional Facility

Progress update

Steve Jernigan – Bay Design

Bob Dye – Facilities Management

## Key Points

- Construction Progress
  - Foundation and Backfilling
    - Concrete poured at the Sally Port
    - Steel base plates in Area D grouted.
    - Excavation, reinforcement and grading completed for connector grade beams and pile caps.
    - First Slab-on-deck pours completed.
  - Juvenile Justice parking lot expansion and renovation substantially completed.
    - Demolition of existing west parking lot initiated in preparation for Storm water Pond construction and connection.
  - Access plan
    - Revised plan submitted to FDOT by GRW
    - Removes closure of neighboring property drive.

## Ongoing activity

Continuing:

- Precast wall panels
- Structural Steel
- Stairways
- Storm water pond

The project is on course and on glide path for 05/2020 substantial completion.

Next progress update – February Committee of the Whole



**New Escambia County Correctional Facility**

**PD 16-17.004**

**Monthly Project Report  
December 2018**

## Table of Contents

<b>1.0 Progress Summary .....</b>	<b>3</b>
<b>2.0 Construction Progress.....</b>	<b>4</b>
<b>3.0 Design Build Entity Schedule .....</b>	<b>4</b>
<b>4.0 Design Status .....</b>	<b>4</b>
<b>5.0 Subcontractor Procurement.....</b>	<b>5</b>
<b>6.0 Design-Build Entity's Safety Program .....</b>	<b>5</b>
<b>7.0 Disputes and Claims.....</b>	<b>5</b>
<b>8.0 Look Ahead Task List.....</b>	<b>5</b>
<b>9.0 Daily Log.....</b>	<b>6</b>



## 1.0 Progress Summary

ITEM	Description	COMMENTS
Original Contract Sum	\$132,445,243.00	
Change Order 1:	(-\$455,530.50)	ODP Change Order deduct for auger cast pile grout.
Change Order 2:	(\$-360.00)	Mathematical error with Alternate Number 5.
Change Order 3:	(-\$147,455.28)	ODP Change Order deduct for auger cast pile rebar.
Change Order 4:	(-\$28,769.30)	ODP Change Order deduct for additional auger cast pile rebar.
Change Order 5:	(-\$2,092,095.52)	ODP Change Order deduct for CIP Concrete and Rebar, Laundry Equipment, and Bi-Folding Doors.
Change Order 6:	(-\$463,697.91)	ODP Change Order deduct for Site Utility Piping and Structures.
Change Order 7:	(-\$32,731.48)	ODP Change Order deduct for Underground Electrical Raceways.
Change Order 8:	(-\$48,746.02)	ODP Change Order deduct for additional auger cast pile grout.
Change Order 9:	(-\$169,758.74)	ODP Change Order deduct for asphalt paving and corrections to existing POs.
Change Order 10:	(-\$9,005,200.12)	ODP Change Order deduct for structural steel, cell walls, hollow metal doors, door hardware and plumbing materials.
Change Order 11:	(-\$47,141.00)	ODP Change Order deduct for additional plumbing materials.
Adjusted Contract Sum	\$119,953,757.13	
Pending Change Order Request/Claims	NONE	
Original Date of Substantial Completion	May 28, 2020	
Forecast Date of Substantial Completion	May 28, 2020	

## 2.0 Construction Progress

Bayside Structures poured concrete at GB1 at the sallyport, and they grouted steel baseplates in Area D. Bayside excavated for the foundations and began reinforcing and forming for grade beams and pile caps at the connector. They began layout for embeds for the first pour of the slab on deck, and they received the reinforcing steel and welded wire mesh to be installed at the sequence 1 pour of the slab on deck.

EAA Sitework were fine-tuned the aggregate base at the JJC parking. They began installation of asphalt paving at the JJC parking lot on Tuesday 12/18/18 and completed laying asphalt on Thursday 12/20/18. After completing installation of the asphalt paving, they began layout of the pavement striping. EAA installed the striping at the JJC parking lot on Wednesday 12/26/18.

A&B Electric wired the terminals at the JJC parking lot light poles, energized the system and verified that the system was working correctly. They also grouted the base plates at the light pole bases in the JJC parking lot.

Emmons Steel Erectors completed erecting structural steel, erecting metal decking, and shooting studs in Area D for sequence 1, elevation 81 to 115. They continued erecting structural steel and metal decking for sequence 2, elevation 81-100 in Area D.

Tindall continued erecting precast in Area C of the building and near the roofline, and they were patching and installing corbels in Area A of the corridor. They also continued grouting, patching and welding panels.

Chavers Construction installed storm manhole S-7 and the 24" storm pipe under the connector, and they installed and backfilled the fire and domestic water piping under the connector. Chavers also formed, poured and finished the top of storm structure S16 at the JJC Parking Lot.

Nash completed underground plumbing work in Area B, and were installing sleeves, drains and inserts in Area D, Elevation 100, in anticipation of pouring sequence 1 slab on deck.

## 3.0 Design Build Entity Schedule

See attached Progress Schedule.

## 4.0 Design Status

### Summary:

The document submittal set for permitting is scheduled as follows:

- Permitting Submittal for Plumbing, HVAC, Electrical, Food Service, Security Electronics & Fire Alarm were issued on November 7, 2018.
- WGI/Caddell received approved permitting documents for Underground, Architectural, Structural, FFE and Precast drawings on December 6, 2018.
- ECUA has finalized the plan approval letter. WGI/Caddell will submit material submittals to ECUA, obtain the Plan Approval Package and schedule a preconstruction meeting.

**Contract Deliverables:**

- NONE

**Areas of Concern:**

- NONE

**Actions and Approvals Needed:**

- A partial FDOT permit has been issued for curb access closures, and WGI/Caddell has drafted a letter acknowledging future lighting work along Fairfield Blvd. GRW has provided FDOT with revised permit documents that are currently under review.
- WGI/Caddell is currently waiting on review of HVAC, Electrical, Food Service, Security Electronics and Fire Alarm permit documents.

**Recommendations:**

- NONE

**5.0 Subcontractor Procurement**

- Ed Emmons Steel Erectors, Inc.
- REYCO Contracting Solutions: Masonry

**6.0 Design-Build Entity's Safety Program**

No incidents were recorded for the month of December 2018.

**7.0 Disputes and Claims**

No disputes or claims were filed in the month of December 2018.

**8.0 Look Ahead Task List**

See attached 90-day Look Ahead Schedule.

## 9.0 Daily Log

See attached Daily Logs for the month of December 2018.

Activity ID	Activity Name	Orig Dur	Rem Dur	Prev Pct%	New Pct %	Actual Start	Actual Finish	Total Float	Early Start	Early Finish	Budgeted Cost	This Period Cost	Cost to Complete
ECCF14 30Dec18 Detailed Baseline Schedule Update - Prelim1		855	222			02-Jan-18		30	02-Jan-18 A	08-Aug-19	\$4,623,230.64	\$2,720,856.63	(\$1,974,667.83)
<b>Progress this Period</b>		855	222			02-Jan-18		30	02-Jan-18 A	08-Aug-19	\$13,845,330.50	\$3,043,246.40	\$6,925,042.26
<b>PRECONSTRUCTION</b>		855	120			02-Jan-18		-34	02-Jan-18 A	28-Apr-19	\$11,161,249.00	\$2,430,603.94	\$5,202,293.06
<b>WEATHER</b>		5	0			01-Dec-18	30-Dec-18		01-Dec-18 A	30-Dec-18 A	\$0.00	\$0.00	\$0.00
890008	ANTICIPATED ADVERSE WEATHER - DEC18	5	0	0%	100%	01-Dec-18	30-Dec-18		01-Dec-18 A	30-Dec-18 A	\$0.00	\$0.00	\$0.00
<b>DESIGN</b>		100	10			25-Jul-18		125	25-Jul-18 A	08-Jan-19	\$50,000.00	\$0.00	\$13,500.00
001171	SITE/CIVIL DESIGN - FENCING/MISC. SITE ITEMS	30	10	73%	73%	25-Jul-18		125	25-Jul-18 A	08-Jan-19	\$50,000.00	\$0.00	\$13,500.00
001420	EC REVIEW - FF&E DESIGN (100% DESIGN)	14	10	75%	75%	10-Oct-18		111	10-Oct-18 A	08-Jan-19	\$0.00	\$0.00	\$0.00
<b>PERMITS</b>		177	10			13-Feb-18		120	13-Feb-18 A	08-Jan-19	\$20,000.00	\$7,400.00	\$2,000.00
009004	PERMITS - SITE/CIVIL - ECUA ACCEPTANCE	46	0	95%	100%	14-Mar-18	18-Dec-18		14-Mar-18 A	18-Dec-18 A	\$0.00	\$0.00	\$0.00
009009	PERMITS - SITE/CIVIL - FOR ACCOUNTING ONLY	1	1	24%	90%	13-Feb-18		35	13-Feb-18 A	30-Dec-18	\$10,000.00	\$6,600.00	\$1,000.00
009020	PERMITS - BUILDING	60	10	82%	90%	13-Mar-18		111	13-Mar-18 A	08-Jan-19	\$10,000.00	\$800.00	\$1,000.00
<b>PRECONSTRUCTION SUBMITTALS</b>		447	90			30-Jan-18		45	30-Jan-18 A	29-Mar-19	\$0.00	\$0.00	\$0.00
000600	PREPARE & SUBMIT LOD 300/400 FEDERATED MODEL	143	90	0%	0%	07-Nov-18		45	07-Nov-18 A	29-Mar-19	\$0.00	\$0.00	\$0.00
000620	SUBMIT FINAL BASELINE DESIGN/CONSTRUCTION SCHEDULE	90	33	0%	0%	30-Jan-18		81	30-Jan-18 A	31-Jan-19	\$0.00	\$0.00	\$0.00
<b>PROCUREMENT</b>		450	120			02-Jan-18		65	02-Jan-18 A	28-Apr-19	\$11,091,249.00	\$2,423,203.94	\$5,186,793.06
010000	PROCUREMENT OF LONG-LEAD ITEMS	450	120	0%	0%	02-Jan-18		65	02-Jan-18 A	28-Apr-19	\$0.00	\$0.00	\$0.00
010031	PRECAST PROCUREMENT - MATERIAL COST	1	1	51%	71%	26-Sep-18		169	26-Sep-18 A	30-Dec-18	\$6,285,564.00	\$1,231,224.44	\$1,822,813.56
010061	STEEL PROCUREMENT (STR & MISC) - MATERIAL COST	1	1	5%	30%	07-Nov-18		113	07-Nov-18 A	30-Dec-18	\$4,805,685.00	\$1,191,979.50	\$3,363,979.50
<b>CONSTRUCTION</b>		479	222			16-Jul-18		294	16-Jul-18 A	08-Aug-19	\$2,684,081.50	\$612,642.46	\$1,722,749.20
<b>DESIGN</b>		25	20			05-Sep-18		496	05-Sep-18 A	18-Jan-19	\$1,626,811.50	\$65,072.46	\$1,301,449.20
003000	A/E CONSTRUCTION ADMINISTRATION SERVICES (25 MONTHS)	25	20	16%	20%	05-Sep-18		496	05-Sep-18 A	18-Jan-19	\$1,626,811.50	\$65,072.46	\$1,301,449.20
<b>SITWORK</b>		149	19			16-Jul-18		328	16-Jul-18 A	28-Jan-19	\$107,270.00	\$40,070.00	\$53,200.00
100002	MAINTAIN EROSION CONTROLS (25 MONTHS)	25	19	20%	24%	16-Jul-18		211	16-Jul-18 A	28-Jan-19	\$70,000.00	\$2,800.00	\$53,200.00
150000	STRIPING - NE JUVENILE PARKING LOT (INCL OFFICER PARKING)	2	0	0%	100%	19-Dec-18	21-Dec-18		19-Dec-18 A	21-Dec-18 A	\$1,010.00	\$1,010.00	\$0.00
150002	WHEEL STOPS - NE JUVENILE PARKING LOT (INCL OFFICER PARKING)	2	0	0%	100%	21-Dec-18	21-Dec-18		21-Dec-18 A	21-Dec-18 A	\$2,000.00	\$2,000.00	\$0.00

Activity ID	Activity Name	Orig Dur	Rem Dur	Prev Pct%	New Pct %	Actual Start	Actual Finish	Total Float	Early Start	Early Finish	Budgeted Cost	This Period Cost	Cost to Complete
150004	EXT SIGNAGE - NE JUVENILE PARKING LOT (INCL OFFICER PARKING)	2	0	0%	100%	21-Dec-18	21-Dec-18		21-Dec-18 A	21-Dec-18 A	\$2,000.00	\$2,000.00	\$0.00
150150	ASPHALT - NE JUVENILE PARKING LOT (INCL OFFICER PARKING)	10	0	0%	100%	18-Dec-18	19-Dec-18		18-Dec-18 A	19-Dec-18 A	\$32,260.00	\$32,260.00	\$0.00
<b>CORRECTIONAL FACILITY</b>		<b>174</b>	<b>154</b>			<b>26-Nov-18</b>		<b>29</b>	<b>26-Nov-18 A</b>	<b>08-Aug-19</b>	<b>\$950,000.00</b>	<b>\$507,500.00</b>	<b>\$368,100.00</b>
200420	UNDER SLAB PLUMBING B	10	8	0%	20%	17-Dec-18		29	17-Dec-18 A	08-Aug-19	\$50,000.00	\$10,000.00	\$40,000.00
200880	SLAB ON DECK D ELEV 100 - 2ND LVL	6	4	0%	33%	26-Dec-18		-20	26-Dec-18 A	25-Jan-19	\$250,000.00	\$82,500.00	\$167,500.00
201000	IN-SLAB PLUMBING D 2ND LVL CL 14-29	5	4	0%	20%	18-Dec-18		-15	18-Dec-18 A	04-Jan-19	\$50,000.00	\$10,000.00	\$40,000.00
201200	IN-SLAB ELECTRICAL D 2ND LVL CL 14-29	5	0	0%	100%	17-Dec-18	21-Dec-18		17-Dec-18 A	21-Dec-18 A	\$50,000.00	\$50,000.00	\$0.00
210100	STRUCTURAL STEEL D ELEV 100-102 (1/2)	8	0	12%	100%	28-Nov-18	10-Dec-18		28-Nov-18 A	10-Dec-18 A	\$70,000.00	\$61,600.00	\$0.00
210110	STRUCTURAL STEEL D ELEV 100-102 (2/2)	8	3	0%	62%	19-Dec-18		-20	19-Dec-18 A	03-Jan-19	\$70,000.00	\$43,400.00	\$26,600.00
210180	DETAIL STRUCTURAL STEEL D ELEV 100 (1/2)	11	0	0%	100%	11-Dec-18	20-Dec-18		11-Dec-18 A	20-Dec-18 A	\$10,000.00	\$10,000.00	\$0.00
211020	PRECAST C (1/3)	15	0	33%	100%	26-Nov-18	13-Dec-18		26-Nov-18 A	13-Dec-18 A	\$200,000.00	\$134,000.00	\$0.00
211030	PRECAST C (2/3)	15	7	0%	53%	14-Dec-18		-19	14-Dec-18 A	09-Jan-19	\$200,000.00	\$106,000.00	\$94,000.00
<b>Added Activity This Period / Modifications</b>		<b>1</b>	<b>0</b>			<b>01-Dec-18</b>		<b>516</b>	<b>01-Dec-18 A</b>	<b>30-Dec-18</b>	<b>(\$9,222,099.86)</b>	<b>(\$322,389.77)</b>	<b>(\$8,899,710.09)</b>
<b>MODIFICATIONS</b>		<b>1</b>	<b>0</b>			<b>01-Dec-18</b>		<b>516</b>	<b>01-Dec-18 A</b>	<b>30-Dec-18</b>	<b>(\$9,222,099.86)</b>	<b>(\$322,389.77)</b>	<b>(\$8,899,710.09)</b>
<b>MODIFICATIONS</b>		<b>1</b>	<b>0</b>			<b>01-Dec-18</b>		<b>516</b>	<b>01-Dec-18 A</b>	<b>30-Dec-18</b>	<b>(\$9,222,099.86)</b>	<b>(\$322,389.77)</b>	<b>(\$8,899,710.09)</b>
900006	CHANGE ORDER NO.6	1	0		3%	01-Dec-18		516	01-Dec-18 A	30-Dec-18	(\$9,174,958.86)	(\$275,248.77)	(\$8,899,710.09)
900007	CHANGE ORDER NO.7	1	0		100%	01-Dec-18	30-Dec-18		01-Dec-18 A	30-Dec-18 A	(\$47,141.00)	(\$47,141.00)	\$0.00

Activity ID	Activity Name	Orig Dur	Rem Dur	Early Start	Early Finish	Total Float	2018			2019										
							Jan	Feb	Mar	Jan	Feb	Mar								
<b>ECCF14 30Dec18 Detailed Baseline Schedule Update - Prelim1</b>																				
<b>PRECONSTRUCTION</b>																				
<b>MILESTONES</b>																				
800015	QUARTERLY TOWN HALL PROGRESS MEETING (COC) 1ST WED OF QTR	0	0		02-Jan-19*	0														
800016	PFRR BOARD MEETING - BCC RECOMMENDATION DEVELOPMENT WORKSHOP	0	0		02-Jan-19*	0														
009999	OBTAIN LICENSES, FEES, PERMITS	0	0		08-Jan-19	211														
001599	DESIGN COMPLETE	0	0		22-Jan-19	111														
000629	APPROVE CONSTRUCTION SCHEDULE	0	0		21-Feb-19	81														
800017	PFRR BOARD MEETING - BCC RECOMMENDATION DEVELOPMENT WORKSHOP	0	0		01-Mar-19*	0														
<b>WEATHER</b>																				
890018	ANTICIPATED ADVERSE WEATHER - OCT19	3	3	31-Dec-18	03-Jan-19	352														
890019	ANTICIPATED ADVERSE WEATHER - NOV19	4	4	31-Dec-18	04-Jan-19	351														
890020	ANTICIPATED ADVERSE WEATHER - DEC19	5	5	31-Dec-18	07-Jan-19	350														
890021	ANTICIPATED ADVERSE WEATHER - JAN20	5	5	31-Dec-18	07-Jan-19	350														
890022	ANTICIPATED ADVERSE WEATHER - FEB20	5	5	31-Dec-18	07-Jan-19	350														
890023	ANTICIPATED ADVERSE WEATHER - MAR20	5	5	31-Dec-18	07-Jan-19	350														
890024	ANTICIPATED ADVERSE WEATHER - APR20	3	3	31-Dec-18	03-Jan-19	352														
890025	ANTICIPATED ADVERSE WEATHER - MAY20	3	3	31-Dec-18	03-Jan-19	352														
<b>DESIGN</b>																				
001171	SITE/CIVIL DESIGN - FENCING/MISC. SITE ITEMS	30	10	25-Jul-18 A	08-Jan-19	125														
001420	EC REVIEW - FF&E DESIGN (100% DESIGN)	14	10	10-Oct-18 A	08-Jan-19	111														
001500	CONSOLIDATED CONSTRUCTION SET (100% CD)	14	14	09-Jan-19	22-Jan-19	111														
<b>PERMITS</b>																				
009009	PERMITS - SITE/CIVIL - FOR ACCOUNTING ONLY	1	1	13-Feb-18 A	30-Dec-18	35														
009020	PERMITS - BUILDING	60	10	13-Mar-18 A	08-Jan-19	111														
<b>PRECONSTRUCTION SUBMITTALS</b>																				
000620	SUBMIT FINAL BASELINE DESIGN/CONSTRUCTION SCHEDULE	90	33	30-Jan-18 A	31-Jan-19	81														
000600	PREPARE & SUBMIT LOD 300/400 FEDERATED MODEL	143	90	07-Nov-18 A	29-Mar-19	45														
000625	APPROVE FINAL BASELINE DESIGN/CONSTRUCTION SCHEDULE	21	21	01-Feb-19	21-Feb-19	81														
<b>PROCUREMENT</b>																				
010000	PROCUREMENT OF LONG-LEAD ITEMS	450	120	02-Jan-18 A	28-Apr-19	65														
010031	PRECAST PROCUREMENT - MATERIAL COST	1	1	26-Sep-18 A	30-Dec-18	169														
010061	STEEL PROCUREMENT (STR & MISC) - MATERIAL COST	1	1	07-Nov-18 A	30-Dec-18	113														
<b>CONSTRUCTION</b>																				
<b>ADMINISTRATION</b>																				
700031	EXTERIOR IMPROVEMENTS	418	232	06-Apr-18 A	02-Dec-19	43														

Activity ID	Activity Name	Orig Dur	Rem Dur	Early Start	Early Finish	Total Float	2018												2019																							
							Jan												Feb												Mar											
700004	MASONRY	519	379	11-Jun-18 A	01-Jul-20	-24																																				
700006	ROUGH CARPENTRY	519	379	11-Jun-18 A	01-Jul-20	-24																																				
700007	FINISH CARPENTRY & CASEWORK	519	379	11-Jun-18 A	01-Jul-20	-24																																				
700008	WATERPROOFING, JOINT SEALANTS, AIR BARRIER, EXP. JTS.	519	379	11-Jun-18 A	01-Jul-20	-24																																				
700010	STEEL DOORS & FRAMES, WOOD DOORS, HARDWARE	519	379	11-Jun-18 A	01-Jul-20	-24																																				
700011	ALUMINUM ENTRANCES, DOORS, FRAMES, GLASS & GLAZING	519	379	11-Jun-18 A	01-Jul-20	-24																																				
700012	OVERHEAD COILING DOORS, VEHICLE SALLYPORT DOORS	519	379	11-Jun-18 A	01-Jul-20	-24																																				
700013	GYPSON BOARD, METAL FRAMING, ACOUSTICAL TREATMENTS	519	379	11-Jun-18 A	01-Jul-20	-24																																				
700014	FLOORING & PAINTING	519	379	11-Jun-18 A	01-Jul-20	-24																																				
700015	SPECIALTIES	519	379	11-Jun-18 A	01-Jul-20	-24																																				
700017	MISCELLANEOUS EQUIPMENT	519	379	11-Jun-18 A	01-Jul-20	-24																																				
700018	DETENTION HOLLOW METAL DOORS, FRAMES, GLAZING	519	379	11-Jun-18 A	01-Jul-20	-24																																				
700019	MODULAR STEEL CELLS, STEEL PANELS, DETENTION CEILINGS	519	379	11-Jun-18 A	01-Jul-20	-24																																				
700020	DETENTION FURNISHINGS & EQUIPMENT	519	379	11-Jun-18 A	01-Jul-20	-24																																				
700021	FURNISHINGS	519	379	11-Jun-18 A	01-Jul-20	-24																																				
700022	SPECIAL CONSTRUCTION	519	379	11-Jun-18 A	01-Jul-20	-24																																				
700024	FIRE SUPPRESSION	519	379	11-Jun-18 A	01-Jul-20	-24																																				
700025	PLUMBING	519	379	11-Jun-18 A	01-Jul-20	-24																																				
700026	HEATING, VENTILATING, AND AIR CONDITIONING	519	379	11-Jun-18 A	01-Jul-20	-24																																				
700027	ELECTRICAL	519	379	11-Jun-18 A	01-Jul-20	-24																																				
700028	COMMUNICATIONS	519	379	11-Jun-18 A	01-Jul-20	-24																																				
700029	ELECTRONIC SECURITY SYSTEMS	519	379	11-Jun-18 A	01-Jul-20	-24																																				
700016	FOOD SERVICE & LAUNDRY EQUIPMENT	513	379	18-Jun-18 A	01-Jul-20	-24																																				
700003	PRECAST CONCRETE	243	101	22-Jun-18 A	23-May-19	16																																				
700002	CAST-IN-PLACE CONCRETE	262	176	20-Aug-18 A	10-Sep-19	27																																				
700030	EARTHWORK	356	189	20-Aug-18 A	27-Sep-19	82																																				
700001	BUILDING & SITE DEMOLITION	56	23	24-Aug-18 A	01-Feb-19	20																									BUILDING & SITE DEMOLITION											
700032	UTILITIES	103	73	06-Sep-18 A	15-Apr-19	55																																				
700005	METALS	145	121	14-Nov-18 A	21-Jun-19	-13																																				
401000	ALTERNATE 01 - FULL EMERGENCY POWER	1	1	31-Dec-18	31-Dec-18	354																									ALTERNATE 01 - FULL EMERGENCY POWER											
402000	ALTERNATE 02 - DOMESTIC HOT WATER, CHILLED WATER, & HEATING	1	1	31-Dec-18	31-Dec-18	354																									ALTERNATE 02 - DOMESTIC HOT WATER, CHILLED WATER, & HEATING											
403000	ALTERNATE 03 - INMATE PLUMBING CONTROL SYSTEM	1	1	31-Dec-18	31-Dec-18	354																									ALTERNATE 03 - INMATE PLUMBING CONTROL SYSTEM											

 Actual Work  
 Remaining Work  
 Critical Remaining Work  
 Milestone

D/B New Escambia County Correctional Facility  
Pensacola, FL

**ECCF14-DEC1** ECCF14 30Dec18 Detailed Baseline Schedule Update - Prelim1

- 90-Day Schedule 11x17

Page 2 of 6  
03-Jan-19 13:31

Data Date: 30-Dec-18

Caddell - WGI

#1054



Activity ID	Activity Name	Orig Dur	Rem Dur	Early Start	Early Finish	Total Float	2018		2019			
									Jan	Feb	Mar	
405000	ALTERNATE 05 - FULL OPERABLE SLIDER DOORS	1	1	31-Dec-18	31-Dec-18	354						
409000	ALTERNATE 09 - EXACQ VISION VMS	1	1	31-Dec-18	31-Dec-18	354						
410000	ALTERNATE 10 - PERVIOUS CONCRETE PAVING	1	1	31-Dec-18	31-Dec-18	354						
414000	ALTERNATE 14 - SECOND BUNK FOR CELLS	1	1	31-Dec-18	31-Dec-18	354						
700009	ROOFING & INSULATED METAL PANELS	119	119	04-Mar-19	19-Aug-19	-13						
<b>DESIGN</b>												
003000	A/E CONSTRUCTION ADMINISTRATION SERVICES (25 MONTHS)	25	20	05-Sep-18 A	18-Jan-19	496						
<b>SITWORK</b>												
100002	MAINTAIN EROSION CONTROLS (25 MONTHS)	25	19	16-Jul-18 A	28-Jan-19	211						
101400	UTILITY DEMOLITION - CONNECTOR/CORRIDOR AREA	15	2	13-Sep-18 A	05-Feb-19	28						
112300	SITE UTILITIES - U/G ELECTRIC FOR SITE LIGHTING WEST	10	10	22-Oct-18 A	04-Mar-19	62						
101110	SITE & UTILITY DEMOLITION - EXISTING SE JUVENILE PARKING LOT 2 OF 2 (DELETE)	0	0	31-Dec-18	31-Dec-18	355						
100110	SITE GRADING - STORMWATER POND (EXIST SE JUV PLOT) 2 OF 2 (DELETE)	0	0	31-Dec-18	31-Dec-18	355						
100007	CONSTRUCTION FENCE - EXISTING SE JUVENILE PARKING LOT	3	3	31-Dec-18	03-Jan-19	20						
101100	SITE & UTILITY DEMOLITION - EXISTING SE JUVENILE PARKING LOT	10	10	04-Jan-19	17-Jan-19	20						
101200	SITE & UTILITY DEMOLITION - REMAINING SITE	10	10	18-Jan-19	01-Feb-19	20						
100100	SITE GRADING - STORMWATER POND (EXIST SE JUV PLOT)	10	10	18-Jan-19	01-Feb-19	55						
159300	LANDSCAPING - NE JUVENILE PARKING LOT	5	5	29-Jan-19	04-Feb-19	323						
100200	SITE GRADING - REMAINING SITE	10	10	04-Feb-19	15-Feb-19	20						
110000	SITE UTILITIES - STORMWATER POND	10	10	04-Feb-19	15-Feb-19	55						
100400	SITE GRADING - CONNECTOR/CORRIDOR AREA	10	10	19-Feb-19	04-Mar-19	20						
151010	GRAVEL - STORMWATER POND	5	5	19-Feb-19	25-Feb-19	182						
111000	SITE UTILITIES - SANITARY SOUTH	10	10	19-Feb-19	04-Mar-19	57						
110010	SITE UTILITIES - STORM SOUTH 1 OF 2	10	10	19-Feb-19	04-Mar-19	55						
113000	SITE UTILITIES - GAS EAST	10	10	19-Feb-19	04-Mar-19	85						
152000	DECORATIVE FENCE/GATE - RETENTION POND	10	10	26-Feb-19	11-Mar-19	182						
112400	SITE UTILITIES - TELECOM NORTH (INCL CONNECTOR/CORRIDOR)	10	10	05-Mar-19	18-Mar-19	75						
112310	SITE UTILITIES - U/G ELECTRIC FOR SITE LIGHTING EAST	10	10	05-Mar-19	18-Mar-19	62						
112380	SITE UTILITIES - U/G ELECTRIC NORTH (BY GULF POWER)	20	20	05-Mar-19	01-Apr-19	20						
158000	FRP CANTILEVER WALL - ROADS/DRIVES SITE NORTH	15	15	05-Mar-19	25-Mar-19	112						
112000	SITE UTILITIES - WATER WEST/NORTH (INCL CONNECTOR/CORRIDOR)	10	10	05-Mar-19	18-Mar-19	75						
110015	SITE UTILITIES - STORM SOUTH 2 OF 2	10	10	05-Mar-19	18-Mar-19	55						
111010	SITE UTILITIES - SANITARY EAST	15	15	05-Mar-19	25-Mar-19	57						

Activity ID	Activity Name	Orig Dur	Rem Dur	Early Start	Early Finish	Total Float	2018			2019												
							Jan	Feb	Mar	Jan	Feb	Mar										
111020	SITE UTILITIES - SANITARY LATERALS NORTH (CONNECTOR/CORRIDOR)	5	5	05-Mar-19	11-Mar-19	112																
110020	SITE UTILITIES - STORM NORTH (INCL CONNECTOR/CORRIDOR) 1 OF 2	10	10	19-Mar-19	01-Apr-19	55																
158190	RAILING @ CANTILEVER WALL	5	5	26-Mar-19	01-Apr-19	212																
158200	FRP CONC GRAVITY WALL - ROAD SITE WEST	15	15	26-Mar-19	15-Apr-19	112																
<b>CORRECTIONAL FACILITY</b>																						
200300	STRUCTURAL BACKFILL A	5	2	24-Oct-18 A	19-Jun-19	54																
200320	STRUCTURAL BACKFILL B	8	5	29-Oct-18 A	29-Jul-19	27																
211030	PRECAST C (2/3)	15	7	14-Dec-18 A	09-Jan-19	-19																
200420	UNDER SLAB PLUMBING B	10	8	17-Dec-18 A	08-Aug-19	29																
201000	IN-SLAB PLUMBING D 2ND LVL CL 14-29	5	4	18-Dec-18 A	04-Jan-19	-15																
210110	STRUCTURAL STEEL D ELEV 100-102 (2/2)	8	3	19-Dec-18 A	03-Jan-19	-20																
200880	SLAB ON DECK D ELEV 100 - 2ND LVL	6	4	26-Dec-18 A	25-Jan-19	-20																
210300	SWITCHBACK STAIRS C	15	15	31-Dec-18	22-Jan-19	-24																
200450	UNDER SLAB PLUMBING C (1/2)	10	10	31-Dec-18	14-Jan-19	168																
200460	UNDER SLAB ELECTRICAL C (1/2)	10	10	31-Dec-18	14-Jan-19	168																
201210	IN-SLAB ELECTRICAL D 2ND LVL CL 29-50	5	5	31-Dec-18	07-Jan-19	-11																
211090	PRECAST CENTER CORRIDOR CL 14-50	15	15	04-Jan-19	25-Jan-19	-20																
210190	DETAIL STRUCTURAL STEEL D ELEV 100 (2/2)	11	11	04-Jan-19	18-Jan-19	-20																
201010	IN-SLAB PLUMBING D 2ND LVL CL 29-50	5	5	07-Jan-19	11-Jan-19	-15																
200455	UNDER SLAB PLUMBING C (2/2)	10	10	15-Jan-19	29-Jan-19	168																
200465	UNDER SLAB ELECTRICAL C (2/2)	10	10	15-Jan-19	29-Jan-19	168																
211040	PRECAST C (3/3)	15	15	17-Jan-19	07-Feb-19	-24																
210310	LARGE STAIR C	6	6	23-Jan-19	30-Jan-19	-24																
200900	SLAB ON DECK D ELEV 102 - 2ND LVL	6	6	28-Jan-19	04-Feb-19	69																
211060	PRECAST D ELEV 100	9	9	28-Jan-19	07-Feb-19	-20																
210320	MEZZANINE STAIR C	6	6	31-Jan-19	07-Feb-19	-24																
210000	PRECAST A (1/3)	15	15	08-Feb-19	01-Mar-19	-24																
210120	STRUCTURAL STEEL D ELEV 115	5	5	08-Feb-19	14-Feb-19	-20																
210330	SWITCHBACK STAIRS A	15	15	08-Feb-19	01-Mar-19	-19																
201090	IN-SLAB PLUMBING C ROOF	5	5	08-Feb-19	14-Feb-19	31																
201290	IN-SLAB ELECTRICAL C ROOF	5	5	08-Feb-19	14-Feb-19	31																
200790	TOPPING SLAB C ROOF	10	10	15-Feb-19	01-Mar-19	31																
211070	PRECAST D EXTERIOR WALLS	9	9	15-Feb-19	28-Feb-19	-20																

■ Actual Work  
■ Remaining Work  
■ Critical Remaining Work  
◆ Milestone

D/B New Escambia County Correctional Facility  
Pensacola, FL

**ECCF14-DEC1** ECCF14 30Dec18 Detailed Baseline Schedule Update - Prelim1  
- 90-Day Schedule 11x17

Page 4 of 6  
03-Jan-19 13:31  
Data Date: 30-Dec-18

Caddell - WGI  
#1054

Activity ID	Activity Name	Orig Dur	Rem Dur	Early Start	Early Finish	Total Float	2018												2019																
							Jan												Feb												Mar				
210130	DETAIL STRUCTURAL STEELD ELEV 115 (1/2)	13	13	15-Feb-19	06-Mar-19	23													DETAIL STRUCTURAL STEELD ELEV 115 (1/2)																
201020	IN-SLAB PLUMBING D3RD LVL CL 14-29	5	5	15-Feb-19	22-Feb-19	39													IN-SLAB PLUMBING D3RD LVL CL 14-29																
201080	IN-SLAB PLUMBING C3RD LVL	5	5	15-Feb-19	22-Feb-19	36													IN-SLAB PLUMBING C3RD LVL																
201220	IN-SLAB ELECTRICAL D3RD LVL CL 14-29	5	5	15-Feb-19	22-Feb-19	39													IN-SLAB ELECTRICAL D3RD LVL CL 14-29																
201280	IN-SLAB ELECTRICAL C3RD LVL	5	5	15-Feb-19	22-Feb-19	36													IN-SLAB ELECTRICAL C3RD LVL																
201030	IN-SLAB PLUMBING D3RD LVL CL 29-50	5	5	25-Feb-19	01-Mar-19	39													IN-SLAB PLUMBING D3RD LVL CL 29-50																
201070	IN-SLAB PLUMBING C2ND LVL	5	5	25-Feb-19	01-Mar-19	41													IN-SLAB PLUMBING C2ND LVL																
201230	IN-SLAB ELECTRICAL D3RD LVL CL 29-50	5	5	25-Feb-19	01-Mar-19	39													IN-SLAB ELECTRICAL D3RD LVL CL 29-50																
201270	IN-SLAB ELECTRICAL C2ND LVL	5	5	25-Feb-19	01-Mar-19	41													IN-SLAB ELECTRICAL C2ND LVL																
210150	STRUCTURAL STEEL D LOW ROOF	12	12	01-Mar-19	18-Mar-19	-20													STRUCTURAL STEEL D LOW ROOF																
200780	TOPPING SLAB C3RD LVL	10	10	04-Mar-19	15-Mar-19	31													TOPPING SLAB C3RD LVL																
210010	PRECASTA (2/3)	15	15	04-Mar-19	22-Mar-19	-24													PRECASTA (2/3)																
211110	PRECAST D ELEV 115-137	3	3	04-Mar-19	06-Mar-19	-7													PRECAST D ELEV 115-137																
210340	MECHANICAL STAIRSA	10	10	04-Mar-19	15-Mar-19	-19													MECHANICAL STAIRSA																
230000	ROOF SYSTEM C	20	20	04-Mar-19	29-Mar-19	43													ROOF SYSTEM C																
201040	IN-SLAB PLUMBING D4TH LVL & HIGH ROOF	5	5	04-Mar-19	08-Mar-19	61													IN-SLAB PLUMBING D4TH LVL & HIGH ROOF																
201240	IN-SLAB ELECTRICAL D4TH LVL & HIGH ROOF	5	5	04-Mar-19	08-Mar-19	61													IN-SLAB ELECTRICAL D4TH LVL & HIGH ROOF																
220000	EXTERIOR BUILDING FINISHES (PCST/MTL PNL/C.WALL)	140	140	07-Mar-19	23-Sep-19	47													EXTERIOR BUILDING FINISHES (PCST/MTL PNL/C.WALL)																
210170	DETAIL STRUCTURAL STEELD ELEV 115 (2/2)	13	13	07-Mar-19	25-Mar-19	23													DETAIL STRUCTURAL STEELD ELEV 115 (2/2)																
210270	STRUCTURAL STEEL D ELEV 137	3	3	07-Mar-19	11-Mar-19	-7													STRUCTURAL STEEL D ELEV 137																
210280	DETAIL STRUCTURAL STEELD ELEV 137	9	9	12-Mar-19	22-Mar-19	-7													DETAIL STRUCTURAL STEELD ELEV 137																
200770	TOPPING SLAB C2ND LVL	10	10	18-Mar-19	29-Mar-19	31													TOPPING SLAB C2ND LVL																
210350	MAIN ACCESS STAIRSA	15	15	18-Mar-19	05-Apr-19	-19													MAIN ACCESS STAIRSA																
210360	PRECAST STAIR SHAFT B B	4	4	19-Mar-19	22-Mar-19	-20													PRECAST STAIR SHAFT B B																
211130	PRECAST CONNECTOR	7	7	19-Mar-19	27-Mar-19	183													PRECAST CONNECTOR																
210160	DETAIL STRUCTURAL STEELD LOW ROOF	15	15	19-Mar-19	08-Apr-19	8													DETAIL STRUCTURAL STEELD LOW ROOF																
201050	IN-SLAB PLUMBING D LOW ROOF CL 14-29	5	5	19-Mar-19	25-Mar-19	13													IN-SLAB PLUMBING D LOW ROOF CL 14-29																
201250	IN-SLAB ELECTRICAL D LOW ROOF CL 14-29	5	5	19-Mar-19	25-Mar-19	13													IN-SLAB ELECTRICAL D LOW ROOF CL 14-29																
200890	SLAB ON DECK D ELEV 137 - 4TH LVL	3	3	25-Mar-19	27-Mar-19	-7													SLAB ON DECK D ELEV 137 - 4TH LVL																
210020	PRECASTA (3/3)	15	15	25-Mar-19	12-Apr-19	-24													PRECASTA (3/3)																
210370	PRECAST STAIR SHAFT B D	4	4	25-Mar-19	28-Mar-19	-20													PRECAST STAIR SHAFT B D																
210400	PAN STAIRS B B	5	5	25-Mar-19	29-Mar-19	33													PAN STAIRS B B																

Actual Work  
 Remaining Work  
 Critical Remaining Work  
 Milestone

D/B New Escambia County Correctional Facility  
Pensacola, FL

ECCF14-DEC1 ECCF14 30Dec18 Detailed Baseline Schedule Update - Prelim1  
- 90-Day Schedule 11x17

Page 5 of 6  
03-Jan-19 13:31  
Data Date: 30-Dec-18

Caddell - WGI  
#1054

Activity ID	Activity Name	Orig Dur	Rem Dur	Early Start	Early Finish	Total Float	2018	2019																
								Jan				Feb				Mar								
200700	SLAB ON DECK D ELEV 115 - 3RD LVL	12	12	26-Mar-19	10-Apr-19	23																		
201060	IN-SLAB PLUMBING D LOW ROOF CL 29-50	5	5	26-Mar-19	01-Apr-19	13																		
201260	IN-SLAB ELECTRICAL D LOW ROOF CL 29-50	5	5	26-Mar-19	01-Apr-19	13																		
210030	PRECAST ELEVATOR SHAFTS B	4	4	29-Mar-19	03-Apr-19	-20																		
210410	PAN STAIRS B D	5	5	29-Mar-19	04-Apr-19	29																		
<b>TESTING &amp; CLOSEOUT</b>																								
<b>SITWORK</b>																								
190040	PREPARE & COMPLETE GC/SUB SITE PUNCHLIST - NE JUVENILE PARKING LOT	3	3	05-Feb-19	07-Feb-19	323																		
190050	PREPARE OWNER SITE PUNCHLIST - NE JUVENILE PARKING LOT	1	1	08-Feb-19	08-Feb-19	323																		
190060	COMPLETE OWNER SITE PUNCHLIST - NE JUVENILE PARKING LOT	4	4	11-Feb-19	14-Feb-19	323																		
<b>MODIFICATIONS</b>																								
900006	CHANGE ORDER NO.6	1	0	01-Dec-18 A	30-Dec-18	516																		

■ PREPARE & COMPLETE GC/SUB SITE PUNCHLIST - NE JUVENILE PARKING LOT  
 ■ PREPARE OWNER SITE PUNCHLIST - NE JUVENILE PARKING LOT  
 ■ COMPLETE OWNER SITE PUNCHLIST - NE JUVENILE PARKING LOT

Actual Work  
 Remaining Work  
 Critical Remaining Work  
 Milestone

D/B New Escambia County Correctional Facility  
Pensacola, FL

**ECCF14-DEC1** ECCF14 30Dec18 Detailed Baseline Schedule Update - Prelim1

- 90-Day Schedule 11x17

Page 6 of 6  
03-Jan-19 13:31

Data Date: 30-Dec-18

Caddell - WGI

#1054



## Daily Log: Saturday 12/1/2018

**Daily Log Completed**  
 The Daily Log was completed by Payton Holley on Mon Dec 3, 2018 at 04:49 pm CST.

### WEATHER REPORT

Temperature			Precipitation Since			Humidity				Windspeed		
Low	High	Avg	Midnight	2 Days Ago	3 Days Ago	Low	Avg	High	Dew	Avg	Max	Gust
66°F	72°F	70°F	1.39 in.	1.49 in.	1.49 in.	91%	95%	99%	68°F	11.0 mph	14 mph	23 mph

### DAILY SNAPSHOT

06:00 AM	09:00 AM	12:00 PM	03:00 PM	06:00 PM	09:00 PM
rain 70°F	partly-cloudy-day 72°F	rain 69°F	rain 71°F	rain 70°F	rain 71°F

### MANPOWER LOG

11 Workers | 55.0 Man Hours

No.	Contact/Company	Cost Code	Workers	# Hours	Man Hours	Location
1	Caddell Construction Co. (DE), LLC		1	5.0	5.0	Site
<b>Notes:</b> WGI/Caddell supervision, quality control and safety onsite.						
2	A&B Electric Co., Inc.		1	5.0	5.0	
<b>Notes:</b> Markup remedial precast panels. Survey Area "A" below grade conduit layout						
3	Tindall Corporation		9	5.0	45.0	Building>C
<b>Notes:</b> Precast Erection Rained out. Crew stayed to grout and weld out embeds from 14 to 50-line, elevation 81 to 115.						
			<b>11</b>	<b>55.0</b>		

### Manpower Log's Attachments:

- 2. A&B Electric Co., Inc.

**Daily Construction Report**

Contract Number: 1054  
 Project Number: 1054-18-001  
 Report Date: 12/1/18 2:51 PM  
 Weather: 40°F  
 Temp: 41  
 Daily High: 72  
 Daily Low: 69  
 Completed on: 12/1/18 7:20 PM

[Daily Construction Report -- 12\\_1\\_18.pdf](#)

PHOTOS



DJI\_0085.jpg



DJI\_0068.jpg



DJI\_0091.jpg



DJI\_0080.jpg



DJI\_0076.jpg



DJI\_0078.jpg



DJI\_0079.jpg



DJI\_0097.jpg



[DJI\\_0072.jpg](#)



[DJI\\_0074.jpg](#)



[DJI\\_0086.jpg](#)



[DJI\\_0067.jpg](#)



[DJI\\_0087.jpg](#)



[DJI\\_0093.jpg](#)



[DJI\\_0073.jpg](#)



[DJI\\_0082.jpg](#)



[DJI\\_0118.jpg](#)



[DJI\\_0069.jpg](#)



[DJI\\_0095.jpg](#)



[DJI\\_0116.jpg](#)



[DJI\\_0092.jpg](#)



[DJI\\_0065.jpg](#)



[DJI\\_0081.jpg](#)



[DJI\\_0062.jpg](#)





[DJI\\_0064.jpg](#)



[DJI\\_0112.jpg](#)

### OBSERVED WEATHER CONDITIONS

No.	Weather Delay	Sky	Temp	Average	Precipitation	Wind	Ground/Sea
1	No	Rain	Mild		3 in.		

By \_\_\_\_\_

Date \_\_\_\_\_

Copies To \_\_\_\_\_



## Daily Log: Sunday 12/2/2018

**Daily Log Completed**  
 The Daily Log was completed by Payton Holley on Mon Dec 3, 2018 at 04:47 pm CST.

### WEATHER REPORT

Temperature			Precipitation Since			Humidity				Windspeed		
Low	High	Avg	Midnight	2 Days Ago	3 Days Ago	Low	Avg	High	Dew	Avg	Max	Gust
61°F	72°F	68°F	0.39 in.	1.77 in.	1.87 in.	65%	88%	100%	64°F	3.6 mph	11 mph	19 mph

### DAILY SNAPSHOT

06:00 AM	09:00 AM	12:00 PM	03:00 PM	06:00 PM	09:00 PM
cloudy 70°F	cloudy 68°F	partly-cloudy-day 71°F	cloudy 71°F	partly-cloudy-night 65°F	partly-cloudy-night 61°F

### MANPOWER LOG

11 Workers | 88.0 Man Hours

No.	Contact/Company	Cost Code	Workers	# Hours	Man Hours	Location
1	A&B Electric Co., Inc.		1	8.0	8.0	Site
<b>Notes:</b> Review lighting controls, markup remedial precast wall panels, assist dewatering entry at juvenile justice parking lot						
2	Caddell Construction Co. (DE), LLC		1	8.0	8.0	Site
<b>Notes:</b> WGI/Caddell supervision, quality control and safety onsite.						
3	Tindall Corporation		9	8.0	72.0	Building>C
<b>Notes:</b> Precast Erection Rained out. Crew stayed to grout and weld out embeds from 14 to 50-line, elevation 81 to 115.						
			<b>11</b>	<b>88.0</b>		

### Manpower Log's Attachments:

- A&B Electric Co., Inc.

**Daily Construction Report**

Contract Number:  
00000  
Project Number:  
000000000  
Report Date:  
12/02/2018 02:52 PM  
Weather:  
CLOUDY  
Temp:  
61  
Wind High:  
78  
Wind Low:  
0  
Completed on:  
12/02/2018 02:52 PM

[Daily Construction Report -- 12\\_2\\_18.pdf](#)

## OBSERVED WEATHER CONDITIONS

No.	Weather Delay	Sky	Temp	Average	Precipitation	Wind	Ground/Sea
1	No						

---

By

Date

Copies To



## Daily Log: Monday 12/3/2018

### WEATHER REPORT

Temperature			Precipitation Since			Humidity				Windspeed		
Low	High	Avg	Midnight	2 Days Ago	3 Days Ago	Low	Avg	High	Dew	Avg	Max	Gust
52°F	71°F	62°F	0.04 in.	0.43 in.	1.81 in.	42%	72%	96%	52°F	4.2 mph	8 mph	13 mph

### DAILY SNAPSHOT

06:00 AM	09:00 AM	12:00 PM	03:00 PM	06:00 PM	09:00 PM
cloudy 60°F	rain 61°F	partly-cloudy-day 69°F	partly-cloudy-day 72°F	clear-night 62°F	clear-night 57°F

### MANPOWER LOG

63 Workers | 588.0 Man Hours

No.	Contact/Company	Cost Code	Workers	# Hours	Man Hours	Location
1	A&B Electric Co., Inc.		7	10.0	70.0	Site
<b>Notes:</b> Work on rental property, Locate existing conduits for camera and light pole circuits in the back where tie in to existing prison takes place for grade beams.						
2	Bayside Structures, LLC		6	8.0	48.0	Site
<b>Notes:</b> Poured pour one in sally port. Had to regrade everything in the connector due to rain over the weekend.						
3	Caddell Construction Co. (DE), LLC		9	10.5	94.5	Site
<b>Notes:</b> WGI/Caddell supervision, quality control and safety onsite.						
4	Chavers Construction Inc.		4	8.0	32.0	Site
<b>Notes:</b> Excavation for S-7 Storm Manhole.						
5	Tindall Corporation		19	10.5	199.5	Building>D
<b>Notes:</b> **Erecting panels near corridor between lines 3 and 17 **Welding and grouting						
6	Ed Emmons Steel Erectors, Inc.		10	8.0	80.0	Building>D
<b>Notes:</b> Erected structural steel at elevation 100 in Area D. Also, welded angel at corridor in same area.						
7	EAA Site Contractors LLC		8	8.0	64.0	Site
<b>Notes:</b> Total man hours 80. The JJC parking lot was completely flooded Saturday. The water entering the storm drains has no where to go and backs up into the parking lot. Pete pumped the water out Sunday. We removed the remaining asphalt at the St Mary entrance and filled with base material. All base for parking lot has been placed. We continued to compact base but the material is too wet to test for density. There wasn't any backfilling conducted in the bldg pad today. All dirt delivery was stopped on Pete's instructions. Friday 67 loads of dirt was delivered.						
			<b>63</b>	<b>588.0</b>		


### Manpower Log's Attachments:

1. A&B Electric Co., Inc.



[Daily Construction Report -- 12\\_3\\_18.pdf](#)

2. Bayside Structures, LLC




[Bayside Daily Report 120318.pdf](#)

5. Tindall Corporation

[Tindall Escambia Daily 12-3-18.xlsx](#)

6. Ed Emmons Steel Erectors, Inc.

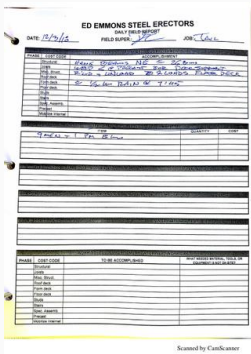

[New Doc 2018-12-03 15.13.35\\_1.pdf](#)

**OBSERVED WEATHER CONDITIONS**

No.	Weather Delay	Sky	Temp	Average	Precipitation	Wind	Ground/Sea
1	No	Clear	Cold	62	0	Calm	Wet/Muddy

---

By

---

Date

---

Copies To



## Daily Log: Tuesday 12/4/2018

### WEATHER REPORT

Temperature			Precipitation Since			Humidity				Windspeed		
Low	High	Avg	Midnight	2 Days Ago	3 Days Ago	Low	Avg	High	Dew	Avg	Max	Gust
42°F	58°F	49°F	0.00 in.	0.04 in.	0.43 in.	43%	63%	78%	37°F	7.5 mph	11 mph	16 mph

### DAILY SNAPSHOT

06:00 AM	09:00 AM	12:00 PM	03:00 PM	06:00 PM	09:00 PM
clear-night 44°F	clear-day 49°F	clear-day 56°F	clear-day 59°F	clear-night 49°F	clear-night 43°F

### MANPOWER LOG

47 Workers | 408.0 Man Hours

No.	Contact/Company	Cost Code	Workers	# Hours	Man Hours	Location
1	A&B Electric Co., Inc.		7	10.0	70.0	Site>Juvenile Justice Parking Lot
<b>Notes:</b> Grout pole bases, Drill and remount anchor bolt cover for pole lights, Rub and finish concrete of pole bases. Power up lights and check lighting. (All existing lights & poles) (Juvenile parking)						
2	Bayside Structures, LLC		6	8.0	48.0	Building
<b>Notes:</b> Finished grading connector and one sided 80ft of grade beam in connector.						
3	Caddell Construction Co. (DE), LLC		9	10.0	90.0	Site
<b>Notes:</b> WGI/Caddell supervision, quality control and safety onsite.						
4	Chavers Construction Inc.		4	8.0	32.0	Site
<b>Notes:</b> Excavated and set S-7 manhole, and excavated and installed 24" piping toward manhole S-8.						
5	Ed Emmons Steel Erectors, Inc.		10	8.0	80.0	Site
<b>Notes:</b> Hung out beams to precast panels at elevation 100 in Area D						
6	EAA Site Contractors LLC		10	8.0	80.0	Site
<b>Notes:</b> Total man hours 100. No backfilling or compacting conducted in bldg slab today. Set grades for base material in JJC parking lot. Continuing to grade, compact base and remove clippings. David and Pete had a discussion about the need for a valley curb at St Mary entrance. Pete does not agree with David and plans to continue with the asphalt valley plan.						
7	Larry M. Jacobs & Associates, Inc.		1	8.0	8.0	Site
<b>Notes:</b> Conducted desity Test in loading dock Area D and 2nd and 3rd lift of S7 backfill .						
			<b>47</b>	<b>408.0</b>		

### Manpower Log's Attachments:

1. A&B Electric Co., Inc.




[Daily Construction Report -- 12\\_4\\_18.pdf](#)

2. Bayside Structures, LLC



[Bayside Daily Report 120518.pdf](#)

5. Ed Emmons Steel Erectors, Inc.

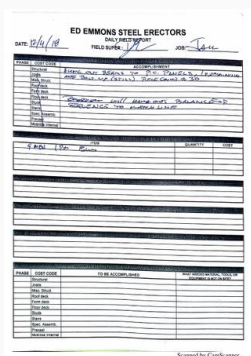

[New Doc 2018-12-04 15.35.46\\_1.pdf](#)

**EQUIPMENT LOG**

No.	Equipment Name	Cost Code	Hrs Operating	Hrs Idle	Inspected?	Inspection Time	Location
1	Kobelco Crane CKE2500		0.0	0.0	No	07:00 AM	Site>C
<b>Notes:</b>							
2	JLG Lift 660SJ		0.0	0.0	No	07:00 AM	Site>C
<b>Notes:</b>							



## EQUIPMENT LOG

No.	Equipment Name	Cost Code	Hrs Operating	Hrs Idle	Inspected?	Inspection Time	Location
3	JLG Lift 660SJ		0.0	0.0	No	07:00 AM	Site>C
	<b>Notes:</b>						
4	JLG Lift 660SJ		0.0	0.0	No	07:00 AM	Site>A
	<b>Notes:</b>						
5	JLG Lift 660SJ		0.0	0.0	No	07:00 AM	Site>A
	<b>Notes:</b>						
6	JLG Skytrak Telehandler		0.0	0.0	No	07:00 AM	Site
	<b>Notes:</b>						
7	JLG Skytrak Telehandler		0.0	0.0	No	07:00 AM	Site
	<b>Notes:</b>						
8	Cat Telehandler		0.0	0.0	No	07:00 AM	Site
	<b>Notes:</b>						
9	L60H Volvo Loader		0.0	0.0	No	07:00 AM	Site
	<b>Notes:</b>						
10	Grove Crane AT700D		0.0	0.0	No	07:00 AM	Site>D
	<b>Notes:</b>						
11	John Deere 85G Excavator		0.0	0.0	No	07:00 AM	Site
	<b>Notes:</b>						
12	Genie GTH-636 Telehandler		0.0	0.0	No	07:00 AM	Site>D
	<b>Notes:</b>						
13	JLG Skytrak Telehandler		0.0	0.0	No	07:00 AM	Site>D
	<b>Notes:</b>						
14	Bobcat Miniexcavator		0.0	0.0	No	07:00 AM	Site
	<b>Notes:</b>						
15	John Deere 700 Dozer		0.0	0.0	No	07:00 AM	Site>Juvenile Justice Parking Lot
	<b>Notes:</b>						
16	Vibratory Roller		0.0	0.0	No	07:00 AM	Site>Juvenile Justice Parking Lot
	<b>Notes:</b>						
17	Komatsu 78MR Excavator		0.0	0.0	No	07:00 AM	Site>Juvenile Justice Parking Lot
	<b>Notes:</b>						
18	Komatsu 320 PT Loader		0.0	0.0	No	07:00 AM	Site>Juvenile Justice Parking Lot
	<b>Notes:</b>						
19	Lee Grader		0.0	0.0	No	07:00 AM	Site>Juvenile Justice Parking Lot
	<b>Notes:</b>						
20	60C Champion Grader		0.0	0.0	No	07:00 AM	Site>Juvenile Justice Parking Lot
	<b>Notes:</b>						

## OBSERVED WEATHER CONDITIONS

No.	Weather Delay	Sky	Temp	Average	Precipitation	Wind	Ground/Sea
1	No	Clear	Cold	49	0	Light Wind	Wet/Muddy

---

By

---

Date

---

Copies To



## Daily Log: Wednesday 12/5/2018

### WEATHER REPORT

Temperature			Precipitation Since			Humidity				Windspeed		
Low	High	Avg	Midnight	2 Days Ago	3 Days Ago	Low	Avg	High	Dew	Avg	Max	Gust
36°F	54°F	43°F	0.00 in.	0.00 in.	0.04 in.	41%	65%	86%	31°F	6.3 mph	9 mph	16 mph

### DAILY SNAPSHOT

06:00 AM	09:00 AM	12:00 PM	03:00 PM	06:00 PM	09:00 PM
clear-night 37°F	partly-cloudy-day 44°F	clear-day 52°F	clear-day 54°F	clear-night 45°F	clear-night 40°F

### MANPOWER LOG

56 Workers | 497.0 Man Hours

No.	Contact/Company	Cost Code	Workers	# Hours	Man Hours	Location
1	A&B Electric Co., Inc.		7	10.0	70.0	
<b>Notes:</b> Working on Juvenile parking light poles, Drill and mount anchor bolt covers, grout bases, grout around bolt cover and dress up pole bases, Turn power on and start checking out pole lights. Tested lights.						
2	Bayside Structures, LLC		6	6.0	36.0	Site
<b>Notes:</b> Forming foundations at connector.						
3	Caddell Construction Co. (DE), LLC		1	8.0	8.0	
<b>Notes:</b> WGI/Caddell supervision, quality control and safety onsite.						
4	Chavers Construction Inc.		4	8.0	32.0	Site
<b>Notes:</b> Backfilling 24" stormwater piping at S-7 Manhole.						
5	Ed Emmons Steel Erectors, Inc.		10	8.0	80.0	Site>D
<b>Notes:</b> Hung and Bolted-up at match line. Prep for deck and next steel deliveries						
6	Larry M. Jacobs & Associates, Inc.		1	1.0	1.0	
<b>Notes:</b> Conducted Density Test in loading dock Area D and 4th left S7						
7	Tindall Corporation		18	10.0	180.0	Site>D
<b>Notes:</b> **Erecting panels in C **Welding and grouting **Patching 181 Total Man Hours						
8	EAA Site Contractors LLC		9	10.0	90.0	Site
<b>Notes:</b> Total man hours 90. No backfilling or compacting conducted in bldg slab today. Continued to grade, compact and remove clippings of base material in JJC parking lot. No density test conducted today. Base is still too wet.						


MANPOWER LOG

56 Workers | 497.0 Man Hours

No. Contact/Company	Cost Code	Workers	# Hours	Man Hours	Location
		56		497.0	


Manpower Log's Attachments:

1. A&B Electric Co., Inc.



[Daily Construction Report - - 12\\_5\\_18.pdf](#)

5. Ed Emmons Steel Erectors, Inc.



[New Doc 2018-12-05 15.16.08\\_1.pdf](#)

7. Tindall Corporation



[Tindall Escambia daily 12-5-18 \(003\).pdf](#)

## EQUIPMENT LOG

No.	Equipment Name	Cost Code	Hrs Operating	Hrs Idle	Inspected?	Inspection Time	Location
1	Kobelco Crane CKE2500				No	07:00 AM	Site>D
	<b>Notes:</b>						
2	JLG Lift 660SJ				No	07:00 AM	Site>D
	<b>Notes:</b>						
3	JLG Lift 660SJ				No	07:00 AM	Site>D
	<b>Notes:</b>						
4	JLG Lift 660SJ				No	07:00 AM	Site
	<b>Notes:</b>						
5	JLG Lift 660SJ				No	07:00 AM	Site
	<b>Notes:</b>						
6	JLG Skytrak Telehandler				No	07:00 AM	Site
	<b>Notes:</b>						
7	JLG Skytrak Telehandler				No	07:00 AM	Site
	<b>Notes:</b>						
8	Bobcat Telehandler				No	07:00 AM	Site
	<b>Notes:</b>						
9	L60H Volvo Loader				No	07:00 AM	Site
	<b>Notes:</b>						
10	Grove Crane AT700D				No	07:00 AM	Site>D
	<b>Notes:</b>						
11	JLG Skytrak Telehandler				No	07:00 AM	Site>D
	<b>Notes:</b>						
12	John Deere 85G Excavator				No	07:00 AM	Site
	<b>Notes:</b>						
13	Genie GTH-636 Telehandler				No	07:00 AM	Site>D
	<b>Notes:</b>						
14	Bobcat Miniexcavator				No	07:00 AM	Site
	<b>Notes:</b>						
15	John Deere 700 Dozer				No	07:00 AM	Site>Juvenile Justice Parking Lot
	<b>Notes:</b>						
16	Vibratory Roller				No	07:00 AM	Site>Juvenile Justice Parking Lot
	<b>Notes:</b>						
17	Komatsu 320 PT Loader				No	07:00 AM	Site>Juvenile Justice Parking Lot
	<b>Notes:</b>						
18	Komatsu 78MR Excavator				No	07:00 AM	Site>Juvenile Justice Parking Lot
	<b>Notes:</b>						

## EQUIPMENT LOG

No.	Equipment Name	Cost Code	Hrs Operating	Hrs Idle	Inspected?	Inspection Time	Location
19	Lee Grader				No	07:00 AM	Site>Juvenile Justice Parking Lot

Notes:

20	60 C Champion Grader				No	07:00 AM	Site>Juvenile Justice Parking Lot
----	----------------------	--	--	--	----	----------	-----------------------------------

Notes:

## OBSERVED WEATHER CONDITIONS

No.	Weather Delay	Sky	Temp	Average	Precipitation	Wind	Ground/Sea
1	No	Clear	Cold	43	0	Light Wind	Dry

By \_\_\_\_\_

Date \_\_\_\_\_

Copies To \_\_\_\_\_



## Daily Log: Thursday 12/6/2018

### WEATHER REPORT

Temperature			Precipitation Since			Humidity				Windspeed		
Low	High	Avg	Midnight	2 Days Ago	3 Days Ago	Low	Avg	High	Dew	Avg	Max	Gust
33°F	54°F	43°F	0.01 in.	0.01 in.	0.01 in.	47%	64%	79%	32°F	3.8 mph	6 mph	7 mph

### DAILY SNAPSHOT

06:00 AM	09:00 AM	12:00 PM	03:00 PM	06:00 PM	09:00 PM
clear-night 34°F	partly-cloudy-day 43°F	partly-cloudy-day 51°F	partly-cloudy-day 54°F	partly-cloudy-night 48°F	clear-night 45°F


### MANPOWER LOG

62 Workers | 593.0 Man Hours

No.	Contact/Company	Cost Code	Workers	# Hours	Man Hours	Location
1	A&B Electric Co., Inc.		7	10.0	70.0	Site>Juvenile Justice Parking Lot
	<b>Notes:</b> Trouble shoot pole lights not working, Finish grouting pole bases, grout around anchor bolt covers, Clean up all trash behind rental property.					
2	Bayside Structures, LLC		6	8.0	48.0	Site
	<b>Notes:</b> Forming around columns in preparation of grouting steel baseplates for sequence 1 of Area D. Continued forms for connector of Area D.					
3	Caddell Construction Co. (DE), LLC		8	11.0	88.0	
	<b>Notes:</b> WGI/Caddell supervision, quality control and safety onsite.					
4	Chavers Construction Inc.		4	10.0	40.0	
	<b>Notes:</b> Excavated and installed fire main piping that crosses under connector. Fire Marshall Quinn inspected at 4 PM, inspection passed. Began backfilling first lift.					
5	Ed Emmons Steel Erectors, Inc.		10	8.0	80.0	Building>D
	<b>Notes:</b> Continued erection of structural steel in area D from elevation 81 to 100 and bolted connections.					
6	Larry M. Jacobs & Associates, Inc.		1	3.0	3.0	
	<b>Notes:</b> Density test at fire main, 3 lifts. Performed density test for base at new JJC Parking Lot.					
7	Tindall Corporation		16	10.5	168.0	Building>C
	<b>Notes:</b> Erected 11 panels in area C. Welding, grouting and patching of panels.					
8	EAA Site Contractors LLC		10	9.6	96.0	Site
	<b>Notes:</b> Total man hours 96. Used the remaining red dirt on site to backfill east side of section D. This did not complete section D. The dirt was also too wet to compact. Loading dock area in section D failed density test. Ruffed up dirt to help it dry. We will lay it back down and seal it tomorrow. Passed density test in JJC parking lot except on heavy duty travel lane. This area is still too wet. Continued to grade and compact base.					
			<b>62</b>	<b>593.0</b>		

**Manpower Log's Attachments:**

1. A&B Electric Co., Inc.

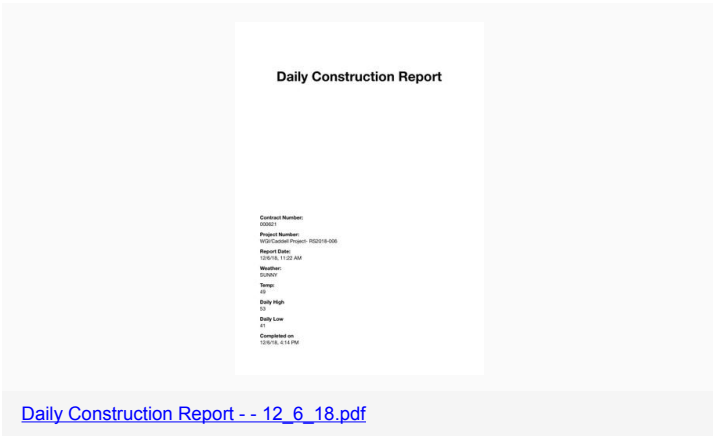

[Daily Construction Report - - 12\\_6\\_18.pdf](#)

7. Tindall Corporation

[Copy of Tindall Escambia daily 12-6-18 \(002\).xlsx](#)

**EQUIPMENT LOG**

No.	Equipment Name	Cost Code	Hrs Operating	Hrs Idle	Inspected?	Inspection Time	Location
1	Kobelco Crane CKE2500				No	07:00 AM	Site>D
	<b>Notes:</b>						
2	JLG Lift 660SJ				No	07:00 AM	Site>D
	<b>Notes:</b>						
3	JLG Lift 660SJ				No	07:00 AM	Site>D
	<b>Notes:</b>						
4	JLG Lift 660SJ				No	07:00 AM	Site
	<b>Notes:</b>						
5	JLG Lift 660SJ				No	07:00 AM	Site
	<b>Notes:</b>						
6	JLG Skytrak Telehandler				No	07:00 AM	Site
	<b>Notes:</b>						
7	JLG Skytrak Telehandler				No	07:00 AM	Site
	<b>Notes:</b>						
8	Cat Telehandler				No	07:00 AM	Site
	<b>Notes:</b>						
9	L60H Volvo Loader				No	07:00 AM	Site
	<b>Notes:</b>						
10	Grove Crane AT700D				No	07:00 AM	Site>D
	<b>Notes:</b>						
11	Genie GTH-636 Telehandler				No	07:00 AM	Site>D
	<b>Notes:</b>						
12	JLG Skytrak Telehandler				No	07:00 AM	Site>D
	<b>Notes:</b>						



## EQUIPMENT LOG

No.	Equipment Name	Cost Code	Hrs Operating	Hrs Idle	Inspected?	Inspection Time	Location
13	John Deere 85G Excavator				No	07:00 AM	Site
	<b>Notes:</b>						
14	Bobcat Miniexcavator				No	07:00 AM	Site
	<b>Notes:</b>						
15	John Deere 700 Dozer				No	07:00 AM	Site>Juvenile Justice Parking Lot
	<b>Notes:</b>						
16	Vibratory Roller				No	07:00 AM	Site>Juvenile Justice Parking Lot
	<b>Notes:</b>						
17	Komatsu 78MR Excavator				No	07:00 AM	Site>Juvenile Justice Parking Lot
	<b>Notes:</b>						
18	Komatsu 320 PT Loader				No	07:00 AM	Site>Juvenile Justice Parking Lot
	<b>Notes:</b>						
19	Lee Grader				No	07:00 AM	Site>Juvenile Justice Parking Lot
	<b>Notes:</b>						
20	60 C Champion Grader				No	07:00 PM	Site>Juvenile Justice Parking Lot
	<b>Notes:</b>						

## INSPECTION LOG

No.	Start Time	End Time	Inspection Type	Inspecting Entity	Inspector Name	Location	Area
1	04:00 PM	04:35 PM	Fire Main Piping Inspection	Escambia County	Joe Quinn	Site	
	<b>Comments:</b> Inspection of fire main, passed.						
2	09:35 AM	12:35 PM	Density Test	LMJ	Manny Colon		
	<b>Comments:</b> Density test on 3 lifts, all 3 passed. Performed density tests at JJC parking lot, all tests passed.						

## PHOTOS



[IMG\\_0500.jpg](#)

Juvenile Justice Parking Lot



[IMG\\_0498.jpg](#)

Precast Erection in Area C

### OBSERVED WEATHER CONDITIONS

No.	Weather Delay	Sky	Temp	Average	Precipitation	Wind	Ground/Sea
1	No	Clear	Cold	43	0	Light Wind	Dry

---

By

---

Date

---

Copies To



## Daily Log: Friday 12/7/2018

### WEATHER REPORT

Temperature			Precipitation Since			Humidity				Windspeed		
Low	High	Avg	Midnight	2 Days Ago	3 Days Ago	Low	Avg	High	Dew	Avg	Max	Gust
38°F	59°F	49°F	0.01 in.	0.01 in.	0.01 in.	46%	67%	91%	38°F	5.4 mph	8 mph	16 mph

### DAILY SNAPSHOT

06:00 AM	09:00 AM	12:00 PM	03:00 PM	06:00 PM	09:00 PM
clear-night 40°F	clear-day 51°F	clear-day 59°F	partly-cloudy-day 60°F	partly-cloudy-night 54°F	partly-cloudy-night 52°F

### MANPOWER LOG

51 Workers | 448.0 Man Hours

No.	Contact/Company	Cost Code	Workers	# Hours	Man Hours	Location
1	Caddell Construction Co. (DE), LLC		6	10.0	60.0	
<b>Notes:</b> WGI/Caddell quality control, supervision and safety onsite.						
2	A&B Electric Co., Inc.		8	10.0	80.0	Site>Juvenile Justice Parking Lot
<b>Notes:</b> Finish up grouting of pole bases and clean anchor bolt covers, Trouble shoot fixture not working, Rental property clean up of old lumber, Build frames for temporary power backboards.						
3	Ed Emmons Steel Erectors, Inc.		10	8.0	80.0	Building>D
<b>Notes:</b> Install metal deck in Area D, weld and snug bolts.						
4	EAA Site Contractors LLC		4	7.75	31.0	Site
<b>Notes:</b> Total man hours 31. Conducted hand work at ST Mary entrance, along curb edges and islands. Continued to roll and light compaction. Sealed up to prep for rain. There are still some soft spots in parking lot. We also lightly compacted and sealed the dirt in section D and the loading dock. Again to prep for rain.						
5	Chavers Construction Inc.		4	8.0	32.0	Site
<b>Notes:</b> Excavated and installed domestic water piping under connector foundation.						
6	Tindall Corporation		16	10.0	160.0	Building>C
<b>Notes:</b> Erecting 9 precast pieces in area C. Continued to grout precast in corridor on level 3.						
7	Larry M. Jacobs & Associates, Inc.		1	3.0	3.0	Site
<b>Notes:</b> Density tests for domestic water piping backfill at connector. All lifts passed. Performed 1 density test at JJC parking lot, it passed.						
8	Ruben Surveying		2	1.0	2.0	
<b>Notes:</b> Received remaining as-builts at connector for auger cast pile locations.						
			<b>51</b>	<b>448.0</b>		

### Manpower Log's Attachments:

3. Ed Emmons Steel Erectors, Inc.

**ED EMMONS STEEL ERECTORS**  
DAILY FIELD REPORT

DATE: 12/07/18 FIELD SUPERVISOR: JOB:

TIME	ACTIVITY	OPERATOR
06:00	Site inspection	John Doe
07:00	Equipment check	John Doe
08:00	Work start	John Doe
09:00	Installation of steel beams	John Doe
10:00	Break	John Doe
11:00	Continuation of steel beam installation	John Doe
12:00	Lunch	John Doe
13:00	Work resumes	John Doe
14:00	Installation of steel beams	John Doe
15:00	Work ends	John Doe

REMARKS: 1 x 20' 25' BEAMS

Site: Whitesell Green / Caddell

Scanned by CamScanner

[Emmons Daily Report 2018-12-07 15.00.04.pdf](#)

**OBSERVED WEATHER CONDITIONS**

No.	Weather Delay	Sky	Temp	Average	Precipitation	Wind	Ground/Sea
1	No	Clear	Cold			Light Wind	

By \_\_\_\_\_

Date \_\_\_\_\_

Copies To \_\_\_\_\_



**Whitesell Green / Caddell, a Joint Venture**  
 2700 Lagoon Park Drive  
 Montgomery, Alabama 36109  
 P: (334) 272-7723  
 F: (334) 394-0193

**Project: 1054 - Escambia County Correctional Facility**  
 3080 N. Pace Boulevard  
 Pensacola, Florida 32501

## Daily Log: Saturday 12/8/2018

### WEATHER REPORT

Temperature			Precipitation Since			Humidity				Windspeed		
Low	High	Avg	Midnight	2 Days Ago	3 Days Ago	Low	Avg	High	Dew	Avg	Max	Gust
49°F	68°F	56°F	0.71 in.	0.72 in.	0.72 in.	62%	80%	98%	50°F	8.4 mph	15 mph	25 mph

### DAILY SNAPSHOT

06:00 AM	09:00 AM	12:00 PM	03:00 PM	06:00 PM	09:00 PM
cloudy 50°F	cloudy 53°F	cloudy 56°F	cloudy 58°F	rain 63°F	rain 68°F

### MANPOWER LOG

17 Workers | 136.0 Man Hours

No.	Contact/Company	Cost Code	Workers	# Hours	Man Hours	Location
1	Caddell Construction Co. (DE), LLC		1	8.0	8.0	Site
<b>Notes:</b> WGI/Caddell quality control, supervision and safety onsite.						
2	Tindall Corporation		16	8.0	128.0	Building>C
<b>Notes:</b> Erected 4 pieces of precast in area C, and grouted level 3 corridor precast from 3 line to 17.5. Rained out at 1pm.						
			<b>17</b>	<b>136.0</b>		

### OBSERVED WEATHER CONDITIONS

No.	Weather Delay	Sky	Temp	Average	Precipitation	Wind	Ground/Sea
1	Yes	Rain	Cold		2-3/8"	High Wind	

By \_\_\_\_\_

Date \_\_\_\_\_

Copies To \_\_\_\_\_



**Whitesell Green / Caddell, a Joint Venture**  
 2700 Lagoon Park Drive  
 Montgomery, Alabama 36109  
 P: (334) 272-7723  
 F: (334) 394-0193

**Project: 1054 - Escambia County Correctional Facility**  
 3080 N. Pace Boulevard  
 Pensacola, Florida 32501

## Daily Log: Sunday 12/9/2018

### WEATHER REPORT

Temperature			Precipitation Since			Humidity				Windspeed		
Low	High	Avg	Midnight	2 Days Ago	3 Days Ago	Low	Avg	High	Dew	Avg	Max	Gust
43°F	61°F	50°F	0.01 in.	0.72 in.	0.73 in.	77%	88%	99%	47°F	8.2 mph	10 mph	20 mph

### DAILY SNAPSHOT

06:00 AM	09:00 AM	12:00 PM	03:00 PM	06:00 PM	09:00 PM
cloudy 51°F	cloudy 49°F	cloudy 51°F	cloudy 51°F	cloudy 47°F	cloudy 45°F

### MANPOWER LOG

18 Workers | 108.0 Man Hours

No.	Contact/Company	Cost Code	Workers	# Hours	Man Hours	Location
1	Tindall Corporation		16	6.0	96.0	Building
<b>Notes:</b> Continued grouting level 3, 3 line to 17.5 line. Removed wall braces for precast in level 1, from 17.5 line to 50 line.						
2	Caddell Construction Co. (DE), LLC		2	6.0	12.0	Site
<b>Notes:</b> WGI/Caddell quality control, supervision and safety onsite. 1 Laborer.						
			<b>18</b>	<b>108.0</b>		

### OBSERVED WEATHER CONDITIONS

No.	Weather Delay	Sky	Temp	Average	Precipitation	Wind	Ground/Sea
1	No	Overcast	Cold		>0.1	Light Wind	

By \_\_\_\_\_

Date \_\_\_\_\_

Copies To \_\_\_\_\_



## Daily Log: Monday 12/10/2018

**Daily Log Completed**  
 The Daily Log was completed by Donald Shelton on Mon Dec 17, 2018 at 07:21 am CST.

### WEATHER REPORT

Temperature			Precipitation Since			Humidity				Windspeed		
Low	High	Avg	Midnight	2 Days Ago	3 Days Ago	Low	Avg	High	Dew	Avg	Max	Gust
39°F	43°F	42°F	0.00 in.	0.01 in.	0.72 in.	78%	82%	88%	37°F	7.1 mph	10 mph	15 mph

### DAILY SNAPSHOT

06:00 AM	09:00 AM	12:00 PM	03:00 PM	06:00 PM	09:00 PM
cloudy 41°F	cloudy 40°F	cloudy 42°F	cloudy 43°F	cloudy 43°F	cloudy 43°F

### MANPOWER LOG

46 Workers | 442.5 Man Hours

No.	Contact/Company	Cost Code	Workers	# Hours	Man Hours	Location	
1	A&B Electric Co., Inc.		6	10.0	60.0	Site	
<b>Notes:</b> Working on temporary power, Build temporary backboards.							
2	Bayside Structures, LLC		6	8.0	48.0	Site	
<b>Notes:</b> Continued grading and reinforcing on connector grade beams and PC-3's. Began to grout base plates in area D.							
3	Caddell Construction Co. (DE), LLC		9	10.5	94.5	Site	
<b>Notes:</b> WGI/Caddell supervision, quality control and safety onsite.							
4	Ed Emmons Steel Erectors, Inc.		9	8.0	72.0	Site>D	
<b>Notes:</b> Unloaded three truck, stood column at sequence 2 elevation 81-100, welded column at North End, and installed deck support angle at west precast.							
5	Tindall Corporation		16	10.5	168.0	Site	
<b>Notes:</b> **Erecting near roof line on corridor **Grouting and welding **Patching							
			<b>46</b>	<b>442.5</b>			

#### Manpower Log's Attachments:

1. A&B Electric Co., Inc.




[Daily Construction Report -- 12\\_10\\_18.pdf](#)

2. Bayside Structures, LLC



[Bayside Daily Report 121018.pdf](#)

4. Ed Emmons Steel Erectors, Inc.

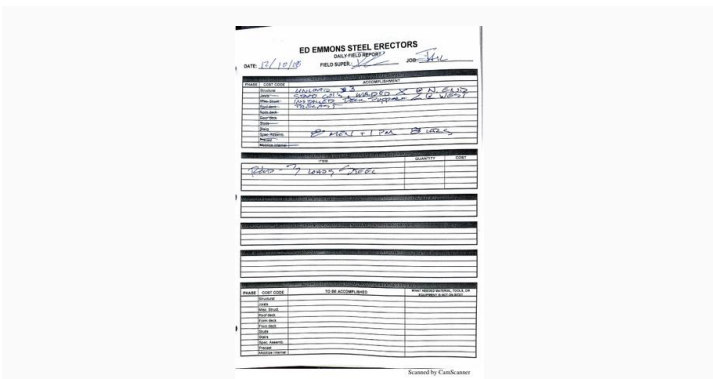

[New Doc 2018-12-10 15.28.20.pdf](#)

5. Tindall Corporation

[Tindall Escambia daily 12-10-18.xlsx](#)

**EQUIPMENT LOG**

No.	Equipment Name	Cost Code	Hrs Operating	Hrs Idle	Inspected?	Inspection Time	Location
1	Kobelco Crane CKE2500				No	07:00 AM	Site>D

**Notes:**



## EQUIPMENT LOG

No.	Equipment Name	Cost Code	Hrs Operating	Hrs Idle	Inspected?	Inspection Time	Location
2	JLG Lift 660SJ				No	07:00 AM	Site>D
	<b>Notes:</b>						
3	JLG Lift 660SJ				No	07:00 AM	Site>D
	<b>Notes:</b>						
4	JLG Lift 660SJ				No	07:00 AM	Site
	<b>Notes:</b>						
5	JLG Lift 660SJ				No	07:00 AM	Site
	<b>Notes:</b>						
6	Genie GTH-636 Telehandler				No	07:00 AM	Site
	<b>Notes:</b>						
7	Genie GTH-636 Telehandler				No	07:00 AM	Site
	<b>Notes:</b>						
8	JLG Skytrak Telehandler				No	07:00 AM	Site
	<b>Notes:</b>						
9	JLG Skytrak Telehandler				No	07:00 AM	Site
	<b>Notes:</b>						
10	Cat Telehandler				No	07:00 AM	Site
	<b>Notes:</b>						
11	Bobcat Miniexcavator				No	07:00 AM	Site
	<b>Notes:</b>						
12	CAT Miniexcavator				No	07:00 AM	Site
	<b>Notes:</b>						

## OBSERVED WEATHER CONDITIONS

No.	Weather Delay	Sky	Temp	Average	Precipitation	Wind	Ground/Sea
1	No	Cloudy	Cold	42	0	Light Wind	Wet/Muddy

By \_\_\_\_\_

Date \_\_\_\_\_

Copies To \_\_\_\_\_



## Daily Log: Tuesday 12/11/2018

**Daily Log Completed**  
 The Daily Log was completed by Donald Shelton on Mon Dec 17, 2018 at 07:21 am CST.

### WEATHER REPORT

Temperature			Precipitation Since			Humidity				Windspeed		
Low	High	Avg	Midnight	2 Days Ago	3 Days Ago	Low	Avg	High	Dew	Avg	Max	Gust
34°F	56°F	44°F	0.00 in.	0.00 in.	0.01 in.	42%	74%	95%	36°F	3.8 mph	8 mph	10 mph

### DAILY SNAPSHOT

06:00 AM	09:00 AM	12:00 PM	03:00 PM	06:00 PM	09:00 PM
partly-cloudy-night 41°F	partly-cloudy-day 44°F	clear-day 53°F	clear-day 57°F	clear-night 44°F	clear-night 38°F


### MANPOWER LOG

42 Workers | 385.0 Man Hours

No.	Contact/Company	Cost Code	Workers	# Hours	Man Hours	Location
1	A&B Electric Co., Inc.		7	10.0	70.0	Site
<b>Notes:</b> Build rack for 400 amp temporary panel, Mount panel and install						
2	Bayside Structures, LLC		6	8.0	48.0	Site
<b>Notes:</b> Finished one siding remainder of west grade beam in connector and began one siding the remainder of the East grade beam in the connector. Formed (Qty:1) PC-3 in the connector. Finished excavating the connector. Continued grouting base plates for pour 1 in Area D.						
3	Caddell Construction Co. (DE), LLC		1	8.0	8.0	Site
<b>Notes:</b> WGI/Caddell supervision, quality control and safety onsite.						
4	Ed Emmons Steel Erectors, Inc.		9	8.0	72.0	Site>D
<b>Notes:</b> Install composite deck to match line, prep for studs, and prep for perimeter cables.						
5	Tindall Corporation		18	10.0	180.0	Site
<b>Notes:</b> **Erecting near roof line on corridor **Grouting and welding **Patching Total of 182 Man Hours						
6	Larry M. Jacobs & Associates, Inc.		1	7.0	7.0	Site
<b>Notes:</b> Inspecting welds on precast						
			<b>42</b>	<b>385.0</b>		

#### Manpower Log's Attachments:

1. A&B Electric Co., Inc.

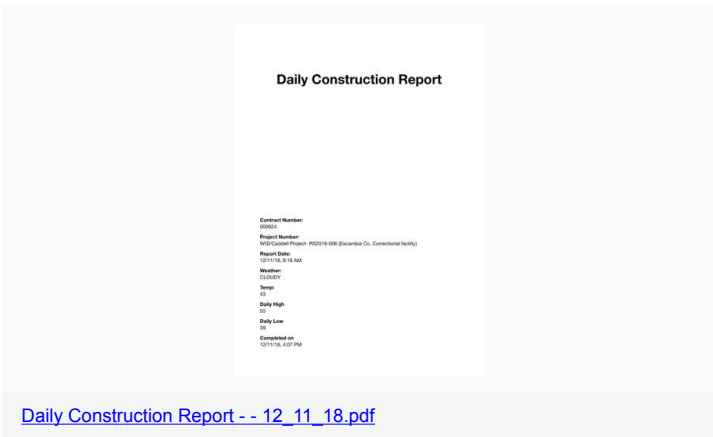


[Daily Construction Report -- 12\\_11\\_18.pdf](#)

2. Bayside Structures, LLC



[Bayside Daily Report 121118.pdf](#)

4. Ed Emmons Steel Erectors, Inc.

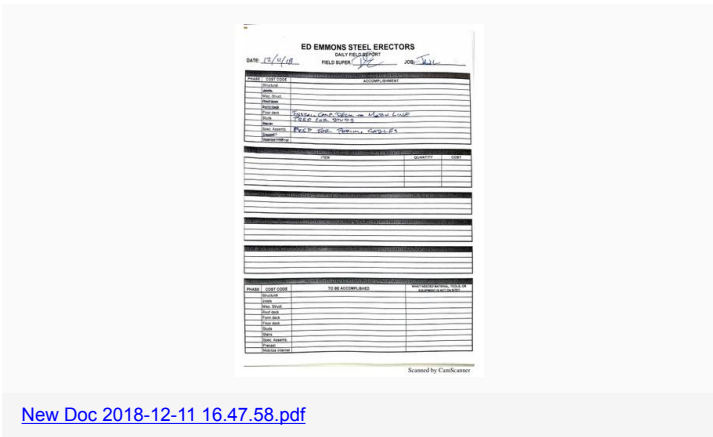

[New Doc 2018-12-11 16.47.58.pdf](#)

5. Tindall Corporation

[Tindall Escambia daily 12-11-18.xlsx](#)

**EQUIPMENT LOG**

No.	Equipment Name	Cost Code	Hrs Operating	Hrs Idle	Inspected?	Inspection Time	Location
1	Kobelco Crane CKE2500				No	07:00 AM	Site>C

**Notes:**

## EQUIPMENT LOG

No.	Equipment Name	Cost Code	Hrs Operating	Hrs Idle	Inspected?	Inspection Time	Location
2	JLG Lift 660SJ				No	07:00 AM	Site>C
	<b>Notes:</b>						
3	JLG Lift 660SJ				No	07:00 AM	Site>C
	<b>Notes:</b>						
4	JLG Lift 660SJ				No	07:00 AM	Site
	<b>Notes:</b>						
5	JLG Lift 660SJ				No	07:00 AM	Site
	<b>Notes:</b>						
6	JLG Lift 660SJ				No	07:00 AM	Site>D
	<b>Notes:</b>						
7	JLG Skytrak Telehandler				No	07:00 AM	Site>D
	<b>Notes:</b>						
8	JLG Skytrak Telehandler				No	07:00 AM	Site
	<b>Notes:</b>						
9	Bobcat Telehandler				No	07:00 AM	Site
	<b>Notes:</b>						
10	Grove Crane AT700D				No	07:00 AM	Site>D
	<b>Notes:</b>						
11	Genie GTH-636 Telehandler				No	07:00 AM	Site
	<b>Notes:</b>						
12	Genie GTH-636 Telehandler				No	07:00 AM	Site
	<b>Notes:</b>						
13	Sky Power Lift 600AJ				No	07:00 AM	Site>B
	<b>Notes:</b>						
14	CAT Miniexcavator				No	07:00 AM	Site>A
	<b>Notes:</b>						
15	Bobcat Miniexcavator				No	07:00 AM	Site
	<b>Notes:</b>						

## OBSERVED WEATHER CONDITIONS

No.	Weather Delay	Sky	Temp	Average	Precipitation	Wind	Ground/Sea
1	No	Clear	Mild	45	0	Calm	Wet/Muddy

By \_\_\_\_\_

Date \_\_\_\_\_

Copies To \_\_\_\_\_



## Daily Log: Wednesday 12/12/2018

**Daily Log Completed**  
 The Daily Log was completed by Donald Shelton on Mon Dec 17, 2018 at 07:20 am CST.

### WEATHER REPORT

Temperature			Precipitation Since			Humidity				Windspeed		
Low	High	Avg	Midnight	2 Days Ago	3 Days Ago	Low	Avg	High	Dew	Avg	Max	Gust
31°F	61°F	47°F	0.00 in.	0.00 in.	0.00 in.	57%	81%	100%	41°F	3.4 mph	7 mph	8 mph

### DAILY SNAPSHOT

06:00 AM	09:00 AM	12:00 PM	03:00 PM	06:00 PM	09:00 PM
clear-night 32°F	partly-cloudy-day 44°F	partly-cloudy-day 60°F	partly-cloudy-day 61°F	partly-cloudy-night 55°F	partly-cloudy-night 57°F

### MANPOWER LOG

43 Workers | 402.0 Man Hours

No.	Contact/Company	Cost Code	Workers	# Hours	Man Hours	Location	
1	A&B Electric Co., Inc.		2	10.0	20.0	Site	
<b>Notes:</b> Working on new 400amp temporary panel, finish dirt work, pull strings in conduit, finish fence around panel and paint support legs hi-vis to help heavy equipment with visibility of new panel location.							
2	Bayside Structures, LLC		6	8.0	48.0	Site	
<b>Notes:</b> Finish one siding east grade beam in connector. Begin tying rebar on east grade beam in connector.							
3	Caddell Construction Co. (DE), LLC		9	10.0	90.0	Site	
<b>Notes:</b> WGI/Caddell supervision, quality control and safety onsite.							
4	Ed Emmons Steel Erectors, Inc.		8	8.0	64.0	Site>D	
<b>Notes:</b> Shot studs at NE to West. Approximate 50% complete							
5	Tindall Corporation		18	10.0	180.0	Site	
<b>Notes:</b> **Erecting near roof line on corridor and just east **Grouting and welding **Patching 170 Total Man Hours							
			<b>43</b>	<b>402.0</b>			

#### Manpower Log's Attachments:

1. A&B Electric Co., Inc.




Daily Construction Report -- 12\_12\_18.pdf

2. Bayside Structures, LLC



Bayside Daily Report 121218.pdf

4. Ed Emmons Steel Erectors, Inc.



New Doc 2018-12-12 14.55.39.pdf

5. Tindall Corporation

Tindall Escambia daily 12-12-18.xlsx

EQUIPMENT LOG

No.	Equipment Name	Cost Code	Hrs Operating	Hrs Idle	Inspected?	Inspection Time	Location
1	Kobelco Crane CKE2500				No	07:00 AM	Site>C

Notes:

**EQUIPMENT LOG**

No.	Equipment Name	Cost Code	Hrs Operating	Hrs Idle	Inspected?	Inspection Time	Location
2	JLG Lift 660SJ				No	07:00 AM	Site>C
	<b>Notes:</b>						
3	JLG Lift 660SJ				No	07:00 AM	Site>C
	<b>Notes:</b>						
4	JLG Lift 660SJ				No	07:00 AM	Site
	<b>Notes:</b>						
5	Sky Power Lift 600AJ				No	07:00 AM	Site
	<b>Notes:</b>						
6	Genie Lift S80				No	07:05 PM	Site
	<b>Notes:</b>						
7	Genie Lift S85				No	07:05 PM	Site
	<b>Notes:</b>						
8	JLG Skytrak Telehandler				No	07:05 PM	Site
	<b>Notes:</b>						
9	JLG Skytrak Telehandler				No	07:05 PM	Site
	<b>Notes:</b>						
10	JLG Skytrak Telehandler				No	07:05 PM	Site>D
	<b>Notes:</b>						
11	Grove Crane AT700D				No	07:05 PM	Site>D
	<b>Notes:</b>						
12	Bobcat Miniexcavator				No	07:05 PM	Site
	<b>Notes:</b>						

**OBSERVED WEATHER CONDITIONS**

No.	Weather Delay	Sky	Temp	Average	Precipitation	Wind	Ground/Sea
1	No	Clear	Mild	47	0	Calm	Wet/Muddy

By \_\_\_\_\_

Date \_\_\_\_\_

Copies To \_\_\_\_\_



## Daily Log: Thursday 12/13/2018

**Daily Log Completed**  
 The Daily Log was completed by Donald Shelton on Mon Dec 17, 2018 at 07:17 am CST.

### WEATHER REPORT

Temperature			Precipitation Since			Humidity				Windspeed		
Low	High	Avg	Midnight	2 Days Ago	3 Days Ago	Low	Avg	High	Dew	Avg	Max	Gust
54°F	63°F	58°F	0.73 in.	0.73 in.	0.73 in.	78%	89%	97%	55°F	6.7 mph	11 mph	28 mph

### DAILY SNAPSHOT

06:00 AM	09:00 AM	12:00 PM	03:00 PM	06:00 PM	09:00 PM
cloudy 56°F	cloudy 55°F	cloudy 61°F	cloudy 63°F	cloudy 60°F	rain 59°F

### MANPOWER LOG


36 Workers | 328.0 Man Hours

No.	Contact/Company	Cost Code	Workers	# Hours	Man Hours	Location
1	EAA Site Contractors LLC		1	8.0	8.0	Site
	<b>Notes:</b> The striping and signage preconstruction meeting was held today. EAA and GCTE was present at the meeting. Asphalt paving was scheduled for the JJC parking lot today but unexpected rain required re scheduling. No work was conducted today.					
2	A&B Electric Co., Inc.		2	10.0	20.0	Site
	<b>Notes:</b> Working on rental property, Building temporary panels .					
3	Caddell Construction Co. (DE), LLC		9	10.0	90.0	Site
	<b>Notes:</b> WGI/Caddell supervision, quality control and safety onsite.					
4	Tindall Corporation		18	9.0	162.0	Site
	<b>Notes:</b> **Erecting near roof line on corridor and just east **Grouting and welding					
5	Bayside Structures, LLC		6	8.0	48.0	Site
	<b>Notes:</b> Continued rebar in East and West grade beams on the connector.					
			<b>36</b>		<b>328.0</b>	

#### Manpower Log's Attachments:



2. A&B Electric Co., Inc.

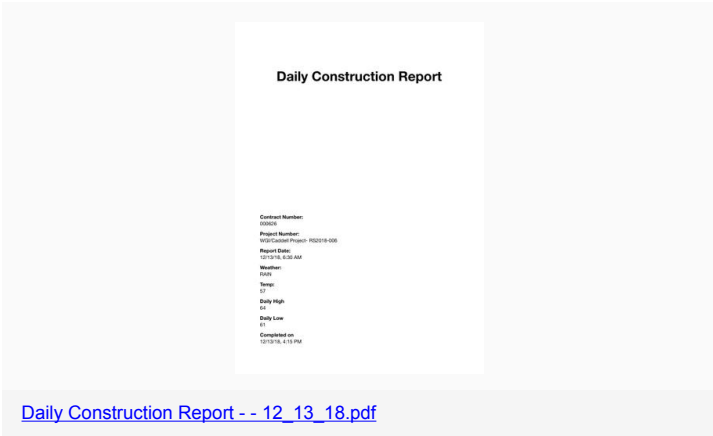

4. Tindall Corporation

[Tindall Escambia Daily 12-13-18.xlsx](#)

5. Bayside Structures, LLC



**EQUIPMENT LOG**

No.	Equipment Name	Cost Code	Hrs Operating	Hrs Idle	Inspected?	Inspection Time	Location
1	Kobelco Crane CKE2500				No	07:00 AM	Site>D
	<b>Notes:</b>						
2	Genie Lift S80				No	07:00 AM	Site
	<b>Notes:</b>						
3	JLG Lift 660SJ				No	07:00 AM	Site
	<b>Notes:</b>						
4	JLG Lift 860SJ				No	07:00 AM	Site
	<b>Notes:</b>						
5	JLG Skytrak Telehandler				No	07:00 AM	Site
	<b>Notes:</b>						

**OBSERVED WEATHER CONDITIONS**

No.	Weather Delay	Sky	Temp	Average	Precipitation	Wind	Ground/Sea
-----	---------------	-----	------	---------	---------------	------	------------

## OBSERVED WEATHER CONDITIONS

1	Yes	Rain	Mild	58	1/2"	Calm	Wet/Muddy	
---	-----	------	------	----	------	------	-----------	---

### Observed Weather Conditions' Attachments:

1



[IMG\\_0157.jpg](#)

By

Date

Copies To



## Daily Log: Friday 12/14/2018

**Daily Log Completed**  
 The Daily Log was completed by Donald Shelton on Mon Dec 17, 2018 at 10:53 am CST.

### WEATHER REPORT

Temperature			Precipitation Since			Humidity				Windspeed		
Low	High	Avg	Midnight	2 Days Ago	3 Days Ago	Low	Avg	High	Dew	Avg	Max	Gust
55°F	68°F	62°F	0.11 in.	0.85 in.	0.85 in.	79%	90%	98%	59°F	8.6 mph	12 mph	25 mph

### DAILY SNAPSHOT

06:00 AM	09:00 AM	12:00 PM	03:00 PM	06:00 PM	09:00 PM
cloudy 65°F	cloudy 65°F	partly-cloudy-day 69°F	cloudy 59°F	partly-cloudy-night 58°F	partly-cloudy-night 57°F


### MANPOWER LOG

45 Workers | 436.0 Man Hours

No.	Contact/Company	Cost Code	Workers	# Hours	Man Hours	Location	
1	A&B Electric Co., Inc.		2	10.0	20.0	Site	
	<b>Notes:</b> Working on temporary panel backboards						
2	Bayside Structures, LLC		1	8.0	8.0	Site	
	<b>Notes:</b> No work Water flooded connector.						
3	Caddell Construction Co. (DE), LLC		9	10.0	90.0	Site	
	<b>Notes:</b> WGI/Caddell supervision, quality control and safety onsite.						
4	Ed Emmons Steel Erectors, Inc.		9	8.0	72.0	Site>D	
	<b>Notes:</b> Studs and closures Install perimeter cable						
5	Tindall Corporation		18	11.0	198.0	Site	
	<b>Notes:</b> **Erecting near roof line on corridor and just east **Grouting and welding **Patching						
6	Chavers Construction Inc.		6	8.0	48.0	Site	
	<b>Notes:</b> Formed top S16.						
			<b>45</b>		<b>436.0</b>		

#### Manpower Log's Attachments:

1. A&B Electric Co., Inc.

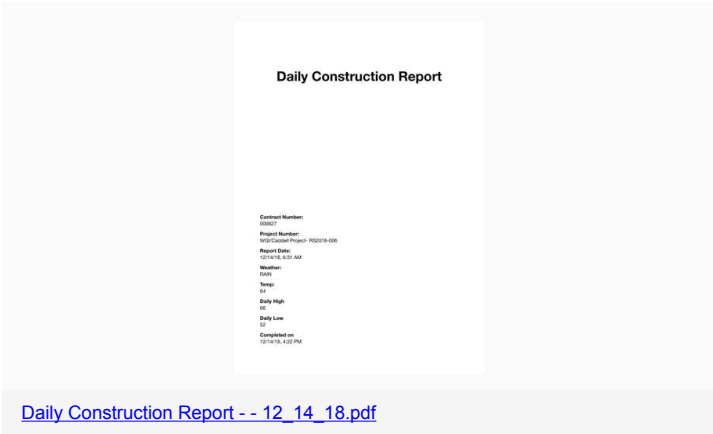


[Daily Construction Report -- 12\\_14\\_18.pdf](#)

2. Bayside Structures, LLC



[Bayside Daily Report 121418.pdf](#)

4. Ed Emmons Steel Erectors, Inc.

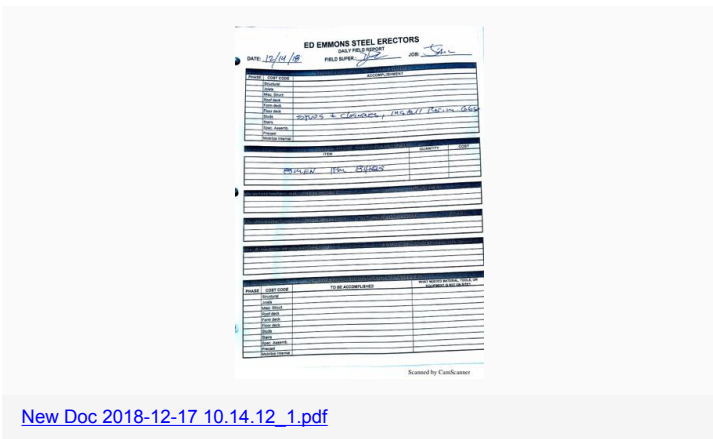

[New Doc 2018-12-17 10.14.12\\_1.pdf](#)

5. Tindall Corporation

[Tindall Escambia Daily 12-14-18.xlsx](#)

**EQUIPMENT LOG**

No.	Equipment Name	Cost Code	Hrs Operating	Hrs Idle	Inspected?	Inspection Time	Location
1	Kobelco Crane CKE2500				No	07:00 AM	Site>C

**Notes:**

## EQUIPMENT LOG

No.	Equipment Name	Cost Code	Hrs Operating	Hrs Idle	Inspected?	Inspection Time	Location
2	JLG Lift 860SJ				No	07:00 AM	Site
	<b>Notes:</b>						
3	JLG Lift 660SJ				No	07:00 AM	Site>C
	<b>Notes:</b>						
4	Genie Lift S85				No	07:00 AM	Site
	<b>Notes:</b>						
5	JLG Skytrak Telehandler				No	07:00 AM	Site
	<b>Notes:</b>						
6	JLG Skytrak Telehandler				No	07:00 AM	Site
	<b>Notes:</b>						

## OBSERVED WEATHER CONDITIONS

No.	Weather Delay	Sky	Temp	Average	Precipitation	Wind	Ground/Sea
1	No	Rain	Mild	62	<.1	Light Wind	Wet/Muddy

By \_\_\_\_\_

Date \_\_\_\_\_

Copies To \_\_\_\_\_



## Daily Log: Saturday 12/15/2018

**Daily Log Completed**  
 The Daily Log was completed by Donald Shelton on Mon Dec 17, 2018 at 10:45 am CST.

### WEATHER REPORT

Temperature			Precipitation Since			Humidity				Windspeed		
Low	High	Avg	Midnight	2 Days Ago	3 Days Ago	Low	Avg	High	Dew	Avg	Max	Gust
51°F	57°F	54°F	0.00 in.	0.11 in.	0.85 in.	73%	81%	93%	48°F	5.9 mph	8 mph	18 mph

### DAILY SNAPSHOT

06:00 AM	09:00 AM	12:00 PM	03:00 PM	06:00 PM	09:00 PM
partly-cloudy-night 54°F	cloudy 55°F	cloudy 57°F	cloudy 56°F	partly-cloudy-night 53°F	partly-cloudy-night 51°F

### MANPOWER LOG

20 Workers | 196.0 Man Hours

No.	Contact/Company	Cost Code	Workers	# Hours	Man Hours	Location
1	Caddell Construction Co. (DE), LLC		1	10.0	10.0	Site
	<b>Notes:</b> WGI/Caddell supervision, quality control and safety onsite.					
2	Chavers Construction Inc.		2	8.0	16.0	Site>Juvenile Justice Parking Lot
	<b>Notes:</b> Poured and finish top of S16					
3	Tindall Corporation		17	10.0	170.0	Site
	<b>Notes:</b> **Erecting near roof line on corridor and just east **Grouting and welding **Patching					
			<b>20</b>	<b>196.0</b>		

3. Tindall Corporation

[Tindall Escambia Daily 12-15-18.xlsx](#)

### EQUIPMENT LOG

No.	Equipment Name	Cost Code	Hrs Operating	Hrs Idle	Inspected?	Inspection Time	Location
1	Kobelco Crane CKE2500				No	07:00 AM	Site>C
	<b>Notes:</b>						
2	Genie Lift S85				No	07:00 AM	Site>C
	<b>Notes:</b>						
3	JLG Lift 860SJ				No	07:00 AM	Site
	<b>Notes:</b>						

## EQUIPMENT LOG

No.	Equipment Name	Cost Code	Hrs Operating	Hrs Idle	Inspected?	Inspection Time	Location
4	JLG Lift 660SJ				No	07:00 AM	Site
<b>Notes:</b>							
5	JLG Skytrak Telehandler				No	07:00 AM	Site
<b>Notes:</b>							

## OBSERVED WEATHER CONDITIONS

No.	Weather Delay	Sky	Temp	Average	Precipitation	Wind	Ground/Sea
1	No	Cloudy	Mild	54	< .1	Light Wind	Wet/Muddy

By \_\_\_\_\_

Date \_\_\_\_\_

Copies To \_\_\_\_\_



## Daily Log: Sunday 12/16/2018

**Daily Log Completed**  
 The Daily Log was completed by Donald Shelton on Mon Dec 17, 2018 at 10:37 am CST.

### WEATHER REPORT

Temperature			Precipitation Since			Humidity				Windspeed		
Low	High	Avg	Midnight	2 Days Ago	3 Days Ago	Low	Avg	High	Dew	Avg	Max	Gust
46°F	59°F	52°F	0.00 in.	0.00 in.	0.11 in.	65%	82%	94%	47°F	5.3 mph	9 mph	17 mph

### DAILY SNAPSHOT

06:00 AM	09:00 AM	12:00 PM	03:00 PM	06:00 PM	09:00 PM
clear-night 48°F	clear-day 54°F	partly-cloudy-day 58°F	clear-day 60°F	clear-night 52°F	clear-night 50°F

### MANPOWER LOG

9 Workers | 54.0 Man Hours

No.	Contact/Company	Cost Code	Workers	# Hours	Man Hours	Location
1	Caddell Test Subcontractor		1	6.0	6.0	Site
<b>Notes:</b> WGI/Caddell supervision, quality control and safety onsite.						
2	Tindall Corporation		8	6.0	48.0	Site
<b>Notes:</b> **Layout farther east in C **Grouting and welding						
			<b>9</b>	<b>54.0</b>		

2. Tindall Corporation

[Tindall Escambia Daily 12-16-18.xlsx](#)

### EQUIPMENT LOG

No.	Equipment Name	Cost Code	Hrs Operating	Hrs Idle	Inspected?	Inspection Time	Location
1	Kobelco Crane CKE2500				No	07:00 AM	Site>C
<b>Notes:</b>							
2	JLG Lift 660SJ				No	07:00 AM	Site>C
<b>Notes:</b>							
3	Genie Lift S85				No	07:00 AM	Site
<b>Notes:</b>							
4	JLG Lift 860SJ				No	07:00 AM	Site
<b>Notes:</b>							



## EQUIPMENT LOG

No.	Equipment Name	Cost Code	Hrs Operating	Hrs Idle	Inspected?	Inspection Time	Location
5	JLG Skytrak Telehandler				No	07:00 AM	Site

Notes:

## OBSERVED WEATHER CONDITIONS

No.	Weather Delay	Sky	Temp	Average	Precipitation	Wind	Ground/Sea
1	No	Cloudy	Mild	52	0	Calm	Wet/Muddy

By \_\_\_\_\_

Date \_\_\_\_\_

Copies To \_\_\_\_\_



## Daily Log: Monday 12/17/2018

**Daily Log Completed**  
 The Daily Log was completed by Donald Shelton on Wed Dec 26, 2018 at 08:27 am CST.

### WEATHER REPORT

Temperature			Precipitation Since			Humidity				Windspeed		
Low	High	Avg	Midnight	2 Days Ago	3 Days Ago	Low	Avg	High	Dew	Avg	Max	Gust
45°F	64°F	53°F	0.00 in.	0.00 in.	0.00 in.	56%	83%	97%	47°F	3.8 mph	5 mph	7 mph

### DAILY SNAPSHOT

06:00 AM	09:00 AM	12:00 PM	03:00 PM	06:00 PM	09:00 PM
partly-cloudy-night 48°F	partly-cloudy-day 53°F	partly-cloudy-day 63°F	clear-day 64°F	partly-cloudy-night 54°F	partly-cloudy-night 49°F

### MANPOWER LOG

61 Workers | 538.0 Man Hours

No.	Contact/Company	Cost Code	Workers	# Hours	Man Hours	Location
1	A&B Electric Co., Inc.		2	10.0	20.0	Site
<b>Notes:</b> Working on temporary power panels, Working on rental property.						
2	Bayside Structures, LLC		6	8.0	48.0	Site
<b>Notes:</b> Began tying rebar on West GB in Connector. Continued to grout base plates on pour 1 in Area D. Began embed layout for Pour 1.						
3	Caddell Construction Co. (DE), LLC		9	10.0	90.0	Site
<b>Notes:</b> WGI/Caddell supervision, quality control and safety onsite.						
4	Ed Emmons Steel Erectors, Inc.		8	8.0	64.0	Site>Juvenile Justice Parking Lot
<b>Notes:</b> Worked on studs and closures						
5	Larry M. Jacobs & Associates, Inc.		1	2.0	2.0	Site
<b>Notes:</b> Conducted weld inspection at elevation 100						
6	EAA Site Contractors LLC		4	8.0	32.0	Site
<b>Notes:</b> Total man hours 31. Conducted final touch up on JJC parking lot base after rain this past weekend. Asphalt paving equipment on site. Asphalt paving is scheduled to start tomorrow morning. Regraded the crane path in section C. Also regraded the asphalt millings construction road.						
7	Tindall Corporation		17	10.0	170.0	Site
<b>Notes:</b> **Crane moves east in C **Grouting and welding **Erecting in C **Patching and installing 30k corbels on A side of corridor						

**MANPOWER LOG**

61 Workers | 538.0 Man Hours

No.	Contact/Company	Cost Code	Workers	# Hours	Man Hours	Location
8	Nash Plumbing and Mechanical, LLC		14	8.0	112.0	Site
<b>Notes:</b> Started underground work in Area B						
			<b>61</b>		<b>538.0</b>	

**Manpower Log's Attachments:**

1. A&B Electric Co., Inc.




[Daily Construction Report - - 12\\_17\\_18.pdf](#)

2. Bayside Structures, LLC



[Bayside Daily Report 121718.pdf](#)

4. Ed Emmons Steel Erectors, Inc.



[New Doc 2018-12-17 16.12.35\\_1.pdf](#)

7. Tindall Corporation

[Tindall Escambia Daily 12-17-18 .xlsx](#)

8. Nash Plumbing and Mechanical, LLC

[Project Superintendent Daily Report 12-17-2018.xlsx](#)

### EQUIPMENT LOG

No.	Equipment Name	Cost Code	Hrs Operating	Hrs Idle	Inspected?	Inspection Time	Location
1	Kobelco Crane CKE2500				No	07:00 AM	Site>C
	<b>Notes:</b>						
2	JLG Skytrak Telehandler				No	07:00 AM	Site
	<b>Notes:</b>						
3	JLG Skytrak Telehandler				No	07:00 AM	Site
	<b>Notes:</b>						
4	JLG Lift 660SJ				No	07:00 AM	Site
	<b>Notes:</b>						
5	JLG Lift 860SJ				No	07:00 AM	Site
	<b>Notes:</b>						
6	Genie Lift S85				No	07:00 AM	Site
	<b>Notes:</b>						
7	Genie Lift S80				No	07:00 AM	Site
	<b>Notes:</b>						
8	Grove Crane AT700D				No	07:00 AM	Site>C
	<b>Notes:</b>						
9	CAT 303.5E2 Excavator				No	07:00 AM	Site>B
	<b>Notes:</b>						
10	John Deere 550H Dozer				No	07:00 AM	Site
	<b>Notes:</b>						

### INSPECTION LOG

No.	Start Time	End Time	Inspection Type	Inspecting Entity	Inspector Name	Location	Area
1	09:30 AM	12:30 PM	Third Party	Mott MacDonald	Mike Tugwell	Site	
	<b>Comments:</b> Conducted Threshold observation						

### OBSERVED WEATHER CONDITIONS

No.	Weather Delay	Sky	Temp	Average	Precipitation	Wind	Ground/Sea
1	No	Cloudy	Mild	53	0	Calm	Wet/Muddy

By \_\_\_\_\_

Date \_\_\_\_\_

Copies To \_\_\_\_\_



## Daily Log: Tuesday 12/18/2018

**Daily Log Completed**  
 The Daily Log was completed by Donald Shelton on Wed Dec 26, 2018 at 08:26 am CST.

### WEATHER REPORT

Temperature			Precipitation Since			Humidity				Windspeed		
Low	High	Avg	Midnight	2 Days Ago	3 Days Ago	Low	Avg	High	Dew	Avg	Max	Gust
40°F	64°F	51°F	0.00 in.	0.00 in.	0.00 in.	43%	79%	98%	43°F	1.6 mph	3 mph	4 mph

### DAILY SNAPSHOT

06:00 AM	09:00 AM	12:00 PM	03:00 PM	06:00 PM	09:00 PM
clear-night 40°F	clear-day 52°F	clear-day 64°F	partly-cloudy-day 64°F	clear-night 53°F	partly-cloudy-night 48°F


### MANPOWER LOG

69 Workers | 616.5 Man Hours

No.	Contact/Company	Cost Code	Workers	# Hours	Man Hours	Location
1	A&B Electric Co., Inc.		2	10.0	20.0	Site
	<b>Notes:</b> Working on temporary panels					
2	Bayside Structures, LLC		6	8.0	48.0	Site
	<b>Notes:</b> Finished tying rebar on West GB on connector. Began to close west GB on connector. Regraded traverse grade beam at connector and dropped rebar to correct elevation.					
3	Caddell Construction Co. (DE), LLC		9	10.5	94.5	Site
	<b>Notes:</b> WGI/Caddell supervision, quality control and safety onsite.					
4	Ed Emmons Steel Erectors, Inc.		9	8.0	72.0	Site>D
	<b>Notes:</b> Hung columns to deck Hung beams to precast Install pour stop/flashing					
5	Larry M. Jacobs & Associates, Inc.		1	6.0	6.0	Site>Juvenile Justice Parking Lot
	<b>Notes:</b> Asphalt Testing					
6	Tindall Corporation		16	10.5	168.0	Site
	<b>Notes:</b> **Weld inspection for 4th level and roof in corridor **Grouting and welding **Erecting in C **Patching and installing 30k corbels on A side of corridor					

**MANPOWER LOG**

**69 Workers | 616.5 Man Hours**

No.	Contact/Company	Cost Code	Workers	# Hours	Man Hours	Location
7	EAA Site Contractors LLC		12	8.0	96.0	Site
<b>Notes:</b> Total man hours 112. Roads Inc work crew received a safety briefing this morning and started asphalt paving the JJC parking lot. Approximately 400 tons of asphalt was laid down today. Trucks will start loading tomorrow morning @ 0700 to complete parking lot.						
8	Nash Plumbing and Mechanical, LLC		14	8.0	112.0	Site 
<b>Notes:</b> Underground work in Area B						
			<b>69</b>		<b>616.5</b>	

**Manpower Log's Attachments:**

1. A&B Electric Co., Inc.

**Daily Construction Report**

Contract Number:  
00000

Project Number:  
W221Contract Project: P122018-000

Report Date:  
12/18/18, 05:00 AM

Weather:  
Sunny

Temp:  
63

Daily High:  
63

Daily Low:  
52

Completed on:  
12/18/18, 4:18 PM

[Daily Construction Report - - 12\\_18\\_18.pdf](#)

2. Bayside Structures, LLC



**BAYSIDESTRUCTURES**  
CONCRETE CONSTRUCTION SPECIALISTS

Contract No. \_\_\_\_\_

Project No. \_\_\_\_\_

Job No. \_\_\_\_\_

Client Name \_\_\_\_\_

Job Location \_\_\_\_\_

Job Start Date \_\_\_\_\_

Job End Date \_\_\_\_\_

Job Description \_\_\_\_\_

Job Manager \_\_\_\_\_

Job Supervisor \_\_\_\_\_

Job Safety \_\_\_\_\_

Job Quality \_\_\_\_\_

Job Cost \_\_\_\_\_

Job Profit \_\_\_\_\_

Job Status \_\_\_\_\_

Job Notes \_\_\_\_\_

Job Attachments \_\_\_\_\_

Job Comments \_\_\_\_\_

Job History \_\_\_\_\_


Job Details \_\_\_\_\_

Job Summary \_\_\_\_\_

Job Footer \_\_\_\_\_

[Bayside Daily Report 121818.pdf](#)

4. Ed Emmons Steel Erectors, Inc.



[New Doc 2018-12-18 15.12.32\\_1.pdf](#)

6. Tindall Corporation

[Tindall Escambia Daily 12-18-18.xlsx](#)

8. Nash Plumbing and Mechanical, LLC

[Project Superintendent Daily Report 12-18-18.xlsx](#)

**EQUIPMENT LOG**

No.	Equipment Name	Cost Code	Hrs Operating	Hrs Idle	Inspected?	Inspection Time	Location
1	Genie Lift S125		0.0	0.0	No	07:00 AM	Site
	<b>Notes:</b>						
2	Kobelco Crane CKE2500		0.0	0.0	No	07:00 AM	Site>Juvenile Justice Parking Lot
	<b>Notes:</b>						
3	JLG Skytrak Telehandler		0.0	0.0	No	07:00 AM	Site
	<b>Notes:</b>						
4	JLG Lift 660SJ		0.0	0.0	No	07:00 AM	Site
	<b>Notes:</b>						
5	Grove Crane AT700D		0.0	0.0	No	07:00 AM	Site>D
	<b>Notes:</b>						
6	JLG Skytrak Telehandler		0.0	0.0	No	07:00 AM	Site>D
	<b>Notes:</b>						
7	Genie Lift S85		0.0	0.0	No	07:00 AM	Site
	<b>Notes:</b>						
8	JLG Lift 860SJ		0.0	0.0	No	07:00 AM	Site>A
	<b>Notes:</b>						
9	CAT 303.5E2 Excavator		0.0	0.0	No	07:00 AM	Site>B
	<b>Notes:</b>						
10	Sky Power Lift 600AJ		0.0	0.0	No	07:00 AM	Site>D
	<b>Notes:</b>						
11	Genie Lift S80		0.0	0.0	No	07:00 AM	Site>D
	<b>Notes:</b>						

## EQUIPMENT LOG

No.	Equipment Name	Cost Code	Hrs Operating	Hrs Idle	Inspected?	Inspection Time	Location
12	CAT AP600D Paver		0.0	0.0	No	07:00 AM	Site>Juvenile Justice Parking Lot
<b>Notes:</b>							
13	Traffic Roller		0.0	0.0	No	07:00 AM	Site>Juvenile Justice Parking Lot
<b>Notes:</b>							
14	CAT CB24B Drum Roller		0.0	0.0	No	07:00 AM	Site>Juvenile Justice Parking Lot
<b>Notes:</b>							

## PHOTOS



[IMG\\_0506.jpg](#)



[DJI\\_0134.jpg](#)



[DJI\\_0138.jpg](#)



[DJI\\_0130.jpg](#)



[DJI\\_0125.jpg](#)



[DJI\\_0133.jpg](#)





[DJI\\_0135.jpg](#)



[DJI\\_0140.jpg](#)



[DJI\\_0142.jpg](#)



[DJI\\_0141.jpg](#)



[DJI\\_0126.jpg](#)



[DJI\\_0143.jpg](#)



[DJI\\_0136.jpg](#)



[DJI\\_0137.jpg](#)



[DJI\\_0127.jpg](#)



[DJI\\_0132.jpg](#)



[DJI\\_0128.jpg](#)



[DJI\\_0131.jpg](#)



[DJI\\_0129.jpg](#)



[DJI\\_0139.jpg](#)

### OBSERVED WEATHER CONDITIONS

No.	Weather Delay	Sky	Temp	Average	Precipitation	Wind	Ground/Sea
1	No	Clear	Mild	50	0	Light Wind	Dry

By \_\_\_\_\_

Date \_\_\_\_\_

Copies To \_\_\_\_\_



## Daily Log: Wednesday 12/19/2018

**Daily Log Completed**  
 The Daily Log was completed by Donald Shelton on Wed Dec 26, 2018 at 08:31 am CST.

### WEATHER REPORT

Temperature			Precipitation Since			Humidity				Windspeed		
Low	High	Avg	Midnight	2 Days Ago	3 Days Ago	Low	Avg	High	Dew	Avg	Max	Gust
48°F	62°F	56°F	0.44 in.	0.44 in.	0.44 in.	64%	83%	100%	51°F	5.3 mph	11 mph	18 mph

### DAILY SNAPSHOT

06:00 AM	09:00 AM	12:00 PM	03:00 PM	06:00 PM	09:00 PM
<b>clear-night</b> 50°F	<b>partly-cloudy-day</b> 54°F	<b>cloudy</b> 61°F	<b>cloudy</b> 62°F	<b>cloudy</b> 61°F	<b>rain</b> 60°F

### MANPOWER LOG

**60 Workers | 529.5 Man Hours**

No.	Contact/Company	Cost Code	Workers	# Hours	Man Hours	Location	
1	A&B Electric Co., Inc.		3	6.5	19.5	Site	
	<b>Notes:</b> Working on temporary panels. 20 Total Man hours						
2	Bayside Structures, LLC		4	9.0	36.0	Site	
	<b>Notes:</b> Continued forming and rebar in connector section.						
3	Caddell Construction Co. (DE), LLC		9	10.0	90.0	Site	
	<b>Notes:</b> WGI/Caddell supervision, quality control and safety onsite.						
4	Ed Emmons Steel Erectors, Inc.		1	8.0	8.0	Site>D	
	<b>Notes:</b> Hung beams and stacked at Southwest. Cleaned off deck.						
5	Larry M. Jacobs & Associates, Inc.		1	8.0	8.0	Site	
	<b>Notes:</b> Conducted density test for plumbers back fill in Area B. Asphalt testing in JJ Parking lot.						
6	EAA Site Contractors LLC		12	8.0	96.0	Site	
	<b>Notes:</b> Total man hours 87. Roads Inc continued asphalt paving in JJC parking lot. Paving was completed by 2pm. Gulf Coast Traffic Engineers (GCTE) started parking lot layout for striping after lunch.						
7	Tindall Corporation		16	10.0	160.0	Site	
	<b>Notes:</b> **Grouting and welding **Erecting in C **Patching in C						

**MANPOWER LOG**

60 Workers | 529.5 Man Hours

No.	Contact/Company	Cost Code	Workers	# Hours	Man Hours	Location
8	Nash Plumbing and Mechanical, LLC		14	8.0	112.0	Site
<b>Notes:</b>						
Plumbing- prep for elevation 100 North 1/2						
Mechanical- prep for elev. 100 North 1/2						
Underground work in Area B						
			<b>60</b>		<b>529.5</b>	


**Manpower Log's Attachments:**

1. A&B Electric Co., Inc.



[Daily Construction Report -- 12\\_19\\_18.pdf](#)

4. Ed Emmons Steel Erectors, Inc.



[New Doc 2018-12-19 15.06.28\\_1.pdf](#)

7. Tindall Corporation

[Tindall Escambia Daily 12-19-18.xlsx](#)

8. Nash Plumbing and Mechanical, LLC

[Project Superintendent Daily Report 12-19-18.xlsx](#)

**NOTES LOG**

No.	Issue?	Location	Comments
1	No	Site>B	County inspection complete on underground plumbing in Area B

## EQUIPMENT LOG

No.	Equipment Name	Cost Code	Hrs Operating	Hrs Idle	Inspected?	Inspection Time	Location
1	CAT AP600D Paver		0.0	0.0	No	07:00 AM	Site>Juvenile Justice Parking Lot
	<b>Notes:</b>						
2	CAT CB24B Drum Roller		0.0	0.0	No	07:00 AM	Site>Juvenile Justice Parking Lot
	<b>Notes:</b>						
3	Traffic Roller		0.0	0.0	No	07:00 AM	Site>Juvenile Justice Parking Lot
	<b>Notes:</b>						
4	Grove Crane AT700D				No	07:00 AM	Site>D
	<b>Notes:</b>						
5	JLG Lift 660SJ				No	07:00 AM	Site>D
	<b>Notes:</b>						
6	Genie Lift S80				No	07:00 AM	Site>D
	<b>Notes:</b>						
7	JLG Skytrak Telehandler				No	07:00 AM	Site>D
	<b>Notes:</b>						
8	Kobelco Crane CKE2500				No	07:00 AM	Site>C
	<b>Notes:</b>						
9	JLG Lift 660SJ				No	07:00 AM	Site>C
	<b>Notes:</b>						
10	JLG Lift 860SJ				No	07:00 AM	Site>C
	<b>Notes:</b>						
11	Genie Lift S85				No	07:00 AM	Site>C
	<b>Notes:</b>						
12	JLG Skytrak Telehandler				No	07:00 AM	Site
	<b>Notes:</b>						
13	Bobcat Skidsteer				No	07:00 AM	Site>B
	<b>Notes:</b>						
14	Bobcat Miniexcavator				No	07:00 AM	Site>B
	<b>Notes:</b>						

## OBSERVED WEATHER CONDITIONS

No.	Weather Delay	Sky	Temp	Average	Precipitation	Wind	Ground/Sea
1	No	Overcast	Mild	563	0	Calm	Dry

By \_\_\_\_\_

Date \_\_\_\_\_

Copies To \_\_\_\_\_



## Daily Log: Thursday 12/20/2018

**Daily Log Completed**  
 The Daily Log was completed by Payton Holley on Wed Jan 2, 2019 at 05:13 pm CST.

### WEATHER REPORT

Temperature			Precipitation Since			Humidity				Windspeed		
Low	High	Avg	Midnight	2 Days Ago	3 Days Ago	Low	Avg	High	Dew	Avg	Max	Gust
51°F	62°F	58°F	0.74 in.	1.18 in.	1.18 in.	88%	95%	99%	56°F	6.0 mph	9 mph	21 mph

### DAILY SNAPSHOT

06:00 AM	09:00 AM	12:00 PM	03:00 PM	06:00 PM	09:00 PM
cloudy 58°F	fog 59°F	rain 61°F	cloudy 62°F	cloudy 58°F	cloudy 54°F

### MANPOWER LOG

39 Workers | 204.0 Man Hours

No.	Contact/Company	Cost Code	Workers	# Hours	Man Hours	Location	
1	A&B Electric Co., Inc.		2	10.0	20.0	Site	
	<b>Notes:</b> Working on temporary power backboards						
2	Bayside Structures, LLC		6	2.5	15.0	Site	
	<b>Notes:</b> Began to work on the deck getting 2x4 screwed onto edge form for embeds. Rain out						
3	Caddell Test Subcontractor		9	10.0	90.0	Site	
	<b>Notes:</b> WGI/Caddell supervision, quality control and safety onsite.						
4	Ed Emmons Steel Erectors, Inc.		1	8.0	8.0		
	<b>Notes:</b> Rain Out						
5	Tindall Corporation		17	3.0	51.0	Site>C	
	<b>Notes:</b> **Grouting and welding **Erecting in C **Patching in C Rain out after 9 am 53 Total man hours						
6	Larry M. Jacobs & Associates, Inc.		2	2.0	4.0	Site>Juvenile Justice Parking Lot	
	<b>Notes:</b> Drilled cores for Asphalt Density Test						

**MANPOWER LOG**

**39 Workers | 204.0 Man Hours**

No.	Contact/Company	Cost Code	Workers	# Hours	Man Hours	Location
7	Nash Plumbing and Mechanical, LLC		2	8.0	16.0	Site
<b>Notes:</b> Installation of sleeves, insert Rain Out						
			<b>39</b>		<b>204.0</b>	

**Manpower Log's Attachments:**

1. A&B Electric Co., Inc.

**Daily Construction Report**

Contract Number: 122018  
 Project Number: 122018-001  
 Report Date: 12/20/18, 6:20 AM  
 Weather: Partly Sunny  
 Temp: 58  
 Wind: 10  
 Wind High: 15  
 Wind Low: 10  
 Construction: 12/20/18, 4:18 PM

[Daily Construction Report -- 12\\_20\\_18.pdf](#)

2. Bayside Structures, LLC




**BAYSIDE STRUCTURES**  
CONCRETE CONSTRUCTION SPECIALISTS

Contractor: Bayside Structures, LLC  
 Division: 122018  
 Project: 122018-001  
 Report Date: 12/20/18  
 Weather: Partly Sunny  
 Temp: 58  
 Wind: 10  
 Wind High: 15  
 Wind Low: 10  
 Construction: 12/20/18, 4:18 PM

[Bayside Daily Report 122018.pdf](#)

4. Ed Emmons Steel Erectors, Inc.



[New Doc 2018-12-20 08.48.59\\_1.pdf](#)

5. Tindall Corporation

[Tindall Escambia Daily 12-20-18.xlsx](#)

7. Nash Plumbing and Mechanical, LLC

[Project Superintendent Daily Report 12-20-18.xlsx](#)

**EQUIPMENT LOG**

No.	Equipment Name	Cost Code	Hrs Operating	Hrs Idle	Inspected?	Inspection Time	Location
1	Kobelco Crane CKE2500				No	07:00 AM	Site>C
	<b>Notes:</b>						
2	JLG Lift 660SJ				No	07:00 AM	Site>C
	<b>Notes:</b>						
3	Genie Lift S85				No	07:00 AM	Site>C
	<b>Notes:</b>						
4	JLG Lift 860SJ				No	07:00 AM	Site>C
	<b>Notes:</b>						
5	JLG Lift 660SJ				No	07:00 AM	Site>D
	<b>Notes:</b>						

**OBSERVED WEATHER CONDITIONS**

No.	Weather Delay	Sky	Temp	Average	Precipitation	Wind	Ground/Sea
1	Yes	Rain	Mild	58	4.75 in.	Light Wind	Wet/Muddy

By \_\_\_\_\_

Date \_\_\_\_\_

Copies To \_\_\_\_\_





## Daily Log: Friday 12/21/2018

**Daily Log Completed**  
 The Daily Log was completed by Donald Shelton on Wed Dec 26, 2018 at 08:14 am CST.

### WEATHER REPORT

Temperature			Precipitation Since			Humidity				Windspeed		
Low	High	Avg	Midnight	2 Days Ago	3 Days Ago	Low	Avg	High	Dew	Avg	Max	Gust
41°F	50°F	46°F	0.17 in.	0.92 in.	1.35 in.	70%	83%	95%	41°F	11.9 mph	15 mph	24 mph

### DAILY SNAPSHOT

06:00 AM	09:00 AM	12:00 PM	03:00 PM	06:00 PM	09:00 PM
<b>rain</b> 44°F	<b>cloudy</b> 46°F	<b>cloudy</b> 48°F	<b>cloudy</b> 50°F	<b>partly-cloudy-night</b> 46°F	<b>clear-night</b> 42°F

### MANPOWER LOG

56 Workers | 312.5 Man Hours

No.	Contact/Company	Cost Code	Workers	# Hours	Man Hours	Location	
1	A&B Electric Co., Inc.		2	10.0	20.0	Site	
	<b>Notes:</b> Working on temporary panels						
2	Bayside Structures, LLC		5	3.0	15.0	Site>D	
	<b>Notes:</b> Finished putting 2x4 around edge form on pour 1 in Area D.						
3	Caddell Construction Co. (DE), LLC		5	10.0	50.0	Site	
	<b>Notes:</b> WGI/Caddell supervision, quality control and safety onsite.						
4	Ed Emmons Steel Erectors, Inc.		9	2.5	22.5	Site>D	
	<b>Notes:</b> Setup crane Shutdown due to weather and conditions at direction of project manager						
5	Chavers Construction Inc.		4	2.0	8.0	Site>Juvenile Justice Parking Lot	
	<b>Notes:</b> Removed forms from S16						
6	Nash Plumbing and Mechanical, LLC		14	8.0	112.0	Site	
	<b>Notes:</b> Finish inserts and underground in Area C. Started underground in Area A.						

**MANPOWER LOG**

56 Workers | 312.5 Man Hours

No.	Contact/Company	Cost Code	Workers	# Hours	Man Hours	Location
7	Tindall Corporation		17	5.0	85.0	Site>D
			<b>56</b>		<b>312.5</b>	

**Notes:** \*\*Grouting and welding  
 \*\*Erecting in C  
 \*\*Patching in C

**Manpower Log's Attachments:**

1. A&B Electric Co., Inc.




[Daily Construction Report -- 12\\_21\\_18.pdf](#)

2. Bayside Structures, LLC



[Bayside Daily Report 122118.pdf](#)

4. Ed Emmons Steel Erectors, Inc.



[New Doc 2018-12-21 08.51.16\\_1.pdf](#)

6. Nash Plumbing and Mechanical, LLC



[Nash Daily 12-21-18.pdf](#)

7. Tindall Corporation

[Tindall Escambia Daily 12-21-18.xlsx](#)

**EQUIPMENT LOG**

No.	Equipment Name	Cost Code	Hrs Operating	Hrs Idle	Inspected?	Inspection Time	Location
1	Grove Crane AT700D				No	07:00 AM	Site>D
	<b>Notes:</b>						
2	JLG Lift 660SJ				No	07:00 AM	Site>D
	<b>Notes:</b>						
3	Kobelco Crane CKE2500				No	07:00 AM	Site>C
	<b>Notes:</b>						
4	JLG Skytrak Telehandler				No	07:00 AM	Site>C
	<b>Notes:</b>						
5	JLG Lift 660SJ				No	07:00 AM	Site>C
	<b>Notes:</b>						
6	JLG Lift 860SJ				No	07:00 AM	Site>C
	<b>Notes:</b>						
7	Genie Lift S85				No	07:00 AM	Site>C
	<b>Notes:</b>						

## OBSERVED WEATHER CONDITIONS

No.	Weather Delay	Sky	Temp	Average	Precipitation	Wind	Ground/Sea
1	No	Overcast	Mild	46	< .1	Light Wind	Wet/Muddy

---

By

---

Date

---

Copies To



Whitesell Green / Caddell, a Joint Venture  
 2700 Lagoon Park Drive  
 Montgomery, Alabama 36109  
 P: (334) 272-7723  
 F: (334) 394-0193

Project: 1054 - Escambia County Correctional  
**Facility**  
 3080 N. Pace Boulevard  
 Pensacola, Florida 32501

## Daily Log: Saturday 12/22/2018

### WEATHER REPORT

Temperature			Precipitation Since			Humidity				Windspeed		
Low	High	Avg	Midnight	2 Days Ago	3 Days Ago	Low	Avg	High	Dew	Avg	Max	Gust
32°F	58°F	46°F	0.00 in.	0.17 in.	0.92 in.	46%	76%	100%	38°F	3.2 mph	7 mph	10 mph

### DAILY SNAPSHOT

06:00 AM	09:00 AM	12:00 PM	03:00 PM	06:00 PM	09:00 PM
clear-night 32°F	clear-day 48°F	clear-day 57°F	clear-day 58°F	clear-night 49°F	clear-night 50°F

### OBSERVED WEATHER CONDITIONS

No.	Weather Delay	Sky	Temp	Average	Precipitation	Wind	Ground/Sea
1	No						

By \_\_\_\_\_

Date \_\_\_\_\_

Copies To \_\_\_\_\_



Whitesell Green / Caddell, a Joint Venture  
 2700 Lagoon Park Drive  
 Montgomery, Alabama 36109  
 P: (334) 272-7723  
 F: (334) 394-0193

Project: 1054 - Escambia County Correctional  
**Facility**  
 3080 N. Pace Boulevard  
 Pensacola, Florida 32501

## Daily Log: Sunday 12/23/2018

### WEATHER REPORT

Temperature			Precipitation Since			Humidity				Windspeed		
Low	High	Avg	Midnight	2 Days Ago	3 Days Ago	Low	Avg	High	Dew	Avg	Max	Gust
47°F	70°F	59°F	0.00 in.	0.00 in.	0.18 in.	64%	84%	100%	54°F	5.0 mph	11 mph	13 mph

### DAILY SNAPSHOT

06:00 AM	09:00 AM	12:00 PM	03:00 PM	06:00 PM	09:00 PM
partly-cloudy-night 49°F	partly-cloudy-day 61°F	partly-cloudy-day 69°F	partly-cloudy-day 69°F	partly-cloudy-night 62°F	partly-cloudy-night 59°F

### OBSERVED WEATHER CONDITIONS

No.	Weather Delay	Sky	Temp	Average	Precipitation	Wind	Ground/Sea
1	No						

By \_\_\_\_\_

Date \_\_\_\_\_

Copies To \_\_\_\_\_



Whitesell Green / Caddell, a Joint Venture  
 2700 Lagoon Park Drive  
 Montgomery, Alabama 36109  
 P: (334) 272-7723  
 F: (334) 394-0193

Project: 1054 - Escambia County Correctional  
**Facility**  
 3080 N. Pace Boulevard  
 Pensacola, Florida 32501

## Daily Log: Monday 12/24/2018

### WEATHER REPORT

Temperature			Precipitation Since			Humidity				Windspeed		
Low	High	Avg	Midnight	2 Days Ago	3 Days Ago	Low	Avg	High	Dew	Avg	Max	Gust
42°F	62°F	53°F	0.00 in.	0.00 in.	0.00 in.	48%	74%	97%	44°F	4.7 mph	8 mph	9 mph

### DAILY SNAPSHOT

06:00 AM	09:00 AM	12:00 PM	03:00 PM	06:00 PM	09:00 PM
cloudy 50°F	partly-cloudy-day 50°F	partly-cloudy-day 59°F	clear-day 62°F	clear-night 53°F	clear-night 48°F

### MANPOWER LOG

0 Workers | 0.0 Man Hours

No.	Contact/Company	Cost Code	Workers	# Hours	Man Hours	Location
1	Caddell Construction Co. (DE), LLC		0	0.0	0.0	
<b>Notes:</b> No work performed on this day due to Holiday (Christmas Eve).						
			<b>0</b>		<b>0.0</b>	

### OBSERVED WEATHER CONDITIONS

No.	Weather Delay	Sky	Temp	Average	Precipitation	Wind	Ground/Sea
1	No						

By \_\_\_\_\_

Date \_\_\_\_\_

Copies To \_\_\_\_\_



Whitesell Green / Caddell, a Joint Venture  
 2700 Lagoon Park Drive  
 Montgomery, Alabama 36109  
 P: (334) 272-7723  
 F: (334) 394-0193

Project: 1054 - Escambia County Correctional  
**Facility**  
 3080 N. Pace Boulevard  
 Pensacola, Florida 32501

## Daily Log: Tuesday 12/25/2018

### WEATHER REPORT

Temperature			Precipitation Since			Humidity				Windspeed		
Low	High	Avg	Midnight	2 Days Ago	3 Days Ago	Low	Avg	High	Dew	Avg	Max	Gust
43°F	65°F	53°F	0.00 in.	0.00 in.	0.00 in.	56%	80%	95%	47°F	3.6 mph	6 mph	7 mph

### DAILY SNAPSHOT

06:00 AM	09:00 AM	12:00 PM	03:00 PM	06:00 PM	09:00 PM
clear-night 45°F	cloudy 52°F	clear-day 63°F	clear-day 65°F	clear-night 57°F	clear-night 53°F

### MANPOWER LOG

0 Workers | 0.0 Man Hours

No.	Contact/Company	Cost Code	Workers	# Hours	Man Hours	Location
1	Caddell Construction Co. (DE), LLC		0	0.0	0.0	
<b>Notes:</b> No work performed on this day due to Holiday (Christmas Day).						
			<b>0</b>		<b>0.0</b>	

### OBSERVED WEATHER CONDITIONS

No.	Weather Delay	Sky	Temp	Average	Precipitation	Wind	Ground/Sea
1	No						

By \_\_\_\_\_

Date \_\_\_\_\_

Copies To \_\_\_\_\_





## Daily Log: Wednesday 12/26/2018

**Daily Log Completed**  
 The Daily Log was completed by Donald Shelton on Wed Jan 2, 2019 at 12:41 pm CST.

### WEATHER REPORT

Temperature			Precipitation Since			Humidity				Windspeed		
Low	High	Avg	Midnight	2 Days Ago	3 Days Ago	Low	Avg	High	Dew	Avg	Max	Gust
49°F	65°F	57°F	0.00 in.	0.00 in.	0.00 in.	57%	73%	94%	48°F	6.2 mph	10 mph	13 mph

### DAILY SNAPSHOT

06:00 AM	09:00 AM	12:00 PM	03:00 PM	06:00 PM	09:00 PM
partly-cloudy-night 50°F	partly-cloudy-day 57°F	partly-cloudy-day 63°F	partly-cloudy-day 65°F	cloudy 61°F	partly-cloudy-night 60°F

### MANPOWER LOG

28 Workers | 230.0 Man Hours

No.	Contact/Company	Cost Code	Workers	# Hours	Man Hours	Location
1	A&B Electric Co., Inc.		3	10.0	30.0	Site
<b>Notes:</b> Working on temporary power backboards						
2	Bayside Structures, LLC		3	0.0	0.0	Site
<b>Notes:</b> Began to rework connector when told by my boss Justin Mahaney to abandon connector due to upcoming weather. Prep area D deck for embeds.						
3	Caddell Construction Co. (DE), LLC		6	10.0	60.0	Site
<b>Notes:</b> WGI/Caddell supervision, quality control and safety onsite.						
4	Gulf Coast Traffic Engineers		3	6.0	18.0	Site>Juvenile Justice Parking Lot
<b>Notes:</b> Painted strips on parking lot						
5	Nash Plumbing and Mechanical, LLC		4	8.0	32.0	Site>D
<b>Notes:</b> Inserted sleeves in Area D						
6	Ed Emmons Steel Erectors, Inc.		9	10.0	90.0	Site>D
<b>Notes:</b> Hung beams and columns south of match line.						
			<b>28</b>	<b>230.0</b>		

#### Manpower Log's Attachments:

1. A&B Electric Co., Inc.



[Daily Construction Report -- 12\\_26\\_18.pdf](#)


2. Bayside Structures, LLC

[Daily 12-26.docx](#)

5. Nash Plumbing and Mechanical, LLC

[Project Superintendent Daily Report 12-26-2018.xlsx](#)

6. Ed Emmons Steel Erectors, Inc.

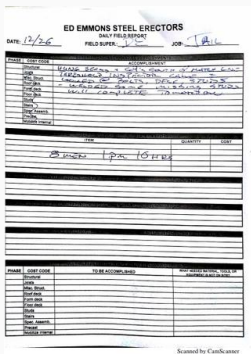

[New Doc 2018-12-26 17.12.27\\_1.pdf](#)

**EQUIPMENT LOG**

No.	Equipment Name	Cost Code	Hrs Operating	Hrs Idle	Inspected?	Inspection Time	Location
1	Grove Crane AT700D				No	07:00 AM	Site>D
<b>Notes:</b>							

**INSPECTION LOG**

No.	Start Time	End Time	Inspection Type	Inspecting Entity	Inspector Name	Location	Area
1	08:00 AM	03:00 PM	Third Party	Mott MacDonald	Mike Tugwell	Building>D	D
<b>Comments:</b> Conducted Threshold Inspection at Elevation 100 in Area D							

**OBSERVED WEATHER CONDITIONS**

No.	Weather Delay	Sky	Temp	Average	Precipitation	Wind	Ground/Sea
1	No	Clear	Mild	57	0	Calm	Wet/Muddy

---

By

---

Date

---

Copies To



## Daily Log: Thursday 12/27/2018

**Daily Log Completed**  
 The Daily Log was completed by Donald Shelton on Wed Jan 2, 2019 at 12:37 pm CST.

### WEATHER REPORT

Temperature			Precipitation Since			Humidity				Windspeed		
Low	High	Avg	Midnight	2 Days Ago	3 Days Ago	Low	Avg	High	Dew	Avg	Max	Gust
57°F	70°F	64°F	0.04 in.	0.04 in.	0.04 in.	70%	88%	96%	60°F	12.8 mph	19 mph	31 mph

### DAILY SNAPSHOT

06:00 AM	09:00 AM	12:00 PM	03:00 PM	06:00 PM	09:00 PM
partly-cloudy-night 59°F	cloudy 63°F	wind 66°F	cloudy 67°F	cloudy 69°F	cloudy 69°F

### MANPOWER LOG

25 Workers | 193.5 Man Hours

No.	Contact/Company	Cost Code	Workers	# Hours	Man Hours	Location
1	A&B Electric Co., Inc.		2	10.0	20.0	Site
<b>Notes:</b> Working on temporary power panels						
2	Bayside Structures, LLC		4	8.0	32.0	Site
<b>Notes:</b> Prep area D deck for slab depressions. Unload truck of wire mesh.						
3	Caddell Construction Co. (DE), LLC		6	10.0	60.0	Site
<b>Notes:</b> WGI/Caddell supervision, quality control and safety onsite.						
4	Ed Emmons Steel Erectors, Inc.		9	5.5	49.5	Site>D
<b>Notes:</b> Stood Columns Shut down due to high winds						
5	Nash Plumbing and Mechanical, LLC		4	8.0	32.0	Site
<b>Notes:</b> Prefabrication preparation						
			<b>25</b>	<b>193.5</b>		

#### Manpower Log's Attachments:

1. A&B Electric Co., Inc.




[Daily Construction Report - - 12\\_27\\_18.pdf](#)

2. Bayside Structures, LLC

[Daily 12-27.docx](#)

4. Ed Emmons Steel Erectors, Inc.

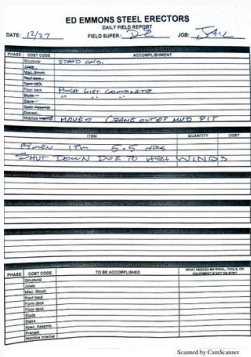

[New Doc 2018-12-27 09.22.34\\_1.pdf](#)

5. Nash Plumbing and Mechanical, LLC

[Project Superintendent Daily Report 12-27-2018.xlsx](#)

**EQUIPMENT LOG**

No.	Equipment Name	Cost Code	Hrs Operating	Hrs Idle	Inspected?	Inspection Time	Location
1	Grove Crane AT700D				No	07:00 AM	Site>D
<b>Notes:</b>							
2	JLG Skytrak Telehandler				No	07:00 AM	Site>D
<b>Notes:</b>							

**OBSERVED WEATHER CONDITIONS**

No.	Weather Delay	Sky	Temp	Average	Precipitation	Wind	Ground/Sea
1	No	Overcast	Mild	64	< .1	Light Wind	Wet/Muddy

By \_\_\_\_\_ Date \_\_\_\_\_ Copies To \_\_\_\_\_



## Daily Log: Friday 12/28/2018

**Daily Log Completed**  
 The Daily Log was completed by Donald Shelton on Wed Jan 2, 2019 at 12:35 pm CST.

### WEATHER REPORT

Temperature			Precipitation Since			Humidity				Windspeed		
Low	High	Avg	Midnight	2 Days Ago	3 Days Ago	Low	Avg	High	Dew	Avg	Max	Gust
59°F	70°F	65°F	2.52 in.	2.57 in.	2.57 in.	93%	97%	100%	64°F	7.2 mph	14 mph	19 mph

### DAILY SNAPSHOT

06:00 AM	09:00 AM	12:00 PM	03:00 PM	06:00 PM	09:00 PM
rain 70°F	rain 65°F	rain 63°F	rain 63°F	rain 63°F	rain 60°F

### MANPOWER LOG

22 Workers | 116.5 Man Hours

No.	Contact/Company	Cost Code	Workers	# Hours	Man Hours	Location
1	A&B Electric Co., Inc.		3	10.0	30.0	Site
<b>Notes:</b> Working on temporary power panels.						
2	Bayside Structures, LLC		6	1.5	9.0	Site
<b>Notes:</b> Began to get wire mesh up onto area D level two deck. Also began to spread wire mesh when we got rained out.						
3	Caddell Construction Co. (DE), LLC		6	10.0	60.0	Site
<b>Notes:</b> WGI/Caddell supervision, quality control and safety onsite.						
4	Ed Emmons Steel Erectors, Inc.		7	2.5	17.5	Site>D
<b>Notes:</b> Erected beams at SW/SE corner of Area D.						
			<b>22</b>	<b>116.5</b>		

#### Manpower Log's Attachments:

1. A&B Electric Co., Inc.



[Daily Construction Report -- 12\\_28\\_18.pdf](#)

2. Bayside Structures, LLC

[Daily 12-28 Rainout.docx](#)

4. Ed Emmons Steel Erectors, Inc.

[Daily 12-28 Rainout.docx](#)

### EQUIPMENT LOG

No.	Equipment Name	Cost Code	Hrs Operating	Hrs Idle	Inspected?	Inspection Time	Location
1	Grove Crane AT700D				No	07:00 AM	Site>D
	<b>Notes:</b>						
2	JLG Skytrak Telehandler				No	07:00 AM	Site>D
	<b>Notes:</b>						
3	Genie Lift S80				No	07:00 AM	Site>D
	<b>Notes:</b>						

### OBSERVED WEATHER CONDITIONS

No.	Weather Delay	Sky	Temp	Average	Precipitation	Wind	Ground/Sea
1	Yes	Rain	Mild	65	3 1/8 in.	Light Wind	Wet/Muddy

Observed Weather Conditions' Attachments:

1



[20181228\\_154041.jpg](#)

---

By

---

Date

---

Copies To





## Daily Log: Saturday 12/29/2018

**Daily Log Completed**  
 The Daily Log was completed by Payton Holley on Wed Jan 2, 2019 at 10:59 am CST.

### WEATHER REPORT

Temperature			Precipitation Since			Humidity				Windspeed		
Low	High	Avg	Midnight	2 Days Ago	3 Days Ago	Low	Avg	High	Dew	Avg	Max	Gust
61°F	65°F	63°F	0.07 in.	2.60 in.	2.64 in.	96%	97%	100%	62°F	4.4 mph	6 mph	7 mph

### DAILY SNAPSHOT

06:00 AM	09:00 AM	12:00 PM	03:00 PM	06:00 PM	09:00 PM
cloudy 62°F	cloudy 62°F	cloudy 63°F	cloudy 64°F	cloudy 64°F	cloudy 64°F


### MANPOWER LOG

10 Workers | 45.0 Man Hours

No.	Contact/Company	Cost Code	Workers	# Hours	Man Hours	Location
1	Caddell Construction Co. (DE), LLC		4	4.5	18.0	
<b>Notes:</b> WGI/Caddell supervision, quality control and safety onsite.						
2	Ed Emmons Steel Erectors, Inc.		6	4.5	27.0	Site>D
<b>Notes:</b> Hung Columns and Beams at SW Area in D.						
			<b>10</b>		<b>45.0</b>	

#### Manpower Log's Attachments:

- 2. Ed Emmons Steel Erectors, Inc.



[New Doc 2018-12-29 08.40.02\\_1.pdf](#)

## EQUIPMENT LOG

No.	Equipment Name	Cost Code	Hrs Operating	Hrs Idle	Inspected?	Inspection Time	Location
1	Grove Crane AT700D				No	07:00 AM	Site>D
<b>Notes:</b>							
2	Genie Lift S80				No	07:00 AM	Site>D
<b>Notes:</b>							

## OBSERVED WEATHER CONDITIONS

No.	Weather Delay	Sky	Temp	Average	Precipitation	Wind	Ground/Sea
1	No	Clear	Mild	63 in.	< .1	Calm	Wet/Muddy

By \_\_\_\_\_

Date \_\_\_\_\_

Copies To \_\_\_\_\_



**Whitesell Green / Caddell, a Joint Venture**  
 2700 Lagoon Park Drive  
 Montgomery, Alabama 36109  
 P: (334) 272-7723  
 F: (334) 394-0193

**Project: 1054 - Escambia County Correctional Facility**  
 3080 N. Pace Boulevard  
 Pensacola, Florida 32501

## Daily Log: Sunday 12/30/2018

### WEATHER REPORT

Temperature			Precipitation Since			Humidity				Windspeed		
Low	High	Avg	Midnight	2 Days Ago	3 Days Ago	Low	Avg	High	Dew	Avg	Max	Gust
66°F	70°F	67°F	0.02 in.	0.10 in.	2.62 in.	95%	97%	100%	67°F	5.6 mph	9 mph	10 mph

### DAILY SNAPSHOT

06:00 AM	09:00 AM	12:00 PM	03:00 PM	06:00 PM	09:00 PM
<b>fog</b> 67°F	<b>fog</b> 68°F	<b>cloudy</b> 70°F	<b>cloudy</b> 69°F	<b>cloudy</b> 67°F	<b>fog</b> 67°F

### MANPOWER LOG

0 Workers | 0.0 Man Hours

No.	Contact/Company	Cost Code	Workers	# Hours	Man Hours	Location
1	Caddell Construction Co. (DE), LLC		0	0.0	0.0	
<b>Notes:</b> No work performed on this day.						
			<b>0</b>		<b>0.0</b>	

### OBSERVED WEATHER CONDITIONS

No.	Weather Delay	Sky	Temp	Average	Precipitation	Wind	Ground/Sea
1	No						

By \_\_\_\_\_

Date \_\_\_\_\_

Copies To \_\_\_\_\_



Whitesell Green / Caddell, a Joint Venture  
 2700 Lagoon Park Drive  
 Montgomery, Alabama 36109  
 P: (334) 272-7723  
 F: (334) 394-0193

Project: 1054 - Escambia County Correctional  
**Facility**  
 3080 N. Pace Boulevard  
 Pensacola, Florida 32501

## Daily Log: Monday 12/31/2018

### WEATHER REPORT

Temperature			Precipitation Since			Humidity				Windspeed		
Low	High	Avg	Midnight	2 Days Ago	3 Days Ago	Low	Avg	High	Dew	Avg	Max	Gust
67°F	71°F	69°F	0.20 in.	0.23 in.	0.30 in.	89%	96%	100%	68°F	10.5 mph	15 mph	20 mph

### DAILY SNAPSHOT

06:00 AM	09:00 AM	12:00 PM	03:00 PM	06:00 PM	09:00 PM
cloudy 69°F	cloudy 69°F	cloudy 71°F	rain 70°F	rain 70°F	cloudy 69°F

### MANPOWER LOG

0 Workers | 0.0 Man Hours

No.	Contact/Company	Cost Code	Workers	# Hours	Man Hours	Location
1	Caddell Construction Co. (DE), LLC		0	0.0	0.0	
<b>Notes:</b> No work performed due to rain.						
			<b>0</b>		<b>0.0</b>	

### OBSERVED WEATHER CONDITIONS

No.	Weather Delay	Sky	Temp	Average	Precipitation	Wind	Ground/Sea
1	Yes						

By \_\_\_\_\_

Date \_\_\_\_\_

Copies To \_\_\_\_\_

**Committee of the Whole**

7.

**Meeting Date:** 01/17/2019

**Issue:** DSM/LDC Modification Explanation

**From:** Joy Jones, Director

---

**Information**

**Recommendation:**

Design Standards Manual/Land Development Code (DSM/LDC) Modifications  
(Colby Brown - 30 min)

- A. Board Discussion
  - B. Board Direction
- 

**Attachments**

DSM/LDC Mods Explanation

---



# Design Standards Manual / Land Development Code Modifications

(Referred from November 1, 2018, 5:48 p.m. Public Hearing)

Explanation of the Professional Advisory Committee and  
Planning Board Approved Modifications

Committee of the Whole

01-17-2019



# Brief History



- Jan 2018 - Discussion of Design Standard Manual (DSM) items began with the Professional Advisory Committee (PAC)
- June 2018 – PAC Approved modifications be recommended to Planning Board
- Oct 2018 – Planning Board Approved modifications be recommended to BCC
- Nov 1, 2018 – BCC approved the “Impervious Cover” limits for Minor Subdivisions, all other DSM items moved to December 2018 COW.



# DSM Items – Recommended Modifications



- Pond Slopes
- Pond Stabilization
- Impervious Cover – Minor Subdivisions
- Mass Clearing / Grading
- Limerock Base
- Utilities in the Right of Way
- Connectivity
  - Residential
  - Commercial





# Pond Slopes



- Staff Initiated
- Due to flat pond bottom, County ponds with some type of filtration system (typically because of poor soils) have trouble "drying up."



# Pond Slope (Photos)





# Pond Slope 2 (Photos)





# Pond Slope 3 (Photos)





# Pond Slope (Proposed Language)



- 0.3% minimum slope on the bottom of the ponds with a filtration device. (0.3% is minimum slope for roadside swales DSM 1-1.5 (b) 2)

## DSM, Chapter 1, Article 1 – STORMWATER

### Sec. 1-1.4 Pond Slopes, Fencing, and Maintenance Access

#### (a) Residential Subdivisions (private and public)

##### (1) Side and bottom slopes

- c. Dry Pond Bottom Slope- Shall have a minimum slope of 0.3% from the toe of pond banks to the nearest edge of any engineered treatment device (i.e. sand filter, sand chimney) for dry ponds in poor soils.



# Pond Stabilization



- Clay Core
  - Local Engineer Initiated
  - No guidelines regarding the wet pond clay core embankment.
- Dry pond side slopes
  - Only pond slopes were being sodded
  - Staff noted erosion issues along the top of bank for many projects



# Pond Stabilization (Proposed Language)



## DSM, Chapter 1, Article 1 – STORMWATER

### Sec. 1-1.4 Pond Slopes, Fencing, and Maintenance Access


#### (3) Stabilization

~~a. Wet ponds — wet ponds shall be stabilized in solid sod above the permanent pool elevation, unless stabilization is obtained through incorporation of littoral plantings.~~

#### a. Wet ponds-

1. Shall be stabilized in solid sod above the permanent pool elevation, unless stabilization is obtained through incorporation of littoral plantings.
2. Pond embankments shall be designed to have an impermeable clay core of sufficient width and stability and be keyed in below the pond bottom according to geotechnical recommendations.

Clay Core 

Dry Pond  
Side Slope 

b. Dry Ponds - Side slopes shall be solid sod from the bottom to three (3) feet beyond the top of bank



# Minor Subdivision Impervious Allowance



- This was approved by the BCC on 11-1-2018

## 1-1.6 Exemptions

Projects that include the addition of 1000 sf or less of impervious surface which are not part of a large development plan shall be exempt from this chapter.

### (a) Residential property improvements

Improvements such as driveways, buildings, pools, etc. and/or accessory structures that do not exceed 1500 sf, shall be exempt from this chapter.

### (b) Minor Subdivisions:

Proposed subdivision of land into no more than five single-family lots, each fronting on and

existing paved public or private streets, and complying with all of the following:

1. No adverse impacts. Impervious cover on the lots will not adversely impact wetlands or create adverse off-site impacts.
2. Impervious cover limits shall not exceed:
  - a. 3000 square feet on lots less than ¼ acre in size or
  - b. 3500 square feet of lot area on ¼ acre up to one acre in size or
  - c. Eight percent of lot area greater than one acre in size.
3. Documented limits. Lot impervious cover limitations are permanently documented in the public records of the county, including the subdivision plat and any covenants and restrictions.
4. Positive outfall. Each lot has a positive drainage outfall.
5. Flood Prone Areas. Each lot shall not be in an area with historical flooding/drainage complaints or noted as an area of concern in the drainage basin study.






# Mass Clearing / Grading



- Developer Initiated
- Multiple requests for mass grading entire / partial subdivision
- Concerns
  - Sedimentation off site
  - Difficult to stabilize
  - Potential large time gap between infrastructure construction and home construction
- Benefits
  - All excavated soil can be used on site
  - Sale of lots with no fill required
- Staff has been addressing on a case by case basis. Intent for the modifications was to provide clarity and consistency.




# Mass Clearing / Grading Example

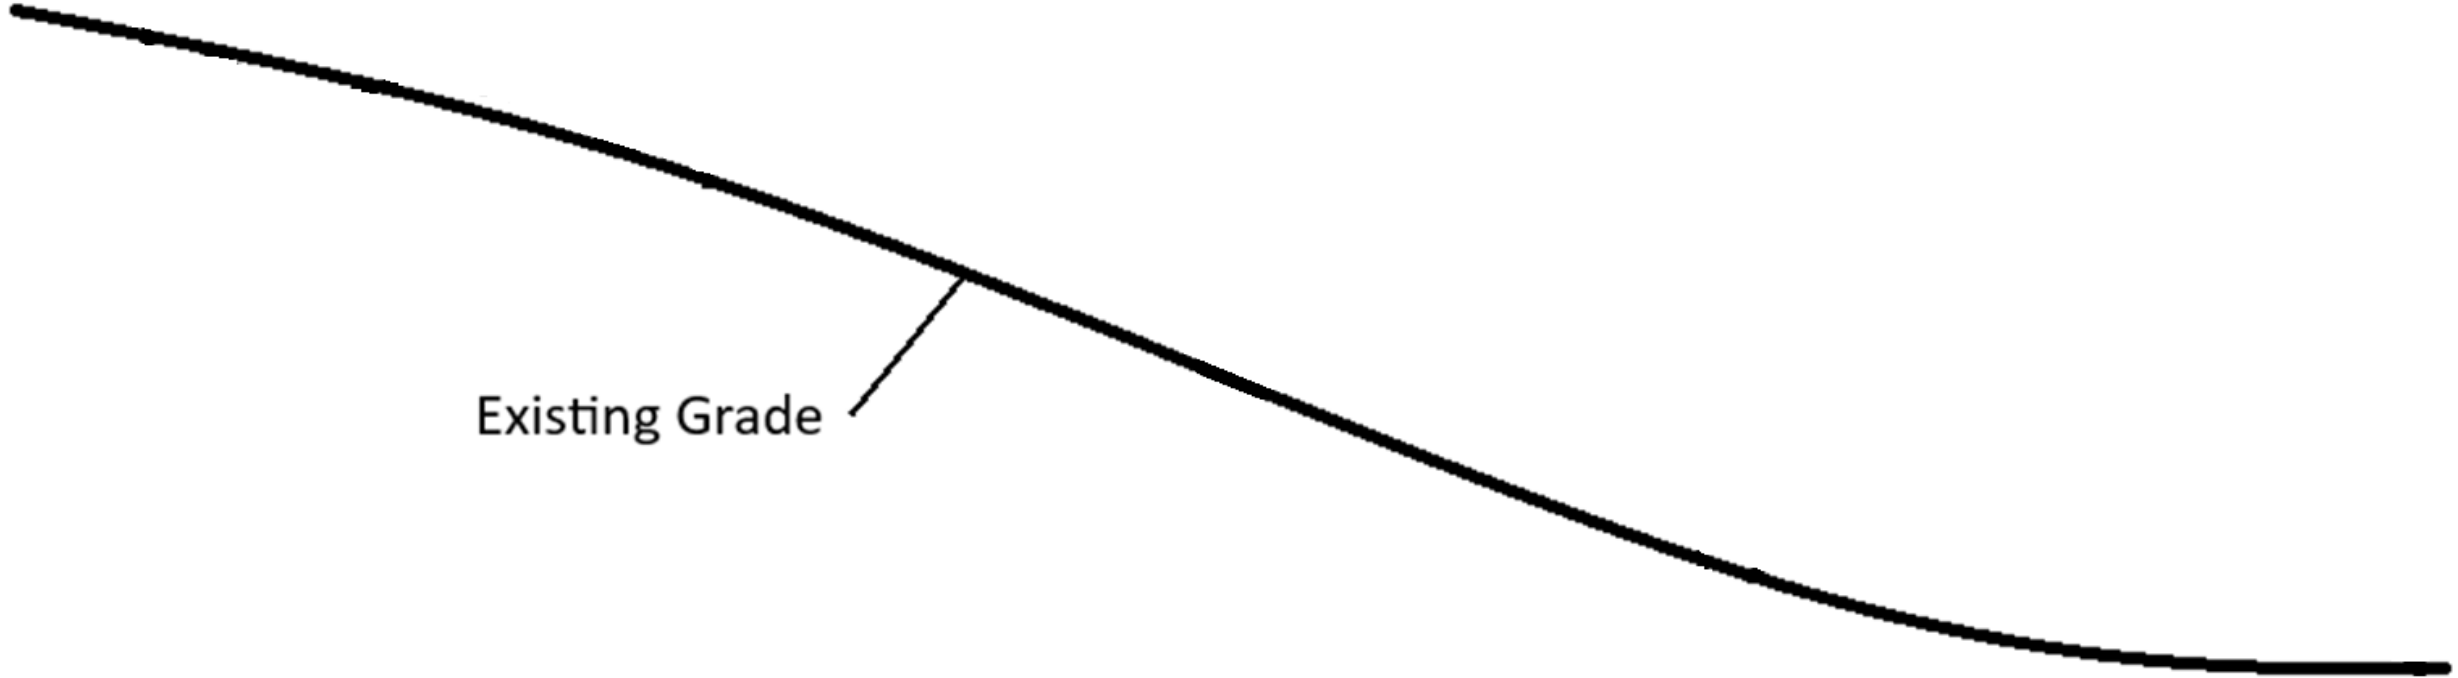

Existing Grade




# Mass Clearing / Grading Example

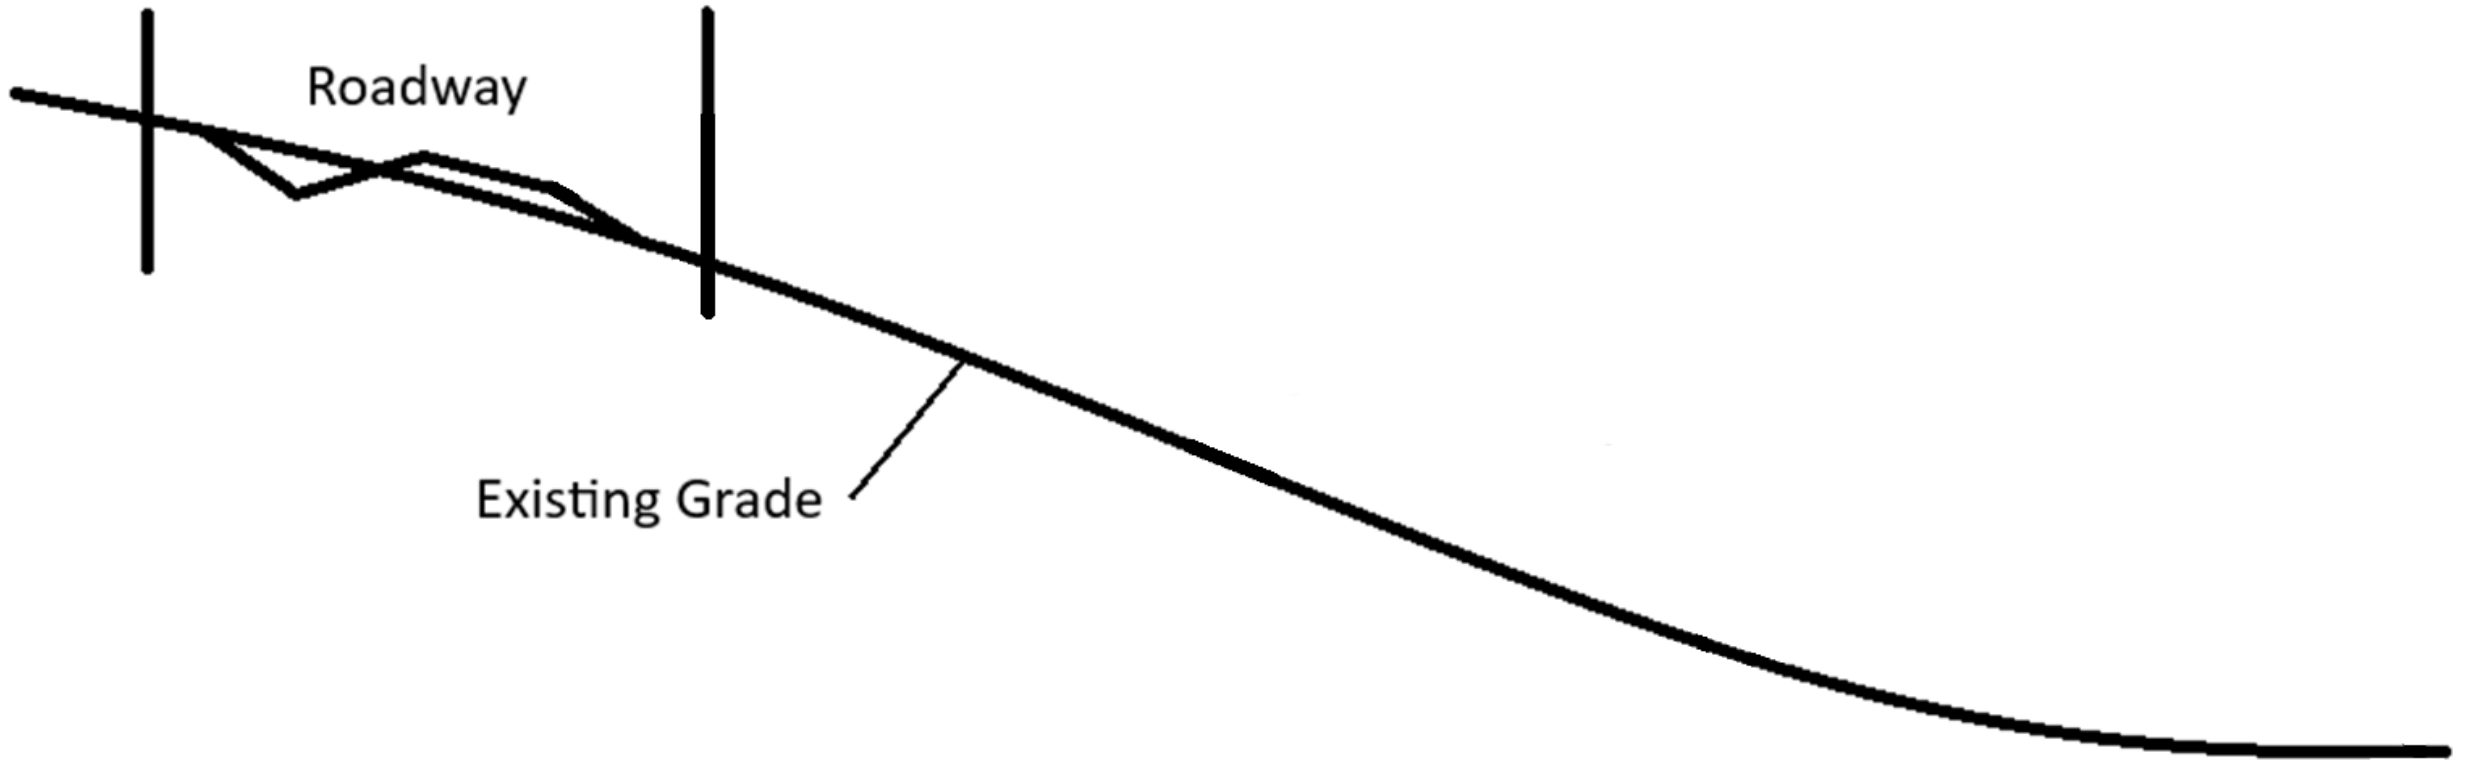




# Mass Clearing / Grading Example

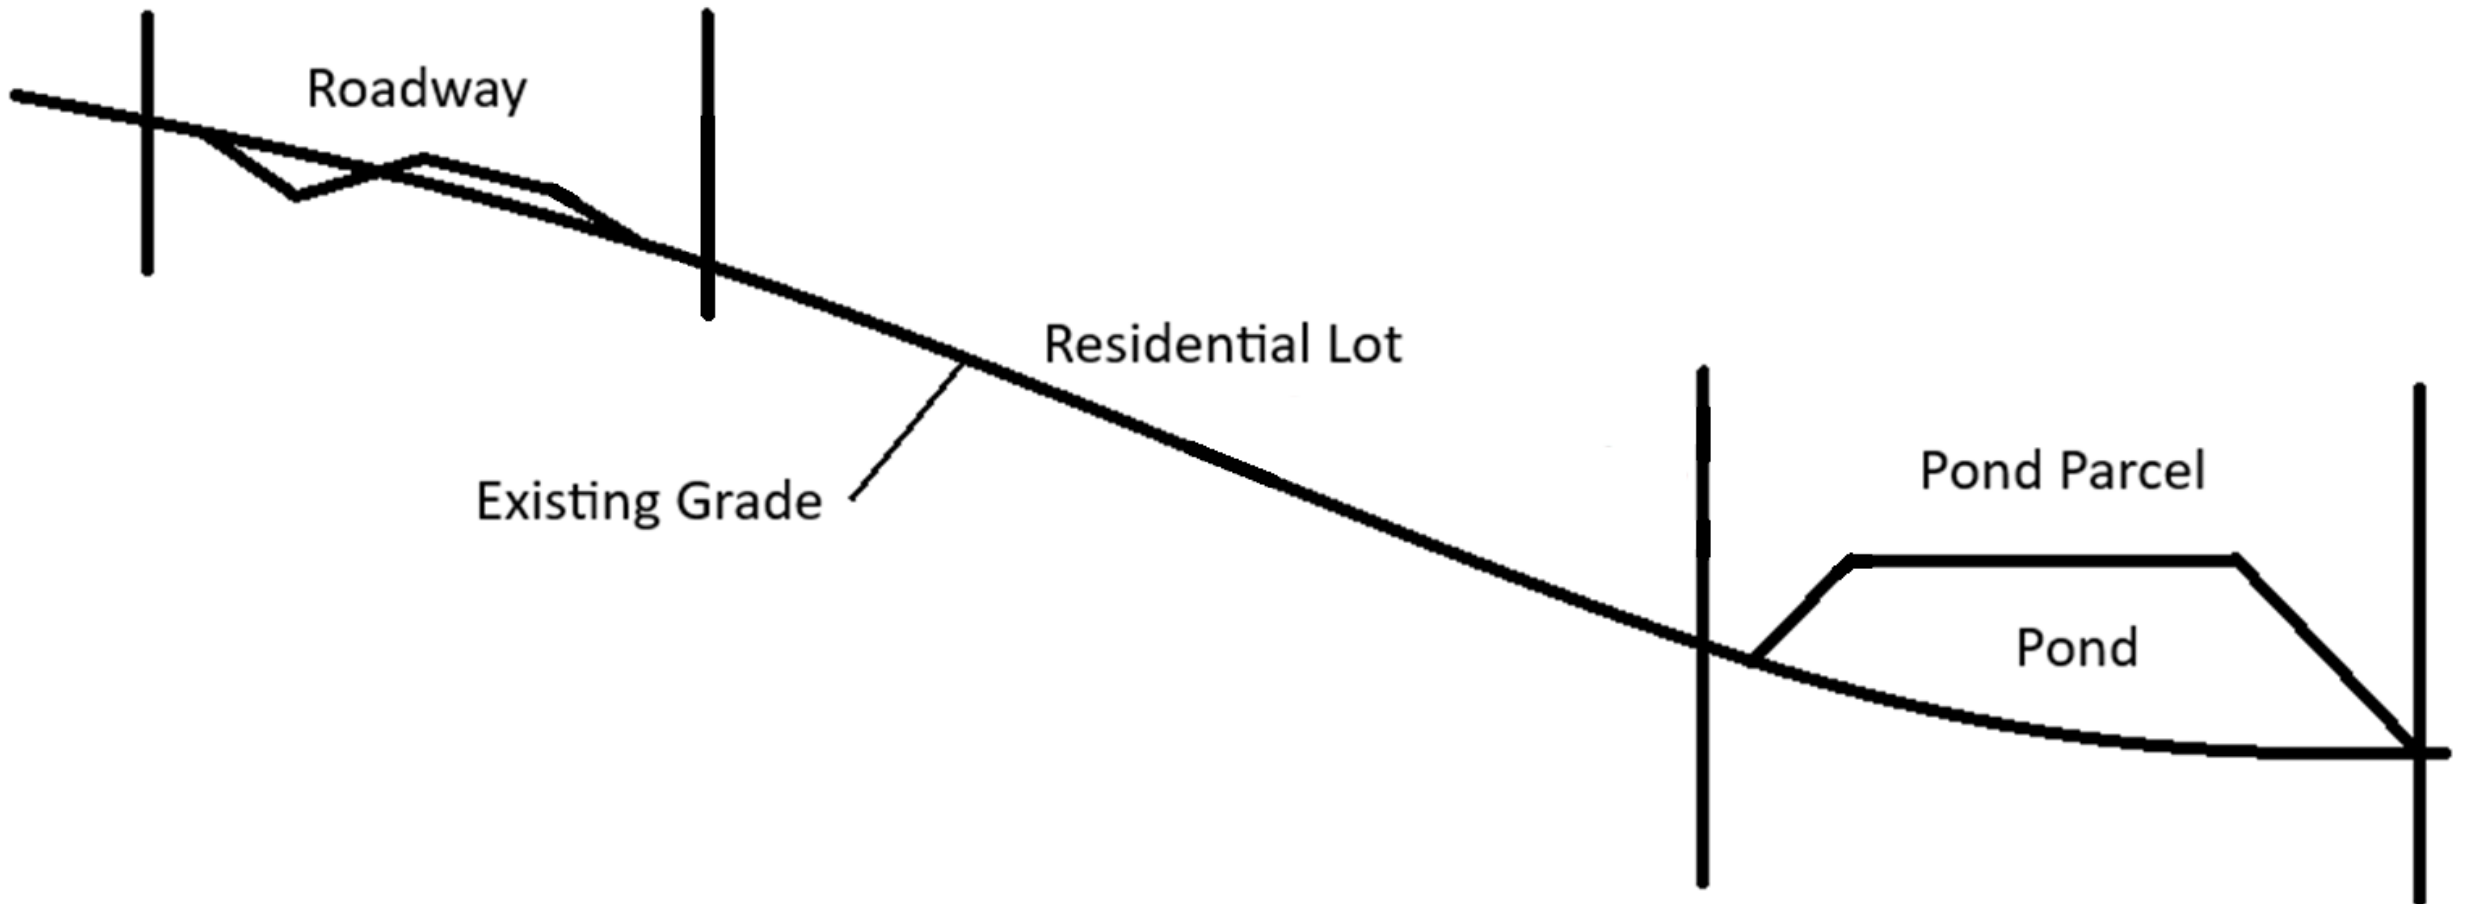




# Mass Clearing / Grading Example

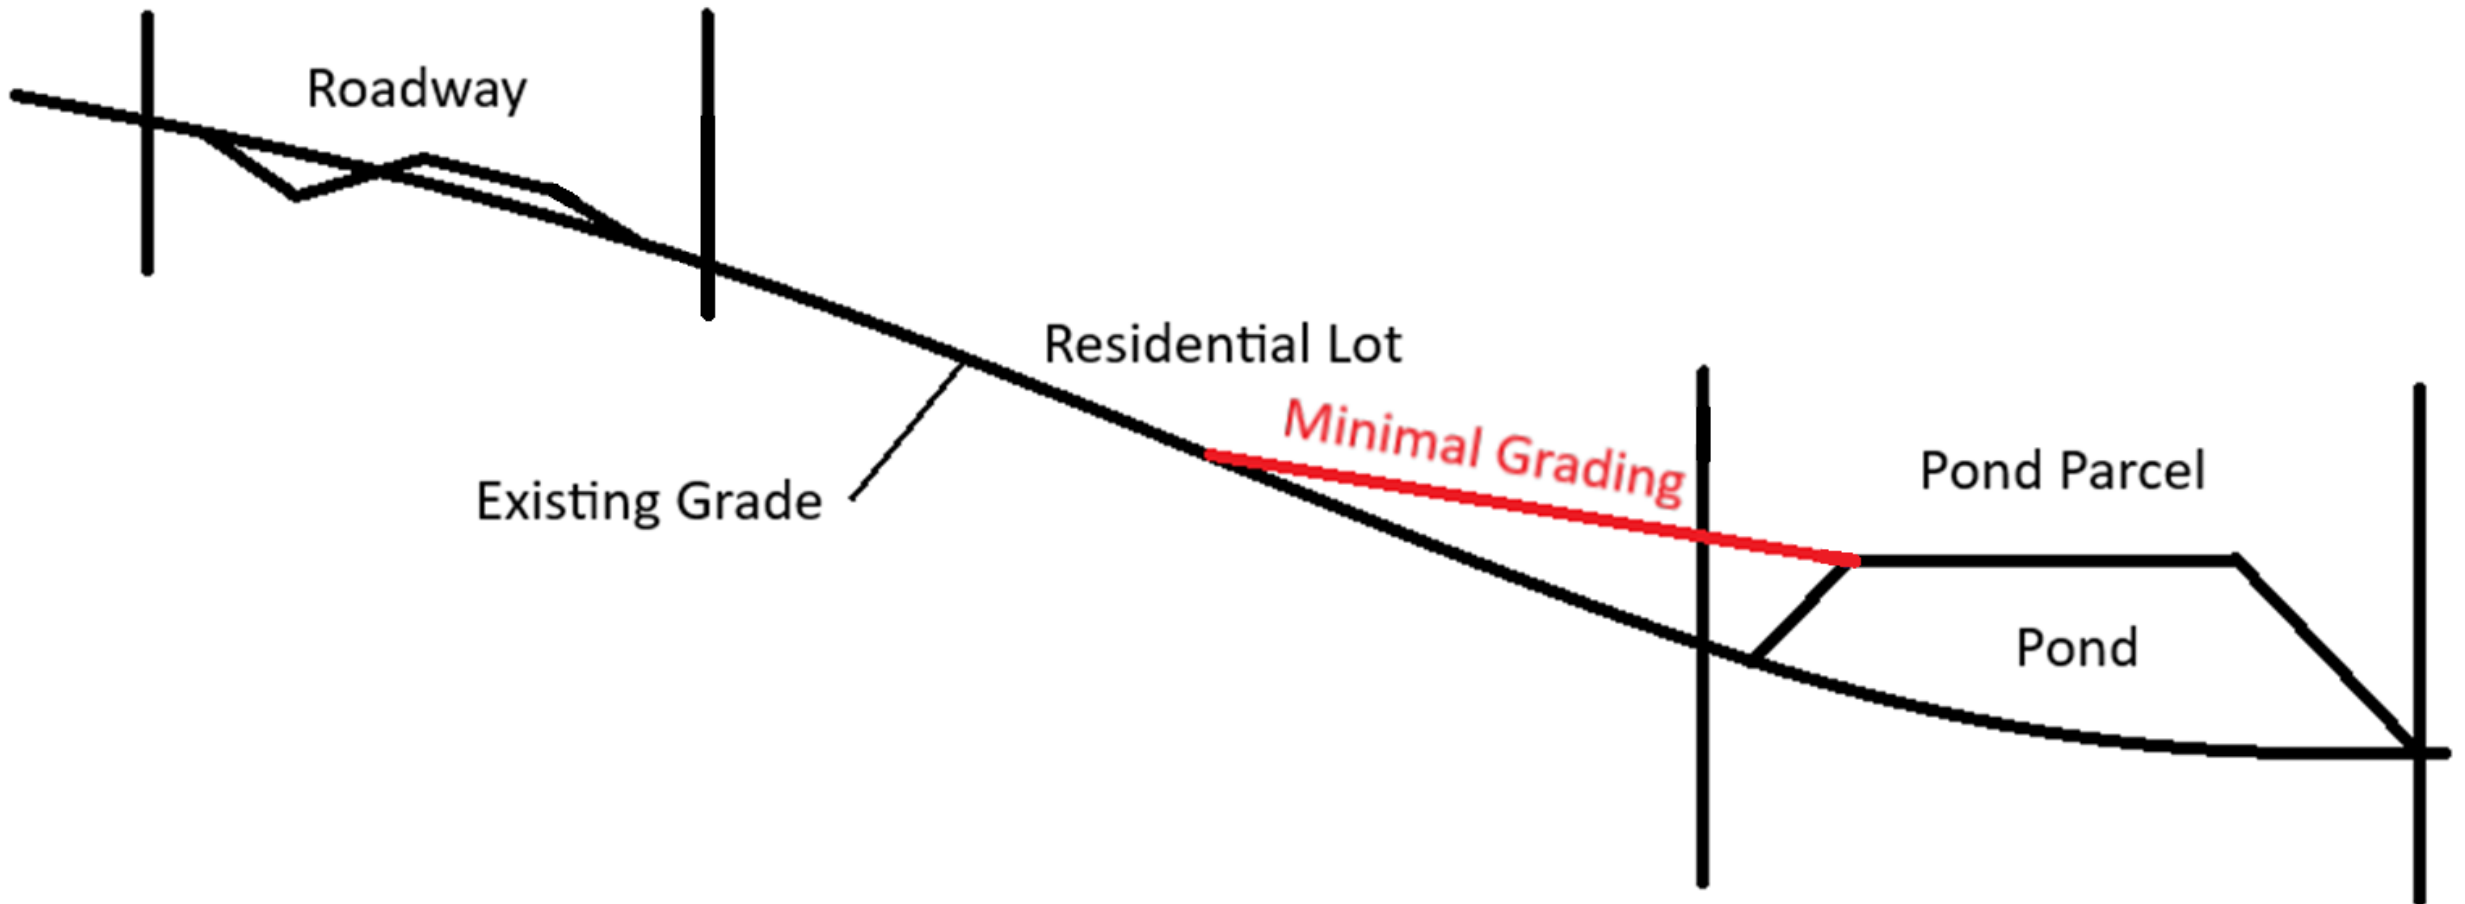



# Mass Clearing / Grading Example

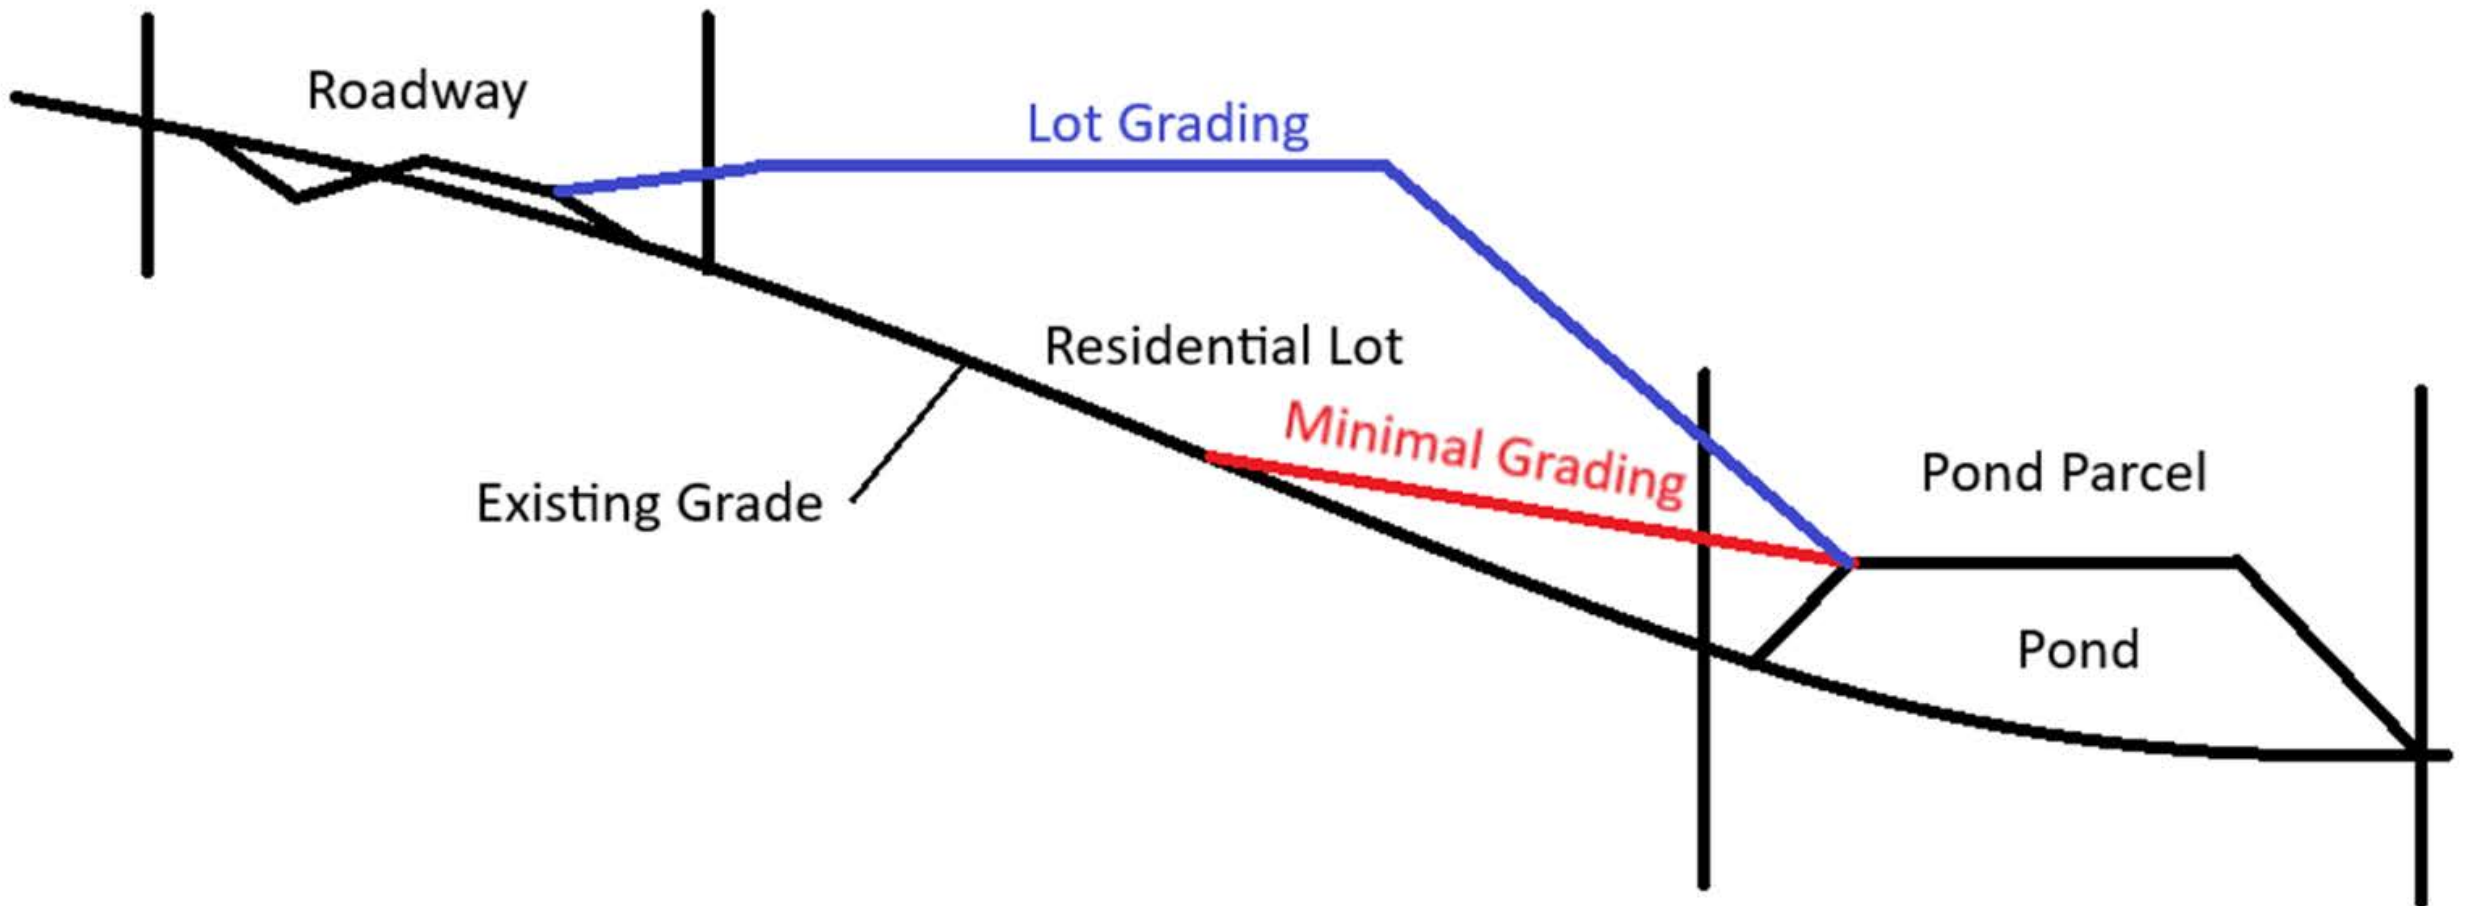



# Mass Clearing / Grading (Proposed Language)



## 1-2.2 Content

### (b) Proposed Improvements

All proposed alterations to the project site shall be detailed and include the following:

- F. Overall lot grading plan for all proposed subdivisions in accordance with the ~~Florida Building Code~~ County approved lot grading plan checklist.
- 6. Grading beyond limits of infrastructure (ROW and pond parcel) – Grading, prior to final plat, shall be described on a separate grading plan sheet and be accompanied by a separate Stormwater Management Permit. This shall only apply to the following (not for entire site development clearing and grading):
  - a. For the use of excess on - site material
  - b. To establish a functioning stormwater system
  - c. To establish right -of -way grades beyond right-of-way line.



# Limerock Base



- Local Engineer Initiated
- DSM allows for Base Material Exception Request
- Request typically comes after plans are approved and prior to construction.
- This particular base material exception was being requested frequently and an exception for the material was requested
- This will allow for either Graded Aggregate Base or Limerock Base to be noted on the plans if approved by Geotechnical Engineer





# Limerock Base (Tech Notice / Request Form)



Board of County Commissioners • Escambia County, Florida

Joy D. Blackmon, P.E.  
Director, County Engineer  
Public Works Department

### TECHNICAL NOTICE

No: (03.11.16)  
Adopted: 04/05/16

To: Developers and Home Builders

Engineers of Record

Engineering Staff

From: Escambia County Engineering Department

This notice is intended to provide information regarding changes and/or clarification of Escambia County's policies, procedures, standards and/or specifications to the general public, design professionals, homebuilders and developers. Below are the changes/clarifications:

#### Roadway Construction – Engineering Department Policy

NOTICE: Escambia County requires the installation of Graded Aggregate Base on all new roadways meeting the requirement of technical specification 2400 per the Escambia County Technical Specifications. Escambia County realizes the benefit of utilizing other FDOT approved base materials when their performance can satisfactorily meet or exceed the properties of Graded Aggregate Base.

If the Engineer of Record would like to utilize an approved FDOT material other than Graded Aggregate Base, this request must be made in writing and will be either granted or denied at the discretion of the County Engineer. Within this request the Engineer of Record must show documentation that the material is FDOT approved and will meet or exceed the properties of Graded Aggregate Base.

The Contractor and Supplier will be held to strict compliance with FDOT quality control measures and documentation of this product as well as FDOT required field testing. All reports and field testing results shall be submitted to the Engineer of Record for submittal to the County Inspector for acceptance.

The performance of this material shall be closely monitored throughout installation in the two-year compliance period. Approved test results shall be required prior to recommendation to the Board of County Commissioners for final Plat recording.



### BASE MATERIAL SUBSTITUTION REQUEST

NAME OF SUBDIVISION \_\_\_\_\_

LOCATION/ADDRESS \_\_\_\_\_

PUBLIC OR PRIVATE \_\_\_\_\_ REQUESTED BASE MATERIAL \_\_\_\_\_

#### SUPPORTED DOCUMENTS:

PROOF THAT THE MATERIAL/SUPPLIER CURRENTLY APPROVED BY FDOT (on current "Approved Products from Mines or Terminals Listing")

CONSTRUCTION PLANS WITH LOCATION OF BASE MATERIAL USAGE (if applicable)  OR ENTIRE S/D

NARRATIVE/JUSTIFICATION \_\_\_\_\_

CERTIFICATION BY REGISTERED PROFESSIONAL ENGINEER: I approve this base material for substitution at this location and will ensure that the base meets all specification prior to paving over this material.

NAME OF ENGINEER \_\_\_\_\_ SIGNATURE OF ENGINEER \_\_\_\_\_ DATE \_\_\_\_\_

COMPANY NAME \_\_\_\_\_

COMPANY ADDRESS \_\_\_\_\_ (Affix Seal)

#### OFFICE USE ONLY

APPROVED  DENIED \_\_\_\_\_ DATE \_\_\_\_\_  
DRAINAGE ENGINEER

APPROVED  DENIED \_\_\_\_\_ DATE \_\_\_\_\_  
JOY JONES, P.E., COUNTY ENGINEER

APPROVAL CONDITIONS  REASON FOR DENIAL: \_\_\_\_\_

- EOR shall ensure that substitute base material used meets specifications and is adequately protected during construction for optimum performance. EOR shall provide a statement that he/she approves the base work prior to paving.
- The performance of this material shall be closely monitored throughout installation and throughout the two-year warranty (compliance) period. If base failure occurs, additional testing and removal and installation of GAB may be required at no expense to the County.
- The Contractor and Supplier will be held to strict compliance with FDOT quality control measures and documentation of this product as well as FDOT required field testing.
- All reports and field testing results shall be submitted to the County for acceptance.
- Approved test results shall be required prior to recommendation to the Board of County Commissioners for Final Plat recording.



# Limerock Base (Proposed Language)



## DSM, Chapter 1, Article 2 – TRANSPORTATION

### 2-1 Roadway Design

All roads and bridges constructed within Escambia County, public or private, shall be constructed to meet the design and materials standards identified within the DSM and Escambia County Technical Specifications.

Escambia County base requirements are as follows:

a. All roadways shall require the installation of Graded Aggregate Base from an FDOT approved supplier, and meeting the requirements of technical specification 2400 per the Escambia County Technical Specifications.

<https://myescambia.com/our-services/public-works/engineering-and-construction>

b. Lime rock may be substituted for Graded Aggregate Base on all roadways with at least four (4) foot separation between the bottom of the base and the seasonal high ground water table if supported by the geotechnical engineering report. A note shall be included on the plans as follows: The Limerock must meet FDOT specifications and shall be from an FDOT approved supplier. The contractor shall utilize appropriate methods to prevent moisture intrusion until completely paved. Any apparent failure during the 2 year warranty period shall require the removal of the asphalt and limerock base material (across the entire roadway width and 50' either side of the failed area), replacement with Graded Aggregate Base, and re-paving of the area.

c. All roadways on the barrier islands shall require the installation of Bahama Rock.

Approval by the County Engineer is required prior to the use of any other substitution of base material. This approval process shall utilize the County approval form.




# Utilities in Right of Way (Utility Depth)



- Staff Initiated
- Utility Depth
  - Changes are to clarify where the installation for the utility depth is to be measured from.




# Utility Depth (Example)

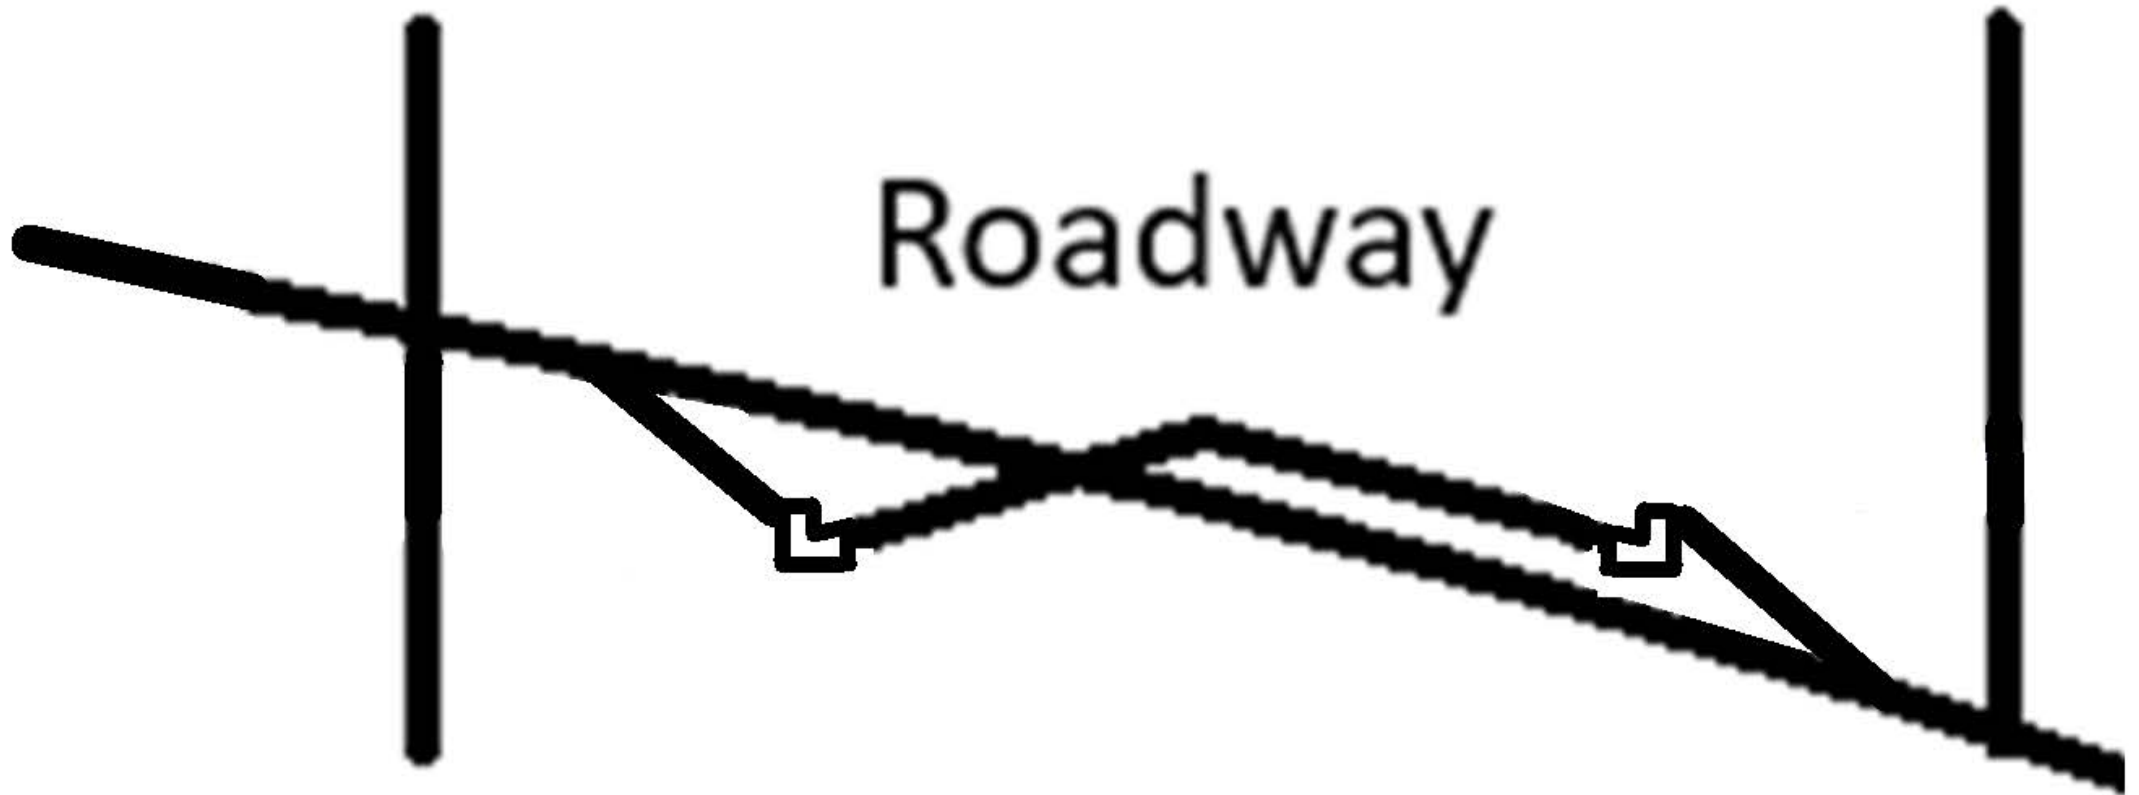




# Utility Depth (Example)

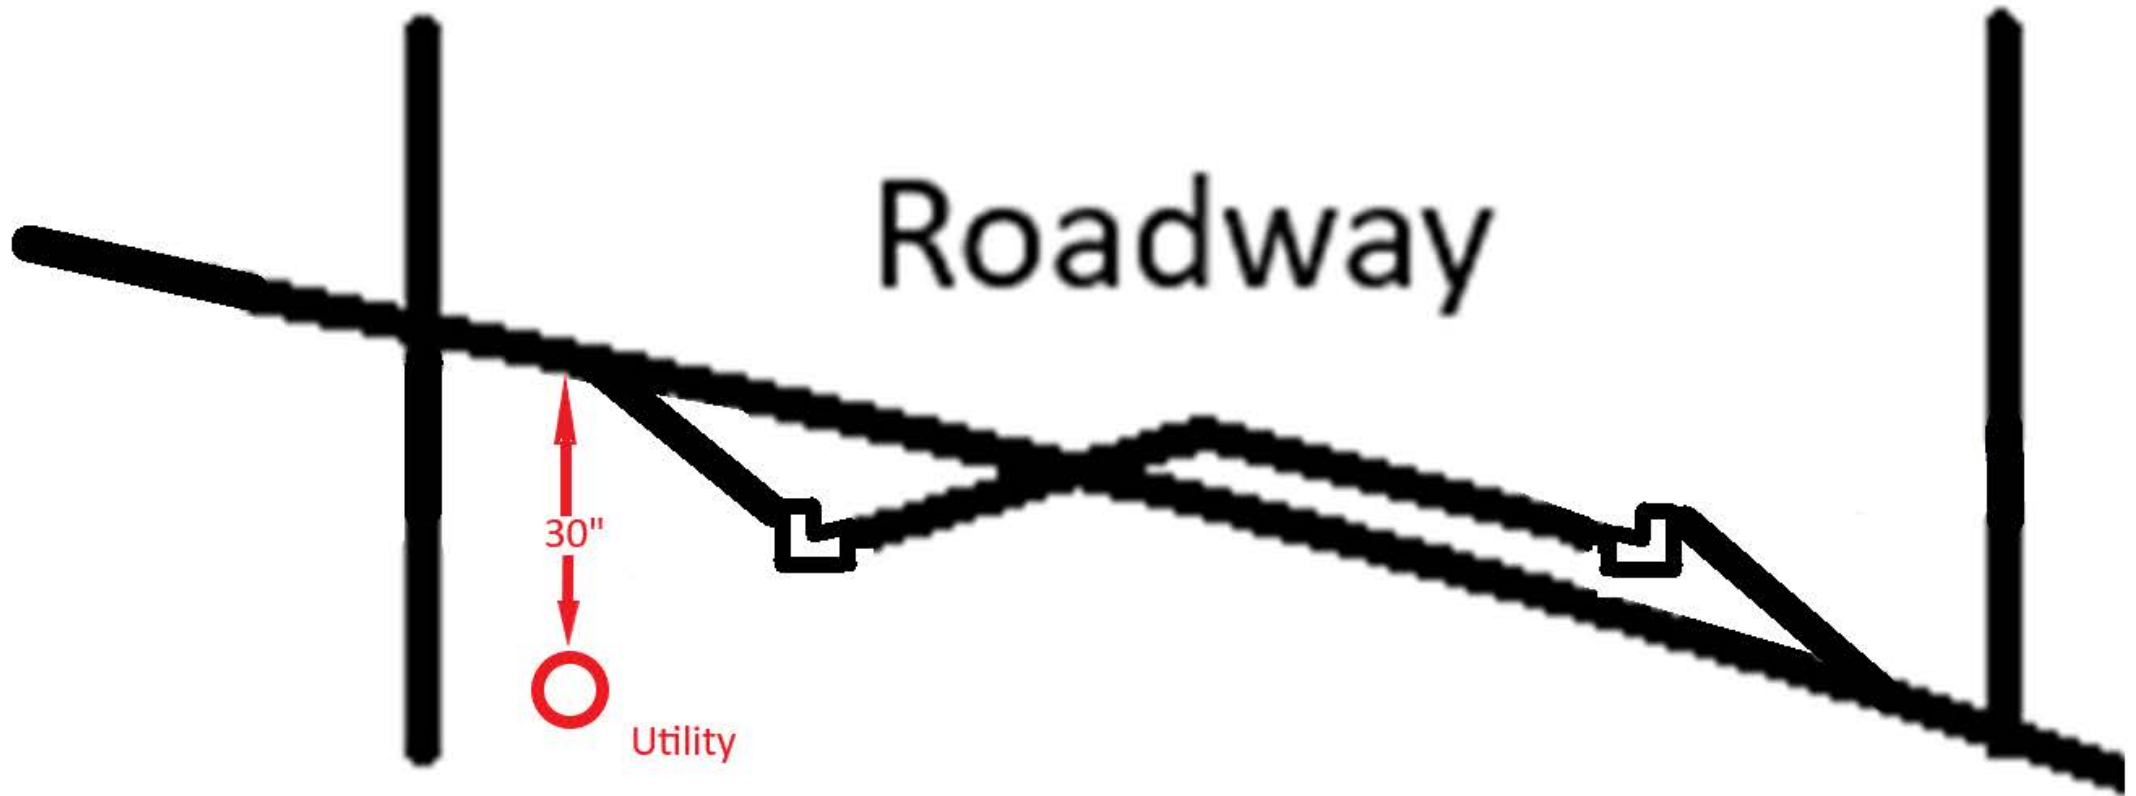



# Utility Depth (Example)

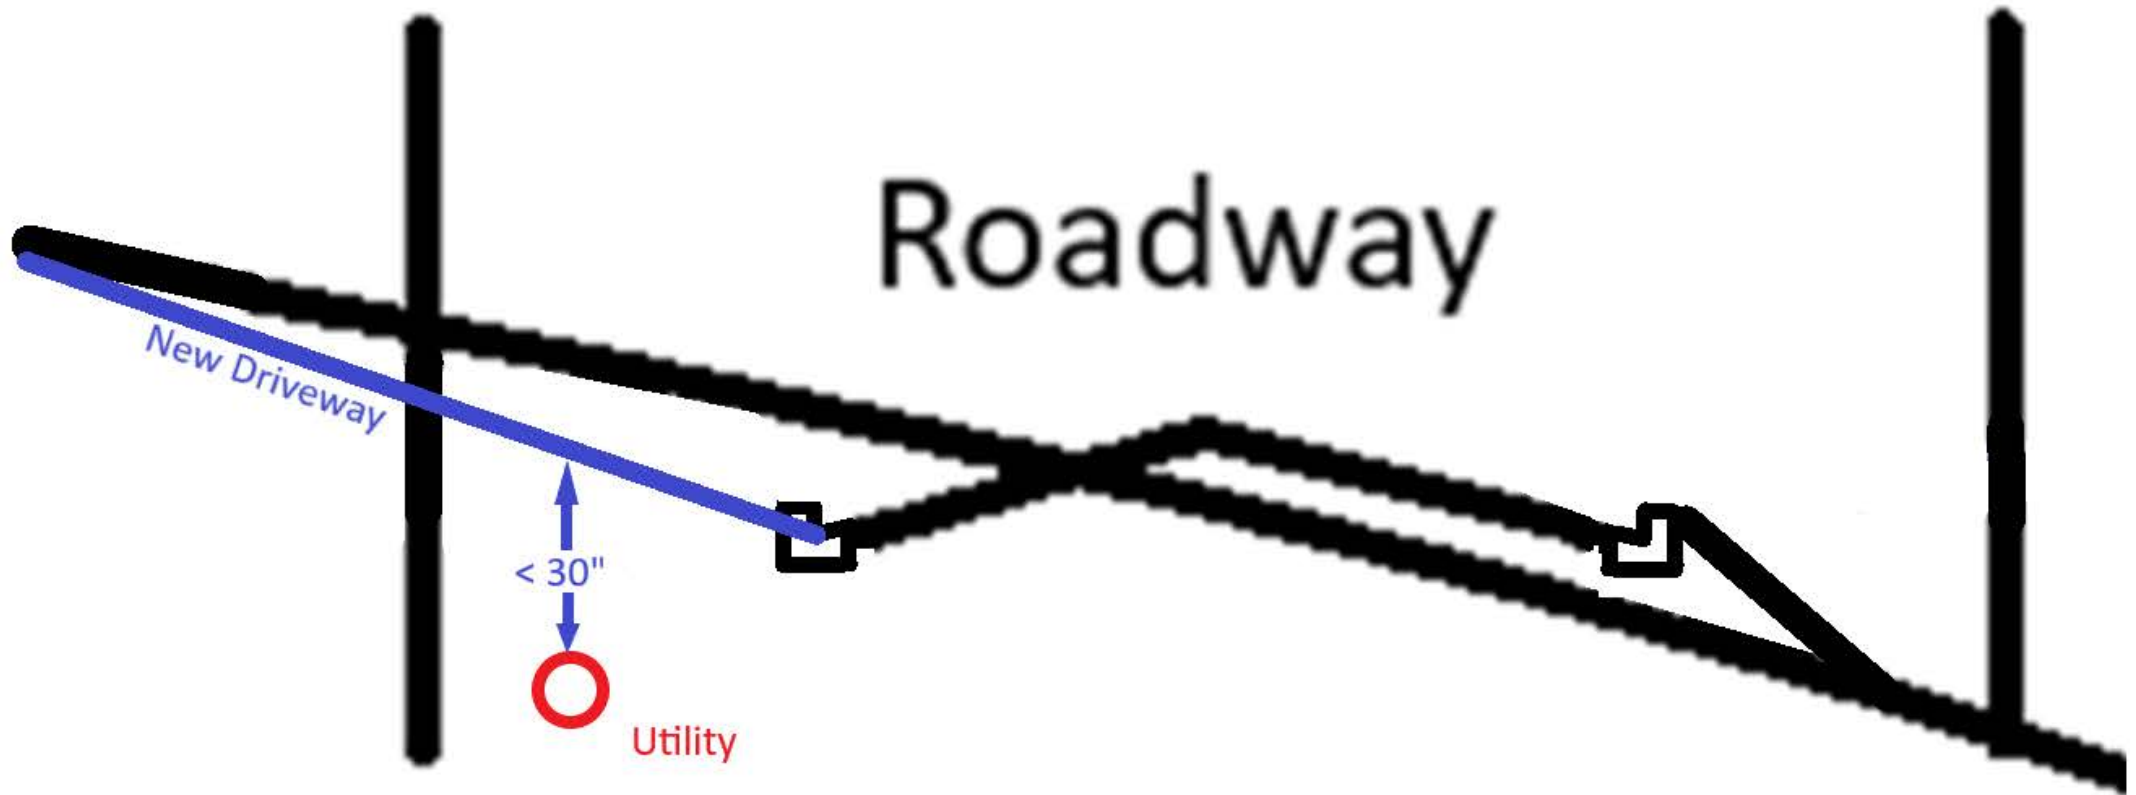



# Utilities in the Right of Way (Proposed Language – Utility Depth)




## 2-1.6 Street Layout

### ~~(d)~~(4) Utilities in road right of ways

No streets or roads under the two-year warranty will be allowed to be open cut, or bored. To accomplish this requirement, common trenching is required whenever possible. The engineer of record shall provide proof of request for all utility layouts (to include but not limited to power, communications, gas, etc.) prior to construction plan approval. Conduit locations for utility roadway crossings shall be included in construction plans. If locations are not provided by the utility, the engineer of record shall provide conduit locations for utility road crossings. Conduit shall be installed with tracer wire and/or other locating methods. The following notes shall be included in the plans: ~~Contractors shall communicate with utility provider(s) a minimum of two weeks prior to curb installation or roadway base installation. Contractors shall ensure integrity of conduit throughout roadway installation.~~

- a. Contractors shall coordinate with utility provider(s) a minimum of two weeks prior to curb installation or roadway base installation. Contractors shall ensure integrity of conduit throughout roadway installation.
- b. New utilities shall be installed at a minimum depth of cover of 30 inches in accordance with the final lot grading plan or from the top of curb, as appropriate.

Utility Depth 



# Connectivity (Residential)



- Staff Initiated
- Concerns with multiple S/D lots fronting an arterial or collector
  - Unsafe for residents to be backing out on to these type roadways





# Connectivity (Proposed Language - Residential)



## DSM, Chapter 1, Article 2 – TRANSPORTATION

### 2-1.6 Street Layout

#### (a) Residential.

#### ~~(a)~~ (1) Connectivity

b. Proposed subdivision along arterial or collector roadways, where lots front the arterial or collector, shall provide a single access route within the subdivision to the roadway with the lowest traffic volume. (LDC 5-5.4 (f)(q)).

#### Sec. 5-5.4 Site access.

- (f) **Internal access.** Proposed development along arterial or collector streets shall provide access routes within the development for all uses such that a return to the arterial or collector street is not necessary to access another use within the development.
- (g) **Multiple street frontages.** When a lot or parcel is located at a street intersection or otherwise fronts more than one street, vehicle access for all uses on the lot, including single-family dwellings, may be limited to the roadway with the lowest traffic volume, least operational impact, or lowest functional classification, provided that the restriction is consistent with existing FDOT standards. Potential traffic impacts to residential neighborhoods shall be considered when applying this restriction. Non-access easements may be required on site plans and plats to implement this restriction.

LDC 5:25



# Connectivity (Commercial)



- Staff Initiated
- Concerns with multiple Commercial lots along arterial and collector each with single access
- Item to be removed from recommendation
  - Multiple Legal concerns



# Connectivity (Proposed Language – Commercial)



## **DSM, Chapter 1, Article 2 – TRANSPORTATION**

### **2-1.6 Street Layout**

#### **(b) Commercial Connectivity**

Any proposed commercial site adjacent to another commercial site or vacant site fronting a collector / arterial road with AADT greater than 9000 shall provide internal connectivity with the adjacent lots, unless a hardship can be documented. Hardships can be defined as:

1. Creates a non-conformity.
2. Physical impediment (elevation, structural, etc.).
3. Existing, built-out, configuration of adjacent development.
4. Cost increase of 25% above cost without providing connectivity.
5. Other hardships as determined by Planning Official and County Engineer.

Planning Official and County Engineer shall determine if the inability to provide connectivity is a hardship.



# Questions / Direction



- Direct Staff to:
  1. Bring back All and/or Specific Items (except Commercial Connectivity) via recommendation to next BCC; or
  2. Remand All and/or Specific Items back to Planning Board / PAC for further discussion.

**Committee of the Whole**

8.

**Meeting Date:** 01/17/2019

**Issue:** Advanced Traffic Management System (ATMS)/Intelligent Transportation System (ITS) Signalization Upgrades - LOST IV

**From:** David Forte, Division Manager

---

**Information**

**Recommendation:**

Advanced Traffic Management System (ATMS)/Intelligent Transportation System (ITS)

Signalization Upgrades - LOST IV

(Colby Brown/David Forte - 15 min)

A. Board Discussion

B. Board Direction

---

**Attachments**

Presentation

Signalization Upgrades List

---



# ITS / ATMS Signalization Upgrades

Committee of the Whole Workshop  
Board of County Commissioners

Board Chambers  
Suite 100  
Ernie Lee Magaha Government Building – First Floor  
221 Palafox Place

January 17, 2019  
9:00 a.m.



# Acronyms and Responsibility

- Intelligent Transportation Systems (ITS) – General connectivity / communications / technology in Transportation
- Advanced Traffic Management System (ATMS) - primary “subfield” within ITS to improve traffic flow and safety.
- Transportation Management Center (TMC) or Traffic Signals Operations Center (TSOC) – central location(s) where signal communication and data is integrated, processed, and signal modifications are implemented.
- County maintains and operates all of the traffic signal devices in the County (Local and State)



# LOST IV – District 2 Discretionary Payback

- May 25, 2017 - BCC reallocated \$1M from the ITS Fund to Perdido Key Beach Access Land Purchase
- FY 2024 - \$1M payback currently programmed due to LOST IV budgetary constraints
- \$1M Payback this FY from D2 (Possible partial FY2018 and FY 2019 D2 discretionary dollars)
- \$226K reimbursement from FDOT (Expected within the next couple months)
- Payback and reimbursement, this FY, will allow acquisition and installation of ATMS upgrades at the various locations (see attached list) and coordination with IT Department for the TSOC upgrades.





# Proposed Signalization Upgrades

- Device Upgrades – See attached List
  - Funding (totaling approx. \$1.226M)
    - Currently \$2K in ITS fund
    - \$226K being refunded from FDOT Camera upgrade project
    - \$1M District 2 Payback
  - Equipment Targeted for Connectivity Upgrades (based on prioritized needs)
    - 31 traffic signals
    - 26 school beacons
    - Additional equipment (software and hardware) would be needed in the TSOC to accommodate the increased capacity.



# Board Discussion/Direction

1. Designate LOST IV Funding allocation
2. Approve the Signalization Upgrades List

**LOST III - ATMS / ITS Application Box Fund Plan**

<b>District</b>	<b>Major Road</b>	<b>Minor Road</b>	<b>Upgrades</b>	<b>Total Cost</b>
3	CR 443 ("E" Street)	Jordan Street	ATMS Upgrades For Traffic Signals Operations Center (TSOC) Connectivity	\$ 23,025.00
3	"E" Street	CR 480 (Leonard Street)	ATMS Upgrades For TSOC Connectivity	\$ 23,025.00
3	CR 453 ("W" Street)	Scott Street	ATMS Upgrades For TSOC Connectivity	\$ 25,540.00
3	"W" Street	Avery Street	ATMS Upgrades For TSOC Connectivity	\$ 23,690.00
2 & 3	"W" Street	CR298A (Jackson Street)	ATMS Upgrades For TSOC Connectivity	\$ 24,135.00
1	CR 293 (Bauer Rd.)	Southwest Escambia Sports Complex	ATMS Upgrades For TSOC Connectivity	\$ 8,095.00
5	CR 4 (Bratt Rd.)	CR 4A (Byrneville Rd)	ATMS Upgrades For TSOC Connectivity	\$ 5,535.00
5	CR 749 (Chemstrand Rd.)	CR 186 (Kingsfield Rd.)	ATMS Upgrades For TSOC Connectivity	\$ 16,360.00
5	Chemstrand Rd.	Ten Mile Rd.	ATMS Upgrades For TSOC Connectivity	\$ 16,360.00
2	Jackson Street	57th Avenue	ATMS Upgrades For TSOC Connectivity	\$ 24,135.00
1 & 2	Jackson Street	65th Avenue	ATMS Upgrades For TSOC Connectivity	\$ 24,135.00
5	Kingsfield Rd.	CR95A (Palafox Street)	ATMS Upgrades For TSOC Connectivity	\$ 2,560.00
4	Langley Avenue	9th Avenue & Tippin Avenue	ATMS Upgrades For TSOC Connectivity	\$ 50,000.00
1	Longleaf Drive	Community Drive	ATMS Upgrades For TSOC Connectivity	\$ 26,415.00
1	Marcus Pointe Blvd	Enterprise Drive	ATMS Upgrades For TSOC Connectivity	\$ 2,560.00
2	CR 295A (Old Corry Field Road)	Jackson Street	ATMS Upgrades For TSOC Connectivity	\$ 24,135.00
3 & 4	CR 290 (Olive Road)	Cody Lane	ATMS Upgrades For TSOC Connectivity	\$ 23,025.00
3	Palafox Street	Detroit Blvd/Johnson Ave	ATMS Upgrades For TSOC Connectivity	\$ 2,560.00
3	Palafox Street	Ensley St	ATMS Upgrades For TSOC Connectivity	\$ 23,025.00
3	Palafox Street	Hancock Lane	ATMS Upgrades For TSOC Connectivity	\$ 24,280.00
3	Palafox Street	Olive Road	ATMS Upgrades For TSOC Connectivity	\$ 24,135.00
5	Palafox Street	Ten Mile Rd.	ATMS Upgrades For TSOC Connectivity	\$ 25,360.00
5	SR 297 (Pine Forest Road)	CR 297A	ATMS Upgrades For TSOC Connectivity	\$ 2,560.00
1	CR 296 (Saufley Field Road)	Muldoon Road	ATMS Upgrades For TSOC Connectivity	\$ 23,025.00
5	Ten Mile Rd.	Ashton Brosnaham Drive	ATMS Upgrades For TSOC Connectivity	\$ 2,560.00
5	University Parkway	Campus Drive	ATMS Upgrades For TSOC Connectivity	\$ 2,560.00
5	University Parkway	Hillview Road	ATMS Upgrades For TSOC Connectivity	\$ 20,025.00
4	University Parkway	Johnson Avenue	ATMS Upgrades For TSOC Connectivity	\$ 20,025.00
3	"W" Street	Airport Road	ATMS Upgrades For TSOC Connectivity	\$ 24,135.00
3	"W" Street	Marcus Pointe Blvd	ATMS Upgrades For TSOC Connectivity	\$ 2,560.00
3	"W" Street	Massachusetts Avenue	ATMS Upgrades For TSOC Connectivity	\$ 24,135.00
			<b>Subtotal</b>	<b>\$ 563,675.00</b>
	<b>School Zone Beacons</b>			
1	Bailey Middle School		ATMS Upgrades For TSOC Connectivity	\$ 4,710.00
1	Bellview Elementary School		ATMS Upgrades For TSOC Connectivity	\$ 4,710.00
1	Beulah Academy of Science		ATMS Upgrades For TSOC Connectivity	\$ 4,710.00
3	Woodham High School		ATMS Upgrades For TSOC Connectivity	\$ 4,710.00
5	Byrneville Elementary School		ATMS Upgrades For TSOC Connectivity	\$ 2,355.00
4	Ferry Pass Elementary School		ATMS Upgrades For TSOC Connectivity	\$ 4,710.00
1	Blue Angel Elementary School		ATMS Upgrades For TSOC Connectivity	\$ 4,710.00
2	Pleasant Grove Elementary School		ATMS Upgrades For TSOC Connectivity	\$ 4,710.00
3	Brown Barge Middle School		ATMS Upgrades For TSOC Connectivity	\$ 4,710.00
3	Lincoln Park Elementary School		ATMS Upgrades For TSOC Connectivity	\$ 9,420.00
3	Ensley Elementary School		ATMS Upgrades For TSOC Connectivity	\$ 4,710.00
4	Holm Elementary School		ATMS Upgrades For TSOC Connectivity	\$ 9,420.00
1 & 2	Little Flower Catholic School		ATMS Upgrades For TSOC Connectivity	\$ 4,710.00
2	Myrtle Grove Elementary School		ATMS Upgrades For TSOC Connectivity	\$ 4,710.00
1	Longleaf Elementary School		ATMS Upgrades For TSOC Connectivity	\$ 4,710.00

1	Pine Forest High School	ATMS Upgrades For TSOC Connectivity	\$	4,710.00
3	Montclair Elementary School	ATMS Upgrades For TSOC Connectivity	\$	4,710.00
1	Hellen Caro Elementary School	ATMS Upgrades For TSOC Connectivity	\$	9,420.00
1	Bellview Middle School	ATMS Upgrades For TSOC Connectivity	\$	4,710.00
1	Beulah Elementary School	ATMS Upgrades For TSOC Connectivity	\$	4,710.00
2	St. Johns Catholic School	ATMS Upgrades For TSOC Connectivity	\$	4,710.00
2	Warrington Elementary School	ATMS Upgrades For TSOC Connectivity	\$	4,710.00
2	Warrington Middle School	ATMS Upgrades For TSOC Connectivity	\$	4,710.00
4	Ferry Pass Middle School	ATMS Upgrades For TSOC Connectivity	\$	4,710.00
5	Jim Allen Elementary School	ATMS Upgrades For TSOC Connectivity	\$	4,710.00
3	Brentwood Elementary School	ATMS Upgrades For TSOC Connectivity	\$	4,710.00
2	Navy Point Elementary School	ATMS Upgrades For TSOC Connectivity	\$	4,710.00
3	Catholic High School	ATMS Upgrades For TSOC Connectivity	\$	4,710.00
		<b>Subtotal</b>	<b>\$</b>	<b>143,655.00</b>
		<b>ATMS Signals and Beacons Upgrades Total</b>	<b>\$</b>	<b>850,985.00</b>
		TSOC Software and Hardware Upgrades, and field equipment to accommodate upgrades	\$	375,500.00
		<b>Signals, Beacons, and TSOC Upgrades Total</b>	<b>\$</b>	<b>1,226,485.00</b>

**Committee of the Whole**

9.

**Meeting Date:** 01/17/2019

**Issue:** Employee Engagement Survey/Performance Audit

**From:** Amy Lovoy, Assistant County Administrator

---

**Information**

**Recommendation:**

Employee Engagement Survey/Performance Audit

(Amy Lovoy/Eric Kleinert - 20 min)

A. Board Discussion

B. Board Direction

---

**Attachments**

Performance Audit

Engagement Survey

---



## Performance Audit

### **Purpose**

The Board of County Commissioners of Escambia County, Florida wishes to deliver services to the citizens of the County in the most effective and efficient manner possible while still ensuring the highest quality of services delivered. The Escambia County Board of County Commissioners is therefore requesting proposals from qualified firms to perform a performance audit for all departments under its purview.

### **General Information**

Escambia County is a non-charter county in the extreme northwestern portion of the panhandle of Florida. The County has an annual budget of approximately \$477,000,000 and an employee workforce of 1,918 with the following departments under its direct control:

<u>Department</u>	<u>Employees</u>
Board of County Commissioners	10.00
Building Services Department	69.00
Community & Media Relations	4.00
Corrections Department	575.00
County Administrator	9.00
County Attorney	13.00
Development Services Department	28.00
Extension Services	15.00
Facilities Management Department	64.00
Human Resources Department	14.00
Information Resources Department	22.00
Library Department*	76.00
Management & Budget Services Department	18.00
Mass Transit Department	140.00
Natural Resources Management	50.00
Neighborhood & Human Services	22.00
Parks and Recreation Department	27.00
Public Safety Department	488.00
Public Works Department	228.00
Solid Waste Management Department	46.00

### **Scope of Services**

The Escambia County Board of County Commissioners wishes to retain the services of appropriately qualified firms to conduct a performance audit of each of the County's departments and the County as a whole to include the following tasks for each department:

- Assessing the extent to which regulatory or organizational goals and objectives are being achieved;

- Assessing the relative ability of alternative approaches to yield better program performance or eliminate factors that inhibit program effectiveness;
- Analyzing the relative cost-effectiveness of a program or activity, focusing on combining cost information or other inputs with 1) information about outputs or the benefit provided or 2) outcomes or the results achieved;
- Determining whether a program produced intended results or produced results that were not consistent with the program's objectives;
- Determining the current status or condition of program operations or progress in implementing Board requirements;
- Assessing the extent (if any) to which programs duplicate, overlap or conflict with other related programs;
- Determining on a selected case-by-case basis whether appropriate value was obtained based on the cost or amount paid;
- Determining whether and how the program's unit costs can be decreased or its productivity increased.
- Assessing County processes and procedures to determine their efficiency and effectiveness, and if not optimal, suggesting changes.

The review should follow as closely as possible the 2018 Governmental Auditing Standards from the General Accounting Office.

### **Qualifications and Experience**

Interested parties, both corporate and individual should be fully licensed and certified for the type of work to be performed in the State of Florida at the time of the proposal receipt. Qualified firms should have experience with performance auditing of local governments. The preferred firm should have performance auditing experience with local governments in the State of Florida.

During the term of this agreement the Consultant or any employee or associate, shall not be involved in political campaign for County elective office nor make financial contributions(s) to any such campaign.

### **Response Format**

#### Independence

- A. The firm shall provide an affirmative statement that it is independent of the County as defined by generally accepted auditing standards and the US General Accounting Office's Governmental Auditing Standards.
- B. The firm shall also disclose any relationships or business dealings either the firm itself or its key partners and personnel have with the County or key County personnel that could appear to be a conflict.
- C. The firm should list and describe the firm's or any individual in the firm's professional relationships, if any, involving the County or key County personnel for the past five (5) years.

### License to Practice in Florida

An affirmative statement must be included indicating that the firm and all assigned key professional staff are properly registered/licensed to practice in Florida.

### Firm Qualifications and Experience

Proposer to identify the following:

- State whether the firm is local, national, or international
  - Size of the firm
  - Size of the firm's governmental audit staff
  - Location of the offices from which the work on this engagement is to be performed
  - Number and nature of the professional staff to be employed in this engagement on a full-time basis.
  - Number and nature of the staff to be so employed on a part-time basis and a delineation of the responsibilities of the firm.
- A. The firm shall also provide information on the results of any federal or state desk reviews or field reviews of its audits during the past three (3) years.
- B. The firm shall provide information on the circumstances and status of any disciplinary action taken or pending against the firm or any professional staff during the past three (3) years with State Board of Accountancy or the Auditor General.
- C. The firm shall also describe any litigation or proceeding whereby, during the past two years, a court or any administrative agency has ruled against the firm in any manner related to its professional activities. Similar information shall be provided for any current or pending litigation.

Failure to return this information with your proposal may result in the rejection of your proposal.

### Partner, Supervisory and Staff Qualifications and Experience

- A. The proposal shall identify the principal supervisory and management staff of engagement office, including engagement partners, managers, other supervisors and specialists, who would be assigned to the engagement.
- B. The proposal shall also include information on the governmental performance auditing experience of each person on the team, including information on relevant continuing professional education for the past three (3) years and membership in professional organizations and on standards setting advisory boards and committees relevant to the performance of this audit. As much information as possible should be provided regarding the number, qualifications, experience and training of the specific staff to be assigned to this engagement. The proposal shall also indicate how the quality of staff over the term of the agreement will be assured.

### Similar Engagements with Other Government Entities

- A. For the engagement office assigned responsibility for the audit, list and rank the five (5) most significant engagements performed in the last five years that are similar to the engagement described



- Indicate:
  - the scope of work
  - date
  - engagement partners
  - total hours
  - the name and telephone number of the principal client contact

The County reserves the right to contact the above-mentioned references and any other clients.

#### Conflict of Interest

The proposal must also disclose any potential real or perceived (as outlined in GAS Chapter 3) conflicts of interest due to any other client's contract or property interests or include a notarized statement certifying that no member of your firm's ownership, management or staff currently have a vested interest which might be considered a conflict of interest. Any potential conflict of interest listed by a firm will be reviewed by the County Attorney to determine its substantiveness. If the conflict of interest is found to be substantive, the proposal will be rejected.

#### Specific Audit Approach

The proposal must set forth a work plan, including an explanation of the audit methodology to be followed to perform the services required. Proposers will be required to provide the following information on their audit approach.

- A. Proposed segmentation of the engagement.
- B. Staffing assignments and levels to be designated to each proposed segment of the engagement.
- C. Approach to be taken to gain and document an understanding of the County's organizational structure.
- D. Approach to be taken in determining laws and regulations that will be subject to audit test work.
- E. Approach to be taken in determining audit samples for purposes of test compliance

#### Cost

The proposal should include an all-inclusive maximum price to include all direct and indirect costs including all out-of-pocket expenses. The proposal should further include a schedule of professional fees and expenses that supports the total all-inclusive maximum price.

#### Selection Criteria

- Responsiveness of the proposal related to the scope of work 0 - 15
- Ability, capacity, and skill of the proposer to perform the services on a timely basis 0 - 30
- Responses of the clients' governmental references 0 - 10
- Experience of the business and individual members of the business in accomplishing similar services 0 – 5
- Total price 0 - 30
- The quality, availability, and adaptability of the services to the particular need requested 0 - 10

## I. SCOPE OF WORK

Escambia County Board of County Commissioners is seeking proposals from qualified consultants to perform the following proposed Scope of Work:

- a. The consultant will provide a timeline that addresses the BCC goal of having results available prior to the selection of a County Administrator later in 2019. The consultant shall develop a high-level project plan that lists all anticipated survey tasks with target dates and roles/responsibilities for each step in the survey process.
- b. Through collaboration with the BCC, the selected consultant will develop the 2019 Employee Engagement Survey. The selected consultant will develop the survey through a combination of:
  - i. Input from the County Commissioners;
  - ii. Standard questions delivered to other public sector clients;
  - iii. Previous surveys;
  - iv. Demographic questions;
  - v. Input from BCC Human Resources and Administration.
- c. Deploy the 2019 Employee Engagement Survey:
  - i. Through consultation with BCC Human Resources and Administration, the selected consultant will create platform(s) to deploy the employee engagement survey.
    1. Electronic and paper surveys will be deployed. The survey will have the capabilities to be accessible by smartphone.
    2. Procedures will be in place that guarantee participation only by bonafide employees.
  - ii. The selected consultant will deliver have the following capabilities:
    1. Compile and analyze survey results, including benchmarking against comparable public sector organizations especially with the State of Florida. This data will be a baseline for future employee engagement surveys.
    2. Consultant shall provide technical help desk support to employees wishing to complete the survey electronically.
    3. Prepare an overall research and departmental reports.
    4. Prepare supervisor toolkits. This is to include recommendations of activities to increase engagement and promote an environment of inclusion.
    5. Present findings at a Committee of the Whole Meeting.
    6. Regarding the Employee Engagement Survey, the BCC requires an 80%+ response rate.
  - iii. The following strategies will be used to develop employee trust in the survey process and improve response rate:
    1. Support BCC leadership and management in the implementation of an aggressive campaign to promote the survey and convey that candid feedback is essential to creating a great workplace.
    2. Conduct kickoff meeting(s) that allow participation by all employees throughout the organization. These meeting(s) would allow for employees' and managers' questions and concerns to be addressed. Conduct union leader meetings as required.

3. Brand the survey as a BCC survey.
4. Promise anonymity to employees in communications to the employee and ensure individual responses other than narrative responses will never be shared with the BCC. Narrative responses will be redacted as necessary to ensure no responses can be used to personally identify individual employees.
5. Collaborate with BCC leadership to present the survey (identify the executive as the “from” in communications such as e-mail, reminders, and introduction). The consultant is primarily responsible for developing these communications and they should include announcements, reminders, and post-survey follow-up.
6. Where feasible, offer employees the opportunity to complete the survey during business hours.
7. Send a minimum of four reminder notifications to non-respondents.

## II. DELIVERABLES

The selected consultant will prepare and provide to the Board the following deliverables:

- a. Overall Research Report in Microsoft PowerPoint format. This report should present the overall key findings and recommendations in one comprehensive report. It should also include a narrative of the story behind the data (i.e., what are the employees trying to tell leadership and what specifically does the BCC as a whole and individual departments need to do to improve employee engagement?).
- b. The content and format for the report should be as follows:
  - i. Tables, bar charts, and graphs to display frequencies for responses to all questions.
  - ii. Charts showing the percentages of all response categories for all questions, for all departments in the organization.
  - iii. Comparison of how the score for each question compares to the internal top 25% and the external top 25% for benchmarking purposes.
- c. Identify top 3 strengths and weaknesses for departments on which they can take action;
- d. Benchmark data for best-in-class employers as well as for public sector employers.
- e. Provide an analysis of the verbatim responses from the surveys. This analysis should be presented in a qualitative way, highlighting any trends or key concepts, and not just as an attachment of all verbatim responses.
- f. A key driver analysis that:
  - i. Identifies key drivers of employee overall ratings of satisfaction with the BCC as a place to work for all employees (and provides the incremental gain in overall rating associated with a 5% improvement at the individual level).
  - ii. Identifies key drivers of employee engagement based on engagement questions.
  - iii. Identifies the Department-specific exceptions to those all-employee key drivers.
- g. After the Board Presentation is conducted, the consultant shall conduct an executive round table briefing for County Administration and department directors at the BCC. This briefing will be used to:
  - i. Acquaint the BCC leadership team with the key findings;
  - ii. Identify the key drivers of employee satisfaction and engagement;
  - iii. Identify the management implications of the results; and

- iv. Identify any additional analyses that should be conducted.
- h. Supervisor Toolkit. In consultation with the BCC, the selected consultant will assist in the development of a supervisor toolkit that provides resources and suggestions for supervisors to implement solutions to increase engagement.
- i. Copy of raw data. Selected consultant will provide to the BCC a copy of the raw data file in Microsoft Excel format. The data file will be configured to ensure compliance with the promise of anonymity made to all survey participants.

DRAFT

**Committee of the Whole**

**10.**

**Meeting Date:** 01/17/2019

**Issue:** Public Forums/Agenda Reviews

**From:** Amy Lovoy, Assistant County Administrator

---

**Information**

**Recommendation:**

Public Forums/Agenda Reviews

(Amy Lovoy - 10 min)

A. Board Discussion

B. Board Direction

---

**Attachments**

*No file(s) attached.*

---
