



## AGENDA

### COMMITTEE OF THE WHOLE WORKSHOP BOARD OF COUNTY COMMISSIONERS

Board Chambers  
Suite 100  
Ernie Lee Magaha Government Building - First Floor  
221 Palafox Place

February 14, 2019  
9:00 a.m.

Escambia County is committed to making our website accessible. If you use assistive technology, for example a screen reader, and have difficulty accessing information in this agenda online, please contact our ADA Coordinator at [ADA@myescambia.com](mailto:ADA@myescambia.com) or 850-595-1637.

**Notice: This meeting is televised live on ECTV and recorded for rebroadcast on the same channel. Refer to your cable provider's channel lineup to find ECTV.**

1. Call to Order  
  
(PLEASE TURN YOUR CELL PHONE TO THE SILENCE OR OFF SETTING.)
2. Was the meeting properly advertised?
3. OLF8/OLFX  
(Amy Lovoy - 30 min)
  - A. Board Discussion
  - B. Board Direction
4. Midtown Commerce Park/Memorandum of Understanding (MOU)  
(Jason Nail, Parkside Partners/Dave Robau, National Energy - 30 min)
  - A. Board Discussion
  - B. Board Direction
5. New Escambia County Correctional Facility Progress Report  
(Steve Jernigan, Bay Design/Bob Dye, Facilities Management - 15 min)
  - A. Board Discussion
  - B. Board Direction

6. Gulf Coast Minority Chamber of Commerce  
(Brian Wyer, President/CEO, Gulf Coast Minority Chamber of Commerce - 20 min)
  - A. Board Discussion
  - B. Board Direction
  
7. Escambia County Healthy Start Coalition, Inc.  
(Teresa Neal - 20 min)
  - A. Board Discussion
  - B. Board Direction
  
8. Rolling Hills Update  
(Chips Kirschenfeld - 15 min)
  - A. Board Discussion
  - B. Board Direction
  
9. Interim Medical Examiner  
(Alison Rogers - 15 min)
  - A. Board Discussion
  - B. Board Direction
  
10. Adjourn

**Committee of the Whole**

**3.**

**Meeting Date:** 02/14/2019

**Issue:** OLF8/OLFX

**From:** Amy Lovoy, Assistant County Administrator

---

**Information**

**Recommendation:**

OLF8/OLFX

(Amy Lovoy - 30 min)

A. Board Discussion

B. Board Direction

---

**Attachments**

Presentation

OLF8 Master Plan Scope of Work

---



# DEVELOPMENT SERVICES DEPARTMENT

NAVY OUTLYING FIELD (OLF) & OVERVIEW



# General Overview of Commercial Zoning Per Land Development Code (LDC), Sec. 3-2.10

## Commercial district (COM)

- Allows for wide range of diverse/intense commercial/retail type uses, services and activities.
- All commercial activities limited to confines of buildings unless specified in zoning category and not allowed to produce undesirable effects on surrounding property.
- Residential uses are allowed; **but if within Commercial (C) future land use (FLU) category**, they are only permitted (allowed) if part of a predominately commercial development.
- **Predominately Commercial Development** is defined as development for which more than two-thirds of the development parcel area and more than two-thirds of all gross floor area within the parcel is devoted to commercial use. (*Chapter 6 Definitions LDC*)



## Option A: Zoning of Commercial with FLU of C

### Zoning Designation of Commercial

- Allows for a wide variety of commercial/retail type uses, services and activities - Very flexible Zoning Category

### FLU Category of **C** (Commercial), if chosen:

- Allows for retail uses and services; professional offices, light industrial, recreational facilities, public and civic; **HOWEVER, RESIDENTIAL USES MAY BE ONLY BE PERMITTED IF SECONDARY TO PRIMARY COMMERCIAL DEVELOPMENT - A LIMITING STANDARD**
- Because of the Commercial FLU category, the LDC Zoning will require a proposed project with a zoning of Commercial and FLU of C, for a specific parcel, to meet the predominately commercial development definition as defined accordingly in the LDC.



## Option B: Zoning of Commercial with FLU of Mixed Use Urban (MU-U)

### Zoning designation of Commercial

- Allows for wide variety of commercial/retail types uses, services and activities - Very flexible in Zoning Category.

### FLU Category of MU-U (Commercial), if chosen:

- Allows for residential, retail uses and services, professional offices, light industrial, recreational facilities, public and civic, and limited agriculture
- **NO REQUIREMENT** that a project be a predominately commercial development
- **Very Flexible in the range of allowable residential uses** from single-family (including subdivisions and townhomes developments) to multifamily (apartments and condominiums) as allowed per the FLU category of Mixed Use Urban (MU-U)

# Summary

## Option A: Zoning C FLU C

- Consistency requirement would be met.
- Allows a wide range of Com. Uses.
- Limits Residential Development of any type.
- Automatic limitation that would definitely impact mixed use development.
- Limitation could require a substantial process to change.

## Option B: Zoning C FLU MU-U

- Consistency requirement would be met
- Allows for residential and intense commercial uses
- Allows for all types of residential development
- No limitation on residential development except those of the site plan review process
- Provides flexibility for the planner/developer to propose alternative mix of residential **and** non-residential development designs.





## Action Needed

Staff direction to proceed with:

- Option A or
- Option B or
- No action at this time



## Request for Proposals

### OLF8 Master Plan

#### 1. PURPOSE

Escambia County is seeking a qualified firm to create a master plan for a 640-acre parcel called Outlying Landing Field 8 (OLF8) in the Pensacola suburb of Beulah. Expertise in Florida land use planning, Geographic Information Systems, economic analysis, planning for commercial as well as housing development and public participation is required. The master planner will determine and balance the highest and best economic use for the property with uses that enhance the quality of life for those who live or work in Beulah, while maximizing the creation of jobs with wages higher than the Escambia County median income. All uses compatible with the surrounding community are to be considered including the potential for public uses (School, Post Office, Fire Station).

The master plan should: establish a vision for OLF 8; provide ample opportunities for stakeholder engagement; analyze the commercial and residential markets and identify needs and opportunities; complete a site-specific development opportunity analysis; recommend and prioritize strategies and projects for place-making and public spaces; provide initial wayfinding signage recommendations; recommend strategies for addressing parking needs; and provide a plan for implementing recommendations.

#### 2. GENERAL INFORMATION

**Location** - OLF8 is an approximately 640-acre parcel in the Beulah community of Escambia County, Fla., 15 miles northwest of downtown Pensacola. Approximately 425 acres are cleared uplands and the rest is wetlands, forest and lowlands. OLF8 fronts Nine Mile Road (Alt-Highway 90) to the South and Frank Reeder Road to the North. The parcel is adjacent to the Beulah campus of Navy Federal Credit Union (NFCU), which is anticipated to employ over 10,000 people by 2022.

**Parcel ownership** - The U.S. Department of the Navy currently owns OLF8 and uses it as a Navy helicopter training field. Escambia County and the U.S. Department of the Navy have executed a Land Exchange Agreement (LEA) to transfer title to the property to Escambia County. Title transfer is expected to occur by January 2019.

**Negotiations with Navy Federal Credit Union** - Escambia County has entered negotiations with NFCU to sell the eastern-most 100 acres of the OLF8 property to them at market price subject to NFCU's commitment to a mutually agreed upon number of jobs to be added to their existing campus. Navy Federal Credit Union has presented a concept design that includes preservation of the wetlands, parking to support their existing operations and recreation facilities (pavilions, multi-purpose fields, walking trails and stormwater ponds). Navy Federal has agreed that upon reasonable conditions, the recreation facilities will be available for use by the public.

**Mid-West Sector Plan** – North of Interstate 10, west of Highway 29 and south of Highway 196, there is a 15,000-acre Sector Plan with a large swath of land set aside for commerce just north of OLF8 in Cantonment. The "Regional Employment" area on the sector plan map is between I-10 and Muscogee

Road. Additional information on the Sector Plan can be found at <https://myescambia.com/our-services/development-services/planning-zoning/optional-sector-plan>.

**Changing Conditions in Beulah** - Escambia County pursued the acquisition of OLF8 in 2013 with the intent to enhance economic development opportunities for the region. Since that process was initiated, conditions near OLF8 have changed. Navy Federal Credit Union's growth along with 7,000 residences being built, approved or under development since 2010 has degraded the capacity of Nine Mile Road. FDOT is currently improving 9-Mile Road to make this a four-lane roadway, and this project is expected to be completed in 2019. Brantley & Associates completed a property appraisal of OLF8 in 2016 that estimated the population within five miles of OLF8 will grow to 32,993 by 2020, with a median household income of \$63,471. The median home value within a five-mile radius of OLF8 was projected to be \$209,814 by 2021.

**Beulah Community Assets and Goals** - Beulah has natural assets like the Perdido River, an Outstanding Florida Waterway, with a new park and boat ramp, and the Perdido River Wildlife Management Area with hiking trails, a small park and canoe launch. From Nine Mile Road across OLF8, there are views of sunsets over the open field, undulating sweeps of trees on the eastern and western edges and wetlands along the road. There are horses, donkeys, goats, chickens and remnants of agriculture like pecan orchards and home gardens. On Nine Mile Road, a new middle school opened this fall. Other assets include a Dollar General, two gas stations, a veterinarian, a small used car lot, a garden center and a recreational vehicle park. On Mobile Highway, there is a small community park with a playground and a dog park, a large equestrian center with a covered show ring and stables, and a small, older senior center is nearby.

Community goals and topics under discussion include alleviating traffic, greater street connectivity, a second elementary school, a local high school or smaller magnet high school, replacing the dilapidated fire station with no shower, a police substation, a library, a post office, a community center, a multipurpose government building that combines many uses, an outdoor concert venue, walking trails and sidewalks and a medical clinic.

**Transportation** – As previously mentioned, Nine Mile Road is widening from two lanes to four lanes and efforts are underway to eventually add a new Beulah interchange on Interstate 10. Widening Beulah Road is also planned, as well as a likely traffic light at the intersection of Frank Reeder Road and Beulah Road in the future. The Florida Department of Transportation is also studying ways to improve traffic flow along Nine Mile Road from Foxtail Loop to I-10 Exit 5 section of roadway in front of Navy Federal Credit Union, Nature Trail residential neighborhood and multiple commercial developments that are under permitting and construction. Throughout the area, subdivisions with hundreds of homes have been approved or built that are exacerbating traffic congestion - with one or two exits dumping cars onto Frank Reeder Road, Beulah Road, Nine Mile Road and Mobile Highway. Within walking distance of NFCU's campus on Nine Mile Road, there are currently more than 2,000 apartments, condominiums, and single-family residences approved or currently under construction.

### 3. GRANT REQUIREMENTS

The 2010 Deepwater Horizon oil spill led to passage of the RESTORE Act in 2012. The Act dedicates 80 percent of all Clean Water Act penalties related to the spill to the Gulf Coast Restoration Trust Fund. The Escambia County Board of County Commissioners selected the OLF8 Master Plan as one of ten initial projects to fund with Escambia County's RESTORE Direct Component (Pot 1) allocation.

The OLF8 Master Plan shall be consistent with Escambia County's RESTORE Direct Component Multi-Year Implementation Plan (MYIP) and Treasury Grant Application (awaiting approval). The plan shall not prejudice the RESTORE Act and all applicable rules and laws. For more information on Escambia County's Direct Component projects please visit <https://myescambia.com/our-services/natural-resources-management/restore/multi-year-implementation-plan>.

Valuable public comments were provided as part of the application process and the net result was that the MYIP states on page 74 that although the initial concept for developing OLF 8 was a traditional commerce park, all options are available.

Regarding the Triumph Gulf Coast grant, the planner shall fully consider the BCC's pre-application to Triumph Gulf Coast whereby the county may win a significant monetary award approaching \$30 Million dollars if the goal of creating a minimum of 1,000 good-paying jobs is achieved utilizing this property. (Escambia's pre-application can be accessed here <https://www.myfloridatriumph.com/proposal-details/404/>)

#### **4. SCOPE OF SERVICES**

The Master Plan will balance the highest and best economic use of the OLF8 property with the needs of the County, region, and the Beulah community in creating a plan for a sustainable and resilient development with a plan for implementation. The master plan will be based on an Existing Conditions Analysis, Technical Analysis, and on Stakeholder Engagement and Community Participation. The Existing Conditions Analysis will analyze historic and current site attributes, the character of the community and the site's connectivity and compatibility with the surrounding community. The Technical Analysis will weigh the listed considerations in determining the arrangement, use, and form of the site. Specifically, the Economic Impact Analysis will analyze supportable industries based on market demand and economic sustainability, and the Natural Assets Analysis will look at existing natural amenities that can be preserved and integrated into the design. Stakeholder Engagement and Community Participation will be key to the Master Plan; Interactive public stakeholder meetings will be held throughout the master planning process.

All data and mapping for the site and surrounding area shall be delivered in a Geographic Information System (GIS) compatible format such as a shapefile or a file geodatabase format in an ARCMAP 10.1 or higher version. Escambia County will provide base data to firms interested in submitting a proposal. It is expected that the submittals for this project provide maps and data in said format, which will demonstrate that the interested firm or firms has the GIS capabilities to deliver the desired data.

#### **Master Plan Tasks**

The Master Plan will include at least the following tasks:

- 1. Existing Conditions Analysis**
  - a. Project Site & Context
  - b. History, Culture and Character of the Beulah community
  - c. Regional Context/Impacts (Development of Regional Impact)
  - d. Site Conditions and proposed offsite projects in the subject area
  - e. Constraints & Opportunities
  
- 2. Technical Analysis**
  - a. Environmental Analysis

- b. Land Use – preserving natural assets like wetlands and forests, recreational open space, walking/hiking trails, landscaping with trees and native vegetation
- c. Economic Impact Analysis – quantitative and qualitative information including economic trends, need for economic incentives, employment forecasting and uses; property and retail tax analysis using 3-D fiscal analysis; compatibility with the Mid-West Sector Plan
- d. Beulah Community Needs – for public facilities, retail, housing, professional services and others as identified; housing densities, zones and codes
- e. Infrastructure Analysis
- f. Transportation Analysis – Review of all existing roads and streets along with their level of service; review current transportation plans and maps; review capital improvements that are associated with the project area; review all existing transportation studies and models and analyze parking needs; circulation within OLF8 and pedestrian accessibility; compatibility with the Mid-West Sector Plan
- g. Architectural Standards and Design Considerations Plan

### **3. Stakeholder Engagement and Community Participation**

The firm must develop a Stakeholder Engagement and Community Participation Plan that actively and fully engages the citizens and stakeholders in the preparation of the master plan. They are also to be included as the Land Development Code regulations and architectural standards in support of the master plan are created and implemented. It is expected that the firm will utilize a charrette process and/or any other similar smart planning citizen engagement process. It is essential that all residents, stakeholders, government, and non-governmental entities, including the Northwest District One Advisory Committee, have adequate opportunity to comment on the Plan and that those comments be well documented. It is equally important that due consideration be given to those comments.

### **4. Master Plan and Implementation Plan**

The firm should utilize information obtained from Tasks 1 through 3 for the preparation of the Master Plan. The Master Plan should determine the highest and best economic use of the OLF8 property as well as the best uses that are in the public interest of stakeholders like regional, County, and nearby Beulah residents and those who work there, while maximizing economic impact through job creation.

The firm should strive to balance the desires of the stakeholders with the results of the Economic Impact Analysis. The firm should prepare an actionable Implementation Plan, including supplemental architectural and developmental standards for the Master Plan area.

**Deliverables** - Key deliverables include, but are not limited to (electronic and hard copies):

- Project Schedule
- Existing Conditions Analysis Report
- Technical Analysis Report
- Economic Impact Report
- GIS Data and analysis results which will allow county staff to continue future analyses and maintenance for tracking and maintaining the OLF8 facility as it evolves
- Stakeholder Engagement & Community Participation Plan
- Draft Master Plan & Implementation Plan, including supplemental architectural and developmental standards for the Master Plan area. These recommended standards shall be in a format consistent for inclusion in the Land Development Code.

- Final Master Plan & Implementation Plan, including supplemental architectural and developmental standards for the Master Plan area. These recommended standards shall be in a format consistent for inclusion in the Land Development Code.

## 5. PROJECT APPROACH

Firm should demonstrate with RFP submittal a conceptual approach for developing the OLF8 Master Plan. The conceptual approach should consider the following factors:

1. Strategy for addressing Plan Objectives.
2. Approach to conducting the Existing Conditions Analysis and Technical Analysis.
3. Approach to conducting the Economic Impact Analysis.
4. Demonstration of innovative methods for soliciting, assessing, and using community input, comments, and suggestions during project development and for working with diverse stakeholders to achieve Plan Objectives.
5. Demonstration of successfully implementing other similar master plans.
6. Strategy for implementing the OLF8 Master Plan.

### **Funding Availability:**

Funding is available in Fund 118, Gulf Coast Restoration Fund, Cost Center **XXXXXX**.

### **Project Timeline:**

Project should be substantially completed by January 2020.

### **Anticipated Disciplines (Function Codes SF 330):**

	<b><u>GSA Code</u></b>	<b><u>Description</u></b>
<b><u>Primary Disciplines</u></b>	12	Civil Engineer
	20	Economist
	47	Planner: Urban/Regional
<b><u>Secondary Disciplines</u></b>	06	Architect
	18	Cost Engineer/Estimator
	23	Environmental Engineer
	29	Geographic Information System Specialist
	38	Land Surveyor
	39	Landscape Architect
	48	Project Manager
	60	Transportation Engineer
	<b><u>GSA Code</u></b>	<b><u>Description</u></b>
<b><u>Primary Experience</u></b>	P05	Planning (Community, Regional, Areawide, and State)
	P06	Planning (Site, Installation, and Project)
<b><u>Secondary Experience</u></b>	C08	Codes; Standards; Ordinances
	C10	Commercial Building; Shopping Centers
	C18	Cost Estimating; Cost Engineering and Analysis
	E09	Environmental Impact Studies, Assessments

E11	Environmental Planning
G04	Geographic Information System Services
H07	Highways; Streets
L02	Land Surveying
L03	Landscape Architecture
O01	Office Buildings; Industrial Parks
P100	Deliverables for Government Facilities <a href="https://www.gsa.gov/cdnstatic/GSA_GIS_Standards.pdf">https://www.gsa.gov/cdnstatic/GSA_GIS_Standards.pdf</a>
R04	Recreational Facilities
S11	Sustainable Design
S13	Stormwater Handling & Facilities
Z01	Zoning; Land Use Studies

**Evaluations and Selection:**

Escambia County shall follow the procedures outlined in the Consultants’ Competitive Negotiation Act, Title XIX, Chapter 287, Section 055 of the Florida Statutes. The Selection committee shall consider the following factors:

**County Staff - Shortlisting Committee Criteria**


	<b>Points</b>
1. <b><u>Project Approach:</u></b> Firm should demonstrate a clear understanding of the project goals and objectives. Firm should address with their submission a thorough response to the items requested in Section 5, Project Approach.	<b>10</b>
2. <b><u>Regional and Site Context:</u></b> Firm should demonstrate a clear understanding of the regional and site context and significance of the project on the surrounding community.	<b>10</b>
3. <b><u>Past Record and Performance of the Team:</u></b> Firm should document past record and performance of the project team. Firm should document successfully implemented similar scale master plans including economic analysis. Consultant evaluation records should be positive. Any previous negative consultant evaluations should result in significantly lower scores. A previous working relationship with Escambia County should not be considered a prerequisite for selection. A positive record of performance may also be demonstrated within the firm’s submittal.	<b>8</b>
4. <b><u>Experience and Technical Expertise of the Team:</u></b> Firm should document background experience of the project team. Team experience should specifically address master planning and economic analysis and any other experience the firm identifies as relevant to the project. Experience of the firm shall be considered with respect to the project specific GSA codes identified above. Firm should document technical expertise of the team. Firm should address the following 5 Subtasks found in Section 4.2:	<b>19</b>
<ul style="list-style-type: none"> <li>a) Environmental Analysis (3 points)</li> <li>b) Transportation Analysis (3 points)</li> <li>c) Infrastructure Analysis (3 points)</li> <li>d) Economic Impact Analysis (5 points)</li> <li>e) Master Plan Considerations (5 points)</li> </ul>	

5. **Ability to Meet Project Schedule and Be Readily Accessible:** Project schedule is determined by terms and conditions of the grant agreement. Firm should demonstrate their understanding and need for flexibility to meet the project and grant schedule. Project team members should be readily accessible to avoid unnecessary delays. Firm should demonstrate how their team will be readily accessible to the County. **3**

**Board of County Commissioners - Selection Committee Criteria**

1. Strategy for addressing Plan Objectives. **15**
2. Approach to conducting the Existing Conditions Analysis and Technical Analysis. **15**
3. Approach to conducting the Economic Impact Analysis. **20**
4. Demonstration of innovative methods for soliciting, assessing, and using community input, comments, and suggestions during project development and for working with diverse stakeholders to achieve Plan Objectives. **20**
5. Demonstration of successfully implementing other similar master plans. **15**
6. Strategy for implementing the OLF8 Master Plan. **15**

Award(s) resulting from this solicitation shall be subject to provisions of Chapter 1-9-5, CONSULTANTS of the Ordinances of Escambia County and Procedure PP-250 VENDOR PERFORMANCE EVALUATIONS of the Purchasing Policies and Procedures of Escambia County.

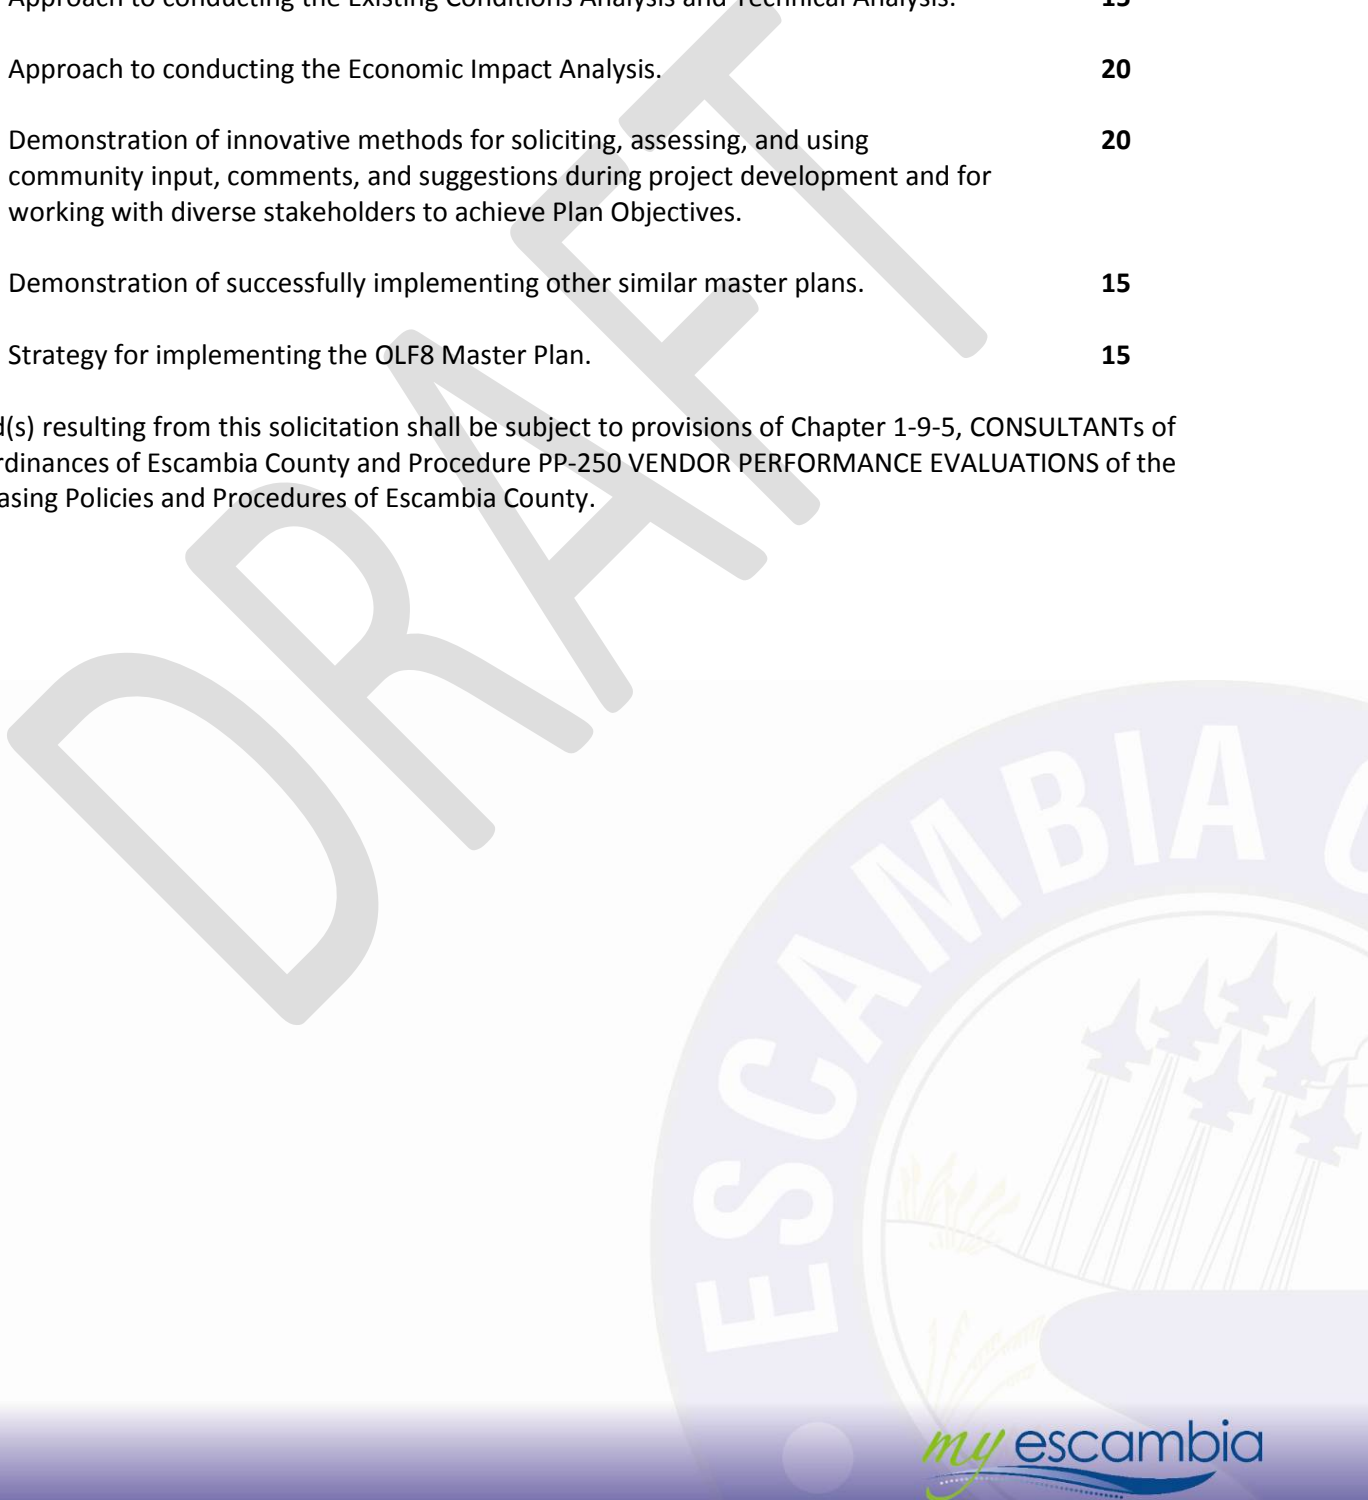



**Committee of the Whole**

**4.**

**Meeting Date:** 02/14/2019

**Issue:** Midtown Commerce Park Proposal Memorandum of Understanding (MOU)

**From:** Amy Lovoy, Assistant County Administrator

---

**Information**

**Recommendation:**

Midtown Commerce Park/Memorandum of Understanding (MOU)  
(Jason Nail, Parkside Partners/Dave Robau, National Energy - 30 min)

- A. Board Discussion
  - B. Board Direction
- 

**Attachments**

*No file(s) attached.*

---

**Committee of the Whole**

**5.**

**Meeting Date:** 02/14/2019

**Issue:** Progress Report on New Correctional Facility

**From:** Robert Dye, Division Manager

---

**Information**

**Recommendation:**

New Escambia County Correctional Facility Progress Report  
(Steve Jernigan, Bay Design/Bob Dye, Facilities Management - 15 min)

- A. Board Discussion
  - B. Board Direction
- 

**Attachments**

presentation

DBE progress report

---

# New Escambia County Correctional Facility

Progress update

Steve Jernigan – Bay Design

Bob Dye – Facilities Management

Colby Brown – Assistant County Engineer

## Key Points

- Construction Progress
  - Foundation and Backfilling
    - Poured the slab on deck for Area D.
    - Formed, reinforced and poured concrete for grade beams and pile caps at the Connector.
  - JJC Parking lot inspected and accepted.
    - Turned over for use on 08 January.
  - Excavation of storm water pond begun.
    - Installing storm water piping and inlets between structures S-15 and S-23.
  - Critical path update
    - Currently showing -28 days due to inclement weather.
    - Correcting to meet scheduled May of 2020 substantial completion date.

# Access Plan Update

- Mr. Colby Brown
  - Revised access plan approved by FDOT.
    - Allows 7 access points.
    - Shared Access Joint Use Acknowledgment/Agreement to be presented to Board for approval Feb 21st.

## Ongoing activity

### Continuing:

- Precast wall panels
- Structural Steel
- Stairways
- Storm water pond
  
- Continue to reduce delta on timeline

Next progress update – March Committee of the Whole



**New Escambia County Correctional Facility**

**PD 16-17.004**

**Monthly Project Report  
January 2019**

## Table of Contents

<b>1.0 Progress Summary</b> .....	3
<b>2.0 Construction Progress</b> .....	4
<b>3.0 Design Build Entity Schedule</b> .....	4
<b>4.0 Design Status</b> .....	5
<b>5.0 Subcontractor Procurement</b> .....	5
<b>6.0 Design-Build Entity’s Safety Program</b> .....	5
<b>7.0 Disputes and Claims</b> .....	6
<b>8.0 Look Ahead Task List</b> .....	6
<b>9.0 Daily Log</b> .....	6



## 1.0 Progress Summary

ITEM	Description	COMMENTS
Original Contract Sum	\$132,445,243.00	
Change Order 1:	(-\$455,530.50)	ODP Change Order deduct for auger cast pile grout.
Change Order 2:	(\$-360.00)	Mathematical error with Alternate Number 5.
Change Order 3:	(-\$147,455.28)	ODP Change Order deduct for auger cast pile rebar.
Change Order 4:	(-\$28,769.30)	ODP Change Order deduct for additional auger cast pile rebar.
Change Order 5:	(-\$2,092,095.52)	ODP Change Order deduct for CIP Concrete and Rebar, Laundry Equipment, and Bi-Folding Doors.
Change Order 6:	(-\$463,697.91)	ODP Change Order deduct for Site Utility Piping and Structures.
Change Order 7:	(-\$32,731.48)	ODP Change Order deduct for Underground Electrical Raceways.
Change Order 8:	(-\$48,746.02)	ODP Change Order deduct for additional auger cast pile grout.
Change Order 9:	(-\$169,758.74)	ODP Change Order deduct for asphalt paving and corrections to existing POs.
Change Order 10:	(-\$9,005,200.12)	ODP Change Order deduct for structural steel, cell walls, hollow metal doors, door hardware and plumbing materials.
Change Order 11:	(-\$47,141.00)	ODP Change Order deduct for additional plumbing materials.
Change Order 12:	(4,380,132.83)	ODP Change Order deduct for mechanical equipment, commercial HM and hardware, security glazing, and security electronics.
Adjusted Contract Sum	\$115,573,624.30	
Pending Change Order Request/Claims	NONE	
Original Date of Substantial Completion	May 28, 2020	
Forecast Date of Substantial Completion	May 28, 2020	

## 2.0 Construction Progress

Bayside Structures reinforced and poured the slab on deck for Area D, elevation 100, sequence 1 and sequence 2. They also formed, reinforced and poured concrete for the grade beams and pile caps at the connector. Bayside prepped and placed Stair A slab-on-grade, and they continued to grout baseplates in Area D.

EAA Sitework installed parking signage and wheel stops, finish graded, and removed the silt fence at the new JJC parking lot. They also installed silt fence and began demolition of trees, wheel stops, signage and asphalt at the old JJC Parking Lot. They have begun excavation of the storm pond in this area.

The JJC Parking Lot was inspected and received final acceptance to be turned over on January 8, 2019.

A&B Electric repaired a light at the new JJC Parking Lot prior to the final inspection. They also disconnected and removed the existing light poles at the old JJC Parking Lot that is being demoed for the retention pond. A&B worked on embeds in the precast walls and rough-in of under-slab conduits of the corridor. They are continuing the rough-in of underground conduits in Area C.

Emmons Steel Erectors completed erecting structural steel, erecting metal decking, and shooting studs in Area D for sequence 2, elevation 81-100. They are currently erecting structural steel at Area D, elevation 115.

Tindall erected precast in Area C of the building and they continued grouting, patching and welding panels. They moved the crane into Area D on January 15, 2018 to erect precast panels at elevation 100, sequence 1 in Area D. Tindall then moved to Area A to erect precast, including grouting, patching and welding panels. They currently have moved to Area D and are erecting precast panels at elevation 100, sequence 2.

Chavers Construction is installing storm piping and inlets between structures S-15 and S-23.

Nash installed blockouts, sleeves, drains and inserts for mechanical penetrations in Area D, elevation 100 slab on deck. They also installed underground sanitary sewer piping in Area A and under-slab piping at the corridor.

Allstop Waterproofing installed dampproofing at the double and single elevator pits in Area B.

## 3.0 Design Build Entity Schedule

See attached Progress Schedule.

## 4.0 Design Status

### Summary:

The document submittal set for permitting is scheduled as follows:

- Permitting Submittal for Plumbing, HVAC, Electrical, Food Service, Security Electronics & Fire Alarm were issued on November 7, 2018.
- WGI/Caddell received approved permitting documents for Underground, Architectural, Structural, FFE and Precast drawings on December 6, 2018.
- WGI/Caddell received approved Fire Suppression, Telecommunications and Plumbing permitting documents on January 10, 2019.
- WGI/Caddell received the Electrical, Security Electronics, Fire Alarm and Food Service Permitting documents on Friday February 01, 2019.

### Contract Deliverables:

- Supplemental Instruction 007-Issued January 11, 2019
- Supplemental Instruction 008-Issued January 28, 2019

### Areas of Concern:

- WGI/Caddell is currently waiting on review of HVAC permit documents that were issued November 7, 2018.

### Actions and Approvals Needed:

- A partial FDOT permit has been issued for curb access closures, and WGI/Caddell has drafted a letter acknowledging future lighting work along Fairfield Blvd. GRW has provided FDOT with revised permit documents that are currently under review.

### Recommendations:

- NONE

## 5.0 Subcontractor Procurement

- Acousti Engineering Company of Florida-Acoustical Ceilings
- DPF Construction, LLC-Cold-Formed Metal Framing and Drywall
- Warehouse Equipment & Supply Company, Inc.-Overhead Coiling Doors
- Builders FirstSource Southeast Group LLC-Cold-Formed Metal Trusses and Steel Decking

## 6.0 Design-Build Entity's Safety Program

No incidents were recorded for the month of January 2019.

## **7.0 Disputes and Claims**

No disputes or claims were filed in the month of January 2019.

## **8.0 Look Ahead Task List**

See attached 90-day Look Ahead Schedule.

## **9.0 Daily Log**

See attached Daily Logs for the month of January 2019.

Activity ID	Activity Name	Orig Dur	Rem Dur	Prev Pct%	New Pct %	Actual Start	Actual Finish	Total Float	Early Start	Early Finish	Budgeted Cost	This Period Cost	Cost to Complete
ECCF15 30Jan19 Detailed Baseline Schedule Update - Prelim2		541	148			02-Jan-18		398	02-Jan-18 A	26-Jun-19	\$5,310,101.64	\$1,435,561.94	(\$2,384,229.77)
<b>Progress this Period</b>		541	148			02-Jan-18		398	02-Jan-18 A	26-Jun-19	\$5,310,101.64	\$1,435,561.94	(\$2,384,229.77)
<b>PRECONSTRUCTION</b>		475	84			02-Jan-18		462	02-Jan-18 A	23-Apr-19	\$11,151,249.00	\$1,246,836.18	\$3,954,456.88
<b>MILESTONES</b>		0	0			02-Jan-19	02-Jan-19		02-Jan-19 A	02-Jan-19 A	\$0.00	\$0.00	\$0.00
800015	QUARTERLY TOWN HALL PROGRESS MEETING (COC) 1ST WED OF QTR	0	0	0%	100%		02-Jan-19			02-Jan-19 A	\$0.00	\$0.00	\$0.00
800016	PFRR BOARD MEETING - BCC RECOMMENDATION DEVELOPMENT WORKSHOP	0	0	0%	100%		02-Jan-19			02-Jan-19 A	\$0.00	\$0.00	\$0.00
<b>DESIGN</b>		30	1			25-Jul-18		103	25-Jul-18 A	30-Jan-19	\$50,000.00	\$11,000.00	\$2,500.00
001171	SITE/CIVIL DESIGN - FENCING/MISC. SITE ITEMS	30	1	73%	95%	25-Jul-18		103	25-Jul-18 A	30-Jan-19	\$50,000.00	\$11,000.00	\$2,500.00
<b>PERMITS</b>		1	0			13-Feb-18	09-Jan-19		13-Feb-18 A	09-Jan-19 A	\$10,000.00	\$1,000.00	\$0.00
009009	PERMITS - SITE/CIVIL - FOR ACCOUNTING ONLY	1	0	90%	100%	13-Feb-18	09-Jan-19		13-Feb-18 A	09-Jan-19 A	\$10,000.00	\$1,000.00	\$0.00
<b>PRECONSTRUCTION SUBMITTALS</b>		447	59			30-Jan-18		45	30-Jan-18 A	29-Mar-19	\$0.00	\$0.00	\$0.00
000600	PREPARE & SUBMIT LOD 300/400 FEDERATED MODEL	143	59	0%	0%	07-Nov-18		45	07-Nov-18 A	29-Mar-19	\$0.00	\$0.00	\$0.00
000620	SUBMIT FINAL BASELINE DESIGN/CONSTRUCTION SCHEDULE	90	17	0%	0%	30-Jan-18		66	30-Jan-18 A	15-Feb-19	\$0.00	\$0.00	\$0.00
<b>PROCUREMENT</b>		450	84			02-Jan-18		70	02-Jan-18 A	23-Apr-19	\$11,091,249.00	\$1,234,836.18	\$3,951,956.88
010000	PROCUREMENT OF LONG-LEAD ITEMS	450	84	0%	30%	02-Jan-18		70	02-Jan-18 A	23-Apr-19	\$0.00	\$0.00	\$0.00
010031	PRECAST PROCUREMENT - MATERIAL COST	1	1	71%	83%	26-Sep-18		138	26-Sep-18 A	30-Jan-19	\$6,285,564.00	\$754,267.68	\$1,068,545.88
010061	STEEL PROCUREMENT (STR & MISC) - MATERIAL COST	1	1	30%	40%	07-Nov-18		82	07-Nov-18 A	30-Jan-19	\$4,805,685.00	\$480,568.50	\$2,883,411.00
<b>CONSTRUCTION</b>		442	148			16-Jul-18		337	16-Jul-18 A	26-Jun-19	\$3,333,811.50	\$922,722.46	\$1,827,026.74
<b>DESIGN</b>		25	19			05-Sep-18		466	05-Sep-18 A	17-Feb-19	\$1,626,811.50	\$65,072.46	\$1,236,376.74
003000	A/E CONSTRUCTION ADMINISTRATION SERVICES (25 MONTHS)	25	19	20%	24%	05-Sep-18		466	05-Sep-18 A	17-Feb-19	\$1,626,811.50	\$65,072.46	\$1,236,376.74
<b>SITework</b>		180	18			16-Jul-18		192	16-Jul-18 A	25-Feb-19	\$302,000.00	\$58,800.00	\$226,400.00
100002	MAINTAIN EROSION CONTROLS (25 MONTHS)	25	18	24%	28%	16-Jul-18		192	16-Jul-18 A	25-Feb-19	\$70,000.00	\$2,800.00	\$50,400.00
100007	CONSTRUCTION FENCE - EXISTING SE JUVENILE PARKING LOT	3	0	0%	100%	09-Jan-19	10-Jan-19		09-Jan-19 A	10-Jan-19 A	\$2,000.00	\$2,000.00	\$0.00
100100	SITE GRADING - STORMWATER POND (EXIST SE JUV PLOT)	10	8	0%	20%	21-Jan-19		50	21-Jan-19 A	08-Feb-19	\$220,000.00	\$44,000.00	\$176,000.00
101100	SITE & UTILITY DEMOLITION - EXISTING SE JUVENILE PARKING LOT	10	0	0%	100%	10-Jan-19	24-Jan-19		10-Jan-19 A	24-Jan-19 A	\$10,000.00	\$10,000.00	\$0.00
<b>CORRECTIONAL FACILITY</b>		137	104			14-Dec-18		59	14-Dec-18 A	26-Jun-19	\$1,405,000.00	\$798,850.00	\$364,250.00
200400	UNDER SLAB PLUMBING A	10	8	0%	20%	07-Jan-19		59	07-Jan-19 A	26-Jun-19	\$50,000.00	\$10,000.00	\$40,000.00

Activity ID	Activity Name	Orig Dur	Rem Dur	Prev Pct%	New Pct %	Actual Start	Actual Finish	Total Float	Early Start	Early Finish	Budgeted Cost	This Period Cost	Cost to Complete
200460	UNDER SLAB ELECTRICAL C (1/2)	10	0	0%	100%	18-Jan-19	30-Jan-19		18-Jan-19 A	30-Jan-19 A	\$50,000.00	\$50,000.00	\$0.00
200880	SLAB ON DECK D ELEV 100 - 2ND LVL	6	0	33%	100%	26-Dec-18	21-Jan-19		26-Dec-18 A	21-Jan-19 A	\$250,000.00	\$167,500.00	\$0.00
201000	IN-SLAB PLUMBING D 2ND LVL CL 14-29	5	0	20%	100%	18-Dec-18	11-Jan-19		18-Dec-18 A	11-Jan-19 A	\$50,000.00	\$40,000.00	\$0.00
201010	IN-SLAB PLUMBING D 2ND LVL CL 29-50	5	0	0%	100%	10-Jan-19	18-Jan-19		10-Jan-19 A	18-Jan-19 A	\$50,000.00	\$50,000.00	\$0.00
201210	IN-SLAB ELECTRICAL D 2ND LVL CL 29-50	5	0	0%	100%	04-Jan-19	07-Jan-19		04-Jan-19 A	07-Jan-19 A	\$50,000.00	\$50,000.00	\$0.00
210000	PRECAST A (1/3)	15	10	0%	33%	21-Jan-19		-21	21-Jan-19 A	26-Feb-19	\$200,000.00	\$66,000.00	\$134,000.00
210110	STRUCTURAL STEEL D ELEV 100-102 (2/2)	8	0	62%	100%	19-Dec-18	03-Jan-19		19-Dec-18 A	03-Jan-19 A	\$70,000.00	\$26,600.00	\$0.00
210120	STRUCTURAL STEEL D ELEV 115	5	3	0%	40%	22-Jan-19		-28	22-Jan-19 A	27-Feb-19	\$50,000.00	\$20,000.00	\$30,000.00
210190	DETAIL STRUCTURAL STEEL D ELEV 100 (2/2)	11	0	0%	100%	03-Jan-19	18-Jan-19		03-Jan-19 A	18-Jan-19 A	\$10,000.00	\$10,000.00	\$0.00
211030	PRECAST C (2/3)	15	0	53%	100%	14-Dec-18	07-Jan-19		14-Dec-18 A	07-Jan-19 A	\$200,000.00	\$94,000.00	\$0.00
211040	PRECAST C (3/3)	15	9	0%	40%	08-Jan-19		-21	08-Jan-19 A	11-Feb-19	\$200,000.00	\$80,000.00	\$120,000.00
211060	PRECAST D ELEV 100	9	2	0%	77%	15-Jan-19		-28	15-Jan-19 A	22-Feb-19	\$175,000.00	\$134,750.00	\$40,250.00
<b>TESTING &amp; CLOSEOUT</b>		8	0			08-Jan-19	11-Jan-19		08-Jan-19 A	11-Jan-19 A	\$0.00	\$0.00	\$0.00
<b>SITWORK</b>		8	0			08-Jan-19	11-Jan-19		08-Jan-19 A	11-Jan-19 A	\$0.00	\$0.00	\$0.00
190040	PREPARE & COMPLETE GC/SUB SITE PUNCHLIST - NE JUVENILE PARKING LOT	3	0	0%	100%	08-Jan-19	11-Jan-19		08-Jan-19 A	11-Jan-19 A	\$0.00	\$0.00	\$0.00
190050	PREPARE OWNER SITE PUNCHLIST - NE JUVENILE PARKING LOT	1	0	0%	100%	08-Jan-19	08-Jan-19		08-Jan-19 A	08-Jan-19 A	\$0.00	\$0.00	\$0.00
190060	COMPLETE OWNER SITE PUNCHLIST - NE JUVENILE PARKING LOT	4	0	0%	100%	09-Jan-19	10-Jan-19		09-Jan-19 A	10-Jan-19 A	\$0.00	\$0.00	\$0.00
<b>MODIFICATIONS</b>		1	0			01-Dec-18		485	01-Dec-18 A	30-Jan-19	(\$9,174,958.86)	(\$733,996.70)	(\$8,165,713.39)
<b>MODIFICATIONS</b>		1	0			01-Dec-18		485	01-Dec-18 A	30-Jan-19	(\$9,174,958.86)	(\$733,996.70)	(\$8,165,713.39)
900006	CHANGE ORDER NO.6	1	0	3%	11%	01-Dec-18		485	01-Dec-18 A	30-Jan-19	(\$9,174,958.86)	(\$733,996.70)	(\$8,165,713.39)



Activity ID	Activity Name	Orig Dur	Rem Dur	Early Start	Early Finish	Total Float	2019																		
							Jan			Feb			Mar			Apr			May						
<b>CONSTRUCTION</b>																									
<b>ADMINISTRATION</b>																									
700031	EXTERIOR IMPROVEMENTS	418	214	06-Apr-18 A	04-Dec-19	41																			
700004	MASONRY	519	363	11-Jun-18 A	08-Jul-20	-28																			
700006	ROUGH CARPENTRY	519	363	11-Jun-18 A	08-Jul-20	-28																			
700007	FINISH CARPENTRY & CASEWORK	519	363	11-Jun-18 A	08-Jul-20	-28																			
700008	WATERPROOFING, JOINT SEALANTS, AIR BARRIER, EXP. JTS.	519	363	11-Jun-18 A	08-Jul-20	-28																			
700010	STEEL DOORS & FRAMES, WOOD DOORS, HARDWARE	519	363	11-Jun-18 A	08-Jul-20	-28																			
700011	ALUMINUM ENTRANCES, DOORS, FRAMES, GLASS & GLAZING	519	363	11-Jun-18 A	08-Jul-20	-28																			
700012	OVERHEAD COILING DOORS, VEHICLE SALLYPORT DOORS	519	363	11-Jun-18 A	08-Jul-20	-28																			
700013	GYPSUM BOARD, METAL FRAMING, ACOUSTICAL TREATMENTS	519	363	11-Jun-18 A	08-Jul-20	-28																			
700014	FLOORING & PAINTING	519	363	11-Jun-18 A	08-Jul-20	-28																			
700015	SPECIALTIES	519	363	11-Jun-18 A	08-Jul-20	-28																			
700017	MISCELLANEOUS EQUIPMENT	519	363	11-Jun-18 A	08-Jul-20	-28																			
700018	DETENTION HOLLOW METAL DOORS, FRAMES, GLAZING	519	363	11-Jun-18 A	08-Jul-20	-28																			
700019	MODULAR STEEL CELLS, STEEL PANELS, DETENTION CEILINGS	519	363	11-Jun-18 A	08-Jul-20	-28																			
700020	DETENTION FURNISHINGS & EQUIPMENT	519	363	11-Jun-18 A	08-Jul-20	-28																			
700021	FURNISHINGS	519	363	11-Jun-18 A	08-Jul-20	-28																			
700022	SPECIAL CONSTRUCTION	519	363	11-Jun-18 A	08-Jul-20	-28																			
700024	FIRE SUPPRESSION	519	363	11-Jun-18 A	08-Jul-20	-28																			
700025	PLUMBING	519	363	11-Jun-18 A	08-Jul-20	-28																			
700026	HEATING, VENTILATING, AND AIR CONDITIONING	519	363	11-Jun-18 A	08-Jul-20	-28																			
700027	ELECTRICAL	519	363	11-Jun-18 A	08-Jul-20	-28																			
700028	COMMUNICATIONS	519	363	11-Jun-18 A	08-Jul-20	-28																			
700029	ELECTRONIC SECURITY SYSTEMS	519	363	11-Jun-18 A	08-Jul-20	-28																			
700016	FOOD SERVICE & LAUNDRY EQUIPMENT	513	363	18-Jun-18 A	08-Jul-20	-28																			
700003	PRECAST CONCRETE	243	78	22-Jun-18 A	20-May-19	19																			
700002	CAST-IN-PLACE CONCRETE	262	161	20-Aug-18 A	17-Sep-19	22																			
700030	EARTHWORK	356	171	20-Aug-18 A	01-Oct-19	80																			
700001	BUILDING & SITE DEMOLITION	56	10	24-Aug-18 A	12-Feb-19	13																			
700032	UTILITIES	103	60	06-Sep-18 A	24-Apr-19	48																			
700005	METALS	145	98	14-Nov-18 A	18-Jun-19	-10																			



Activity ID	Activity Name	Orig Dur	Rem Dur	Early Start	Early Finish	Total Float	2019															
							Feb			Mar			Apr			May						
401000	ALTERNATE 01 - FULL EMERGENCY POWER	1	1	30-Jan-19	30-Jan-19	334																
402000	ALTERNATE 02 - DOMESTIC HOT WATER, CHILLED WATER, & HEATING	1	1	30-Jan-19	30-Jan-19	334																
403000	ALTERNATE 03 - INMATE PLUMBING CONTROL SYSTEM	1	1	30-Jan-19	30-Jan-19	334																
405000	ALTERNATE 05 - FULL OPERABLE SLIDER DOORS	1	1	30-Jan-19	30-Jan-19	334																
409000	ALTERNATE 09 - EXACQ VISION VMS	1	1	30-Jan-19	30-Jan-19	334																
410000	ALTERNATE 10 - PERVIOUS CONCRETE PAVING	1	1	30-Jan-19	30-Jan-19	334																
414000	ALTERNATE 14 - SECOND BUNK FOR CELLS	1	1	30-Jan-19	30-Jan-19	334																
700009	ROOFING & INSULATED METAL PANELS	122	122	06-Mar-19	26-Aug-19	-18																
<b>DESIGN</b>																						
003000	A/E CONSTRUCTION ADMINISTRATION SERVICES (25 MONTHS)	25	19	05-Sep-18 A	17-Feb-19	466																
<b>SITWORK</b>																						
100002	MAINTAIN EROSION CONTROLS (25 MONTHS)	25	18	16-Jul-18 A	25-Feb-19	192																
101400	UTILITY DEMOLITION - CONNECTOR/CORRIDOR AREA	15	2	13-Sep-18 A	14-Feb-19	21																
112300	SITE UTILITIES - U/G ELECTRIC FOR SITE LIGHTING WEST	10	10	22-Oct-18 A	13-Mar-19	55																
100100	SITE GRADING - STORMWATER POND (EXIST SE JUV PLOT)	10	8	21-Jan-19 A	08-Feb-19	50																
101200	SITE & UTILITY DEMOLITION - REMAINING SITE	10	10	30-Jan-19	12-Feb-19	13																
101110	SITE & UTILITY DEMOLITION - EXISTING SE JUVENILE PARKING LOT 2 OF 2 (DELETE)	0	0	30-Jan-19	30-Jan-19	335																
100110	SITE GRADING - STORMWATER POND (EXIST SE JUV PLOT) 2 OF 2 (DELETE)	0	0	30-Jan-19	30-Jan-19	335																
110000	SITE UTILITIES - STORMWATER POND	10	10	11-Feb-19	25-Feb-19	50																
100200	SITE GRADING - REMAINING SITE	10	10	13-Feb-19	27-Feb-19	13																
151010	GRAVEL - STORMWATER POND	5	5	26-Feb-19	04-Mar-19	177																
159300	LANDSCAPING - NE JUVENILE PARKING LOT	5	5	26-Feb-19	04-Mar-19	312																
100400	SITE GRADING - CONNECTOR/CORRIDOR AREA	10	10	28-Feb-19	13-Mar-19	13																
111000	SITE UTILITIES - SANITARY SOUTH	10	10	28-Feb-19	13-Mar-19	50																
110010	SITE UTILITIES - STORM SOUTH 1 OF 2	10	10	28-Feb-19	13-Mar-19	48																
113000	SITE UTILITIES - GAS EAST	10	10	28-Feb-19	13-Mar-19	78																
152000	DECORATIVE FENCE/GATE - RETENTION POND	10	10	05-Mar-19	18-Mar-19	177																
112400	SITE UTILITIES - TELECOM NORTH (INCL CONNECTOR/CORRIDOR)	10	10	14-Mar-19	27-Mar-19	68																
112310	SITE UTILITIES - U/G ELECTRIC FOR SITE LIGHTING EAST	10	10	14-Mar-19	27-Mar-19	55																
112380	SITE UTILITIES - U/G ELECTRIC NORTH (BY GULF POWER)	20	20	14-Mar-19	10-Apr-19	13																
158000	FRP CANTILEVER WALL - ROADS/DRIVES SITE NORTH	15	15	14-Mar-19	03-Apr-19	105																
112000	SITE UTILITIES - WATER WEST/NORTH (INCL CONNECTOR/CORRIDOR)	10	10	14-Mar-19	27-Mar-19	68																

Activity ID	Activity Name	Orig Dur	Rem Dur	Early Start	Early Finish	Total Float	2019															
							Feb				Mar				Apr							
110015	SITE UTILITIES - STORM SOUTH 2 OF 2	10	10	14-Mar-19	27-Mar-19	48																
111010	SITE UTILITIES - SANITARY EAST	15	15	14-Mar-19	03-Apr-19	50																
111020	SITE UTILITIES - SANITARY LATERALS NORTH (CONNECTOR/CORRIDOR)	5	5	14-Mar-19	20-Mar-19	105																
110020	SITE UTILITIES - STORM NORTH (INCL CONNECTOR/CORRIDOR) 1 OF 2	10	10	28-Mar-19	10-Apr-19	48																
151200	SITE CONCRETE - NORTHEAST SITE/UTILITY YARD/LOADING DOCK	10	10	03-Apr-19	16-Apr-19	190																
151300	SITE CONCRETE - STAFF PARKING	10	10	03-Apr-19	16-Apr-19	41																
158190	RAILING @ CANTILEVER WALL	5	5	04-Apr-19	10-Apr-19	205																
158200	FRP CONC GRAVITY WALL - ROAD SITE WEST	15	15	04-Apr-19	24-Apr-19	105																
112390	SITE UTILITIES - BLDG & FIRE PUMP TRANSFORMERS (BY GULF POWER)	10	10	11-Apr-19	24-Apr-19	13																
110025	SITE UTILITIES - STORM NORTH (INCL CONNECTOR/CORRIDOR) 2 OF 2	10	10	11-Apr-19	24-Apr-19	48																
151100	CONCRETE PADS - COOLING TOWERS	6	6	17-Apr-19	24-Apr-19	190																
151150	CONCRETE PADS - GENERATORS	6	6	17-Apr-19	24-Apr-19	190																
150200	CURB & GUTTER - STAFF PARKING LOT	10	10	17-Apr-19	30-Apr-19	41																
151400	SITE CONCRETE - PUBLIC PARKING/ENTRANCE AREA	15	15	17-Apr-19	07-May-19	41																
151000	GRAVEL - UTILITY YARD	5	5	25-Apr-19	01-May-19	190																

**CORRECTIONAL FACILITY**

200300	STRUCTURAL BACKFILL A	5	2	24-Oct-18 A	14-Jun-19	57																
200320	STRUCTURAL BACKFILL B	8	5	29-Oct-18 A	05-Aug-19	22																
200420	UNDER SLAB PLUMBING B	10	8	17-Dec-18 A	15-Aug-19	24																
200400	UNDER SLAB PLUMBING A	10	8	07-Jan-19 A	26-Jun-19	59																
211040	PRECAST C (3/3)	15	9	08-Jan-19 A	11-Feb-19	-21																
211060	PRECAST D ELEV 100	9	2	15-Jan-19 A	22-Feb-19	-28																
210000	PRECAST A (1/3)	15	10	21-Jan-19 A	26-Feb-19	-21																
210120	STRUCTURAL STEEL D ELEV 115	5	3	22-Jan-19 A	27-Feb-19	-28																
200900	SLAB ON DECK D ELEV 102 - 2ND LVL	6	6	30-Jan-19	06-Feb-19	67																
211090	PRECAST CENTER CORRIDOR CL 14-50	15	15	30-Jan-19	20-Feb-19	-28																
200450	UNDER SLAB PLUMBING C (1/2)	10	10	30-Jan-19	12-Feb-19	148																
200465	UNDER SLAB ELECTRICAL C (2/2)	10	10	30-Jan-19	12-Feb-19	158																
210300	SWITCHBACK STAIRS C	15	15	12-Feb-19	05-Mar-19	75																
201090	IN-SLAB PLUMBING C ROOF	5	5	12-Feb-19	19-Feb-19	29																
201290	IN-SLAB ELECTRICAL C ROOF	5	5	12-Feb-19	19-Feb-19	29																
200455	UNDER SLAB PLUMBING C (2/2)	10	10	13-Feb-19	27-Feb-19	148																









**Whitesell Green / Caddell, a Joint Venture**  
 2700 Lagoon Park Drive  
 Montgomery, Alabama 36109  
 P: (334) 272-7723  
 F: (334) 394-0193

**Project: 1054 - Escambia County Correctional Facility**  
 3080 N. Pace Boulevard  
 Pensacola, Florida 32501

## Daily Log: Tuesday 1/1/2019

**Daily Log Completed**  
 The Daily Log was completed by Donald Shelton on Mon Jan 7, 2019 at 12:20 pm CST.

### WEATHER REPORT

Temperature			Precipitation Since			Humidity				Windspeed		
Low	High	Avg	Midnight	2 Days Ago	3 Days Ago	Low	Avg	High	Dew	Avg	Max	Gust
67°F	73°F	69°F	0.04 in.	0.24 in.	0.27 in.	89%	96%	100%	68°F	5.3 mph	8 mph	14 mph

### DAILY SNAPSHOT

06:00 AM	09:00 AM	12:00 PM	03:00 PM	06:00 PM	09:00 PM
cloudy 69°F	cloudy 70°F	cloudy 74°F	cloudy 72°F	fog 68°F	fog 68°F

### OBSERVED WEATHER CONDITIONS

No.	Weather Delay	Sky	Temp	Average	Precipitation	Wind	Ground/Sea
1	No						

### MANPOWER LOG

0 Workers | 0.0 Man Hours

No.	Contact/Company	Cost Code	Workers	# Hours	Man Hours	Location
1	Caddell Construction Co. (DE), LLC		0	0.0	0.0	
<b>Notes:</b> Holiday						
			<b>0</b>		<b>0.0</b>	

By \_\_\_\_\_ Date \_\_\_\_\_ Copies To \_\_\_\_\_



## Daily Log: Wednesday 1/2/2019

**Daily Log Completed**  
 The Daily Log was completed by Donald Shelton on Mon Jan 7, 2019 at 12:21 pm CST.

### WEATHER REPORT

Temperature			Precipitation Since			Humidity				Windspeed		
Low	High	Avg	Midnight	2 Days Ago	3 Days Ago	Low	Avg	High	Dew	Avg	Max	Gust
65°F	70°F	68°F	0.06 in.	0.10 in.	0.30 in.	97%	98%	100%	67°F	4.3 mph	7 mph	7 mph

### DAILY SNAPSHOT

06:00 AM	09:00 AM	12:00 PM	03:00 PM	06:00 PM	09:00 PM
<b>rain</b> 66°F	<b>fog</b> 68°F	<b>cloudy</b> 70°F	<b>cloudy</b> 69°F	<b>cloudy</b> 69°F	<b>cloudy</b> 67°F

### OBSERVED WEATHER CONDITIONS

No.	Weather Delay	Sky	Temp	Average	Precipitation	Wind	Ground/Sea
1	No	Cloudy	Mild	67	0	Calm	Wet/Muddy

### MANPOWER LOG

**58 Workers | 533.0 Man Hours**

No.	Contact/Company	Cost Code	Workers	# Hours	Man Hours	Location
1	A&B Electric Co., Inc.		3	10.0	30.0	Site
<b>Notes:</b> Work on temporary panels, Work on parking lot lights in Juvenile parking lot.						
2	Bayside Structures, LLC		13	8.0	104.0	Site>D
<b>Notes:</b> Installed wire mesh and rebar in level 2 area D slab. Also installed bulkheads and began to install depression. Checked edge form grade, and grade no nelson studs in depressed area. Nelson studs will have to be reworked due to wrong elevation pushing slab pour to Saturday.						
3	Caddell Construction Co. (DE), LLC		8	10.0	80.0	Site
<b>Notes:</b> WGI/Caddell supervision, quality control and safety onsite.						
4	Ed Emmons Steel Erectors, Inc.		9	10.0	90.0	Site>D
<b>Notes:</b> Erected beams and columns in sequence to Elevation 100. Started placing decking.						


**MANPOWER LOG**

58 Workers | 533.0 Man Hours

No.	Contact/Company	Cost Code	Workers	# Hours	Man Hours	Location
5	Nash Plumbing and Mechanical, LLC		6	6.5	39.0	Site
<b>Notes:</b> Prefabrication preparations 40 Total Man Hours						
6	Tindall Corporation		19	10.0	190.0	Site>C
<b>Notes:</b> **Grouting and welding **Erecting in C **Patching in C 198.5 Total Man Hours						
			<b>58</b>		<b>533.0</b>	

**Manpower Log's Attachments:**


1. A&B Electric Co., Inc.

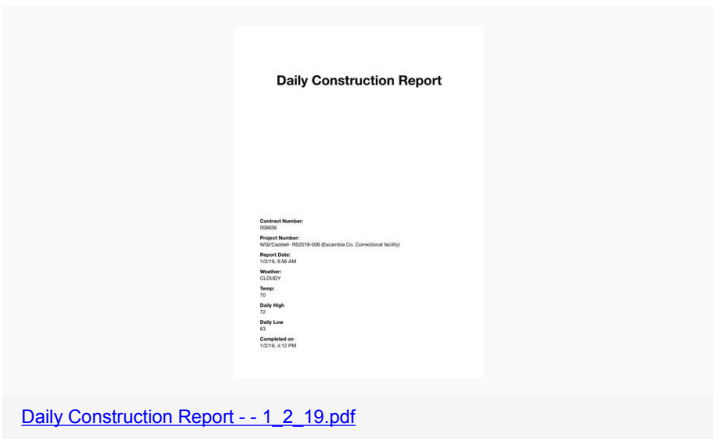

2. Bayside Structures, LLC



4. Ed Emmons Steel Erectors, Inc.

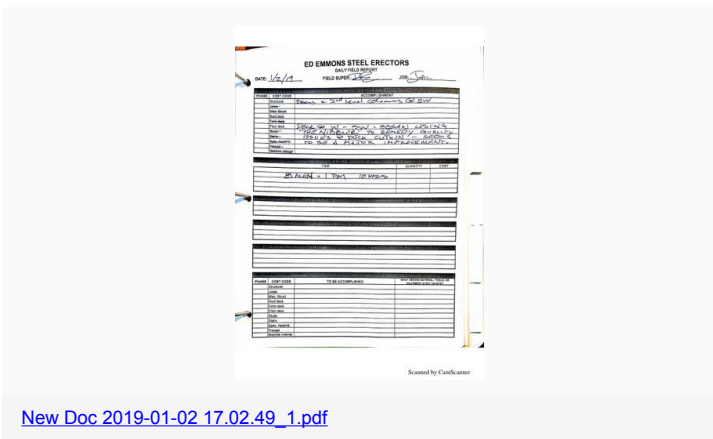

5. Nash Plumbing and Mechanical, LLC






[Tindall Escambia Daily 1-2-19.xlsx](#)

### EQUIPMENT LOG

No.	Equipment Name	Cost Code	Hrs Operating	Hrs Idle	Inspected?	Inspection Time	Location
1	Kobelco Crane CKE2500				No	07:00 AM	Site>C
	<b>Notes:</b>						
2	Genie Lift S125				No	07:00 AM	Site>C
	<b>Notes:</b>						
3	JLG Lift 860SJ				No	07:00 AM	Site>C
	<b>Notes:</b>						
4	JLG Lift 660SJ				No	07:00 AM	Site
	<b>Notes:</b>						
5	Grove Crane AT700D				No	07:00 AM	Site>D
	<b>Notes:</b>						
6	Genie Lift S80				No	07:00 AM	Site>D
	<b>Notes:</b>						
7	JLG Skytrak Telehandler				No	07:00 AM	Site
	<b>Notes:</b>						
8	Cat Telehandler				No	07:00 AM	Site
	<b>Notes:</b>						

### PHOTOS

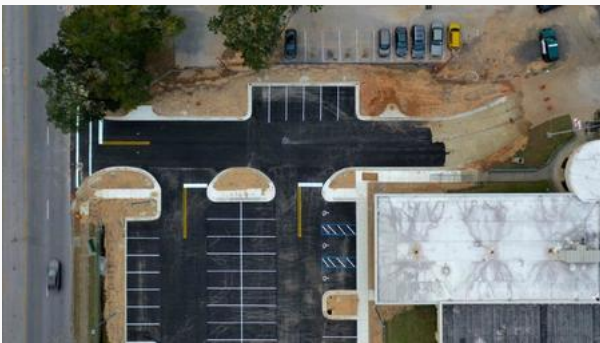

[DJI\\_0177.jpg](#)



[DJI\\_0178.jpg](#)



[DJI\\_0169.jpg](#)



[DJI\\_0173.jpg](#)



[DJI\\_0172.jpg](#)

Jobsite Northwest view of Building



[DJI\\_0174.jpg](#)



[DJI\\_0180.jpg](#)

Juvenile Justice Parking Lot



[DJI\\_0171.jpg](#)



[DJI\\_0170.jpg](#)

---

By

Date

Copies To



**Whitesell Green / Caddell, a Joint Venture**  
 2700 Lagoon Park Drive  
 Montgomery, Alabama 36109  
 P: (334) 272-7723  
 F: (334) 394-0193

**Project: 1054 - Escambia County Correctional Facility**  
 3080 N. Pace Boulevard  
 Pensacola, Florida 32501

## Daily Log: Thursday 1/3/2019

**Daily Log Completed**  
 The Daily Log was completed by Donald Shelton on Mon Jan 7, 2019 at 12:21 pm CST.

### WEATHER REPORT

Temperature			Precipitation Since			Humidity				Windspeed		
Low	High	Avg	Midnight	2 Days Ago	3 Days Ago	Low	Avg	High	Dew	Avg	Max	Gust
60°F	67°F	65°F	0.12 in.	0.18 in.	0.22 in.	91%	96%	100%	64°F	4.5 mph	10 mph	16 mph

### DAILY SNAPSHOT

06:00 AM	09:00 AM	12:00 PM	03:00 PM	06:00 PM	09:00 PM
cloudy 64°F	cloudy 62°F	partly-cloudy-day 64°F	cloudy 68°F	cloudy 66°F	cloudy 66°F

### OBSERVED WEATHER CONDITIONS

No.	Weather Delay	Sky	Temp	Average	Precipitation	Wind	Ground/Sea
1	No	Overcast	Mild	65	0	Calm	Wet/Muddy

### MANPOWER LOG

49 Workers | 436.0 Man Hours

No.	Contact/Company	Cost Code	Workers	# Hours	Man Hours	Location
1	A&B Electric Co., Inc.		3	10.0	30.0	Site
<b>Notes:</b> Working on temporary backboard panels, Working on Juvenile parking lot lights.						
2	Bayside Structures, LLC		5	8.0	40.0	Site>D
<b>Notes:</b> Installed embeds around perimeter of level 2 area D slab. Continued forming depressions in level 2 area D slab.						
3	Caddell Construction Co. (DE), LLC		8	8.0	64.0	Site
<b>Notes:</b> WGI/Caddell supervision, quality control and safety onsite.						
4	Ed Emmons Steel Erectors, Inc.		9	8.0	72.0	Site>D
<b>Notes:</b> Erected columns and beams in sequence to Line 50 at Elevation 100.						
5	Tindall Corporation		19	10.0	190.0	Site>C
<b>Notes:</b> **Grouting and welding **Erecting in C **Patching in C						


**MANPOWER LOG**

49 Workers | 436.0 Man Hours

No.	Contact/Company	Cost Code	Workers	# Hours	Man Hours	Location
6	Nash Plumbing and Mechanical, LLC		3	8.0	24.0	Site
<b>Notes:</b> Worked on perforation for piping						
7	EAA Site Contractors LLC		2	8.0	16.0	Site
<b>Notes:</b> GCTE installed signs and painted stop bars at the ST Mary entrance to the JJC parking lot.						
			<b>49</b>		<b>436.0</b>	

**Manpower Log's Attachments:**

1. A&B Electric Co., Inc.

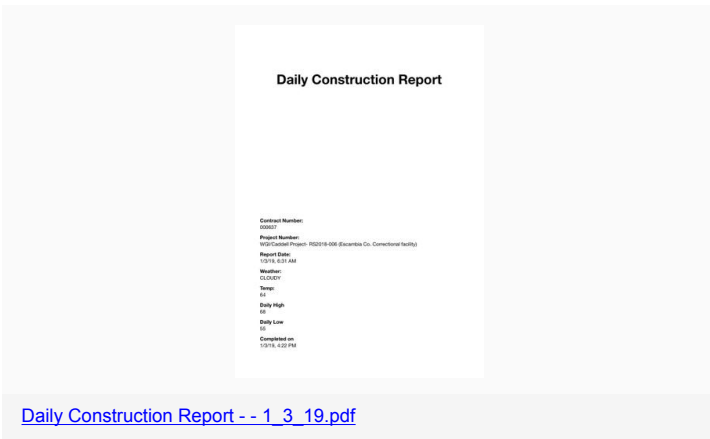


[Daily Construction Report - - 1\\_3\\_19.pdf](#)

2. Bayside Structures, LLC

[Daily 1-3.docx](#)

4. Ed Emmons Steel Erectors, Inc.

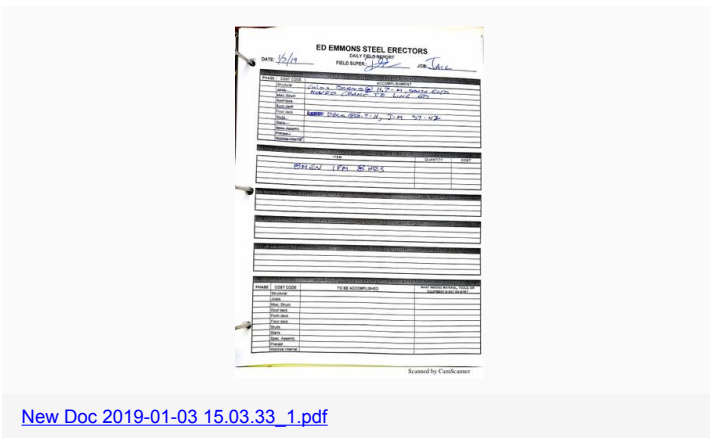

[New Doc 2019-01-03 15.03.33\\_1.pdf](#)

5. Tindall Corporation

[Tindall Escambia Daily 1-3-19.xlsx](#)

6. Nash Plumbing and Mechanical, LLC

[Project Superintendent Daily Report 1-3-2019.xlsx](#)

## EQUIPMENT LOG

No.	Equipment Name	Cost Code	Hrs Operating	Hrs Idle	Inspected?	Inspection Time	Location
1	Kobelco Crane CKE2500				No	07:00 AM	Site>C
	<b>Notes:</b>						
2	JLG Lift 860SJ				No	07:00 AM	Site>C
	<b>Notes:</b>						
3	JLG Lift 660SJ				No	07:00 AM	Site>C
	<b>Notes:</b>						
4	Genie Lift S85				No	07:00 AM	Site>C
	<b>Notes:</b>						
5	Grove Crane AT700D				No	07:00 AM	Site>D
	<b>Notes:</b>						
6	Genie Lift S80				No	07:00 AM	Site>D
	<b>Notes:</b>						

---

By

Date

Copies To



## Daily Log: Friday 1/4/2019

**Daily Log Completed**  
 The Daily Log was completed by Donald Shelton on Mon Jan 7, 2019 at 12:22 pm CST.

### WEATHER REPORT

Temperature			Precipitation Since			Humidity				Windspeed		
Low	High	Avg	Midnight	2 Days Ago	3 Days Ago	Low	Avg	High	Dew	Avg	Max	Gust
46°F	70°F	58°F	0.27 in.	0.39 in.	0.45 in.	49%	77%	100%	50°F	11.4 mph	17 mph	33 mph

### DAILY SNAPSHOT

06:00 AM	09:00 AM	12:00 PM	03:00 PM	06:00 PM	09:00 PM
partly-cloudy-night 61°F	partly-cloudy-day 57°F	wind 62°F	clear-day 60°F	clear-night 55°F	clear-night 50°F

### OBSERVED WEATHER CONDITIONS

No.	Weather Delay	Sky	Temp	Average	Precipitation	Wind	Ground/Sea
1	No	Cloudy	Mild	58	0	Calm	Wet/Muddy


### MANPOWER LOG

43 Workers | 400.0 Man Hours

No.	Contact/Company	Cost Code	Workers	# Hours	Man Hours	Location
1	A&B Electric Co., Inc.		3	10.0	30.0	Site
<b>Notes:</b> Working on temporary power panels						
2	Bayside Structures, LLC		5	8.0	40.0	Site>D
<b>Notes:</b> Finished installing depressions. Reworked some rebar around depression. Install opening bars at 4 locations.						
3	Caddell Construction Co. (DE), LLC		8	10.0	80.0	Site
<b>Notes:</b> WGI/Caddell supervision, quality control and safety onsite.						
4	Ed Emmons Steel Erectors, Inc.		7	8.0	56.0	Site>D
<b>Notes:</b> Erected beams from H.7 line to M line at elevation 100. Installed deck on South end at elevation 100.						
5	Larry M. Jacobs & Associates, Inc.		1	4.0	4.0	Site>D
<b>Notes:</b> Inspecting steel sequence 1 elevation 100.						



4. Ed Emmons Steel Erectors, Inc.

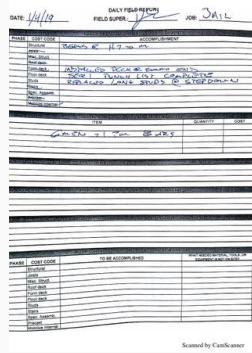

[New Doc 2019-01-04 15.21.12\\_1.pdf](#)

6. Tindall Corporation

[Tindall Escambia Daily 1-4-19.xlsx](#)

**EQUIPMENT LOG**

No.	Equipment Name	Cost Code	Hrs Operating	Hrs Idle	Inspected?	Inspection Time	Location
1	Kobelco Crane CKE2500				No	07:00 AM	Site>C
	<b>Notes:</b>						
2	Genie Lift S85				No	07:00 AM	Site>C
	<b>Notes:</b>						
3	JLG Lift 860SJ				No	07:00 AM	Site>C
	<b>Notes:</b>						
4	JLG Lift 660SJ				No	07:00 AM	Site>C
	<b>Notes:</b>						
5	Grove Crane AT700D				No	07:00 AM	Site>D
	<b>Notes:</b>						
6	Genie Lift S80				No	07:00 AM	Site>D
	<b>Notes:</b>						
7	JLG Skytrak Telehandler				No	07:00 AM	Site
	<b>Notes:</b>						

**INSPECTION LOG**

No.	Start Time	End Time	Inspection Type	Inspecting Entity	Inspector Name	Location	Area
1	08:00 AM	02:00 PM	Third Party	Mott MacDonald	Mikr Tugwell	Site>D	D
	<b>Comments:</b> Inspected for concrete pour sequence 1 elevation 100						

By \_\_\_\_\_

Date \_\_\_\_\_

Copies To \_\_\_\_\_





## Daily Log: Saturday 1/5/2019

**Daily Log Completed**  
 The Daily Log was completed by Donald Shelton on Mon Jan 7, 2019 at 12:23 pm CST.

### WEATHER REPORT

Temperature			Precipitation Since			Humidity				Windspeed		
Low	High	Avg	Midnight	2 Days Ago	3 Days Ago	Low	Avg	High	Dew	Avg	Max	Gust
45°F	62°F	52°F	0.00 in.	0.27 in.	0.39 in.	43%	70%	94%	42°F	5.7 mph	9 mph	18 mph

### DAILY SNAPSHOT

06:00 AM	09:00 AM	12:00 PM	03:00 PM	06:00 PM	09:00 PM
cloudy 48°F	clear-day 50°F	clear-day 58°F	clear-day 63°F	clear-night 54°F	clear-night 47°F

### OBSERVED WEATHER CONDITIONS

No.	Weather Delay	Sky	Temp	Average	Precipitation	Wind	Ground/Sea
1	No	Clear	Mild	52	0	Calm	Wet/Muddy

### MANPOWER LOG

38 Workers | 444.0 Man Hours

No.	Contact/Company	Cost Code	Workers	# Hours	Man Hours	Location
1	Bayside Structures, LLC		16	14.0	224.0	Site>D
<b>Notes:</b> Placing concrete and finishing in Area D elevation 100.						
2	Caddell Construction Co. (DE), LLC		1	14.0	14.0	Site
<b>Notes:</b> WGI/Caddell supervision, quality control and safety onsite.						
3	Tindall Corporation		19	10.0	190.0	Site>C
<b>Notes:</b> **Grouting and welding **Erecting in C **Patching in C						
4	EAA Site Contractors LLC		2	8.0	16.0	Site
<b>Notes:</b> GCTE installed wheel stops in the JJC parking lot						
			<b>38</b>		<b>444.0</b>	

### Manpower Log's Attachments:

1. Bayside Structures, LLC

**BAYSIDESTRUCTURES**  
CONCRETE CONSTRUCTION SPECIALISTS

PROJECT NAME: Lafayette Structure  
DATE: 1-5-19

Inspector: [Signature]  
14 hours

[Bayside Daily Report 1-5-19.pdf](#)


3. Tindall Corporation

[Tindall Escambia Daily 1-5-19.xlsx](#)

**EQUIPMENT LOG**


No.	Equipment Name	Cost Code	Hrs Operating	Hrs Idle	Inspected?	Inspection Time	Location
1	Kobelco Crane CKE2500				No	07:00 AM	Site>D
	<b>Notes:</b>						
2	Genie Lift S125				No	07:00 AM	Site>D
	<b>Notes:</b>						
3	JLG Lift 860SJ				No	07:00 AM	Site>D
	<b>Notes:</b>						
4	JLG Lift 660SJ				No	07:00 AM	Site>D
	<b>Notes:</b>						
5	JLG Skytrak Telehandler				No	07:00 AM	Site
	<b>Notes:</b>						

**PHOTOS**

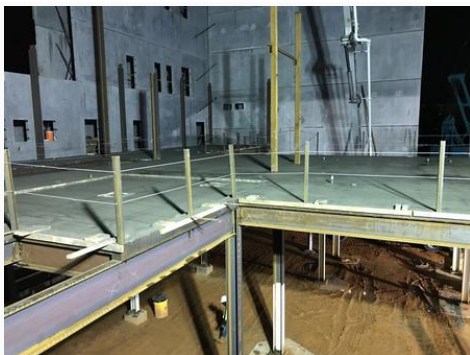

[IMG\\_0529.jpg](#)

Slab on Deck at Area D 2nd Level

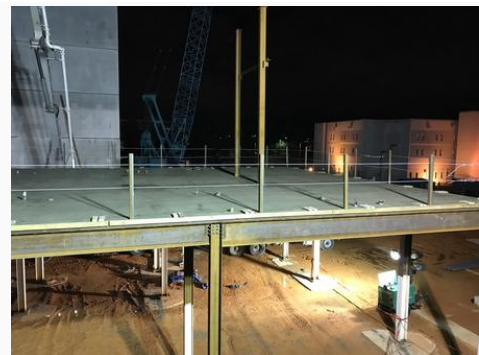

[IMG\\_0530.jpg](#)

Slab on Deck Area D 2nd Level.



[IMG\\_0532.jpg](#)



[IMG\\_0533.jpg](#)



[IMG\\_0534.jpg](#)

---

By

Date

Copies To



## Daily Log: Sunday 1/6/2019

**Daily Log Completed**  
 The Daily Log was completed by Donald Shelton on Mon Jan 7, 2019 at 12:24 pm CST.

### WEATHER REPORT

Temperature			Precipitation Since			Humidity				Windspeed		
Low	High	Avg	Midnight	2 Days Ago	3 Days Ago	Low	Avg	High	Dew	Avg	Max	Gust
41°F	66°F	52°F	0.00 in.	0.00 in.	0.27 in.	42%	77%	98%	44°F	1.8 mph	4 mph	6 mph

### DAILY SNAPSHOT

06:00 AM	09:00 AM	12:00 PM	03:00 PM	06:00 PM	09:00 PM
clear-night 43°F	clear-day 54°F	clear-day 65°F	clear-day 67°F	clear-night 57°F	clear-night 49°F

### OBSERVED WEATHER CONDITIONS

No.	Weather Delay	Sky	Temp	Average	Precipitation	Wind	Ground/Sea
1	No	Clear	Mild	52	0	Calm	Wet/Muddy

### MANPOWER LOG

13 Workers | 116.0 Man Hours

No.	Contact/Company	Cost Code	Workers	# Hours	Man Hours	Location
1	Caddell Construction Co. (DE), LLC		1	8.0	8.0	Site
<b>Notes:</b> WGI/Caddell supervision, quality control and safety onsite.						
2	Tindall Corporation		12	9.0	108.0	Site>C
<b>Notes:</b> **Grouting and welding **Brace removal						
			<b>13</b>	<b>116.0</b>		

2. Tindall Corporation

[Tindall Escambia Daily 1-6-19.xlsx](#)

### EQUIPMENT LOG

No.	Equipment Name	Cost Code	Hrs Operating	Hrs Idle	Inspected?	Inspection Time	Location
1	JLG Skytrak Telehandler				No	07:00 AM	Site>C
<b>Notes:</b>							
2	Genie Lift S85				No	07:00 AM	Site>C
<b>Notes:</b>							

## EQUIPMENT LOG

No.	Equipment Name	Cost Code	Hrs Operating	Hrs Idle	Inspected?	Inspection Time	Location
3	JLG Lift 860SJ				No	07:00 AM	Site>C

Notes:

---

---

By

---

Date

---

Copies To



## Daily Log: Monday 1/7/2019

**Daily Log Completed**  
 The Daily Log was completed by Donald Shelton on Mon Jan 14, 2019 at 09:40 am CST.

### WEATHER REPORT

Temperature			Precipitation Since			Humidity				Windspeed		
Low	High	Avg	Midnight	2 Days Ago	3 Days Ago	Low	Avg	High	Dew	Avg	Max	Gust
41°F	67°F	54°F	0.00 in.	0.00 in.	0.00 in.	63%	86%	100%	50°F	2.8 mph	6 mph	6 mph

### DAILY SNAPSHOT

06:00 AM	09:00 AM	12:00 PM	03:00 PM	06:00 PM	09:00 PM
partly-cloudy-night 42°F	partly-cloudy-day 57°F	partly-cloudy-day 67°F	partly-cloudy-day 67°F	partly-cloudy-night 58°F	partly-cloudy-night 56°F

### OBSERVED WEATHER CONDITIONS

No.	Weather Delay	Sky	Temp	Average	Precipitation	Wind	Ground/Sea
1	No	Clear	Mild	54	0	Calm	Wet/Muddy



### MANPOWER LOG

65 Workers | 559.75 Man Hours

No.	Contact/Company	Cost Code	Workers	# Hours	Man Hours	Location
1	A&B Electric Co., Inc.		9	7.75	69.75	Site
<b>Notes:</b> Trouble shoot temporary power panel west side of bld., Trouble shoot Juvenile parking lot lights not working, Working on temporary power backboards. 70 Total Man Hours.						
2	Bayside Structures, LLC		6	8.0	48.0	Site
<b>Notes:</b> Strip and chip bulkhead from sequence 1 on level two area D elevation 100 slab pour. Continue grouting base plates in area D for sequence 2 slab pour. Began to rework west GB in connector.						
3	Caddell Construction Co. (DE), LLC		8	10.0	80.0	Site
<b>Notes:</b> WGI/Caddell supervision, quality control and safety onsite.						
4	Ed Emmons Steel Erectors, Inc.		8	8.0	64.0	Site>D
<b>Notes:</b> Installed deck to H Line. Installed all step-down deck. Installed 1st run of deck (37-42 to M Line). Began installing handrail post.						
5	Larry M. Jacobs & Associates, Inc.		2	4.0	8.0	Site>D
<b>Notes:</b> Conducted Flat Surface Test on finish concrete in Area D at elevation 100.						

**MANPOWER LOG**

**65 Workers | 559.75 Man Hours**

No.	Contact/Company	Cost Code	Workers	# Hours	Man Hours	Location
6	Ruben Surveying		2	8.0	16.0	Site>Juvenile Justice Parking Lot
<b>Notes:</b> As built for Juvenile Justice Parking Lot						
7	Tindall Corporation		19	10.0	190.0	Site>C 
<b>Notes:</b> **Erecting in area C **Grouting and welding **Patching in area C						
8	Nash Plumbing and Mechanical, LLC		10	8.0	80.0	Site>A 
<b>Notes:</b> Started underground plumbing in Area A						
9	EAA Site Contractors LLC		1	4.0	4.0	Site
<b>Notes:</b> Total man hours 40. EAA returned to job site to finalize JJC parking lot (EAA has not been at site since 19 Dec). GCTE returned to finalize directional arrows in JJC parking lot. EAA finished sloping and grooming dirt along L St and corner of St Mary. Also graded dirt along SW corner of JJC bldg. We are now waiting for old parking lot to be released for demo						
			<b>65</b>	<b>559.75</b>		

**Manpower Log's Attachments:**

1. A&B Electric Co., Inc. \_\_\_\_\_

**Daily Construction Report**

Contract Number:  
00000

Project Number:  
W2C/Contract Phase: RC2018-000 (Encanto Co. Correctional facility)

Report Date:  
1/7/19, 7:27 AM

Weather:  
Sunny

Temp:  
45

Daily High:  
60

Daily Low:  
30


Completed on:  
1/7/19, 6:00 PM

[Daily Construction Report - - 1\\_7\\_19.pdf](#)

2. Bayside Structures, LLC \_\_\_\_\_

 [Daily 1-7.docx](#)

4. Ed Emmons Steel Erectors, Inc.

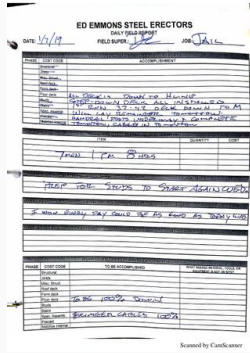

[New Doc 2019-01-07 14.52.23\\_1.pdf](#)

7. Tindall Corporation

[Tindall Escambia Daily 1-7-19.xlsx](#)

8. Nash Plumbing and Mechanical, LLC



[Nash Daily 1-7-19.pdf](#)

**EQUIPMENT LOG**

No.	Equipment Name	Cost Code	Hrs Operating	Hrs Idle	Inspected?	Inspection Time	Location
1	Kobelco Crane CKE2500				No	07:00 AM	Site>C
	<b>Notes:</b>						
2	Genie Lift S125				No	07:00 AM	Site>C
	<b>Notes:</b>						
3	JLG Lift 860SJ				No	07:50 AM	Site>C
	<b>Notes:</b>						
4	JLG Lift 660SJ				No	07:00 AM	Site>C
	<b>Notes:</b>						
5	Sky Power Lift 600AJ				No	07:00 AM	Site>C
	<b>Notes:</b>						
6	Genie Lift S85				No	07:00 AM	Site>A
	<b>Notes:</b>						
7	Grove Crane AT700D				No	07:00 AM	Site>D
	<b>Notes:</b>						



## EQUIPMENT LOG

No.	Equipment Name	Cost Code	Hrs Operating	Hrs Idle	Inspected?	Inspection Time	Location
8	Genie Lift S80				No	07:00 PM	Site>D
	<b>Notes:</b>						
9	JLG Skytrak Telehandler				No	07:00 AM	Site
	<b>Notes:</b>						
10	JLG Skytrak Telehandler				No	07:00 AM	Site
	<b>Notes:</b>						
11	Komatsu 320 PT Loader				No	07:00 AM	Site>Juvenile Justice Parking Lot
	<b>Notes:</b>						
12	John Deere 50G Miniexcavator				No	07:00 AM	Site>Juvenile Justice Parking Lot
	<b>Notes:</b>						
13	CAT Miniexcavator				No	07:00 AM	Site>A
	<b>Notes:</b>						

By \_\_\_\_\_

Date \_\_\_\_\_

Copies To \_\_\_\_\_



## Daily Log: Tuesday 1/8/2019

**Daily Log Completed**  
 The Daily Log was completed by Donald Shelton on Mon Jan 14, 2019 at 10:39 am CST.

### WEATHER REPORT

Temperature			Precipitation Since			Humidity				Windspeed		
Low	High	Avg	Midnight	2 Days Ago	3 Days Ago	Low	Avg	High	Dew	Avg	Max	Gust
49°F	72°F	61°F	0.00 in.	0.00 in.	0.00 in.	65%	87%	100%	56°F	3.3 mph	7 mph	12 mph

### DAILY SNAPSHOT

06:00 AM	09:00 AM	12:00 PM	03:00 PM	06:00 PM	09:00 PM
partly-cloudy-night 52°F	partly-cloudy-day 63°F	partly-cloudy-day 71°F	partly-cloudy-day 72°F	partly-cloudy-night 65°F	partly-cloudy-night 61°F

### OBSERVED WEATHER CONDITIONS

No.	Weather Delay	Sky	Temp	Average	Precipitation	Wind	Ground/Sea
1	No	Cloudy	Mild	61	0	Calm	Wet/Muddy


### MANPOWER LOG

62 Workers | 570.0 Man Hours

No.	Contact/Company	Cost Code	Workers	# Hours	Man Hours	Location
1	A&B Electric Co., Inc.		11	10.0	110.0	Site
<b>Notes:</b> Working on temporary panels, Working on temporary power conduits to building & material Elevator.						
2	Bayside Structures, LLC		4	8.0	32.0	Site
<b>Notes:</b> Completed removing dirt from forms at connector Grade Beams (GB). Started reforming GB at connector.						
3	Caddell Construction Co. (DE), LLC		8	10.0	80.0	Site
<b>Notes:</b> WGI/Caddell supervision, quality control and safety onsite.						
4	Ed Emmons Steel Erectors, Inc.		8	8.0	64.0	Site>D
<b>Notes:</b> Laid all deck up to Sequence 2						
5	Nash Plumbing and Mechanical, LLC		10	8.0	80.0	Site>A
<b>Notes:</b> Underground work in Area A						
6	Ruben Surveying		2	7.0	14.0	Site>Juvenile Justice Parking Lot
<b>Notes:</b> As built for Juvenile Justice Parking Lot						



4. Ed Emmons Steel Erectors, Inc.

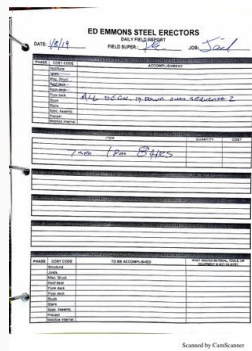

[New Doc 2019-01-08 15.06.26\\_1.pdf](#)

5. Nash Plumbing and Mechanical, LLC

[Nash Daily 1-8-2019.xlsx](#)

7. Tindall Corporation

[Tindall Escambia Daily 1-8-2019.xlsx](#)

**EQUIPMENT LOG**

No.	Equipment Name	Cost Code	Hrs Operating	Hrs Idle	Inspected?	Inspection Time	Location
1	Kobelco Crane CKE2500				No	07:00 AM	Site>C
	<b>Notes:</b>						
2	Genie Lift S125				No	07:00 AM	Site>C
	<b>Notes:</b>						
3	JLG Lift 860SJ				No	07:00 AM	Site>C
	<b>Notes:</b>						
4	JLG Lift 660SJ				No	07:00 AM	Site>C
	<b>Notes:</b>						
5	Genie Lift S85				No	07:00 AM	Site>A
	<b>Notes:</b>						
6	CAT Miniexcavator				No	07:00 AM	Site>A
	<b>Notes:</b>						
7	Grove Crane AT700D				No	07:00 AM	Site>D
	<b>Notes:</b>						
8	Genie Lift S80				No	07:00 AM	Site>D
	<b>Notes:</b>						
9	JLG Skytrak Telehandler				No	07:00 AM	Site>D
	<b>Notes:</b>						
10	JLG Skytrak Telehandler				No	07:00 AM	Site
	<b>Notes:</b>						
11	CAT Miniexcavator				No	07:00 AM	Site>B
	<b>Notes:</b>						
12	Ditch Witch RT45 Trencher				No	07:00 AM	Site>B
	<b>Notes:</b>						

## EQUIPMENT LOG

No.	Equipment Name	Cost Code	Hrs Operating	Hrs Idle	Inspected?	Inspection Time	Location
13	Bobcat Miniexcavator				No	07:00 AM	Site
<b>Notes:</b>							
14	Sky Power Lift 600AJ				No	07:00 AM	Site>C
<b>Notes:</b>							

---

By

---

Date

---

Copies To



## Daily Log: Wednesday 1/9/2019

**Daily Log Completed**  
 The Daily Log was completed by Donald Shelton on Mon Jan 14, 2019 at 09:42 am CST.

### WEATHER REPORT

Temperature			Precipitation Since			Humidity				Windspeed		
Low	High	Avg	Midnight	2 Days Ago	3 Days Ago	Low	Avg	High	Dew	Avg	Max	Gust
44°F	60°F	53°F	0.00 in.	0.00 in.	0.00 in.	25%	51%	96%	34°F	8.4 mph	13 mph	21 mph

### DAILY SNAPSHOT

06:00 AM	09:00 AM	12:00 PM	03:00 PM	06:00 PM	09:00 PM
partly-cloudy-night 52°F	partly-cloudy-day 53°F	clear-day 58°F	clear-day 60°F	clear-night 51°F	clear-night 47°F

### OBSERVED WEATHER CONDITIONS

No.	Weather Delay	Sky	Temp	Average	Precipitation	Wind	Ground/Sea
1	No	Clear	Mild	53	0	Light Wind	Wet/Muddy

### MANPOWER LOG

65 Workers | 598.0 Man Hours

No.	Contact/Company	Cost Code	Workers	# Hours	Man Hours	Location
1	A&B Electric Co., Inc.		13	10.0	130.0	Site
<b>Notes:</b> Dig excavation for temporary power conduits to Building in section "A", Install conduits and backfill. Start rough in of Electrical conduits in stairwell "A". Backfill and test duct bank in area "B".						
2	Bayside Structures, LLC		5	8.0	40.0	Site
<b>Notes:</b> Completed forming connector GB. Started lay out for rebar. Started tying wall dowels in connector GB.						
3	Caddell Construction Co. (DE), LLC		8	10.0	80.0	Site
<b>Notes:</b> WGI/Caddell supervision, quality control and safety onsite.						
4	Ed Emmons Steel Erectors, Inc.		8	8.0	64.0	Site>D
<b>Notes:</b> Fixed beams per RFI #39 Cut in closures at ends and side Began stud installation All short studs complete on line 28 to 32.9						

**MANPOWER LOG**

**65 Workers | 598.0 Man Hours**

No.	Contact/Company	Cost Code	Workers	# Hours	Man Hours	Location
5	Nash Plumbing and Mechanical, LLC		10	8.0	80.0	Site>A
<b>Notes:</b> Partial underground completed, tested and back-filled						
6	Tindall Corporation		20	10.0	200.0	Site>A
<b>Notes:</b> **Erecting in area C **Grouting and welding **Patching in area C **Crane moves outside of area C footprint						
7	Larry M. Jacobs & Associates, Inc.		1	4.0	4.0	Site
<b>Notes:</b> Performed density test in Area A and B						
			<b>65</b>		<b>598.0</b>	


**Manpower Log's Attachments:**

1. A&B Electric Co., Inc.




[Daily Construction Report -- 1\\_9\\_19.pdf](#)

2. Bayside Structures, LLC

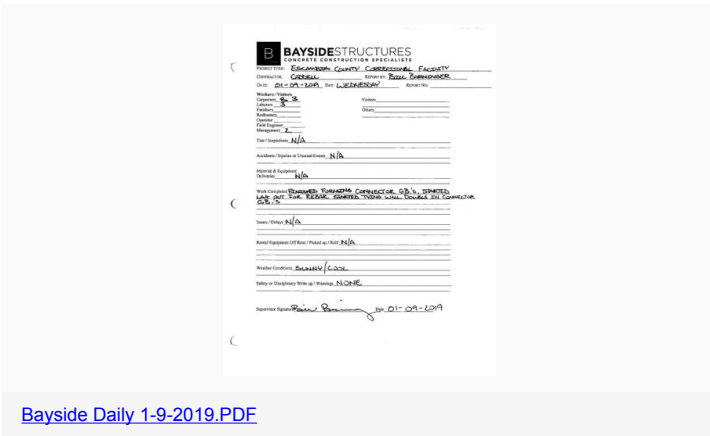

[Bayside Daily 1-9-2019.PDF](#)

4. Ed Emmons Steel Erectors, Inc.



[New Doc 2019-01-09 14.52.10\\_1.pdf](#)

5. Nash Plumbing and Mechanical, LLC

[Nash Daily 1-9-2019.xlsx](#)

6. Tindall Corporation

[Tindall Escambia Daily 1-9-2019.xlsx](#)

**EQUIPMENT LOG**

No.	Equipment Name	Cost Code	Hrs Operating	Hrs Idle	Inspected?	Inspection Time	Location
1	Kobelco Crane CKE2500				No	07:00 AM	Site>C
	<b>Notes:</b>						
2	Genie Lift S125				No	07:00 AM	Site>C
	<b>Notes:</b>						
3	JLG Lift 860SJ				No	07:00 AM	Site>C
	<b>Notes:</b>						
4	JLG Lift 660SJ				No	07:00 AM	Site>C
	<b>Notes:</b>						
5	Sky Power Lift 600AJ				No	07:00 AM	Site>C
	<b>Notes:</b>						
6	Grove Crane AT700D				No	07:00 AM	Site>D
	<b>Notes:</b>						
7	Genie Lift S80				No	07:00 AM	Site>D
	<b>Notes:</b>						
8	JLG Skytrak Telehandler				No	07:00 AM	Site>D
	<b>Notes:</b>						
9	CAT Miniexcavator				No	07:00 AM	Site>A
	<b>Notes:</b>						
10	Genie Lift S85				No	07:00 AM	Site>A
	<b>Notes:</b>						
11	CAT Miniexcavator				No	07:00 AM	Site>B
	<b>Notes:</b>						
12	Bobcat Skidsteer				No	07:00 AM	Site
	<b>Notes:</b>						



## EQUIPMENT LOG

No.	Equipment Name	Cost Code	Hrs Operating	Hrs Idle	Inspected?	Inspection Time	Location
13	Bobcat Miniexcavator				No	07:00 AM	Site
<b>Notes:</b>							
14	Bobcat Telehandler				No	07:00 AM	Site
<b>Notes:</b>							

---

By

---

Date

---

Copies To



## Daily Log: Thursday 1/10/2019

**Daily Log Completed**  
 The Daily Log was completed by Donald Shelton on Mon Jan 14, 2019 at 10:35 am CST.

### WEATHER REPORT

Temperature			Precipitation Since			Humidity				Windspeed		
Low	High	Avg	Midnight	2 Days Ago	3 Days Ago	Low	Avg	High	Dew	Avg	Max	Gust
37°F	58°F	46°F	0.00 in.	0.00 in.	0.00 in.	28%	47%	61%	26°F	7.8 mph	10 mph	20 mph

### DAILY SNAPSHOT

06:00 AM	09:00 AM	12:00 PM	03:00 PM	06:00 PM	09:00 PM
clear-night 38°F	clear-day 44°F	clear-day 54°F	clear-day 59°F	clear-night 50°F	clear-night 45°F

### OBSERVED WEATHER CONDITIONS

No.	Weather Delay	Sky	Temp	Average	Precipitation	Wind	Ground/Sea
1	No	Clear	Cold	46	0	Calm	Dry

### MANPOWER LOG

57 Workers | 533.0 Man Hours

No.	Contact/Company	Cost Code	Workers	# Hours	Man Hours	Location
1	A&B Electric Co., Inc.		16	10.0	160.0	Site
<b>Notes:</b> Working on backfill of two duct banks for temporary power, 3rd lift compaction test complete in section "A" & "B", Build hard Barricade around temporary power panel, Start demo of existing pole lights in Juvenile parking lot. Working on rough in of conduits in stairwell "A". Core drill holes in stairwell "A".						
2	Bayside Structures, LLC		4	8.0	32.0	Site
<b>Notes:</b> Cleaned mud and trash out of GB6 at crossover. tied rebar for crossover GB. Laid out for wall dowels at crossover.						
3	Caddell Construction Co. (DE), LLC		8	10.0	80.0	Site
<b>Notes:</b> WGI/Caddell supervision, quality control and safety onsite.						
4	Ed Emmons Steel Erectors, Inc.		1	8.0	8.0	Site>D
<b>Notes:</b> Completed rework QC checked bolts at seq 2. Patch at column penetrations, Layout and shot studs at south portion pf sequence.						
5	Nash Plumbing and Mechanical, LLC		9	8.0	72.0	Site>D
<b>Notes:</b> Located and Installed inserts for mechanical piping and floor drains at elevation 100.						


**MANPOWER LOG**

57 Workers | 533.0 Man Hours

No.	Contact/Company	Cost Code	Workers	# Hours	Man Hours	Location
6	Tindall Corporation		18	10.0	180.0	Site>C
<b>Notes:</b> **Erecting in area C **Grouting and welding **Patching in area C						
7	Larry M. Jacobs & Associates, Inc.		1	1.0	1.0	Site
<b>Notes:</b> Performed density test in Area A and B						
			<b>57</b>		<b>533.0</b>	


**Manpower Log's Attachments:**

1. A&B Electric Co., Inc.

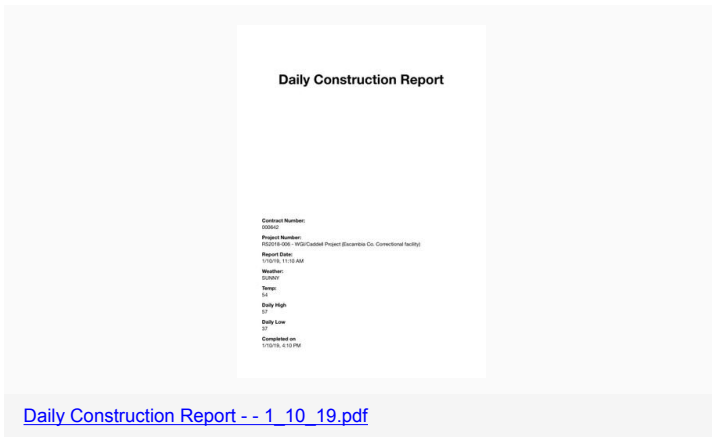


[Daily Construction Report - - 1\\_10\\_19.pdf](#)

2. Bayside Structures, LLC

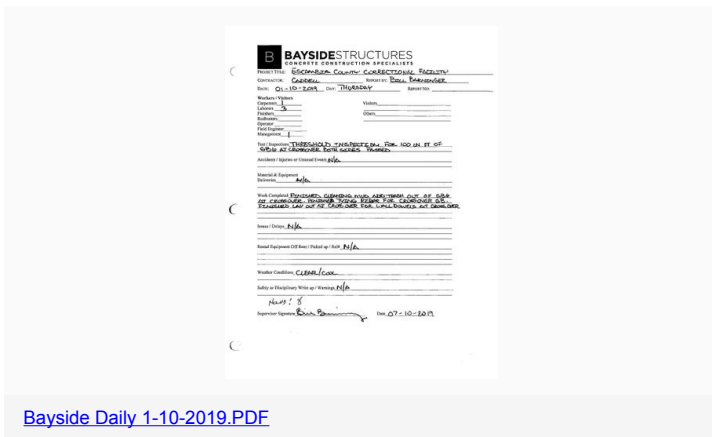


[Bayside Daily 1-10-2019.PDF](#)

4. Ed Emmons Steel Erectors, Inc.

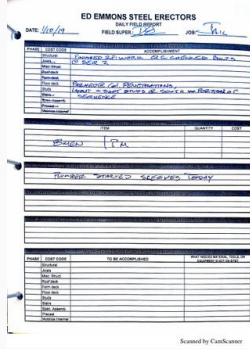

[New Doc 2019-01-10 15.00.27\\_1.pdf](#)

5. Nash Plumbing and Mechanical, LLC



[Nash Daily 1-10-2019.PDF](#)

6. Tindall Corporation

[Tindall Escambia Daily 1-10-2019.xlsx](#)

**EQUIPMENT LOG**

No.	Equipment Name	Cost Code	Hrs Operating	Hrs Idle	Inspected?	Inspection Time	Location
1	Kobelco Crane CKE2500				No	07:00 AM	Site>C
	<b>Notes:</b>						
2	Genie Lift S85				No	07:00 AM	Site>C
	<b>Notes:</b>						
3	JLG Lift 860SJ				No	07:00 AM	Site>C
	<b>Notes:</b>						
4	JLG Lift 660SJ				No	07:00 AM	Site>C
	<b>Notes:</b>						
5	Sky Power Lift 600AJ				No	07:00 AM	Site>C
	<b>Notes:</b>						
6	Grove Crane AT700D				No	07:00 AM	Site>D
	<b>Notes:</b>						
7	Genie Lift S80				No	07:00 AM	Site>D
	<b>Notes:</b>						

## EQUIPMENT LOG

No.	Equipment Name	Cost Code	Hrs Operating	Hrs Idle	Inspected?	Inspection Time	Location
8	JLG Skytrak Telehandler				No	07:00 AM	Site>D
	<b>Notes:</b>						
9	Bobcat Miniexcavator				No	07:00 AM	Site
	<b>Notes:</b>						
10	Bobcat Miniexcavator				No	07:00 AM	Site
	<b>Notes:</b>						
11	JLG Skytrak Telehandler				No	07:00 AM	Site
	<b>Notes:</b>						
12	JLG Skytrak Telehandler				No	07:00 AM	Site
	<b>Notes:</b>						

---

By

Date

Copies To



## Daily Log: Friday 1/11/2019

**Daily Log Completed**  
 The Daily Log was completed by Donald Shelton on Mon Jan 14, 2019 at 10:35 am CST.

### WEATHER REPORT

Temperature			Precipitation Since			Humidity				Windspeed		
Low	High	Avg	Midnight	2 Days Ago	3 Days Ago	Low	Avg	High	Dew	Avg	Max	Gust
35°F	58°F	46°F	0.01 in.	0.01 in.	0.01 in.	43%	64%	90%	34°F	5.4 mph	8 mph	11 mph

### DAILY SNAPSHOT

06:00 AM	09:00 AM	12:00 PM	03:00 PM	06:00 PM	09:00 PM
clear-night 36°F	clear-day 45°F	clear-day 55°F	clear-day 59°F	clear-night 51°F	clear-night 48°F

### OBSERVED WEATHER CONDITIONS

No.	Weather Delay	Sky	Temp	Average	Precipitation	Wind	Ground/Sea
1	No	Clear	Cold	46	0	Calm	Dry

### MANPOWER LOG

67 Workers | 618.0 Man Hours

No.	Contact/Company	Cost Code	Workers	# Hours	Man Hours	Location
1	A&B Electric Co., Inc.		14	10.0	140.0	Site
<b>Notes:</b> Working on rough in of stairwell "A" and starting in corridor at column line 4 Thur 14, Working on pole lights in Juvenile parking, Working on temporary power panels.						
2	Bayside Structures, LLC		9	8.0	72.0	Site
<b>Notes:</b> Poured GB6. 100LN FT Both sides at crossover.						
3	Caddell Construction Co. (DE), LLC		8	10.0	80.0	Site
<b>Notes:</b> WGI/Caddell supervision, quality control and safety onsite.						
4	Ed Emmons Steel Erectors, Inc.		8	8.0	64.0	Site>D
<b>Notes:</b> Continued closures and weld outs Continued stud installation						
5	Nash Plumbing and Mechanical, LLC		9	8.0	72.0	Site>D
<b>Notes:</b> Located and Installed inserts for mechanical piping and floor drains at elevation 100.						

**MANPOWER LOG**

67 Workers | 618.0 Man Hours

No.	Contact/Company	Cost Code	Workers	# Hours	Man Hours	Location
6	Tindall Corporation		19	10.0	190.0	Site>C
<b>Notes:</b>						
**Erecting in area C						
**Grouting and welding						
**Patching in area C						
			<b>67</b>		<b>618.0</b>	

**Manpower Log's Attachments:**

1. A&B Electric Co., Inc.




[Daily Construction Report -- 1\\_11\\_19.pdf](#)

2. Bayside Structures, LLC



[Baayside Daily 1-11-2019.PDF](#)

4. Ed Emmons Steel Erectors, Inc.



[New Doc 2019-01-11 14.56.28\\_1.pdf](#)

5. Nash Plumbing and Mechanical, LLC

[1-11-2019.xlsx](#)

6. Tindall Corporation

[Tindall Escambia Daily 1-11-2019.xlsx](#)

**EQUIPMENT LOG**

No.	Equipment Name	Cost Code	Hrs Operating	Hrs Idle	Inspected?	Inspection Time	Location
1	Kobelco Crane CKE2500				No	07:00 AM	Site>C
	<b>Notes:</b>						
2	Genie Lift S125				No	07:00 AM	Site>C
	<b>Notes:</b>						
3	JLG Lift 860SJ				No	07:00 AM	Site>C
	<b>Notes:</b>						
4	JLG Lift 660SJ				No	07:00 AM	Site>C
	<b>Notes:</b>						
5	JLG Lift 660SJ				No	07:00 AM	Site>C
	<b>Notes:</b>						
6	Sky Power Lift 600AJ				No	07:00 AM	Site>C
	<b>Notes:</b>						
7	Genie Lift S80				No	07:00 AM	Site>D
	<b>Notes:</b>						
8	JLG Skytrak Telehandler				No	07:00 AM	Site>D
	<b>Notes:</b>						
9	Bobcat Miniexcavator				No	07:00 AM	Site
	<b>Notes:</b>						
10	Komatsu 320 PT Loader				No	07:00 AM	Site
	<b>Notes:</b>						
11	JLG Skytrak Telehandler				No	07:00 AM	Site
	<b>Notes:</b>						
12	Cat Telehandler				No	07:00 AM	Site
	<b>Notes:</b>						



## EQUIPMENT LOG

No.	Equipment Name	Cost Code	Hrs Operating	Hrs Idle	Inspected?	Inspection Time	Location
13	John Deere 700 Dozer				No	07:00 AM	Site

Notes:

## INSPECTION LOG

No.	Start Time	End Time	Inspection Type	Inspecting Entity	Inspector Name	Location	Area
1	09:00 AM	01:00 PM	Third Party	Mott MacDonald	Mike Tugwell	Site	

Comments: Threshold inspection for seq. 2 in Area D

By \_\_\_\_\_

Date \_\_\_\_\_

Copies To \_\_\_\_\_



## Daily Log: Saturday 1/12/2019

**Daily Log Completed**  
 The Daily Log was completed by Donald Shelton on Mon Jan 14, 2019 at 09:44 am CST.

### WEATHER REPORT

Temperature			Precipitation Since			Humidity				Windspeed		
Low	High	Avg	Midnight	2 Days Ago	3 Days Ago	Low	Avg	High	Dew	Avg	Max	Gust
43°F	66°F	57°F	0.02 in.	0.02 in.	0.02 in.	75%	83%	95%	52°F	7.2 mph	12 mph	17 mph

### DAILY SNAPSHOT

06:00 AM	09:00 AM	12:00 PM	03:00 PM	06:00 PM	09:00 PM
clear-night 48°F	partly-cloudy-day 55°F	partly-cloudy-day 63°F	cloudy 66°F	cloudy 66°F	cloudy 66°F

### OBSERVED WEATHER CONDITIONS

No.	Weather Delay	Sky	Temp	Average	Precipitation	Wind	Ground/Sea
1	No	Cloudy	Mild	57	0	Calm	Dry

### MANPOWER LOG

20 Workers | 200.0 Man Hours

No.	Contact/Company	Cost Code	Workers	# Hours	Man Hours	Location
1	Caddell Construction Co. (DE), LLC		1	10.0	10.0	Site
<b>Notes:</b> WGI/Caddell supervision, quality control and safety onsite.						
2	Tindall Corporation		19	10.0	190.0	Site>D
<b>Notes:</b> **Erecting in area C **Grouting and welding **Patching in area C						
			<b>20</b>	<b>200.0</b>		

2. Tindall Corporation

[Tindall Escambia Daily 1-12-2019 .xlsx](#)

### EQUIPMENT LOG

No.	Equipment Name	Cost Code	Hrs Operating	Hrs Idle	Inspected?	Inspection Time	Location
1	Kobelco Crane CKE2500				No	07:00 AM	Site>D
<b>Notes:</b>							
2	Genie Lift S85				No	07:00 AM	Site>D
<b>Notes:</b>							

## EQUIPMENT LOG

No.	Equipment Name	Cost Code	Hrs Operating	Hrs Idle	Inspected?	Inspection Time	Location
3	JLG Lift 860SJ				No	07:00 AM	Site>D
	<b>Notes:</b>						
4	JLG Lift 660SJ				No	07:00 AM	Site>D
	<b>Notes:</b>						
5	Sky Power Lift 600AJ				No	07:00 AM	Site>D
	<b>Notes:</b>						

---

By

---

Date

---

Copies To



Whitesell Green / Caddell, a Joint Venture  
 2700 Lagoon Park Drive  
 Montgomery, Alabama 36109  
 P: (334) 272-7723  
 F: (334) 394-0193

Project: 1054 - Escambia County Correctional  
**Facility**  
 3080 N. Pace Boulevard  
 Pensacola, Florida 32501

## Daily Log: Sunday 1/13/2019

### WEATHER REPORT

Temperature			Precipitation Since			Humidity				Windspeed		
Low	High	Avg	Midnight	2 Days Ago	3 Days Ago	Low	Avg	High	Dew	Avg	Max	Gust
49°F	63°F	55°F	0.00 in.	0.02 in.	0.02 in.	64%	80%	97%	49°F	7.3 mph	10 mph	18 mph

### DAILY SNAPSHOT

06:00 AM	09:00 AM	12:00 PM	03:00 PM	06:00 PM	09:00 PM
partly-cloudy-night 57°F	partly-cloudy-day 58°F	partly-cloudy-day 55°F	partly-cloudy-day 53°F	cloudy 51°F	cloudy 50°F

### OBSERVED WEATHER CONDITIONS

No.	Weather Delay	Sky	Temp	Average	Precipitation	Wind	Ground/Sea
1	No						

By \_\_\_\_\_

Date \_\_\_\_\_

Copies To \_\_\_\_\_



## Daily Log: Monday 1/14/2019

**Daily Log Completed**  
 The Daily Log was completed by Donald Shelton on Mon Jan 21, 2019 at 09:42 am CST.

### WEATHER REPORT

Temperature			Precipitation Since			Humidity				Windspeed		
Low	High	Avg	Midnight	2 Days Ago	3 Days Ago	Low	Avg	High	Dew	Avg	Max	Gust
42°F	48°F	44°F	0.00 in.	0.00 in.	0.02 in.	72%	77%	80%	37°F	7.2 mph	8 mph	15 mph

### DAILY SNAPSHOT

06:00 AM	09:00 AM	12:00 PM	03:00 PM	06:00 PM	09:00 PM
cloudy 45°F	cloudy 44°F	cloudy 43°F	cloudy 44°F	cloudy 43°F	cloudy 43°F

### OBSERVED WEATHER CONDITIONS

No.	Weather Delay	Sky	Temp	Average	Precipitation	Wind	Ground/Sea
1	No	Overcast	Cold	44	0	Light Wind	Dry

### MANPOWER LOG

62 Workers | 558.0 Man Hours

No.	Contact/Company	Cost Code	Workers	# Hours	Man Hours	Location
1	A&B Electric Co., Inc.		13	10.0	130.0	Site
<b>Notes:</b> Working on temporary power panels, Working on precast walls in beds, Working on rough in of corridor column line 4-14.						
2	Bayside Structures, LLC		9	8.0	72.0	Site
<b>Notes:</b> Removed forms from GB6 north and south at crossover. Backfilled at GB6 north and south at crossover. Laid out stem walls and pedestals at GB6 north and south. Started installing 2x4 to angle for embeds in Area D second pour at elevation 100.						
3	Caddell Construction Co. (DE), LLC		1	8.0	8.0	Site
<b>Notes:</b> WGI/Caddell supervision, quality control and safety onsite.						
4	Ed Emmons Steel Erectors, Inc.		7	8.0	56.0	Building>D
<b>Notes:</b> 90% detail out of seq 2 elevation 100						
5	Nash Plumbing and Mechanical, LLC		10	8.0	80.0	Building>D
<b>Notes:</b> Lay out sleeves and inserts Installed sleeves, inserts, and floor drains						

**MANPOWER LOG**

**62 Workers | 558.0 Man Hours**

No.	Contact/Company	Cost Code	Workers	# Hours	Man Hours	Location
6	Tindall Corporation		18	10.0	180.0	Building>C
<b>Notes:</b> **Erecting in area C **Grouting and welding						
7	EAA Site Contractors LLC		4	8.0	32.0	Site
<b>Notes:</b> Total man hours 38. EAA started demo on parking lot (future retention pond ). Began clearing trees and started removing and stacking wheel stops.						
			<b>62</b>		<b>558.0</b>	


**Manpower Log's Attachments:**

1. A&B Electric Co., Inc.




[Daily Construction Report - - 1\\_14\\_19.pdf](#)

2. Bayside Structures, LLC

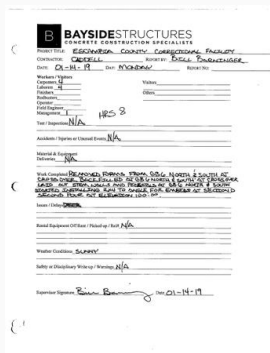

[Bayside Daily 1-14-2019.PDF](#)

4. Ed Emmons Steel Erectors, Inc.



[New Doc 2019-01-14 15.57.43\\_1.pdf](#)

5. Nash Plumbing and Mechanical, LLC

[Nash Daily 1-14-2019.xlsx](#)

6. Tindall Corporation

[Tindall Escambia Daily 1-14-2019.xlsx](#)

**EQUIPMENT LOG**

No.	Equipment Name	Cost Code	Hrs Operating	Hrs Idle	Inspected?	Inspection Time	Location
1	Kobelco Crane CKE2500				No	07:00 AM	Building>C
	<b>Notes:</b>						
2	Genie Lift S85				No	07:00 AM	Building>C
	<b>Notes:</b>						
3	JLG Lift 860SJ				No	07:00 AM	Building>C
	<b>Notes:</b>						
4	JLG Lift 660SJ				No	07:00 AM	Building>C
	<b>Notes:</b>						
5	JLG Skytrak Telehandler				No	07:00 AM	Building>D
	<b>Notes:</b>						
6	Cat Skidsteer				No	07:00 AM	Building
	<b>Notes:</b>						
7	Volvo 330 Excavator				No	07:00 AM	Site>Stormwater Pond
	<b>Notes:</b>						
8	Komatsu 320 PT Loader				No	07:00 AM	Site>Stormwater Pond
	<b>Notes:</b>						
9	Bobcat Miniexcavator				No	07:00 AM	Site
	<b>Notes:</b>						
10	Cat Telehandler				No	07:00 AM	Site
	<b>Notes:</b>						

By \_\_\_\_\_

Date \_\_\_\_\_

Copies To \_\_\_\_\_



## Daily Log: Tuesday 1/15/2019

**Daily Log Completed**  
 The Daily Log was completed by Donald Shelton on Mon Jan 21, 2019 at 10:44 am CST.

### WEATHER REPORT

Temperature			Precipitation Since			Humidity				Windspeed		
Low	High	Avg	Midnight	2 Days Ago	3 Days Ago	Low	Avg	High	Dew	Avg	Max	Gust
39°F	52°F	44°F	0.00 in.	0.00 in.	0.00 in.	55%	75%	90%	36°F	5.5 mph	8 mph	13 mph

### DAILY SNAPSHOT

06:00 AM	09:00 AM	12:00 PM	03:00 PM	06:00 PM	09:00 PM
cloudy 41°F	cloudy 41°F	partly-cloudy-day 48°F	partly-cloudy-day 52°F	partly-cloudy-night 45°F	partly-cloudy-night 42°F

### OBSERVED WEATHER CONDITIONS

No.	Weather Delay	Sky	Temp	Average	Precipitation	Wind	Ground/Sea
1	No	Cloudy	Cold	44	0	Light Wind	Dry

### MANPOWER LOG

77 Workers | 701.0 Man Hours

No.	Contact/Company	Cost Code	Workers	# Hours	Man Hours	Location
1	A&B Electric Co., Inc.		14	10.0	140.0	Site
<b>Notes:</b> Working on embeds in precast walls, Working on rough in of corridor, Working on temporary power panels.						
2	Bayside Structures, LLC		10	9.0	90.0	Building>D
<b>Notes:</b> Grouting column base Area D. Placed WWM on deck elevation 100 in Area D. Cleaned work area.						
3	Caddell Test Subcontractor		9	10.0	90.0	Site
<b>Notes:</b> WGI/Caddell supervision, quality control and safety onsite.						
4	Ed Emmons Steel Erectors, Inc.		9	8.0	72.0	Building>D
<b>Notes:</b> Completed erection of deck, studs, and most of columns (3 remaining) in Area D at elevation 100.						
5	Larry M. Jacobs & Associates, Inc.		1	1.0	1.0	Building
<b>Notes:</b> Performed 3 Density Test in Corridor.						
6	Nash Plumbing and Mechanical, LLC		11	8.0	88.0	Building>D
<b>Notes:</b> Installed sleeves and inserts at elevation 100.						




**MANPOWER LOG**

**77 Workers | 701.0 Man Hours**

No.	Contact/Company	Cost Code	Workers	# Hours	Man Hours	Location
7	Tindall Corporation		18	10.0	180.0	Building>C
<b>Notes:</b> **Erecting in area C **Grouting and welding **Crane moving to area D late in the day.						
8	EAA Site Contractors LLC		5	8.0	40.0	Site
<b>Notes:</b> Total man hours 43. EAA continued demo on parking lot / future retention pond. All wheel stops have been removed from asphalt. Wheel stops are being loaded on trailer to be removed from site. Continued clearing of trees and started removing asphalt. All punch list items for JJC parking lot has been completed.						
			<b>77</b>		<b>701.0</b>	


**Manpower Log's Attachments:**

- 1. A&B Electric Co., Inc.

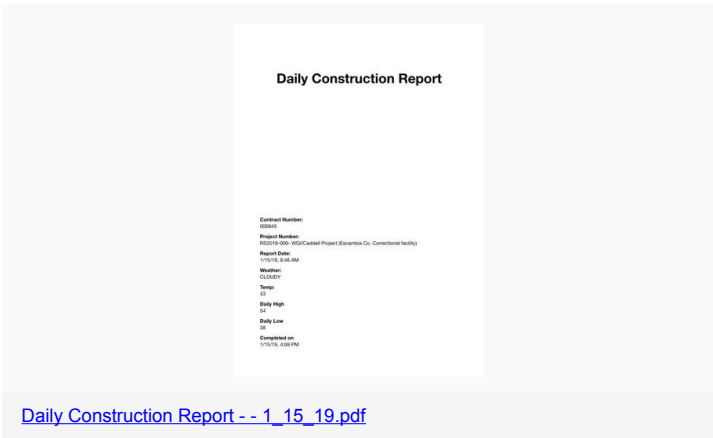


[Daily Construction Report -- 1\\_15\\_19.pdf](#)

- 2. Bayside Structures, LLC

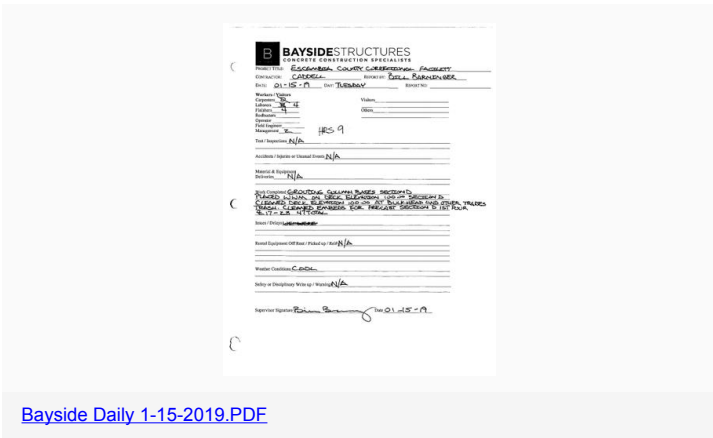

[Bayside Daily 1-15-2019.PDF](#)

4. Ed Emmons Steel Erectors, Inc.

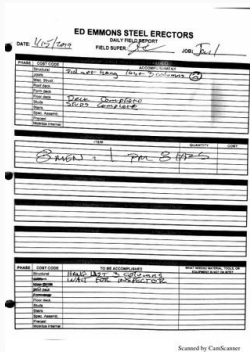

[New Doc 2019-01-15 15.22.05\\_1.pdf](#)

6. Nash Plumbing and Mechanical, LLC

[Nash daily 1-15-2019.xlsx](#)

7. Tindall Corporation

[Tindall Escambia Daily 1-15-2019.xlsx](#)

**EQUIPMENT LOG**

No.	Equipment Name	Cost Code	Hrs Operating	Hrs Idle	Inspected?	Inspection Time	Location
1	Genie Lift S125				No	07:00 AM	Building>A
	<b>Notes:</b>						
2	Kobelco Crane CKE2500				No	07:00 AM	Building>C
	<b>Notes:</b>						
3	Genie Lift S85				No	07:00 AM	Building>C
	<b>Notes:</b>						
4	JLG Lift 860SJ				No	07:00 AM	Building>C
	<b>Notes:</b>						
5	JLG Lift 660SJ				No	07:00 AM	Building>C
	<b>Notes:</b>						
6	JLG Lift 660SJ				No	07:00 AM	Building>C
	<b>Notes:</b>						
7	Grove Crane AT700D				No	07:00 AM	Building>D
	<b>Notes:</b>						
8	Genie Lift S80				No	07:00 AM	Building>D
	<b>Notes:</b>						
9	JLG Skytrak Telehandler				No	07:00 AM	Building>D
	<b>Notes:</b>						
10	Cat Skidsteer				No	07:00 AM	Site
	<b>Notes:</b>						
11	Bobcat Miniexcavator				No	07:00 AM	Site
	<b>Notes:</b>						
12	Volvo 330 Excavator				No	07:00 AM	Site>Stormwater Pond
	<b>Notes:</b>						

## EQUIPMENT LOG

No.	Equipment Name	Cost Code	Hrs Operating	Hrs Idle	Inspected?	Inspection Time	Location
13	Komatsu 320 PT Loader				No	07:00 AM	Site>Stormwater Pond
<b>Notes:</b>							
14	Cat Telehandler				No	07:00 AM	Site
<b>Notes:</b>							
15	John Deere 700 Dozer				No	07:00 AM	Site
<b>Notes:</b>							
16	JLG Skytrak Telehandler				No	07:00 AM	Site
<b>Notes:</b>							

## PHOTOS



[20190115\\_145221.jpg](#)

Project #1054. 1st Precast in Area D



[20190115\\_145544.jpg](#)

Project #1054. 1st Precast in Area D



[20190115\\_151358.jpg](#)

Project #1054. 1st Precast in Area D



[20190115\\_151602.jpg](#)

Project #1054. 1st Precast in Area D



[20190115\\_151749.jpg](#)

Project #1054. 1st Precast in Area D



[IMG\\_0540.jpg](#)

Project #1054. 1st Precast in Area D

---

By

Date

Copies To



## Daily Log: Wednesday 1/16/2019

**Daily Log Completed**  
 The Daily Log was completed by Donald Shelton on Mon Jan 21, 2019 at 09:41 am CST.

### WEATHER REPORT

Temperature			Precipitation Since			Humidity				Windspeed		
Low	High	Avg	Midnight	2 Days Ago	3 Days Ago	Low	Avg	High	Dew	Avg	Max	Gust
38°F	59°F	46°F	0.00 in.	0.00 in.	0.00 in.	42%	75%	100%	37°F	2.6 mph	5 mph	7 mph

### DAILY SNAPSHOT

06:00 AM	09:00 AM	12:00 PM	03:00 PM	06:00 PM	09:00 PM
partly-cloudy-night 41°F	clear-day 46°F	clear-day 54°F	clear-day 59°F	clear-night 49°F	clear-night 42°F

### OBSERVED WEATHER CONDITIONS

No.	Weather Delay	Sky	Temp	Average	Precipitation	Wind	Ground/Sea
1	No	Cloudy	Cold	47	0	Calm	Dry

### MANPOWER LOG

73 Workers | 653.0 Man Hours

No.	Contact/Company	Cost Code	Workers	# Hours	Man Hours	Location
1	A&B Electric Co., Inc.		12	10.0	120.0	Building
<b>Notes:</b> Working on embeds on precast walls, Working on temporary power panels, Working on rough in of corridor between columns 4-14.						
2	Bayside Structures, LLC		4	8.0	32.0	Building>D
<b>Notes:</b> Worked on rebar for deck pour section D elevation 100. While checking grades for embeds in Area D elevation 100. In the corner of center line 28 and M.						
3	Caddell Construction Co. (DE), LLC		9	10.0	90.0	Building
<b>Notes:</b> WGI/Caddell supervision, quality control and safety onsite.						
4	Ed Emmons Steel Erectors, Inc.		9	8.0	72.0	Building>D
<b>Notes:</b> Studs, deck, and bolts inspected and passed contingent upon deck to be welded at 2 intermediate beams at HSS columns- South Bay- Will be welded an d/or screwed tomorrow am.						
5	Larry M. Jacobs & Associates, Inc.		2	3.5	7.0	Building
<b>Notes:</b> Performed density test in corridor Threshold inspection in Area D 2nd sequence at elevation 100.						

**MANPOWER LOG**

73 Workers | 653.0 Man Hours

No.	Contact/Company	Cost Code	Workers	# Hours	Man Hours	Location
6	Nash Plumbing and Mechanical, LLC		12	8.0	96.0	Building>D
<b>Notes:</b> Installed sleeves and inserts for 2nd sequence pour in Area D						
7	Tindall Corporation		18	10.0	180.0	Building>D
<b>Notes:</b> **Erecting in area D on elevation 100' slab **Grouting and welding 188.5 Total Man Hours						
8	EAA Site Contractors LLC		7	8.0	56.0	Site
<b>Notes:</b> Total man hours 48. EAA continued demo on parking lot / future retention pond. All wheel stops have been removed from site. All light pole bases are out of the ground. Continued tree and asphalt removal						
			<b>73</b>		<b>653.0</b>	


**Manpower Log's Attachments:**

1. A&B Electric Co., Inc.




[Daily Construction Report -- 1\\_16\\_19.pdf](#)

2. Bayside Structures, LLC

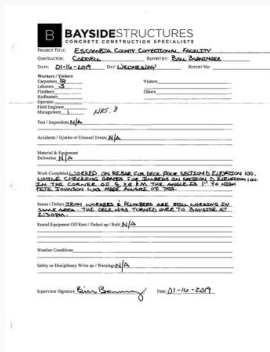

[Bayside Daily 1-16-2019.PDF](#)

4. Ed Emmons Steel Erectors, Inc.



[New Doc 2019-01-16 15.10.39\\_1.pdf](#)

6. Nash Plumbing and Mechanical, LLC

[Nash Daily 1-16-2019.xlsx](#)

7. Tindall Corporation

[Tindall Escambia Daily 1-16-2019 .xlsx](#)

**EQUIPMENT LOG**

No.	Equipment Name	Cost Code	Hrs Operating	Hrs Idle	Inspected?	Inspection Time	Location
1	Genie Lift S125				No	07:00 AM	Site>A
	<b>Notes:</b>						
2	Bobcat Miniexcavator				No	07:00 AM	Site>B
	<b>Notes:</b>						
3	Kobelco Crane CKE2500				No	07:00 AM	Building>C
	<b>Notes:</b>						
4	JLG Lift 860SJ				No	07:00 AM	Building>C
	<b>Notes:</b>						
5	JLG Lift 660SJ				No	07:00 AM	Building>C
	<b>Notes:</b>						
6	JLG Lift 660SJ				No	07:00 AM	Building>C
	<b>Notes:</b>						
7	Genie Lift S85				No	07:00 AM	Building>C
	<b>Notes:</b>						
8	Grove Crane AT700D				No	07:00 AM	Building>D
	<b>Notes:</b>						
9	Genie Lift S80				No	07:00 AM	Building>D
	<b>Notes:</b>						
10	JLG Skytrak Telehandler				No	07:00 AM	Building>D
	<b>Notes:</b>						
11	JLG Skytrak Telehandler				No	07:00 AM	Site
	<b>Notes:</b>						
12	JLG Skytrak Telehandler				No	07:00 AM	Site
	<b>Notes:</b>						

## EQUIPMENT LOG

No.	Equipment Name	Cost Code	Hrs Operating	Hrs Idle	Inspected?	Inspection Time	Location
13	Volvo 330 Excavator				No	07:00 AM	Site>Stormwater Pond
<b>Notes:</b>							
14	Komatsu 320 PT Loader				No	07:00 AM	Site>Stormwater Pond
<b>Notes:</b>							
15	Komatsu 78MR Excavator				No	07:00 AM	Site>Stormwater Pond
<b>Notes:</b>							

## INSPECTION LOG

No.	Start Time	End Time	Inspection Type	Inspecting Entity	Inspector Name	Location	Area
1	11:00 AM	02:00 PM	Third Party	Mott MacDonald	Mike Tugwell	Building>D	D
<b>Comments:</b> Threshold inspection for Area D sequence 2 at elevation 100.							

---

By

---

Date

---

Copies To





## Daily Log: Thursday 1/17/2019

**Daily Log Completed**  
 The Daily Log was completed by Donald Shelton on Mon Jan 21, 2019 at 09:41 am CST.

### WEATHER REPORT

Temperature			Precipitation Since			Humidity				Windspeed		
Low	High	Avg	Midnight	2 Days Ago	3 Days Ago	Low	Avg	High	Dew	Avg	Max	Gust
36°F	62°F	51°F	0.00 in.	0.00 in.	0.00 in.	65%	86%	100%	47°F	2.7 mph	6 mph	8 mph

### DAILY SNAPSHOT

06:00 AM	09:00 AM	12:00 PM	03:00 PM	06:00 PM	09:00 PM
clear-night 39°F	partly-cloudy-day 50°F	partly-cloudy-day 62°F	cloudy 62°F	cloudy 58°F	cloudy 57°F

### OBSERVED WEATHER CONDITIONS

No.	Weather Delay	Sky	Temp	Average	Precipitation	Wind	Ground/Sea
1	No	Cloudy	Mild	51	0	Light Wind	Dry

### MANPOWER LOG

82 Workers | 742.5 Man Hours

No.	Contact/Company	Cost Code	Workers	# Hours	Man Hours	Location
1	A&B Electric Co., Inc.		14	10.0	140.0	Building>D
<b>Notes:</b> Working on temporary panels, Working on embeds in precast and pull strings.						
2	Bayside Structures, LLC		14	9.0	126.0	Building>D
<b>Notes:</b> Continued working on WWM and Deck rebar worked on embed lay out installation.						
3	Caddell Construction Co. (DE), LLC		9	10.0	90.0	Site
<b>Notes:</b> WGI/Caddell supervision, quality control and safety onsite.						
4	Ed Emmons Steel Erectors, Inc.		9	7.5	67.5	Building>D
<b>Notes:</b> Completed 100% deck in Area D elevation 100.						
5	Larry M. Jacobs & Associates, Inc.		1	1.0	1.0	Building
<b>Notes:</b> Conducted Density Test in Corridor						
6	Nash Plumbing and Mechanical, LLC		10	8.0	80.0	Building>D
<b>Notes:</b> Install sleeves, insert, and floor drains in Area D sequence 2 elevation 100.						

**MANPOWER LOG**

**82 Workers | 742.5 Man Hours**

No.	Contact/Company	Cost Code	Workers	# Hours	Man Hours	Location
7	Tindall Corporation		19	10.0	190.0	Building>D
<b>Notes:</b> **Crane moves to area A awaiting elevated slab in D until week of 1/28/19 **Grouting and welding in area D first portion						
8	EAA Site Contractors LLC		6	8.0	48.0	Site
<b>Notes:</b> Total man hours 45. Continued tree and asphalt removal. Installed silt fence along St Mary and construction entrance. Continued hauling asphalt from site. Uncovered box S15 and created drain for site water control						
			<b>82</b>		<b>742.5</b>	


**Manpower Log's Attachments:**

1. A&B Electric Co., Inc.




[Daily Construction Report - - 1\\_17\\_19.pdf](#)

2. Bayside Structures, LLC

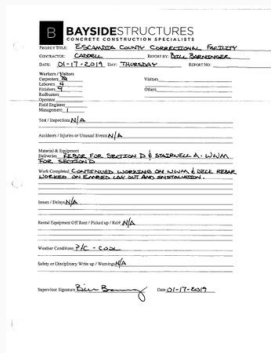

[Bayside Dasily 1-17-2019.PDF](#)

4. Ed Emmons Steel Erectors, Inc.

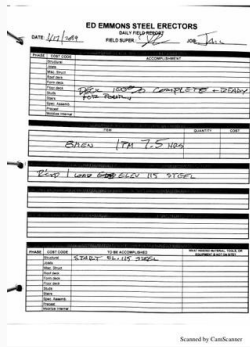

[New Doc 2019-01-17 14.39.14\\_1.pdf](#)

6. Nash Plumbing and Mechanical, LLC

[Nash Daily 1-17-2019.xlsx](#)

7. Tindall Corporation

[Tindall Escambia Daily 1-17-2019.xlsx](#)

**EQUIPMENT LOG**

No.	Equipment Name	Cost Code	Hrs Operating	Hrs Idle	Inspected?	Inspection Time	Location
1	Genie Lift S125				No	07:00 AM	Building>C
	<b>Notes:</b>						
2	Grove Crane AT700D				No	07:00 AM	Building>D
	<b>Notes:</b>						
3	Genie Lift S80				No	07:00 AM	Building>D
	<b>Notes:</b>						
4	JLG Skytrak Telehandler				No	07:00 AM	Site
	<b>Notes:</b>						
5	JLG Skytrak Telehandler				No	07:00 AM	Site
	<b>Notes:</b>						
6	Cat Telehandler				No	07:00 AM	Site
	<b>Notes:</b>						
7	Volvo 330 Excavator				No	07:00 AM	Site>Stormwater Pond
	<b>Notes:</b>						
8	Komatsu 320 PT Loader				No	07:00 AM	Site>Stormwater Pond
	<b>Notes:</b>						
9	John Deere 750 Dozer				No	07:00 AM	Site>Stormwater Pond
	<b>Notes:</b>						
10	Cat Skidsteer				No	07:00 AM	Building
	<b>Notes:</b>						

By \_\_\_\_\_

Date \_\_\_\_\_

Copies To \_\_\_\_\_



## Daily Log: Friday 1/18/2019

**Daily Log Completed**  
 The Daily Log was completed by Donald Shelton on Mon Jan 21, 2019 at 10:40 am CST.

### WEATHER REPORT

Temperature			Precipitation Since			Humidity				Windspeed		
Low	High	Avg	Midnight	2 Days Ago	3 Days Ago	Low	Avg	High	Dew	Avg	Max	Gust
57°F	66°F	61°F	0.01 in.	0.01 in.	0.01 in.	74%	90%	100%	58°F	5.2 mph	7 mph	14 mph

### DAILY SNAPSHOT

06:00 AM	09:00 AM	12:00 PM	03:00 PM	06:00 PM	09:00 PM
cloudy 61°F	cloudy 61°F	partly-cloudy-day 66°F	partly-cloudy-day 66°F	partly-cloudy-night 60°F	partly-cloudy-night 57°F

### OBSERVED WEATHER CONDITIONS

No.	Weather Delay	Sky	Temp	Average	Precipitation	Wind	Ground/Sea
1	No	Cloudy	Mild	61	0	Light Wind	Dry


### MANPOWER LOG

52 Workers | 474.0 Man Hours

No.	Contact/Company	Cost Code	Workers	# Hours	Man Hours	Location
1	A&B Electric Co., Inc.		14	10.0	140.0	Building
<b>Notes:</b> Working on embeds in precast column line 4 Thur 50, Rough in conduits in corridor from column line 50 - 15.2						
2	Bayside Structures, LLC		12	9.0	108.0	Building>D
<b>Notes:</b> Finished form work in Area D 2nd pour. Finished WWM and rebar in Area D.						
3	Caddell Construction Co. (DE), LLC		9	10.0	90.0	Site
<b>Notes:</b> WGI/Caddell supervision, quality control and safety onsite.						
4	Ed Emmons Steel Erectors, Inc.		8	8.0	64.0	Building>D
<b>Notes:</b> Hung elevation 115 steel from G.7 to G, 48 to 32.9 line. Installed deck support angle at same location.						
5	Nash Plumbing and Mechanical, LLC		9	8.0	72.0	Building>D
<b>Notes:</b> Installed sleeves, inserts, and floor drains for 2nd concrete pour in Area D at elevation 100.						
			<b>52</b>		<b>474.0</b>	


Manpower Log's Attachments:

1. A&B Electric Co., Inc.

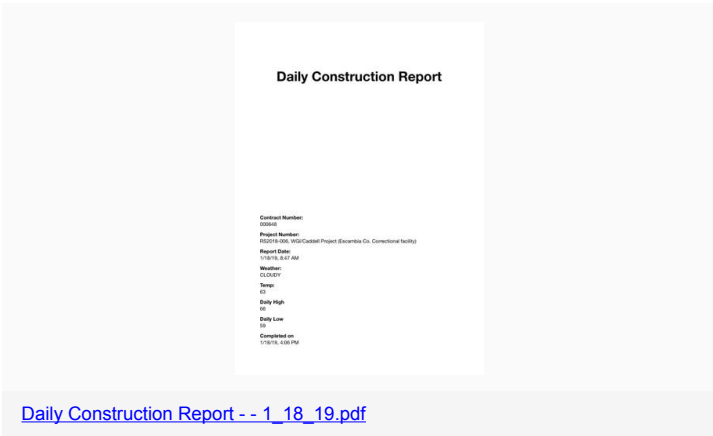


[Daily Construction Report - - 1\\_18\\_19.pdf](#)

2. Bayside Structures, LLC

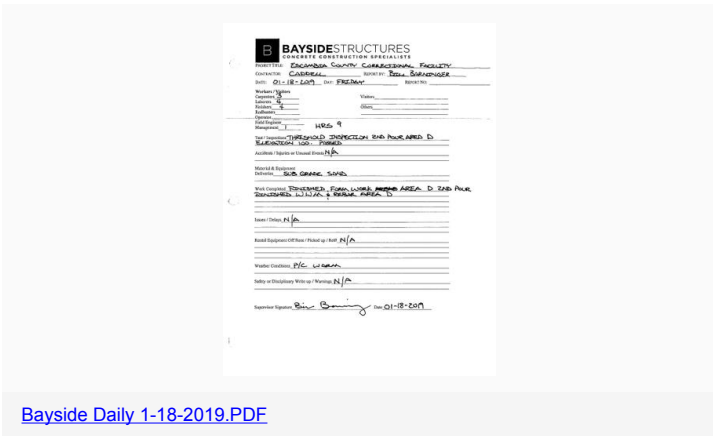

[Bayside Daily 1-18-2019.PDF](#)

4. Ed Emmons Steel Erectors, Inc.

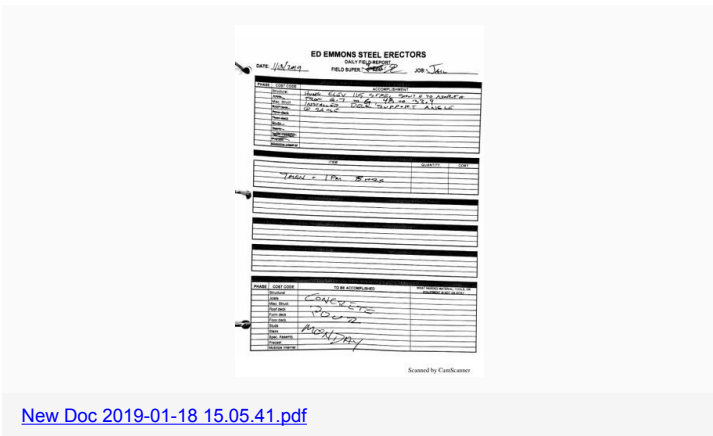

[New Doc 2019-01-18 15.05.41.pdf](#)

5. Nash Plumbing and Mechanical, LLC

[Nash Daily 1-18-2019.xlsx](#)

## EQUIPMENT LOG

No.	Equipment Name	Cost Code	Hrs Operating	Hrs Idle	Inspected?	Inspection Time	Location
1	Grove Crane AT700D				No	07:00 AM	Building>D
	<b>Notes:</b>						
2	Genie Lift S80				No	07:00 AM	Building>D
	<b>Notes:</b>						
3	Cat Skidsteer				No	07:00 AM	Building
	<b>Notes:</b>						
4	JLG Skytrak Telehandler				No	07:00 AM	Site
	<b>Notes:</b>						
5	JLG Skytrak Telehandler				No	07:00 AM	Site
	<b>Notes:</b>						
6	Cat Telehandler				No	07:00 AM	Site
	<b>Notes:</b>						
7	Volvo 330 Excavator				No	07:00 AM	Site>Stormwater Pond
	<b>Notes:</b>						
8	Komatsu 320 PT Loader				No	07:00 AM	Site>Stormwater Pond
	<b>Notes:</b>						
9	John Deere 750 Dozer				No	07:00 AM	Site>Stormwater Pond
	<b>Notes:</b>						

## INSPECTION LOG

No.	Start Time	End Time	Inspection Type	Inspecting Entity	Inspector Name	Location	Area
1	01:30 PM	03:30 PM	Third Party	Mott MacDonald	Mike Tugwell	Building>D	D
	<b>Comments:</b> Threshold inspection in Area D sequence 2 elevation 100 for 2nd concrete pour.						

## PHOTOS



[20190118\\_084359.jpg](#)

Demo for the Stormwater Pond



[20190118\\_084405.jpg](#)

Demo for the Stormwater Pond



[20190118\\_084424.jpg](#)

Demo for the Stormwater Pond

---

By

Date

Copies To



**Whitesell Green / Caddell, a Joint Venture**  
 2700 Lagoon Park Drive  
 Montgomery, Alabama 36109  
 P: (334) 272-7723  
 F: (334) 394-0193

**Project: 1054 - Escambia County Correctional Facility**  
 3080 N. Pace Boulevard  
 Pensacola, Florida 32501

## Daily Log: Saturday 1/19/2019

**Daily Log Completed**  
 The Daily Log was completed by Donald Shelton on Mon Jan 21, 2019 at 10:46 am CST.

### WEATHER REPORT

Temperature			Precipitation Since			Humidity				Windspeed		
Low	High	Avg	Midnight	2 Days Ago	3 Days Ago	Low	Avg	High	Dew	Avg	Max	Gust
50°F	70°F	63°F	0.13 in.	0.13 in.	0.14 in.	77%	90%	98%	60°F	11.4 mph	19 mph	27 mph

### DAILY SNAPSHOT

06:00 AM	09:00 AM	12:00 PM	03:00 PM	06:00 PM	09:00 PM
partly-cloudy-night 66°F	cloudy 67°F	partly-cloudy-day 69°F	wind 69°F	partly-cloudy-night 60°F	partly-cloudy-night 56°F

### OBSERVED WEATHER CONDITIONS

No.	Weather Delay	Sky	Temp	Average	Precipitation	Wind	Ground/Sea
1	No	Cloudy	Mild	63	0	Light Wind	Wet/Muddy

### MANPOWER LOG

14 Workers | 140.0 Man Hours

No.	Contact/Company	Cost Code	Workers	# Hours	Man Hours	Location
1	A&B Electric Co., Inc.		13	10.0	130.0	Building
<b>Notes:</b> Working on embeds in precast, Core drilling holes , Rough in conduits in corridor between column 15.2 and 4, Rough in conduit in security room (East of corridor).						
2	Caddell Construction Co. (DE), LLC		1	10.0	10.0	Site
<b>Notes:</b> WGI/Caddell supervision, quality control and safety onsite.						
			<b>14</b>		<b>140.0</b>	

#### Manpower Log's Attachments:





[Daily Construction Report -- 1\\_19\\_19.pdf](#)

### EQUIPMENT LOG

No.	Equipment Name	Cost Code	Hrs Operating	Hrs Idle	Inspected?	Inspection Time	Location
1	CAT Miniexcavator				No	07:00 AM	Building
<b>Notes:</b>							
2	Cat Telehandler				No	07:00 AM	Site
<b>Notes:</b>							

By \_\_\_\_\_

Date \_\_\_\_\_

Copies To \_\_\_\_\_



Whitesell Green / Caddell, a Joint Venture  
 2700 Lagoon Park Drive  
 Montgomery, Alabama 36109  
 P: (334) 272-7723  
 F: (334) 394-0193

Project: 1054 - Escambia County Correctional  
**Facility**  
 3080 N. Pace Boulevard  
 Pensacola, Florida 32501

## Daily Log: Sunday 1/20/2019

### WEATHER REPORT

Temperature			Precipitation Since			Humidity				Windspeed		
Low	High	Avg	Midnight	2 Days Ago	3 Days Ago	Low	Avg	High	Dew	Avg	Max	Gust
35°F	47°F	40°F	0.00 in.	0.13 in.	0.13 in.	55%	69%	76%	31°F	10.5 mph	16 mph	28 mph

### DAILY SNAPSHOT

06:00 AM	09:00 AM	12:00 PM	03:00 PM	06:00 PM	09:00 PM
cloudy 38°F	cloudy 39°F	cloudy 39°F	clear-day 45°F	clear-night 42°F	clear-night 38°F

### OBSERVED WEATHER CONDITIONS

No.	Weather Delay	Sky	Temp	Average	Precipitation	Wind	Ground/Sea
1	No						

By \_\_\_\_\_

Date \_\_\_\_\_

Copies To \_\_\_\_\_



## Daily Log: Monday 1/21/2019

**Daily Log Completed**  
 The Daily Log was completed by Donald Shelton on Fri Jan 25, 2019 at 09:12 am CST.

### WEATHER REPORT

Temperature			Precipitation Since			Humidity				Windspeed		
Low	High	Avg	Midnight	2 Days Ago	3 Days Ago	Low	Avg	High	Dew	Avg	Max	Gust
31°F	55°F	41°F	0.00 in.	0.00 in.	0.13 in.	33%	60%	79%	28°F	4.8 mph	7 mph	9 mph

### DAILY SNAPSHOT

06:00 AM	09:00 AM	12:00 PM	03:00 PM	06:00 PM	09:00 PM
clear-night 32°F	clear-day 39°F	clear-day 50°F	clear-day 56°F	clear-night 46°F	clear-night 40°F

### OBSERVED WEATHER CONDITIONS

No.	Weather Delay	Sky	Temp	Average	Precipitation	Wind	Ground/Sea
1	No	Cloudy	Mild	41	0	Light Wind	Dry

### MANPOWER LOG

77 Workers | 930.5 Man Hours

No.	Contact/Company	Cost Code	Workers	# Hours	Man Hours	Location
1	A&B Electric Co., Inc.		14	10.0	140.0	Building>C
<b>Notes:</b> Rough in electronic security room, Rough in conduits from security room to mechanical chase behind cells (Area C ), Rough in chase at Col. 9.						
2	Bayside Structures, LLC		19	17.5	332.5	Building>D
<b>Notes:</b> Poured level two Area D elevation 100 sequence 2						
3	Caddell Construction Co. (DE), LLC		8	17.5	140.0	Site
<b>Notes:</b> WGI/Caddell supervision, quality control and safety onsite.						
4	Larry M. Jacobs & Associates, Inc.		2	4.0	8.0	Site
<b>Notes:</b> Conducted concrete test for Area D 2nd pour at elevation 100. Conducted density test in corridor.						
5	Nash Plumbing and Mechanical, LLC		10	8.0	80.0	Building
<b>Notes:</b> Excavated and began repairs of underground broken pipe. Began underground rough-in						

**MANPOWER LOG**

77 Workers | 930.5 Man Hours

No.	Contact/Company	Cost Code	Workers	# Hours	Man Hours	Location
6	Tindall Corporation		19	10.0	190.0	Building>A
<b>Notes:</b> **Erecting in area A about line 3. **Grouting an welding in A and D. 199 Total Man Hours						
7	EAA Site Contractors LLC		5	8.0	40.0	Site
<b>Notes:</b> Total man hours 45. EAA continued demo on parking lot / retention pond. All trees are on the ground. Continued to haul asphalt off site. Installed additional silt fence.						
			<b>77</b>		<b>930.5</b>	

**Manpower Log's Attachments:**

1. A&B Electric Co., Inc.



[Daily Construction Report -- 1\\_21\\_19.pdf](#)

2. Bayside Structures, LLC



[Bayside Daily 1-21-2019.PDF](#)

5. Nash Plumbing and Mechanical, LLC

[Nash Daily 1-21-2019.xlsx](#)

6. Tindall Corporation

[Tindall Escambia Daily 1-21-2019.xlsx](#)

## EQUIPMENT LOG

No.	Equipment Name	Cost Code	Hrs Operating	Hrs Idle	Inspected?	Inspection Time	Location
1	Kobelco Crane CKE2500				No	07:00 AM	Building>A
	<b>Notes:</b>						
2	JLG Lift 660SJ				No	07:00 AM	Building>A
	<b>Notes:</b>						
3	Genie Lift S80				No	07:00 AM	Building>A
	<b>Notes:</b>						
4	JLG Lift 660SJ				No	07:00 AM	Building>C
	<b>Notes:</b>						
5	CAT Miniexcavator				No	07:00 AM	Building>C
	<b>Notes:</b>						
6	Pump Truck				No	07:00 AM	Building>D
	<b>Notes:</b>						
7	Doosan Excavator				No	07:00 AM	Site>Stormwater Pond
	<b>Notes:</b>						
8	Volvo 330 Excavator				No	07:00 AM	Site>Stormwater Pond
	<b>Notes:</b>						
9	John Deere 750 Dozer				No	07:00 AM	Site>Stormwater Pond
	<b>Notes:</b>						
10	Komatsu 320 PT Loader				No	07:00 AM	Site>Stormwater Pond
	<b>Notes:</b>						
11	Cat Telehandler				No	07:00 AM	Site
	<b>Notes:</b>						
12	JLG Skytrak Telehandler				No	07:00 AM	Site
	<b>Notes:</b>						
13	Cat Skidsteer				No	07:00 AM	Site
	<b>Notes:</b>						

By \_\_\_\_\_

Date \_\_\_\_\_

Copies To \_\_\_\_\_



## Daily Log: Tuesday 1/22/2019

**Daily Log Completed**  
 The Daily Log was completed by Donald Shelton on Mon Jan 28, 2019 at 08:17 am CST.

### WEATHER REPORT

Temperature			Precipitation Since			Humidity				Windspeed		
Low	High	Avg	Midnight	2 Days Ago	3 Days Ago	Low	Avg	High	Dew	Avg	Max	Gust
44°F	64°F	54°F	0.00 in.	0.00 in.	0.00 in.	68%	77%	84%	47°F	10.9 mph	15 mph	24 mph

### DAILY SNAPSHOT

06:00 AM	09:00 AM	12:00 PM	03:00 PM	06:00 PM	09:00 PM
cloudy 45°F	cloudy 51°F	cloudy 57°F	cloudy 61°F	cloudy 62°F	cloudy 64°F

### OBSERVED WEATHER CONDITIONS

No.	Weather Delay	Sky	Temp	Average	Precipitation	Wind	Ground/Sea
1	No	Cloudy	Mild	54	0	Light Wind	Dry

### MANPOWER LOG

64 Workers | 594.0 Man Hours

No.	Contact/Company	Cost Code	Workers	# Hours	Man Hours	Location
1	A&B Electric Co., Inc.		14	10.0	140.0	Building>C
<b>Notes:</b> Rough in of security room, Rough in of conduits from security room to chase behind cells in area "C", Rough in chase at Col. 9						
2	Bayside Structures, LLC		4	8.0	32.0	Building>C
<b>Notes:</b> Back-fill, tamped, placed vapor barrier, installed expansion board, and rebar mat for stairwell A.						
3	Caddell Construction Co. (DE), LLC		8	10.0	80.0	Site
<b>Notes:</b> WGI/Caddell supervision, quality control and safety onsite.						
4	Ed Emmons Steel Erectors, Inc.		9	8.0	72.0	Building>D
<b>Notes:</b> Hung beams at 6-G.7, 32.9-25 at elevation 115						
5	Nash Plumbing and Mechanical, LLC		5	8.0	40.0	Site
<b>Notes:</b> Erection of fabricated area						


**MANPOWER LOG**

**64 Workers | 594.0 Man Hours**

No.	Contact/Company	Cost Code	Workers	# Hours	Man Hours	Location
6	Tindall Corporation		19	10.0	190.0	Building>A
<p><b>Notes:</b> **Erecting in area A about line 3.                      **Grouting an welding in A and D.                      193 Total Man Hours</p>						
7	EAA Site Contractors LLC		5	8.0	40.0	Site
<p><b>Notes:</b> Total man hours 50. EAA started hauling off-site clearing debris from the parking lot. Continued to haul asphalt off site. All light pole bases are off site.</p>						
			<b>64</b>		<b>594.0</b>	


**Manpower Log's Attachments:**

1. A&B Electric Co., Inc.

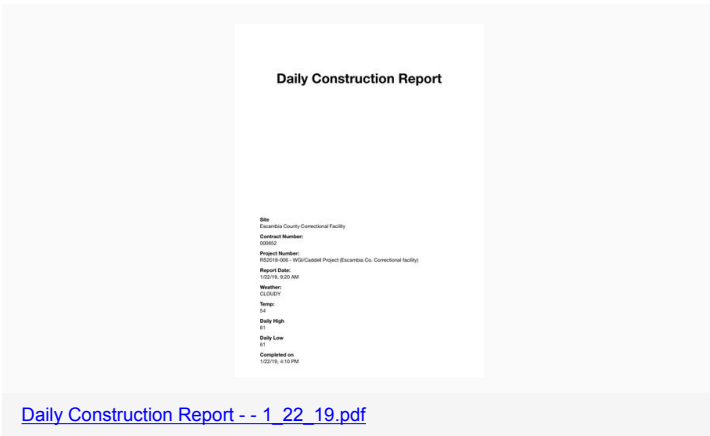


[Daily Construction Report -- 1\\_22\\_19.pdf](#)

2. Bayside Structures, LLC

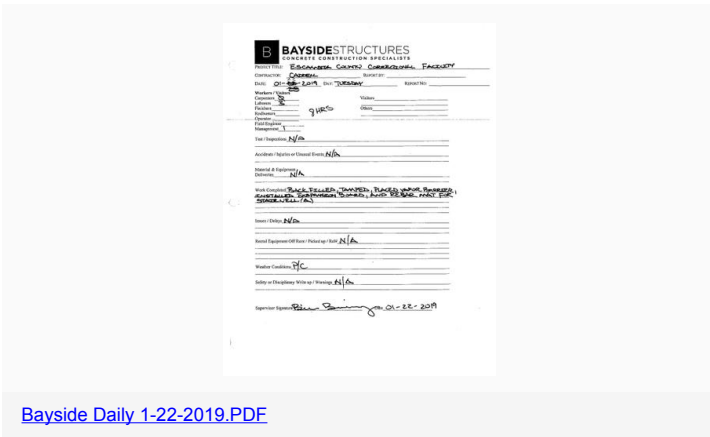

[Bayside Daily 1-22-2019.PDF](#)

4. Ed Emmons Steel Erectors, Inc.



[New Doc 2019-01-22 14.54.10.pdf](#)

5. Nash Plumbing and Mechanical, LLC

[Nash Daily 1-22-2019.xlsx](#)

6. Tindall Corporation

[Tindall Escambia daily 1-22-19.xlsx](#)

**EQUIPMENT LOG**

No.	Equipment Name	Cost Code	Hrs Operating	Hrs Idle	Inspected?	Inspection Time	Location
1	Kobelco Crane CKE2500				No	07:00 AM	Building>A
	<b>Notes:</b>						
2	Genie Lift S85				No	07:00 AM	Building>A
	<b>Notes:</b>						
3	JLG Lift 660SJ				No	07:00 AM	Building>A
	<b>Notes:</b>						
4	Bobcat Miniexcavator				No	07:00 AM	Building>C
	<b>Notes:</b>						
5	Grove Crane AT700D				No	07:00 AM	Building>D
	<b>Notes:</b>						
6	JLG Lift 660SJ				No	07:00 AM	Building>D
	<b>Notes:</b>						
7	JLG Skytrak Telehandler				No	07:00 AM	Building>D
	<b>Notes:</b>						
8	Cat Telehandler				No	07:00 AM	Site
	<b>Notes:</b>						
9	Cat Skidsteer				No	07:00 AM	Site
	<b>Notes:</b>						
10	Volvo 330 Excavator				No	07:00 AM	Site>Stormwater Pond
	<b>Notes:</b>						
11	Doosan Excavator				No	07:00 AM	Site>Stormwater Pond
	<b>Notes:</b>						
12	Komatsu 320 PT Loader				No	07:00 AM	Site>Stormwater Pond
	<b>Notes:</b>						



## EQUIPMENT LOG

No.	Equipment Name	Cost Code	Hrs Operating	Hrs Idle	Inspected?	Inspection Time	Location
13	John Deere 750 Dozer				No	07:00 AM	Site>Stormwater Pond
	<b>Notes:</b>						
14	Bobcat Miniexcavator				No	07:00 AM	Site
	<b>Notes:</b>						
15	JLG Lift 860SJ				No	07:00 AM	Building>A
	<b>Notes:</b>						
16	Genie Lift S125				No	07:00 AM	Building>C
	<b>Notes:</b>						
17	Scissor Lift				No	07:00 AM	Building>D
	<b>Notes:</b>						

---

By

---

Date

---

Copies To



## Daily Log: Wednesday 1/23/2019

**Daily Log Completed**  
 The Daily Log was completed by Donald Shelton on Mon Jan 28, 2019 at 08:15 am CST.

### WEATHER REPORT

Temperature			Precipitation Since			Humidity				Windspeed		
Low	High	Avg	Midnight	2 Days Ago	3 Days Ago	Low	Avg	High	Dew	Avg	Max	Gust
55°F	69°F	64°F	0.59 in.	0.59 in.	0.59 in.	77%	88%	99%	60°F	14.5 mph	22 mph	33 mph

### DAILY SNAPSHOT

06:00 AM	09:00 AM	12:00 PM	03:00 PM	06:00 PM	09:00 PM
cloudy 66°F	wind 68°F	wind 68°F	rain 68°F	rain 61°F	rain 56°F

### OBSERVED WEATHER CONDITIONS

No.	Weather Delay	Sky	Temp	Average	Precipitation	Wind	Ground/Sea
1	No	Cloudy	Mild	64	0	Light Wind	Dry

### MANPOWER LOG

59 Workers | 431.5 Man Hours

No.	Contact/Company	Cost Code	Workers	# Hours	Man Hours	Location
1	EAA Site Contractors LLC		4	8.0	32.0	Site
<b>Notes:</b> Total man hours 30. EAA continued demo on parking lot. All clearing debris has been removed from the site. Continued to haul asphalt off site. Rain stopped work at 230						
2	Bayside Structures, LLC		3	6.0	18.0	Site
<b>Notes:</b> Cleaned up at crossover. Removed forms and organized rebar.						
3	Caddell Construction Co. (DE), LLC		8	10.0	80.0	Site
<b>Notes:</b> WGI/Caddell supervision, quality control and safety onsite.						
4	Ed Emmons Steel Erectors, Inc.		7	2.5	17.5	Building>D
<b>Notes:</b> Attempted to relocate stored material. Shut down due to high wind.						
5	Nash Plumbing and Mechanical, LLC		5	8.0	40.0	Site
<b>Notes:</b> Erection of fabricated area						


**MANPOWER LOG**

59 Workers | 431.5 Man Hours

No.	Contact/Company	Cost Code	Workers	# Hours	Man Hours	Location
6	Tindall Corporation		19	6.0	114.0	Building>A
<p><b>Notes:</b> **Erecting in area A about line 3.                  **Grouting an welding in A and D.                  Shut down crane at 10am due to weather</p>						
7	A&B Electric Co., Inc.		13	10.0	130.0	Building>C
<p><b>Notes:</b> Blow string in security room conduits &amp; chase conduits in area "C", Backfill conduits in security room &amp; chase in area "C". Finish conduit racks before backfill, Cut off unistrut on racks and dress up.</p>						
			<b>59</b>		<b>431.5</b>	


**Manpower Log's Attachments:**

2. Bayside Structures, LLC

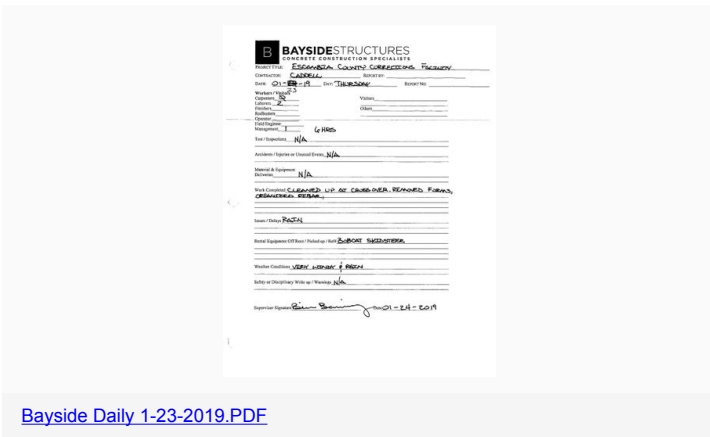

[Bayside Daily 1-23-2019.PDF](#)

4. Ed Emmons Steel Erectors, Inc.

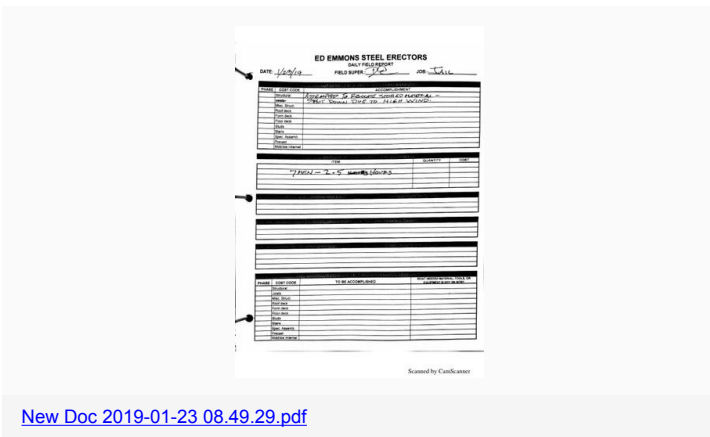

[New Doc 2019-01-23 08.49.29.pdf](#)

5. Nash Plumbing and Mechanical, LLC

[Nash Daily 1-23-2019.xlsx](#)

6. Tindall Corporation

[Tindall Escambia Daily 1-23-2019.xlsx](#)



[Daily Construction Report -- 1\\_23\\_19.pdf](#)

### EQUIPMENT LOG

No.	Equipment Name	Cost Code	Hrs Operating	Hrs Idle	Inspected?	Inspection Time	Location
1	Kobelco Crane CKE2500				No	07:00 AM	Building>A
	<b>Notes:</b>						
2	JLG Lift 860SJ				No	07:00 AM	Building>A
	<b>Notes:</b>						
3	JLG Lift 660SJ				No	07:00 AM	Building>A
	<b>Notes:</b>						
4	JLG Lift 660SJ				No	07:00 AM	Building>A
	<b>Notes:</b>						
5	Genie Lift S85				No	07:00 AM	Building>A
	<b>Notes:</b>						
6	Genie Lift S125				No	07:00 AM	Building>C
	<b>Notes:</b>						
7	Grove Crane AT700D				No	07:00 AM	Building>D
	<b>Notes:</b>						
8	Genie Lift S80				No	07:00 AM	Building>D
	<b>Notes:</b>						
9	JLG Skytrak Telehandler				No	07:00 AM	Site
	<b>Notes:</b>						
10	JLG Skytrak Telehandler				No	07:00 AM	Site
	<b>Notes:</b>						
11	Komatsu 320 PT Loader				No	07:00 AM	Site>Stormwater Pond
	<b>Notes:</b>						
12	Volvo 330 Excavator				No	07:00 AM	Site>Stormwater Pond
	<b>Notes:</b>						
13	Doosan Excavator				No	07:00 AM	Site>Stormwater Pond
	<b>Notes:</b>						
14	John Deere 750 Dozer				No	07:00 AM	Site>Stormwater Pond
	<b>Notes:</b>						

## EQUIPMENT LOG

No.	Equipment Name	Cost Code	Hrs Operating	Hrs Idle	Inspected?	Inspection Time	Location
15	John Deere 550H Dozer				No	07:00 AM	Site>Stormwater Pond
	<b>Notes:</b>						
16	CAT Miniexcavator				No	07:00 AM	Building>C
	<b>Notes:</b>						
17	Cat Skidsteer				No	07:00 AM	Building>C
	<b>Notes:</b>						

---

By

---

Date

---

Copies To



## Daily Log: Thursday 1/24/2019

### WEATHER REPORT

Temperature			Precipitation Since			Humidity				Windspeed		
Low	High	Avg	Midnight	2 Days Ago	3 Days Ago	Low	Avg	High	Dew	Avg	Max	Gust
35°F	55°F	43°F	0.00 in.	0.59 in.	0.59 in.	47%	77%	98%	36°F	7.5 mph	10 mph	19 mph

### DAILY SNAPSHOT

06:00 AM	09:00 AM	12:00 PM	03:00 PM	06:00 PM	09:00 PM
cloudy 41°F	cloudy 39°F	partly-cloudy-day 43°F	clear-day 51°F	clear-night 45°F	clear-night 38°F

### OBSERVED WEATHER CONDITIONS

No.	Weather Delay	Sky	Temp	Average	Precipitation	Wind	Ground/Sea
1	No	Clear	Mild	43	0	Calm	Dry

### MANPOWER LOG

66 Workers | 609.0 Man Hours

No.	Contact/Company	Cost Code	Workers	# Hours	Man Hours	Location
1	A&B Electric Co., Inc.		13	10.0	130.0	Building>C
<b>Notes:</b> Pull string in all conduits and identify before 1st floor corridor pours, Finish backfill of security room and chase where conduit stub ups are, Clean grade beams off.						
2	Bayside Structures, LLC		6	8.0	48.0	Building>A
<b>Notes:</b> Poured stairwell A elevation 83						
3	Caddell Construction Co. (DE), LLC		8	10.0	80.0	Site
<b>Notes:</b> WGI/Caddell supervision, quality control and safety onsite.						
4	Ed Emmons Steel Erectors, Inc.		8	8.0	64.0	Building>D
<b>Notes:</b> Hung beams at G.7-G, 25 to 17 Hung beams 14-17 lines between H and J						
5	Nash Plumbing and Mechanical, LLC		7	8.0	56.0	Building
<b>Notes:</b> Installed 3" pipe in crossing corridor						
6	Tindall Corporation		19	10.0	190.0	Building>A
<b>Notes:</b> **Erecting in area A about line 3. **Grouting an welding in A. 202 Total Man Hours						

**MANPOWER LOG**

**66 Workers | 609.0 Man Hours**

No.	Contact/Company	Cost Code	Workers	# Hours	Man Hours	Location
7	Larry M. Jacobs & Associates, Inc.		1	1.0	1.0	Site>B
<b>Notes:</b> Density Test in Area A and B						
8	EAA Site Contractors LLC		4	10.0	40.0	Site>Stormwater Pond
<b>Notes:</b> Total man hours 34. EAA continued demo on parking lot. Continued to haul asphalt off site. Built up ramp and crane path in Area D.						
			<b>66</b>		<b>609.0</b>	

**Manpower Log's Attachments:**

- 1. A&B Electric Co., Inc.




[Daily Construction Report -- 1\\_24\\_19.pdf](#)

- 2. Bayside Structures, LLC



[Bayside Daily 1-24-2019.PDF](#)

4. Ed Emmons Steel Erectors, Inc.

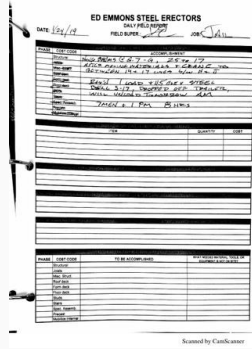

[New Doc 2019-01-24 15.04.30.pdf](#)

5. Nash Plumbing and Mechanical, LLC

[Nash Daily 1-24-2019.xlsx](#)

6. Tindall Corporation

[Tindall scambia Daily 1-24-2019.xlsx](#)

**EQUIPMENT LOG**

No.	Equipment Name	Cost Code	Hrs Operating	Hrs Idle	Inspected?	Inspection Time	Location
1	Kobelco Crane CKE2500				No	07:00 AM	Building>A
	<b>Notes:</b>						
2	JLG Lift 860SJ				No	07:00 AM	Building>A
	<b>Notes:</b>						
3	JLG Lift 660SJ				No	07:00 AM	Building>A
	<b>Notes:</b>						
4	JLG Lift 660SJ				No	07:00 AM	Building>A
	<b>Notes:</b>						
5	Genie Lift S85				No	07:00 AM	Building>A
	<b>Notes:</b>						
6	Komatsu 78MR Excavator				No	07:00 AM	Building>C
	<b>Notes:</b>						
7	Genie Lift S125				No	07:00 AM	Building>C
	<b>Notes:</b>						
8	Kobelco Crane CKE2500				No	07:00 AM	Building>D
	<b>Notes:</b>						
9	Genie Lift S80				No	07:00 AM	Building>D
	<b>Notes:</b>						
10	JLG Skytrak Telehandler				No	07:00 AM	Building>D
	<b>Notes:</b>						
11	JLG Skytrak Telehandler				No	07:00 AM	Site
	<b>Notes:</b>						
12	Doosan Excavator				No	07:00 AM	Site>Stormwater Pond
	<b>Notes:</b>						



## EQUIPMENT LOG

No.	Equipment Name	Cost Code	Hrs Operating	Hrs Idle	Inspected?	Inspection Time	Location
13	Volvo 330 Excavator				No	07:00 AM	Site>Stormwater Pond
	<b>Notes:</b>						
14	Hamm Vibratory Roller				No	07:00 AM	Site
	<b>Notes:</b>						
15	Komatsu 320 PT Loader				No	07:00 AM	Site>Stormwater Pond
	<b>Notes:</b>						
16	John Deere 750 Dozer				No	07:00 AM	Site>Stormwater Pond
	<b>Notes:</b>						
17	John Deere 550H Dozer				No	07:00 AM	Site>Stormwater Pond
	<b>Notes:</b>						

---

By

Date

Copies To



## Daily Log: Friday 1/25/2019

**Daily Log Completed**  
 The Daily Log was completed by Donald Shelton on Mon Jan 28, 2019 at 10:24 am CST.

### WEATHER REPORT

Temperature			Precipitation Since			Humidity				Windspeed		
Low	High	Avg	Midnight	2 Days Ago	3 Days Ago	Low	Avg	High	Dew	Avg	Max	Gust
33°F	55°F	43°F	0.00 in.	0.01 in.	0.60 in.	43%	67%	88%	32°F	5.6 mph	7 mph	12 mph

### DAILY SNAPSHOT

06:00 AM	09:00 AM	12:00 PM	03:00 PM	06:00 PM	09:00 PM
clear-night 35°F	partly-cloudy-day 43°F	partly-cloudy-day 52°F	clear-day 55°F	partly-cloudy-night 50°F	partly-cloudy-night 45°F

### OBSERVED WEATHER CONDITIONS

No.	Weather Delay	Sky	Temp	Average	Precipitation	Wind	Ground/Sea
1	No	Clear	Cold	43	0	Calm	Dry

### MANPOWER LOG

55 Workers | 494.0 Man Hours

No.	Contact/Company	Cost Code	Workers	# Hours	Man Hours	Location
1	A&B Electric Co., Inc.		6	8.0	48.0	Building
<b>Notes:</b> Installed contact info on temp. Power panels, continued blowing strings and identifying underground conduits in main corridor and stub outs.						
2	Bayside Structures, LLC		8	8.0	64.0	Building
<b>Notes:</b> Worked on expansion board installation in corridor at elevation 83. Cleaned embeds for precast elevation 100 second pour Area D. Back-fill at crossover.						
3	Caddell Construction Co. (DE), LLC		8	10.0	80.0	Site
<b>Notes:</b> WGI/Caddell supervision, quality control and safety onsite.						
4	Ed Emmons Steel Erectors, Inc.		9	8.0	72.0	Building>D
<b>Notes:</b> Hung elevation beams G.7-G, 17 to A. Numbers less than 17 nearest to precast wall between D and C.						
5	Nash Plumbing and Mechanical, LLC		5	8.0	40.0	Site
<b>Notes:</b> Erection of fabricated area						

**MANPOWER LOG**

55 Workers | 494.0 Man Hours

No.	Contact/Company	Cost Code	Workers	# Hours	Man Hours	Location
6	Tindall Corporation		19	10.0	190.0	Building>A
Notes: **Erecting in area A about line 3. **Grouting and welding in A. 201 Total Man Hours						
			<b>55</b>		<b>494.0</b>	

**Manpower Log's Attachments:**

1. A&B Electric Co., Inc.




[Daily Construction Report -- 1\\_25\\_19.pdf](#)

2. Bayside Structures, LLC



[Bayside Daily 1-25-2019.PDF](#)

4. Ed Emmons Steel Erectors, Inc.

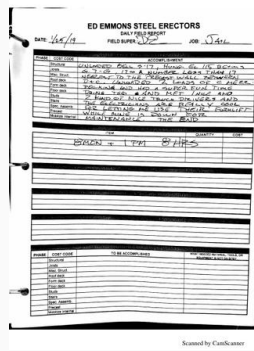

[New Doc 2019-01-25 15.09.03.pdf](#)

5. Nash Plumbing and Mechanical, LLC

[1-25-2019.xlsx](#)

6. Tindall Corporation

[Tindall Escambia Daily 1-25-2019.xlsx](#)

**EQUIPMENT LOG**

No.	Equipment Name	Cost Code	Hrs Operating	Hrs Idle	Inspected?	Inspection Time	Location
1	Kobelco Crane CKE2500				No	07:00 AM	Building>A
	<b>Notes:</b>						
2	JLG Lift 860SJ				No	07:00 AM	Building>A
	<b>Notes:</b>						
3	JLG Lift 660SJ				No	07:00 AM	Building>A
	<b>Notes:</b>						
4	JLG Lift 660SJ				No	07:00 AM	Building>A
	<b>Notes:</b>						
5	Genie Lift S85				No	07:00 AM	Building>A
	<b>Notes:</b>						
6	Genie Lift S125				No	07:00 AM	Building>C
	<b>Notes:</b>						
7	Grove Crane AT700D				No	07:00 AM	Building>D
	<b>Notes:</b>						
8	Genie Lift S80				No	07:00 AM	Building>D
	<b>Notes:</b>						
9	JLG Skytrak Telehandler				No	07:00 AM	Site
	<b>Notes:</b>						
10	JLG Skytrak Telehandler				No	07:00 AM	Site
	<b>Notes:</b>						

By \_\_\_\_\_

Date \_\_\_\_\_

Copies To \_\_\_\_\_



## Daily Log: Saturday 1/26/2019

**Daily Log Completed**  
 The Daily Log was completed by Donald Shelton on Mon Jan 28, 2019 at 09:28 am CST.

### WEATHER REPORT

Temperature			Precipitation Since			Humidity				Windspeed		
Low	High	Avg	Midnight	2 Days Ago	3 Days Ago	Low	Avg	High	Dew	Avg	Max	Gust
30°F	58°F	43°F	0.00 in.	0.00 in.	0.01 in.	35%	74%	100%	34°F	2.0 mph	7 mph	7 mph

### DAILY SNAPSHOT

06:00 AM	09:00 AM	12:00 PM	03:00 PM	06:00 PM	09:00 PM
clear-night 31°F	clear-day 44°F	clear-day 56°F	clear-day 58°F	partly-cloudy-night 49°F	clear-night 44°F

### OBSERVED WEATHER CONDITIONS

No.	Weather Delay	Sky	Temp	Average	Precipitation	Wind	Ground/Sea
1	No	Cloudy	Mild	43	0	Calm	Dry

### MANPOWER LOG

**20 Workers | 200.0 Man Hours**

No.	Contact/Company	Cost Code	Workers	# Hours	Man Hours	Location
1	Caddell Construction Co. (DE), LLC		1	10.0	10.0	Site
<b>Notes:</b> WGI/Caddell supervision, quality control and safety onsite.						
2	Tindall Corporation		19	10.0	190.0	Building>A
<b>Notes:</b> **Erecting in area A about line 3. **Grouting and welding in A.						
			<b>20</b>	<b>200.0</b>		

2. Tindall Corporation

[Tindall Escambia Dailt 1-26-2019.xlsx](#)

### EQUIPMENT LOG

No.	Equipment Name	Cost Code	Hrs Operating	Hrs Idle	Inspected?	Inspection Time	Location
1	Kobelco Crane CKE2500				No	07:00 AM	Building>A
<b>Notes:</b>							
2	JLG Lift 860SJ				No	07:00 AM	Building>A
<b>Notes:</b>							

## EQUIPMENT LOG

No.	Equipment Name	Cost Code	Hrs Operating	Hrs Idle	Inspected?	Inspection Time	Location
3	JLG Lift 660SJ				No	07:00 AM	Building>A
	<b>Notes:</b>						
4	JLG Lift 660SJ				No	07:00 AM	Building>A
	<b>Notes:</b>						
5	Genie Lift S85				No	07:00 AM	Building>A
	<b>Notes:</b>						
6	JLG Skytrak Telehandler				No	07:00 AM	Site
	<b>Notes:</b>						

---

By

---

Date

---

Copies To



Whitesell Green / Caddell, a Joint Venture  
 2700 Lagoon Park Drive  
 Montgomery, Alabama 36109  
 P: (334) 272-7723  
 F: (334) 394-0193

Project: 1054 - Escambia County Correctional  
**Facility**  
 3080 N. Pace Boulevard  
 Pensacola, Florida 32501

## Daily Log: Sunday 1/27/2019

### WEATHER REPORT

Temperature			Precipitation Since			Humidity				Windspeed		
Low	High	Avg	Midnight	2 Days Ago	3 Days Ago	Low	Avg	High	Dew	Avg	Max	Gust
36°F	54°F	45°F	0.00 in.	0.00 in.	0.00 in.	52%	76%	96%	38°F	2.0 mph	4 mph	4 mph

### DAILY SNAPSHOT

06:00 AM	09:00 AM	12:00 PM	03:00 PM	06:00 PM	09:00 PM
clear-night 43°F	clear-day 47°F	clear-day 53°F	partly-cloudy-day 54°F	clear-night 47°F	clear-night 40°F

### OBSERVED WEATHER CONDITIONS

No.	Weather Delay	Sky	Temp	Average	Precipitation	Wind	Ground/Sea
1	No						

By \_\_\_\_\_

Date \_\_\_\_\_

Copies To \_\_\_\_\_



## Daily Log: Monday 1/28/2019

**Daily Log Completed**  
 The Daily Log was completed by Donald Shelton on Wed Jan 30, 2019 at 11:57 am CST.

### WEATHER REPORT

Temperature			Precipitation Since			Humidity				Windspeed		
Low	High	Avg	Midnight	2 Days Ago	3 Days Ago	Low	Avg	High	Dew	Avg	Max	Gust
33°F	62°F	48°F	0.00 in.	0.00 in.	0.00 in.	42%	77%	99%	39°F	2.9 mph	8 mph	13 mph

### DAILY SNAPSHOT

06:00 AM	09:00 AM	12:00 PM	03:00 PM	06:00 PM	09:00 PM
clear-night 34°F	clear-day 52°F	clear-day 62°F	clear-day 62°F	clear-night 54°F	clear-night 47°F

### OBSERVED WEATHER CONDITIONS

No.	Weather Delay	Sky	Temp	Average	Precipitation	Wind	Ground/Sea
1	No	Clear	Mild	49	0	Calm	Dry

### MANPOWER LOG

62 Workers | 552.0 Man Hours

No.	Contact/Company	Cost Code	Workers	# Hours	Man Hours	Location
1	A&B Electric Co., Inc.		11	10.0	110.0	Building
<b>Notes:</b> Blow strings in all corridor conduit, identify all conduits and mark.						
2	Bayside Structures, LLC		3	8.0	24.0	Site
<b>Notes:</b> Worked on chipping out connector flanges that were not blocked out center line 14-G7 and 14-G elevation 100 Area D. Worked on back-fill at connector.						
3	Caddell Construction Co. (DE), LLC		7	10.0	70.0	Site
<b>Notes:</b> WGI/Caddell supervision, quality control and safety onsite.						
4	Chavers Construction Inc.		4	3.5	14.0	Site>Stormwater Pond
<b>Notes:</b> Mobilized Staked out S23 box Lined up 36" pipe for installation						
5	Ed Emmons Steel Erectors, Inc.		8	8.0	64.0	Building>D
<b>Notes:</b> Erecting structural steal at elevation 115 in Area D.						



**MANPOWER LOG**

**62 Workers | 552.0 Man Hours**

No.	Contact/Company	Cost Code	Workers	# Hours	Man Hours	Location
6	Nash Plumbing and Mechanical, LLC		6	8.0	48.0	Building>C
<b>Notes:</b> Completed fabrication Area. Performed plumbing underground in Area C.						
7	Tindall Corporation		19	10.0	190.0	Building>D
<b>Notes:</b> **Crane move to area D, erected panels @ elevation 100' **Grouting and welding in A and D.						
8	EAA Site Contractors LLC		4	8.0	32.0	Site
<b>Notes:</b> Total man hours 35. EAA continued demo on parking lot. Stripping clay base from old parking lot. Also added clay to ramp into section D for ranger trucks						
			<b>62</b>		<b>552.0</b>	

**Manpower Log's Attachments:**

1. A&B Electric Co., Inc.



[Daily Construction Report -- 1\\_28\\_19.pdf](#)

2. Bayside Structures, LLC



[Bayside Daily 1-28-2019.PDF](#)

4. Chavers Construction Inc.

[Chaver Daily 1-28-2019.PDF](#)

5. Ed Emmons Steel Erectors, Inc.

[New Doc 2019-01-28 15.08.58.pdf](#)

6. Nash Plumbing and Mechanical, LLC

[Nash Daily 1-28-2019.xlsx](#)

7. Tindall Corporation

[Tindall Escambia Daily 1-28-2019.xlsx](#)

**EQUIPMENT LOG**

No.	Equipment Name	Cost Code	Hrs Operating	Hrs Idle	Inspected?	Inspection Time	Location
1	Genie Lift S85				No	07:00 AM	Building>A
	<b>Notes:</b>						
2	JLG Lift 860SJ				No	07:00 AM	Building>A
	<b>Notes:</b>						
3	JLG Lift 660SJ				No	07:00 AM	Building>A
	<b>Notes:</b>						
4	JLG Lift 660SJ				No	07:00 AM	Building>D
	<b>Notes:</b>						
5	Grove Crane AT700D				No	07:00 AM	Building>D
	<b>Notes:</b>						
6	Bobcat Skidsteer				No	07:00 AM	Site
	<b>Notes:</b>						

## EQUIPMENT LOG

No.	Equipment Name	Cost Code	Hrs Operating	Hrs Idle	Inspected?	Inspection Time	Location
7	Komatsu 320 PT Loader				No	07:00 AM	Site>Stormwater Pond
<b>Notes:</b>							
8	John Deere 750 Dozer				No	07:00 AM	Site>Stormwater Pond
<b>Notes:</b>							
9	Kobelco Crane CKE2500				No	07:00 AM	Building>D
<b>Notes:</b>							
10	JLG Skytrak Telehandler				No	07:00 AM	Site
<b>Notes:</b>							

---

By

Date

Copies To

## Daily Log: Tuesday 1/29/2019

**Daily Log Completed**

The Daily Log was completed by Payton Holley on Mon Feb 4, 2019 at 11:09 am CST.

### WEATHER REPORT

Temperature			Precipitation Since			Humidity				Windspeed		
Low	High	Avg	Midnight	2 Days Ago	3 Days Ago	Low	Avg	High	Dew	Avg	Max	Gust
36°F	52°F	45°F	0.16 in.	0.16 in.	0.16 in.	48%	76%	99%	37°F	7.6 mph	13 mph	23 mph

### DAILY SNAPSHOT

06:00 AM	09:00 AM	12:00 PM	03:00 PM	06:00 PM	09:00 PM
<b>rain</b> 52°F	<b>rain</b> 47°F	<b>cloudy</b> 43°F	<b>clear-day</b> 49°F	<b>clear-night</b> 43°F	<b>clear-night</b> 38°F

### OBSERVED WEATHER CONDITIONS

No.	Weather Delay	Sky	Temp	Average	Precipitation	Wind	Ground/Sea
1	Yes	Rain	Cold	45	.25"	Light Wind	Wet/Muddy

#### Observed Weather Conditions' Attachments:

1 \_\_\_\_\_



### MANPOWER LOG

**50 Workers | 319.0 Man Hours**

No.	Contact/Company	Cost Code	Workers	# Hours	Man Hours	Location
1	A&B Electric Co., Inc.		8	10.0	80.0	Building

**Notes:** Pull strings in conduits in main corridor to check conduit and identify location, repair and work on temporary lights.  
 Repair broken conduit.



2. Bayside Structures, LLC

[Bayside Daily 1-29-2019.PDF](#)

4. Chavers Construction Inc.

[Chaver Daily 1-29-2019.PDF](#)

5. Ed Emmons Steel Erectors, Inc.

[New Doc 2019-01-29 13.55.49.pdf](#)

6. Nash Plumbing and Mechanical, LLC

[Nash Daily 1-29-2019.xlsx](#)

7. Tindall Corporation

[Tindall Escambia Daily 1-29-2019.xlsx](#)

## EQUIPMENT LOG

No.	Equipment Name	Cost Code	Hrs Operating	Hrs Idle	Inspected?	Inspection Time	Location
1	John Deere 750 Dozer				No	07:00 AM	Site>Stormwater Pond
	<b>Notes:</b>						
2	Terex Articulated Dump Truck				No	07:00 AM	Site>Stormwater Pond
	<b>Notes:</b>						
3	Volvo 330 Excavator				No	07:00 AM	Site>Stormwater Pond
	<b>Notes:</b>						
4	Kobelco Crane CKE2500				No	07:00 AM	Building>D
	<b>Notes:</b>						
5	JLG Lift 660SJ				No	07:00 AM	Building>D
	<b>Notes:</b>						
6	JLG Skytrak Telehandler				No	07:00 AM	Building>D
	<b>Notes:</b>						
7	Genie Lift S85				No	07:00 AM	Building>A
	<b>Notes:</b>						

---

By

---

Date

---

Copies To



## Daily Log: Wednesday 1/30/2019

**Daily Log Completed**  
 The Daily Log was completed by Donald Shelton on Mon Feb 4, 2019 at 10:55 am CST.

### WEATHER REPORT

Temperature			Precipitation Since			Humidity				Windspeed		
Low	High	Avg	Midnight	2 Days Ago	3 Days Ago	Low	Avg	High	Dew	Avg	Max	Gust
32°F	48°F	39°F	0.00 in.	0.16 in.	0.16 in.	28%	49%	76%	20°F	5.0 mph	8 mph	17 mph

### DAILY SNAPSHOT

06:00 AM	09:00 AM	12:00 PM	03:00 PM	06:00 PM	09:00 PM
clear-night 33°F	partly-cloudy-day 37°F	partly-cloudy-day 46°F	partly-cloudy-day 49°F	partly-cloudy-night 43°F	partly-cloudy-night 38°F

### OBSERVED WEATHER CONDITIONS

No.	Weather Delay	Sky	Temp	Average	Precipitation	Wind	Ground/Sea
1	No	Clear	Cold	40	0	Light Wind	Dry

### MANPOWER LOG

71 Workers | 656.75 Man Hours

No.	Contact/Company	Cost Code	Workers	# Hours	Man Hours	Location
1	A&B Electric Co., Inc.		10	10.0	100.0	Building
<b>Notes:</b> Working on conduits in corridor and security room, repair and pull strings to identify, Working on temporary lights, Check lights for correct voltage & rework boxes, Backfill of Main Electrical room.						
2	Bayside Structures, LLC		3	9.0	27.0	Site
<b>Notes:</b> Worked on sand and mud removal at existing building in connector. Worked on backfill at connector.						
3	Caddell Construction Co. (DE), LLC		9	10.25	92.25	Site
<b>Notes:</b> WGI/Caddell supervision, quality control and safety onsite.						
4	Chavers Construction Inc.		6	10.25	61.5	Site>Stormwater Pond
<b>Notes:</b> Install 100' of 36" stormpipe Slop sides of ditch						
5	Ed Emmons Steel Erectors, Inc.		9	8.0	72.0	Building>D
<b>Notes:</b> Erected structural steel at elevation 100 and welded steel.						




**MANPOWER LOG**

71 Workers | 656.75 Man Hours

No.	Contact/Company	Cost Code	Workers	# Hours	Man Hours	Location
6	Nash Plumbing and Mechanical, LLC		7	8.0	56.0	Building>C
<b>Notes:</b> Plumbing underground work						
7	Ruben Surveying		2	6.0	12.0	Site
<b>Notes:</b> Shot control line at 49 and 50						
8	Tindall Corporation		18	10.0	180.0	Building>D
<b>Notes:</b> **Erecting panels in area D at elevation 100' **Grouting and welding in roof level of corridor and D.						
9	EAA Site Contractors LLC		7	8.0	56.0	Site>Stormwater Pond
<b>Notes:</b> Total man hours 68. EAA continued digging retention pond. Placed dirt on North side of the bldg in a low area and along east side of section C. Also started placing dirt in the accessible areas of section A and B.						
			<b>71</b>	<b>656.75</b>		

**Manpower Log's Attachments:**

1. A&B Electric Co., Inc.

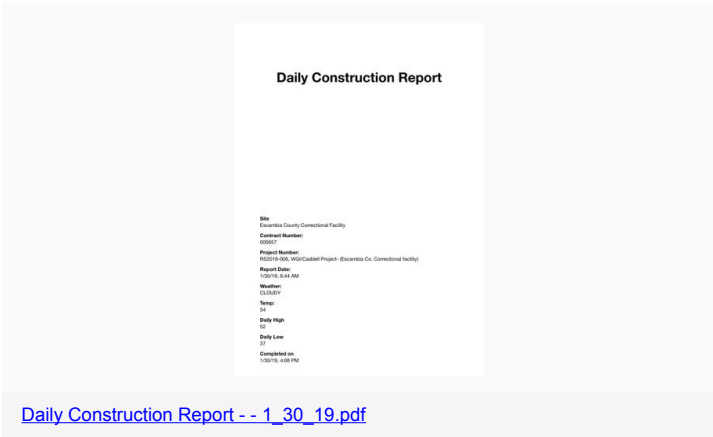

[Daily Construction Report -- 1\\_30\\_19.pdf](#)

2. Bayside Structures, LLC



[Bayside Daily 1-30-2019.PDF](#)

4. Chavers Construction Inc.

[Chaver Daily 1-30-2019.PDF](#)

5. Ed Emmons Steel Erectors, Inc.

[New Doc 2019-01-30 15.11.30.pdf](#)

6. Nash Plumbing and Mechanical, LLC

[Nash Daily 1-30-2019.xlsx](#)

8. Tindall Corporation

[Tindall Escambia Daily 1-30-2019.xlsx](#)

**EQUIPMENT LOG**

No.	Equipment Name	Cost Code	Hrs Operating	Hrs Idle	Inspected?	Inspection Time	Location
1	Genie Lift S85				No	07:00 AM	Building>A
	<b>Notes:</b>						
2	JLG Lift 860SJ				No	07:00 AM	Building>A
	<b>Notes:</b>						
3	JLG Lift 660SJ				No	07:00 AM	Building>A
	<b>Notes:</b>						
4	CAT Miniexcavator				No	07:00 AM	Building>B
	<b>Notes:</b>						
5	Grove Crane AT700D				No	07:00 AM	Building>D
	<b>Notes:</b>						
6	Kobelco Crane CKE2500				No	07:00 AM	Building>D
	<b>Notes:</b>						

## EQUIPMENT LOG

No.	Equipment Name	Cost Code	Hrs Operating	Hrs Idle	Inspected?	Inspection Time	Location
7	JLG Lift 660SJ				No	07:00 AM	Building>D
	<b>Notes:</b>						
8	Bobcat Skidsteer				No	07:00 AM	Building
	<b>Notes:</b>						
9	Volvo 330 Excavator				No	07:00 AM	Site>Stormwater Pond
	<b>Notes:</b>						
10	Volvo 330 Excavator				No	07:00 AM	Site>Stormwater Pond
	<b>Notes:</b>						
11	Komatsu 320 PT Loader				No	07:00 AM	Site>Stormwater Pond
	<b>Notes:</b>						
12	Terex Articulated Dump Truck				No	07:00 AM	Site
	<b>Notes:</b>						
13	John Deere 750 Dozer				No	07:00 AM	Site
	<b>Notes:</b>						
14	John Deere 700 Dozer				No	07:00 AM	Site
	<b>Notes:</b>						
15	John Deere Skidsteer				No	07:00 AM	Site
	<b>Notes:</b>						
16	John Deere Skidsteer				No	07:00 AM	Site
	<b>Notes:</b>						
17	Hamm Vibratory Roller				No	07:00 AM	Site
	<b>Notes:</b>						
18	Cat Telehandler				No	07:00 AM	Site
	<b>Notes:</b>						

## PHOTOS



[DJI\\_0278.jpg](#)



[DJI\\_0279.jpg](#)



[DJI\\_0257.jpg](#)



[DJI\\_0259.jpg](#)



[DJI\\_0258.jpg](#)



[DJI\\_0280.jpg](#)



[DJI\\_0283.jpg](#)



[DJI\\_0254.jpg](#)



[DJI\\_0252.jpg](#)



[DJI\\_0260.jpg](#)



[DJI\\_0261.jpg](#)



[DJI\\_0253.jpg](#)



[DJI\\_0256.jpg](#)



[DJI\\_0266.jpg](#)



[DJI\\_0263.jpg](#)



[DJI\\_0267.jpg](#)



[DJI\\_0255.jpg](#)



[DJI\\_0264.jpg](#)



DJI\_0265.jpg



DJI\_0269.jpg



DJI\_0271.jpg



DJI\_0270.jpg



DJI\_0268.jpg



DJI\_0272.jpg



DJI\_0275.jpg



DJI\_0276.jpg



[DJI\\_0277.jpg](#)



[DJI\\_0273.jpg](#)



[DJI\\_0262.jpg](#)



[DJI\\_0274.jpg](#)

---

By

Date

Copies To



## Daily Log: Thursday 1/31/2019

**Daily Log Completed**  
 The Daily Log was completed by Donald Shelton on Mon Feb 4, 2019 at 07:58 am CST.

### WEATHER REPORT

Temperature			Precipitation Since			Humidity				Windspeed		
Low	High	Avg	Midnight	2 Days Ago	3 Days Ago	Low	Avg	High	Dew	Avg	Max	Gust
37°F	58°F	47°F	0.00 in.	0.00 in.	0.16 in.	35%	54%	77%	30°F	5.2 mph	9 mph	16 mph

### DAILY SNAPSHOT

06:00 AM	09:00 AM	12:00 PM	03:00 PM	06:00 PM	09:00 PM
cloudy 40°F	clear-day 49°F	clear-day 57°F	clear-day 58°F	clear-night 49°F	partly-cloudy-night 44°F

### OBSERVED WEATHER CONDITIONS

No.	Weather Delay	Sky	Temp	Average	Precipitation	Wind	Ground/Sea
1	No	Clear	Mild	47	0	Light Wind	Dry

### MANPOWER LOG

73 Workers | 663.0 Man Hours

No.	Contact/Company	Cost Code	Workers	# Hours	Man Hours	Location
1	A&B Electric Co., Inc.		10	10.0	100.0	Building>C
<b>Notes:</b> Working on underground conduits in section "C". Working on temporary Lights.						
2	Bayside Structures, LLC		4	8.0	32.0	Building
<b>Notes:</b> Finished installing expansion material in corridor at elevation 83. Worked on finishing removal of mud and sand from forms at connector next to existing building.						
3	Caddell Construction Co. (DE), LLC		9	10.0	90.0	Site
<b>Notes:</b> WGI/Caddell supervision, quality control and safety onsite.						
4	Chavers Construction Inc.		5	10.0	50.0	Site>Stormwater Pond
<b>Notes:</b> Demob existing footer Install S23 Compacted first lift around S23						
5	Ed Emmons Steel Erectors, Inc.		9	8.0	72.0	Building>D
<b>Notes:</b> Erected structural steel at elevation 100 and welded steel.						




**MANPOWER LOG**

73 Workers | 663.0 Man Hours

No.	Contact/Company	Cost Code	Workers	# Hours	Man Hours	Location
6	Nash Plumbing and Mechanical, LLC		8	8.0	64.0	Building
<b>Notes:</b> Underground rough-in						
7	Tindall Corporation		19	10.0	190.0	Building
<b>Notes:</b> **Erecting panels in area D, one more to set in the morning before moving back to area A. **Grouting and welding in roof level of corridor and D. 199 Total Man Hours						
8	EAA Site Contractors LLC		8	8.0	64.0	Site
<b>Notes:</b> Total man hours 77. EAA continued to dig retention pond today. Also continued to place dirt in section A and B. Also continued to place dirt on East side of section C.						
9	Larry M. Jacobs & Associates, Inc.		1	1.0	1.0	Site>Stormwater Pond
<b>Notes:</b> Conducted Density test in the Stormwater Pond						
			<b>73</b>	<b>663.0</b>		

**Manpower Log's Attachments:**

- 1. A&B Electric Co., Inc.

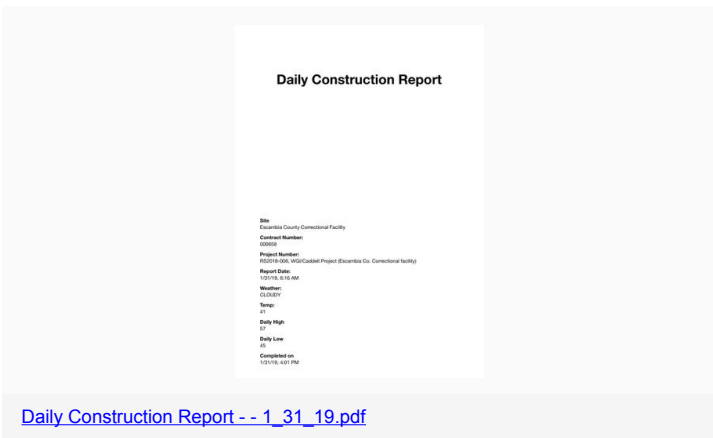

[Daily Construction Report - - 1\\_31\\_19.pdf](#)

- 2. Bayside Structures, LLC



[Bayside Daily 1-31-2019.PDF](#)

4. Chavers Construction Inc.

[Chaver Daily 1-31-2019.PDF](#)

5. Ed Emmons Steel Erectors, Inc.

[New Doc 2019-01-31 15.18.36.pdf](#)

6. Nash Plumbing and Mechanical, LLC

[Nash Daily 1-31-2019 \(1\).xlsx](#)

7. Tindall Corporation

[Tindall Escambia daily 1-31-2019.xlsx](#)

**EQUIPMENT LOG**

No.	Equipment Name	Cost Code	Hrs Operating	Hrs Idle	Inspected?	Inspection Time	Location
1	Genie Lift S85				No	07:00 AM	Building>A
	<b>Notes:</b>						
2	JLG Lift 660SJ				No	07:00 AM	Building>A
	<b>Notes:</b>						
3	John Deere 550H Dozer				No	07:00 AM	Building>B
	<b>Notes:</b>						
4	John Deere Skidsteer				No	07:00 AM	Building>B
	<b>Notes:</b>						
5	Kobelco Crane CKE2500				No	07:00 AM	Building>D
	<b>Notes:</b>						
6	JLG Lift 660SJ				No	07:00 AM	Building>D
	<b>Notes:</b>						

## EQUIPMENT LOG

No.	Equipment Name	Cost Code	Hrs Operating	Hrs Idle	Inspected?	Inspection Time	Location
7	Scissor Lift				No	07:00 AM	Building>D
	<b>Notes:</b>						
8	Scissor Lift				No	07:00 AM	Building>D
	<b>Notes:</b>						
9	Grove Crane AT700D				No	07:00 AM	Building>D
	<b>Notes:</b>						
10	Bobcat Skidsteer				No	07:00 AM	Building
	<b>Notes:</b>						
11	Volvo 330 Excavator				No	07:00 AM	Site>Stormwater Pond
	<b>Notes:</b>						
12	Volvo 330 Excavator				No	07:00 AM	Site
	<b>Notes:</b>						
13	Terex Articulated Dump Truck				No	07:00 AM	Site>Stormwater Pond
	<b>Notes:</b>						
14	John Deere 750 Dozer				No	07:00 AM	Site>Stormwater Pond
	<b>Notes:</b>						
15	Cat Telehandler				No	07:00 AM	Site
	<b>Notes:</b>						
16	JLG Skytrak Telehandler				No	07:00 AM	Site
	<b>Notes:</b>						
17	John Deere 700 Dozer				No	07:00 AM	Site
	<b>Notes:</b>						

## INSPECTION LOG

No.	Start Time	End Time	Inspection Type	Inspecting Entity	Inspector Name	Location	Area
1	12:00 PM	01:00 PM	Third Party	Mott MacDonald	Mike Tugwell	Building>D	
	<b>Comments:</b> Threshold inspection in Area D Line 50 Dowel installation						

By \_\_\_\_\_

Date \_\_\_\_\_

Copies To \_\_\_\_\_

**Committee of the Whole**

**6.**

**Meeting Date:** 02/14/2019

**Issue:** Gulf Coast Minority Chamber of Commerce

**From:** Amy Lovoy, Assistant County Administrator

---

**Information**

**Recommendation:**

Gulf Coast Minority Chamber of Commerce

(Brian Wyer, President/CEO, Gulf Coast Minority Chamber of Commerce - 20 min)

A. Board Discussion

B. Board Direction

---

**Attachments**

*No file(s) attached.*

---

**Committee of the Whole**

7.

**Meeting Date:** 02/14/2019

**Issue:** Escambia County Healthy Start Coalition, Inc.

**From:** Amy Lovoy, Assistant County Administrator

---

**Information**

**Recommendation:**

Escambia County Healthy Start Coalition, Inc.

(Teresa Neal - 20 min)

A. Board Discussion

B. Board Direction

---

**Attachments**

*No file(s) attached.*

---

**Committee of the Whole**

8.

**Meeting Date:** 02/14/2019

**Issue:** Rolling Hills Update

**From:** Chips Kirschenfeld, Director

---

**Information**

**Recommendation:**

Rolling Hills Update

(Chips Kirschenfeld - 15 min)

A. Board Discussion

B. Board Direction

---

**Attachments**

*No file(s) attached.*

---

**Committee of the Whole**

9.

**Meeting Date:** 02/14/2019

**Issue:** Interim Medical Examiner

**From:** Alison Rogers, County Attorney

---

**Information**

**Recommendation:**

Interim Medical Examiner  
(Alison Rogers - 15 min)

- A. Board Discussion
  - B. Board Direction
- 

**Attachments**

Okaloosa County Letter to Mr. Borowski

Florida Administrative Code

---

TALLAHASSEE  
1500 Mahan Drive  
Suite 200  
Tallahassee, Florida 32308  
(850) 224-4070 Tel  
(850) 224-4073 Fax

**Nabors  
Giblin &  
Nickerson** P.A.  
ATTORNEYS AT LAW

TAMPA  
2502 Rocky Point Drive  
Suite 1060  
Tampa, Florida 33607  
(813) 281-2222 Tel  
(813) 281-0129 Fax

FORT LAUDERDALE  
110 East Broward Boulevard  
Suite 1700  
Fort Lauderdale, Florida 33301  
(954) 315-3852 Tel

Reply to Tallahassee

December 21, 2018

Via Electronic Mail

Ted A. Borowski, Esquire  
Borowski & Taylor, P.A.  
Post Office Box 12651  
Pensacola, Florida 32591-7465  
[ted@borowski-traylor.com](mailto:ted@borowski-traylor.com)

Re: Medical Examiner Contracts

Dear Ted:

Please accept this as the response of Walton County, Okaloosa County, Santa Rosa County and Escambia County to your proposal contained in your letter of November 21<sup>st</sup>.

The representatives of the four counties comprising District One have had the opportunity to review your proposal in detail and though we understand the approach and rationale that you have suggested, we believe that the approach does not address some of the concerns that have been raised in the past. Initially, your suggested approach creates a situation where the counties would establish a budgetary amount but have no ability to know whether that amount would be realistic in regard to their actual obligations by the end of the year. All counties, to the extent possible need to establish some degree of financial certainty in the amounts allocated for Medical Examiner services. Further, your suggested approach would continue to allow the payment of professional fees based upon the number of procedures and not the number of individuals performing those procedures. This is an approach that has created significant concerns among the counties. Therefore, we must reject your proposal.

However, as an alternative approach for the establishment of professional services salaries, we would propose the following for the payment of the Chief Medical Examiner and Associate Medical Examiner services:



Ted A. Borowski, Esquire  
December 21, 2018  
Page 2

<u>POSITION</u>	<u>SALARY</u>	<u>BENEFITS</u>	<u>TOTAL</u>
Chief Medical Examiner	\$300,000	\$50,000*	\$350,000
Associate Medical Examiner	\$200,000	\$36,000*	\$236,000
<b>TOTAL</b>			<b>\$586,000</b>

\*Benefits consist of Medicare, Social Security, Health Benefits, Retirement and Workers Compensation and Payroll Fee. (Total benefit rate is calculated at a rate of 20.22% of salary). These amounts are consistent with the benefits charged by the Medical Examiner in the past.

This proposal has not been approved by any of the Boards of County Commissioners of any of the four Counties and is subject to their approval.

In the application of these amounts, the payments would be made on a reimbursement basis so if there is a vacancy or a position is not receiving a particular benefit, then only the amounts paid for an actual medical examiner providing services would be reimbursed. Additionally, the use of a physician operating as a Locum Tennen would not be deemed a substitute for an Associate Medical Examiner nor paid from the appropriation for either the Chief Medical Examiner or the Associate Medical Examiner. The cost for those services should be included as a separate cost in the Medical Examiners budget submission, perhaps under the Contracted Fees or Services category.

To the extent that there is a need to add additional Associate Medical Examiners as a result of workload increases, then the request for funding of that position should be included as part of the annual budget submission request. However, to the extent that there is a need to fund an additional position during the course of a fiscal year, then the budget amendment process would be available to Dr. Minyard and would need to be utilized.

It is recognized that a review of the format of the budget submissions and the establishment of clear guidelines as to what expenditures are included within the various categories is necessary. However, for the purpose of this fiscal year, we believed that is essential to attempt to resolve the issue of payments to the Chief Medical Examiner and Associate Medical Examiner before we begin that review process. This proposal is intended as an effort to resolve the immediate issue with the understanding that discussions will need to occur to clarify the process for future years.

We would appreciate it if you would review this proposal and let me know if it is acceptable. If so, we will then prepare a revised agreement to be utilized by all four counties with these amounts and terms regarding locum tenens, reimbursable expenses and conditions for budget

Ted A. Borowski, Esquire  
December 21, 2018  
Page 3

amendments. We will then schedule the approval of the uniform contract with our respective Board of County Commissioners.

Sincerely,

A handwritten signature in black ink, appearing to be 'G. T. Stewart', with a stylized flourish at the end.

*for* Gregory T. Stewart  
County Attorney  
Okaloosa County, Florida

GTS:lll

cc: (via Electronic Mail)  
Charles Pepler, Esq.  
Alison Rogers, Esq.  
Roy Andrews, Esq.  
Sidney Noyes, Esq.

**West's Florida Administrative Code**  
**Title 11. Department of Law Enforcement**  
**Subtitle 11g. Medical Examiners Commission**  
**Chapter 11G-5. District Medical Examiners**

**Rule 11G-5.004, F.A.C.**  
**Fla. Admin. Code r. 11G-5.004**

**11G-5.004. Process for District Medical Examiner Candidate Nomination to the Governor.**

**Currentness**

(1) **Policy Statement.** Nominations for appointment as a district medical examiner shall be made only after solicitation of comments from city, county and state officials as well as from directors of funeral homes. Candidates nominated by the Medical Examiners Commission will be submitted to the Governor within 30 days after the Commission has voted on the matter. It is not the intent of the Commission to serve as the primary recruiting source for district medical examiner candidates, rather, the Commission intends that this responsibility should remain primarily within the district. The Commission will provide a medical examiner member of the Commission to participate in the candidate screening process at the district level.

(2) **Procedure for Nomination for Reappointment of District Medical Examiners.**

(a) Prior to the expiration of each incumbent district medical examiner's three year term of appointment, the Medical Examiners Commission staff shall survey by written correspondence the district's state attorney(s), public defender(s), sheriff(s), police chief(s), county commissioner(s), funeral home directors and a member of the local medical community. The survey will solicit input from each relevant to performance of the incumbent district medical examiner and ask for a "favorable" or "non-favorable" response regarding nomination for reappointment. Additionally, the survey will ask for suggestions for improving district medical examiner services. The survey shall request recommendations for the nomination of the incumbent or any other qualified candidate(s) to serve as district medical examiner.

(b) A summary of the survey results shall be provided to the Commission. Copies of the survey responses shall be forwarded to the incumbent district medical examiner by Commission staff. The incumbent, together with any other qualified candidates named in the survey responses, shall be notified in writing as to the date, time and place of the Commission meeting which will be considering the reappointment of the district medical examiner.

(c) The Commission chairman may request establishment of a committee, as referred to in paragraph 11G-5.004(3)(b), F.A.C., to address concerns regarding the incumbent district medical examiner raised in the survey responses or to initiate a search for other candidates for nomination by the Commission.

(3) **Procedure to fill a District Medical Examiner Vacancy.**

(a) The Governor will be notified by the Commission upon determination that a district medical examiner position has become vacant or is anticipated to become vacant. The Commission shall also notify the respective state attorney(s), public defender(s), sheriff(s), police chief(s), county commission(s) and funeral home directors for that medical examiner district, requesting that names of potential candidates for the position of district medical examiner be submitted to the candidate search committee established in paragraph [FN1] 11G-5.004(3)(b), F.A.C.

(b) Within 30 days of being notified of a vacancy or anticipated vacancy, the Chairman of the Commission shall call for a district candidate search committee to be established and appoint a chairman. The search committee shall consist of invited representatives from the offices of the state attorney(s), public defender(s), sheriff(s), police chief(s), county commission(s), funeral homes and a representative of the local medical community from within the bounds of that particular medical examiner district and a physician member of the Medical Examiners Commission or other medical examiner designated by the Chairman. The search committee shall be requested to:

1. Seek applications from interested candidates who are licensed physicians and experienced practitioners of pathology who possess qualifications to take the examination or already possess the primary certification offered by the American Board of Pathology, American Osteopathic Board of Pathology, or equal qualification rendered by a non-United States medical specialty certifying agency.
2. Establish an interview team, which shall have a quorum of three participants, to interview interested candidates meeting minimum position qualifications. If the district includes a medical school, the dean of the medical school should be invited to participate as a member of the interview team.
3. Assure that the candidate(s) recommended to the Commission for nomination as district medical examiner is in agreement with the respective county representatives regarding the medical examiner budget as outlined in Section 406.06(3), F.S.
4. Review background information about the final candidate(s) from present and past sources, to include a criminal history check, comments of county medical associations, employment references, local hospitals, government agencies and funeral homes with which the candidate(s) has a prior working relationship. Background inquiries should incorporate information on work performance and working relationships, as well as the candidate(s) reasons for and circumstances of leaving employment.
5. Submit an interview package to the Medical Examiners Commission staff for each candidate recommended to the Commission for nomination consisting of: pertinent correspondence regarding the candidate(s); results of background inquiries; letters of reference; and a letter from the candidate(s) to the Commission staff authorizing the release of information from former employers and the Board of Medicine in the state in which the candidate(s) is or was licensed.
6. Complete the candidate selection and interview process and submit interview packages to the Commission within 90 days of appointment of the candidate search committee unless additional time is requested in writing and approved by the Commission Chairman.

(c) The Commission staff shall review interview packages for completeness, prior to their being submitted to the Medical Examiners Commission and, if directed by the Chairman, make additional inquiries concerning the candidate's background or qualification.

1. The Commission staff shall verify each candidate's medical licensure status.

2. The Commission staff shall notify all candidates in writing of the time and place of the Commission meeting at which the district nomination(s) will be considered.

(d) The Commission, by majority vote, shall nominate one or more candidates to the Governor, to fill a district medical examiner office vacancy prior to the expiration of six months from the date of the vacancy. Nothing herein is intended to restrict the Commission's consideration of candidates for nomination only to those persons who may be recommended by a candidate search committee.

(e) The Commission will notify each candidate in writing as to the action taken by the Commission regarding their nomination as district medical examiner.

(f) The Commission will notify the chairman of the candidate search committee in writing on action taken by the commission regarding candidates submitted by the district to fill a district medical examiner vacancy. If the Commission does not vote to nominate any of the candidates submitted by the candidate search committee, the chairman of the committee may be requested to submit other candidates. The Office of the Governor will be notified that none of the candidates submitted for that district were acceptable and that the position is still vacant.

#### Credits

Adopted Feb. 23, 1993; Amended Sept. 27, 1993. Amended May 21, 2012.

Authority: 406.04 FS. Law Implemented 406.06(1)(a) FS.

[FN1]

So in original.

Current with amendments available through February 4, 2019.

Rule 11G-5.004, F.A.C., 11 FL ADC 11G-5.004
