



## AGENDA

### COMMITTEE OF THE WHOLE WORKSHOP BOARD OF COUNTY COMMISSIONERS

Board Chambers  
Suite 100  
Ernie Lee Magaha Government Building - First Floor  
221 Palafox Place

March 14, 2019  
9:00 a.m.

Escambia County is committed to making our website accessible. If you use assistive technology, for example a screen reader, and have difficulty accessing information in this agenda online, please contact our ADA Coordinator at [ADA@myescambia.com](mailto:ADA@myescambia.com) or 850-595-1637.

**Notice: This meeting is televised live on ECTV and recorded for rebroadcast on the same channel. Refer to your cable provider's channel lineup to find ECTV.**

1. Call to Order  
  
(PLEASE TURN YOUR CELL PHONE TO THE SILENCE OR OFF SETTING.)
2. Was the meeting properly advertised?
3. Economic Development Update  
(Scott Luth, Chief Executive Officer, FloridaWest Economic Development Alliance - 10 min)
  - A. Board Discussion
  - B. Board Direction
4. Master Developers for the Midtown Commerce Park  
(Jason Nail, Parkside Partners - 30 min)
  - A. Board Discussion
  - B. Board Direction
5. New Escambia County Correctional Facility Progress Report  
(Roland Koomen, Bay Design/George Bush, Facilities Management - 15 min)
  - A. Board Discussion
  - B. Board Direction

6. American Red Cross Shelter Staffing  
(John Dosh, Public Safety - 15 min)
  - A. Board Discussion
  - B. Board Direction
  
7. County Administrator Search  
(Amy Lovoy - 15 min)
  - A. Board Discussion
  - B. Board Direction
  
8. Adjourn

**Committee of the Whole**

**3.**

**Meeting Date:** 03/14/2019

**Issue:** Economic Development Update

**From:** AMY LOVOY, Interim County Administrator

---

**Information**

**Recommendation:**

Economic Development Update

(Scott Luth, Chief Executive Officer, FloridaWest Economic Development Alliance - 10 min)

A. Board Discussion

B. Board Direction

---

**Attachments**

*No file(s) attached.*

---

**Committee of the Whole**

**4.**

**Meeting Date:** 03/14/2019

**Issue:** Master Developers for the Midtown Commerce Park

**From:** AMY LOVOY, Interim County Administrator

---

**Information**

**Recommendation:**

Master Developers for the Midtown Commerce Park  
(Jason Nail, Parkside Partners - 30 min)

- A. Board Discussion
  - B. Board Direction
- 

**Attachments**

EMC2 Presentation

Parkside Partners MOU

Letter from Chamblee Mayor

---

# EMC2

*March 14, 2019*



**PARKSIDE** PARTNERS

# Table of Contents

---

Section I – Parkside Partners Overview

Section II – Project Vision

Section III – Marketing Strategy

Section IV – Due Diligence Summary

Section V – Key Prospects

## Parkside Partners

- Atlanta-based commercial real estate development and investment firm founded in 2003
- Recognized leader in adaptive re-use, new ground-up development and value-add real estate investments
- Firm commitment to projects that contribute economically, aesthetically, environmentally and experientially to the community
- Combined total of more than 100 years experience in development, marketing, leasing and investment management



**PARKSIDE PARTNERS**

## DEVELOPMENT SNAPSHOT

---

### MARKET EXPOSURE

**BUCKHEAD · CHAMBLEE · WESTSIDE · BROOKHAVEN · PEACHTREE CORNERS · MIDTOWN · TECH PARK · INMAN PARK · EAST ATLANTA · NORTH FULTON**

---

<b>15</b> YEARS IN BUSINESS	<b>8</b> TRANSIT-ORIENTED DEVELOPMENTS WALKING DISTANCE TO MARTA
<b>37</b> ACQUIRED OR DEVELOPED PROJECTS	<b>9</b> PROJECTS ON THE BELTLINE

---

Development Characteristics:

TRANSIT ORIENTED	SCALABLE
ADAPTIVE REUSE	URBAN INFLUENCE

---

6 current projects under development, totaling	Development reach totaling over
<b>580K SF</b>	<b>1.7MM SF</b>

## Mercy Care Chamblee

- Size: 45,000 SF
- Location: Chamblee, GA
- Features: Land Development, Environmental
- Medical & Housing



## Edison at Eastside

- Size: 330,000 SF
- Location: Chamblee, GA
- Key Features: Land Development, Infrastructure, Master Planning, FAA Restrictions, Entitlements, Bond Financing



## 1280 West Peachtree

- Size: 42,000 SF
- Location: Midtown Atlanta
- Features: LEED Platinum, WELL Certified
- Corporate Headquarters Relocation



## Trackside

- Size: 74,000 SF
- Location: Chamblee, GA
- Features: Public Private Partnership, Environmental, LEED, Public Bond Financing

## Boundary

- Size: 155,000 SF
- Location: Midtown Atlanta
- Features: Public Bond Financing
- Adaptive-Reuse



## Bureau

- Size: 90,000 SF to 120,000 SF
- Location: Norcross, GA
- Features: Environmental
- Corporate Office / R&D

Parkside Partners has developed strong relationships with the following lenders, among others.



## Overview

The development team's objective for Escambia Midtown Commerce Campus (EMC2) is to revitalize the underutilized 87-acre remediated superfund site in the heart of Pensacola into a state-of-the-art business environment for companies at the forefront of their respective industries.



*Potential Entrance for the Proposed Escambia Midtown Commerce Campus (EMC2).*

## Key Objectives

**Economic Growth**



**Local Workforce**



**Stakeholder Collaboration**



**Infrastructure**




**Sustainability**



**Innovation**



- Partnership with state, county and local economic development organizations such as FloridaWest and Gulf Power
- Brokerage partner with local, regional and national experience
- Maximizing functionality, sustainability and the benefit to Pensacola and Escambia County
- Other key stakeholders identified during Due Diligence



During the Due Diligence Period, the development team will engage in the following studies and analyses, among others:

- Confirm Entitlements
- Develop Conceptual Master Plan
- Perform Applicable Geotechnical Studies
- Confirm Environmental Condition Impact on Development
- Market Analysis
- Project Pricing
- Financing

## National Energy (50,000 SF, Lead Tenant)

*Energy Management Strategy Development & Technology Consulting*

## WastAway, LLC (200,000 SF)

*Hi-Tech Recycling*

## DeSol Power Tiles, LLC (160,000 SF)

*Solar Power Tile Manufacturing*

# MEMORANDUM OF UNDERSTANDING

**THIS MEMORANDUM OF UNDERSTANDING** (this “**MOU**”) is executed as of this \_\_\_\_ day of \_\_\_\_\_, 2019 (the “**Effective Date**”) by and among the **ESCAMBIA COUNTY, FLORIDA** (the “**County**”) and **PARKSIDE PARTNERS, LLC**, a Georgia limited liability company (the “**Tenant**,” and, together with the County, the “**Parties**”).

**WHEREAS**, the County owns that certain parcel of land containing approximately 87 acres in the southern Palafox area of Pensacola, Florida more accurately depicted on Exhibit A attached hereto and by this reference incorporated herein (the “**Property**”);

**WHEREAS**, the Parties intend to enter into a ground lease agreement whereby the County will lease the Property to Tenant for a term of ninety-nine (99) years pursuant to the terms and conditions set forth in such agreement (the “**Ground Lease**”) to allow for Tenant’s development of the Property (the “**Project**”);

**WHEREAS**, prior to entering into the Ground Lease, Tenant wishes to perform certain inspections and evaluations of the Property in order to determine its suitability for the Project;

**NOW THEREFORE**, the Parties hereby agree to the following terms and conditions:

## **I. GENERAL CONDITIONS**

1. This MOU shall give Tenant the exclusive right to negotiate and finalize a definitive Ground Lease with the County for a period of six (6) months from the date hereof. During this 6-month negotiation time period, Tenant shall have the right to negotiate and to enter into agreements with third parties for the purpose of securing commitments to become involved in the Project, including, but not limited to, construction, leasing or investing therein which agreements may be binding, subject only to the execution of the Ground Lease.
  2. Unless superseded by an amendment to this MOU or the Ground Lease, this MOU identifies the understanding of the Parties.
  3. The Ground Lease shall, in addition to any other items negotiated between the Parties, contain the following terms:
    - a. The term of the Ground Lease shall be ninety-nine (99) years.
    - b. The initial rent rate under the Ground Lease payable by Tenant shall be Fifty Thousand and No/00 Dollars (\$50,000.00) per year and shall increase by no more than ten percent (10%) every ten (10) years. The Ground Lease shall be “triple-net,” whereby all costs associated with
-



insurance, taxes and maintenance shall be passed through to Tenant and shall be Tenant's sole responsibility.

- c. The County shall continue to be responsible for any and all costs associated with environmental monitoring, cleanup, compliance and all other expenses associated with the Property's previous environmental contamination.

## II. PURPOSE

1. This MOU is entered into with the understanding by the Parties that Tenant shall have the right, subject to the terms and conditions hereof, to enter onto the Property and to conduct such inspections, evaluations and assessments as it deems necessary to assess the feasibility of the Project including, without limitation, title searches, engineering studies, environmental site assessments and surveying. Tenant may, subject to the terms and conditions of this MOU, terminate this MOU at any time, at which point this MOU shall be of no further force and effect and neither Party shall have any further rights or obligations hereunder, except those which expressly survive the termination or expiration of this MOU.

## III. DUE DILIGENCE PERIOD

1. Upon the satisfaction of the condition described in Section III.2 below, Tenant and its agents, representatives, consultants and/or contractors (hereinafter collectively referred to as "**Tenant's Agents**") shall have the right, at Tenant's sole cost and expense and upon reasonable prior written notice to the County, to enter the Property at reasonable times and in a reasonable manner for the purpose of making such tests and inspections (the "**Inspection**") as Tenant deems necessary or desirable in connection with the planning and development of the Project. In no event shall Tenant conduct any drilling, boring or other invasive testing on any part of the Property, without the County's prior written consent, not to be unreasonably withheld, conditioned or delayed.
  2. Tenant shall obtain or cause Tenant's Agents to obtain, at Tenant's sole cost and expense prior to commencement of any investigative activities on the Property, a policy of commercial general liability insurance covering any potential liability of Tenant and the County with respect to or arising out of any investigative activities on the Property. Such policy of insurance shall be kept and maintained in force during the term of this MOU and so long thereafter as necessary to cover any claims of damages suffered by persons or property resulting from any acts or omissions of Tenant or Tenant's Agents. Such policy of insurance shall have liability limits of not less than Two Million Dollars (\$2,000,000.00) combined single limit per occurrence for bodily injury, personal injury and property damage liability and shall name the County as an additional insured.
-

3. Within three (3) business days following the Parties' execution of this MOU, the County shall deliver to Tenant for its review, copies of those documents, materials and/or information listed on Exhibit B attached hereto which are in the County's possession. Except as required by law or otherwise consented to in writing by the County, Tenant agrees to keep confidential and not to use, other than in connection with its determination whether to proceed with entering into the Ground Lease, any of the documents, material or information regarding the Property supplied to Tenant by the County, except Tenant may share such documents, material and information with Tenant's consultants, investors, members, attorneys and necessary employees, as well as prospective lenders and their consultants, attorneys and necessary employees, unless Tenant is required to disclose such documents, material or information by law or by subpoena.
  
4. TENANT SHALL PROTECT, INDEMNIFY, DEFEND AND HOLD THE PROPERTY, THE COUNTY AND THE COUNTY'S OFFICERS, AFFILIATES, EMPLOYEES, REPRESENTATIVES, INVITEES, AGENTS AND CONTRACTORS FREE AND HARMLESS FROM AND AGAINST ANY AND ALL CLAIMS, DAMAGES, LIENS, STOP NOTICES, LIABILITIES, LOSSES, COSTS AND EXPENSES, INCLUDING REASONABLE ATTORNEYS' FEES AND COURT COSTS, DIRECTLY CAUSED BY TENANT'S INSPECTION AND TESTING OF THE PROPERTY, INCLUDING, WITHOUT LIMITATION, REPAIRING ANY AND ALL DAMAGES TO ANY PORTION OF THE PROPERTY, TO THE EXTENT CAUSED BY TENANT'S CONDUCTING SUCH INSPECTIONS, SURVEYS, TESTS, AND STUDIES; PROVIDED, HOWEVER, TENANT'S OBLIGATIONS UNDER THE FOREGOING INDEMNITY SHALL NOT APPLY TO (I) ITEMS RESULTING FROM THE NEGLIGENCE OR WILLFUL MISCONDUCT OF THE COUNTY OR ITS AGENTS, EMPLOYEES, REPRESENTATIVES OR CONTRACTORS OR (II) THE EXISTENCE OR DISCOVERY OF ANY EXISTING ENVIRONMENTAL OR PHYSICAL CONDITIONS AT THE PROPERTY. TENANT SHALL KEEP THE PROPERTY FREE AND CLEAR OF ANY MECHANICS' LIENS OR MATERIALMEN'S LIENS RELATED TO TENANT'S RIGHT OF INSPECTION AND RELATED ACTIVITIES.

#### **IV. TERMINATION**

1. This MOU shall terminate, and the rights granted to Tenant hereunder shall expire, upon the earlier of (i) date which the Parties cease negotiations to enter into the Ground Lease, (ii) the date which the Parties execute the binding Ground Lease; or (iii) the date which is six (6) months following the Effective Date. Notwithstanding anything contained herein to the contrary, Tenant reserves the right to terminate this MOU at any time in its sole and absolute discretion upon prior written notice to the County.
-

## **V. EXCLUSIVITY**

1. While this MOU is in effect, the County agrees (i) not to market the Property, (ii) not to solicit or accept any other offers for the Property, and (iii) to negotiate for the leasing and development of the Property exclusively with Tenant.

## **VI. ATTORNEY'S FEES**

1. If either Party commences an action against the other to interpret or enforce any of the terms of this MOU or because of the breach by the other Party of any of the terms hereof, the losing party shall pay to the prevailing party reasonable attorneys' fees, costs and expenses incurred in connection with the prosecution or defense of such action, whether or not the action is prosecuted to a final judgment.

## **VII. MISCELLANEOUS**

1. This MOU shall be governed by the laws of the State of Florida.
  2. Time is of the essence of this MOU.
  3. This MOU shall inure to the benefit of and be binding upon the respective Parties and their heirs, successors and assigns.
  4. This MOU contains the entire understanding and agreement between the Parties, and supersedes any and all prior agreements and commitments.
  5. Any provisions of this MOU which shall prove to be invalid, void or illegal shall in no way effect, impair or invalidate any other provisions hereof and such other provisions shall remain in full force and effect.
  6. This MOU may not be amended or modified except in writing and signed by the party against whom the amendment or modification is sought to be applied.
  7. This MOU may be executed in one or more counterparts, each of which shall be deemed an original, and together which shall constitute one and the same instrument.
-

**SIGNATURES**

The Parties to this MOU hereby acknowledge their intent to negotiate in good faith to agree upon and finalize a definitive Ground Lease pursuant to the terms herein.

Each party executing this MOU represents that it has the right, power and authority to enter into this MOU and to perform the obligations hereunder.

**COUNTY:**

**[ESCAMBIA COUNTY SIGNATURE  
BLOCK]**

By: \_\_\_\_\_

*[Signatures continue on following page]*

**TENANT:**

**PARKSIDE PARTNERS, LLC**, a Georgia  
limited liability company

By: \_\_\_\_\_

Name: \_\_\_\_\_

Its: \_\_\_\_\_

*[End of signatures]*

---

**EXHIBIT A**

**The Property**

## **EXHIBIT B**

- Most recent policy
  - Most recent
  - Most recent environmental reports
  - Most recent zoning reports
  - Most recent soils reports
  - Most recent geotechnical reports
  - All other documentation or information reasonably necessary for Tenant's inspection, development and operation of the Project
-



CITY OF CHAMBLEE

5468 PEACHTREE ROAD CHAMBLEE, GA 30341

December 14, 2016

To Whom It May Concern:

During my tenure as the Mayor of Chamblee, the City has had the opportunity to work with Parkside Partners on a number of their commercial projects. I can attest to their professionalism, creativity, and the high quality of their work.

Since 2008, Parkside has completed 4 office projects totaling over 100,000 square feet of space in the City. Currently, they have 3 additional projects underway for an additional 200,000 square feet. Once completed, Parkside will have developed 300,000 square feet of office space, bringing more than 1,200 new jobs to the City through numerous employers including AGL, St. Joseph's / Mercy Care, Pattillo Industrial Real Estate, and numerous technology and service companies. Chamblee has greatly benefited from Parkside's vision and efforts, and we would recommend them to any municipality that is considering working with them.

The largest and most creative project to date is Trackside, which is a joint-venture between Parkside and Pattillo Industrial Real Estate on a 2 acre site owned by MARTA. Trackside will contain 80,000 square feet of office and retail space with a three-level parking garage. This transaction was extremely complex, involving not only MARTA, Chamblee and Trackside, but many of the surrounding property owners. MARTA required a rigorous RFQ and RFP process, and Trackside's team presented the most creative and viable option for the site. Chamblee will benefit from Class A office space at one of the most visible corners in the City.

Please feel free to contact me with any questions about Parkside and its team of professionals. They have exceeded the expectations of Chamblee, and we look forward to continuing to work together in the future.

Sincerely,

  
R. Eric Clarkson  
Mayor



**Committee of the Whole**

**5.**

**Meeting Date:** 03/14/2019

**Issue:** Progress Report on New Correctional Facility

**From:** AMY LOVOY, Interim County Administrator

---

**Information**

**Recommendation:**

New Escambia County Correctional Facility Progress Report  
(Roland Koomen, Bay Design/George Bush, Facilities Management - 15 min)

A. Board Discussion

B. Board Direction

---

**Attachments**

presentation

DBE progress report

---

# New Escambia County Correctional Facility

Progress update

Roland Koomen – Bay Design

George Bush – Facilities Management

## Key Points

- Construction Progress
  - Formed, reinforced and poured concrete for:
    - connector foundations and walls.
    - Sequence 1 & 2 of the slab-on-grade at the corridor.
    - Sequence 1 of Elevation 115 (3<sup>rd</sup> floor) in Area D.
  - Rough in of underground electrical conduits in Area C completed.
  - Under ground plumbing in Areas A and C installed.
    - Floor drains, roof drains and sleeves installed at elevation 115 (3<sup>rd</sup> Floor), Area D sequence 1.
  - Excavation of storm water pond reached design depth (35ft).
    - Storm water piping and inlets between structures S-15 and S-23 completed.
  - Installation of Domestic and Fire Main piping connections completed.
    - Backflow preventer installed
  - Critical path update
    - 28 May of 2020 - substantial completion

## Ongoing activity

### Continuing:

- Precast wall panels
  - Area C 100% complete
  - Area A 33% complete
- Structural Steel
- Stairways
- Storm water pond
  
- Continue to reduce delta on timeline

Next progress update – April Committee of the Whole



**New Escambia County Correctional Facility**

**PD 16-17.004**

**Monthly Project Report  
February 2019**

## Table of Contents

<b>1.0 Progress Summary</b> .....	3
<b>2.0 Construction Progress</b> .....	4
<b>3.0 Design Build Entity Schedule</b> .....	4
<b>4.0 Design Status</b> .....	4
<b>5.0 Subcontractor Procurement</b> .....	5
<b>6.0 Design-Build Entity’s Safety Program</b> .....	5
<b>7.0 Disputes and Claims</b> .....	6
<b>8.0 Look Ahead Task List</b> .....	6
<b>9.0 Daily Log</b> .....	6

## 1.0 Progress Summary

ITEM	Description	COMMENTS
Original Contract Sum	\$132,445,243.00	
Change Order 1:	(-\$455,530.50)	ODP Change Order deduct for auger cast pile grout.
Change Order 2:	(\$-360.00)	Mathematical error with Alternate Number 5.
Change Order 3:	(-\$147,455.28)	ODP Change Order deduct for auger cast pile rebar.
Change Order 4:	(-\$28,769.30)	ODP Change Order deduct for additional auger cast pile rebar.
Change Order 5:	(-\$2,092,095.52)	ODP Change Order deduct for CIP Concrete and Rebar, Laundry Equipment, and Bi-Folding Doors.
Change Order 6:	(-\$463,697.91)	ODP Change Order deduct for Site Utility Piping and Structures.
Change Order 7:	(-\$32,731.48)	ODP Change Order deduct for Underground Electrical Raceways.
Change Order 8:	(-\$48,746.02)	ODP Change Order deduct for additional auger cast pile grout.
Change Order 9:	(-\$169,758.74)	ODP Change Order deduct for asphalt paving and corrections to existing POs.
Change Order 10:	(-\$9,005,200.12)	ODP Change Order deduct for structural steel, cell walls, hollow metal doors, door hardware and plumbing materials.
Change Order 11:	(-\$47,141.00)	ODP Change Order deduct for additional plumbing materials.
Change Order 12:	(-\$4,380,132.83)	ODP Change Order deduct for mechanical equipment, commercial HM and hardware, security glazing, and security electronics.
Change Order 13:	(-\$5,000,000.00)	Lump Sum ODP Deduct.
Adjusted Contract Sum	\$110,573,624.30	
Pending Change Order Request/Claims	NONE	
Original Date of Substantial Completion	May 28, 2020	
Forecast Date of Substantial Completion	June 29, 2020	<ul style="list-style-type: none"> <li>• -22 EA Work Days</li> <li>• -32 EA Calendar Days</li> </ul>

## 2.0 Construction Progress

Bayside Structures formed, reinforced and poured concrete for the connector foundations and walls. They also installed reinforcing and poured concrete for sequence 1 and sequence 2 of the slab-on-grade at the corridor. Bayside installed reinforcing and poured concrete for the sequence 1 pour of elevation 115 in Area D.

EAA Sitework continued excavating for the storm pond at the old JJC Parking lot, and they placed structural fill in areas A, B and D of the building.

A&B Electric installed the rough-in of underground conduits in Area C, and they installed temporary lighting in the corridor and in Areas A and D.

Emmons Steel Erectors erected stair A up to the second level, and they completed erecting steel and metal deck at Area D, elevation 115 for the sequence 1 pour. Emmons is currently erecting and detailing steel and metal deck at Area D, elevation 115 for sequence 2.

Tindall moved back to Area A, line 6 to continue erecting panels, grouting, welding and patching. They then moved to Area C and completed erecting precast in this area on February 26, 2018. Tindall has moved to Area D to begin setting the exterior panels from T line to 20.5 line.

Chavers Construction completed installation of storm piping and inlets between structures S-15 and S-23, and they demoed the existing stormwater utilities in the storm pond. They began installation of domestic water and fire main piping towards Fairfield Avenue.

Nash installed underground plumbing in Areas A and C of the building, and they installed floor drains, roof drains and sleeves at elevation 115, Area D sequence 1.

## 3.0 Design Build Entity Schedule

See attached Progress Schedule.

## 4.0 Design Status

### Summary:

The document submittal set for permitting is scheduled as follows:

- WGI/Caddell issued the Underground Permitting documents to the County Permitting Office for review on October 02, 2018.
- WGI/Caddell issued the Architectural, Structural, Fire Suppression and Life Safety Permitting documents to the County Permitting Office for review on October 10, 2018.



- WGI/Caddell issued the Mechanical, Plumbing, Telecommunications, Electrical, Fire Alarm, Security Electronics and Food Service Permitting documents to the County Permitting Office for review on November 07, 2018.
- WGI/Caddell received approved permitting documents for Underground, Architectural, Structural, FFE and Precast drawings on December 6, 2018.
- WGI/Caddell received approved Fire Suppression, Telecommunications and Plumbing permitting documents on January 10, 2019.
- WGI/Caddell received the Electrical, Security Electronics, Fire Alarm and Food Service Permitting documents on February 01, 2019.
- WGI/Caddell received the HVAC Permitting documents on March 01, 2019.

**Contract Deliverables:**

- Supplemental Instruction 009-Issued February 11, 2019
- Supplemental Instruction 010-Issued February 25, 2019

**Areas of Concern:**

- NONE

**Actions and Approvals Needed:**

- A partial FDOT permit has been issued for curb access closures, and WGI/Caddell has drafted a letter acknowledging future lighting work along Fairfield Blvd. GRW has provided FDOT with revised permit documents that are currently under review. The Shared Access Use Agreement was approved by the Board on February 28, 2019.

**Recommendations:**

- NONE

**5.0 Subcontractor Procurement**

- Irvine Access Floors-Raised Access Flooring
- Hill Enterprises-Folding Panel Partitions
- Knight Sign Industries, Inc.-Signage
- Porter Roofing Contractors-Roofing

**6.0 Design-Build Entity's Safety Program**

No incidents were recorded for the month of February 2019.

## **7.0 Disputes and Claims**

No disputes or claims were filed in the month of February 2019.

## **8.0 Look Ahead Task List**

See attached 90-day Look Ahead Schedule.

## **9.0 Daily Log**

See attached Daily Logs for the month of February 2019.

Activity ID	Activity Name	Orig Dur	Rem Dur	Prev Pct%	New Pct %	Actual Start	Actual Finish	Total Float	Early Start	Early Finish	Budgeted Cost	This Period Cost	Cost to Complete
ECCF16 28Feb19 Detailed Baseline Schedule Update		865	191			02-Jan-18		20	02-Jan-18 A	06-Sep-19	\$7,454,662.50	\$2,092,903.98	(\$618,122.52)
<b>Progress this Period</b>		<b>865</b>	<b>76</b>			<b>02-Jan-18</b>		<b>20</b>	<b>02-Jan-18 A</b>	<b>14-May-19</b>	<b>\$9,235,226.50</b>	<b>\$1,727,903.98</b>	<b>\$1,607,441.48</b>
<b>PRECONSTRUCTION</b>		<b>865</b>	<b>76</b>			<b>02-Jan-18</b>		<b>-30</b>	<b>02-Jan-18 A</b>	<b>14-May-19</b>	<b>\$6,285,564.00</b>	<b>\$754,267.68</b>	<b>\$314,278.20</b>
<b>WEATHER</b>		<b>5</b>	<b>0</b>			<b>01-Feb-19</b>	<b>28-Feb-19</b>		<b>01-Feb-19 A</b>	<b>28-Feb-19 A</b>	<b>\$0.00</b>	<b>\$0.00</b>	<b>\$0.00</b>
890010	ANTICIPATED ADVERSE WEATHER - FEB19	5	0	0%	100%	01-Feb-19	28-Feb-19		01-Feb-19 A	28-Feb-19 A	\$0.00	\$0.00	\$0.00
<b>DESIGN</b>		<b>14</b>	<b>1</b>			<b>10-Oct-18</b>		<b>75</b>	<b>10-Oct-18 A</b>	<b>28-Feb-19</b>	<b>\$0.00</b>	<b>\$0.00</b>	<b>\$0.00</b>
001420	EC REVIEW - FF&E DESIGN (100% DESIGN)	14	1	75%	95%	10-Oct-18		75	10-Oct-18 A	28-Feb-19	\$0.00	\$0.00	\$0.00
<b>PROCUREMENT</b>		<b>450</b>	<b>76</b>			<b>02-Jan-18</b>		<b>64</b>	<b>02-Jan-18 A</b>	<b>14-May-19</b>	<b>\$6,285,564.00</b>	<b>\$754,267.68</b>	<b>\$314,278.20</b>
010000	PROCUREMENT OF LONG-LEAD ITEMS	450	76	30%	40%	02-Jan-18		64	02-Jan-18 A	14-May-19	\$0.00	\$0.00	\$0.00
010031	PRECAST PROCUREMENT - MATERIAL COST	1	1	83%	95%	26-Sep-18		124	26-Sep-18 A	28-Feb-19	\$6,285,564.00	\$754,267.68	\$314,278.20
<b>CONSTRUCTION</b>		<b>525</b>	<b>44</b>			<b>16-Jul-18</b>		<b>412</b>	<b>16-Jul-18 A</b>	<b>12-Apr-19</b>	<b>\$2,949,662.50</b>	<b>\$973,636.30</b>	<b>\$1,293,163.28</b>
<b>DESIGN</b>		<b>25</b>	<b>18</b>			<b>05-Sep-18</b>		<b>438</b>	<b>05-Sep-18 A</b>	<b>17-Mar-19</b>	<b>\$1,626,811.50</b>	<b>\$65,072.46</b>	<b>\$1,171,304.28</b>
003000	A/E CONSTRUCTION ADMINISTRATION SERVICES (25 MONTHS)	25	18	24%	28%	05-Sep-18		438	05-Sep-18 A	17-Mar-19	\$1,626,811.50	\$65,072.46	\$1,171,304.28
<b>SITework</b>		<b>213</b>	<b>32</b>			<b>16-Jul-18</b>		<b>168</b>	<b>16-Jul-18 A</b>	<b>12-Apr-19</b>	<b>\$316,295.00</b>	<b>\$155,836.00</b>	<b>\$96,859.00</b>
100002	MAINTAIN EROSION CONTROLS (25 MONTHS)	25	17	28%	32%	16-Jul-18		183	16-Jul-18 A	22-Mar-19	\$70,000.00	\$2,800.00	\$47,600.00
100100	SITE GRADING - STORMWATER POND (EXIST SE JUV P.I.O.T)	10	2	20%	80%	21-Jan-19		46	21-Jan-19 A	01-Mar-19	\$220,000.00	\$132,000.00	\$44,000.00
112000	SITE UTILITIES - WATER WEST/NORTH (INCL CONNECTOR/CORRIDOR)	10	2	0%	80%	09-Feb-19		66	09-Feb-19 A	12-Apr-19	\$26,295.00	\$21,036.00	\$5,259.00
<b>CORRECTIONAL FACILITY</b>		<b>163</b>	<b>5</b>			<b>24-Oct-18</b>		<b>158</b>	<b>24-Oct-18 A</b>	<b>06-Mar-19</b>	<b>\$1,006,556.00</b>	<b>\$752,727.84</b>	<b>\$25,000.00</b>
200300	STRUCTURAL BACKFILL A	5	0	60%	100%	24-Oct-18	15-Feb-19		24-Oct-18 A	15-Feb-19 A	\$8,328.00	\$3,331.20	\$0.00
200320	STRUCTURAL BACKFILL B	8	0	37%	100%	29-Oct-18	08-Feb-19		29-Oct-18 A	08-Feb-19 A	\$8,328.00	\$5,246.64	\$0.00
200450	UNDER SLAB PLUMBING C (1/2)	10	0	0%	100%	28-Jan-19	08-Feb-19		28-Jan-19 A	08-Feb-19 A	\$50,000.00	\$50,000.00	\$0.00
200455	UNDER SLAB PLUMBING C (2/2)	10	5	0%	50%	11-Feb-19		153	11-Feb-19 A	06-Mar-19	\$50,000.00	\$25,000.00	\$25,000.00
200590	SLAB ON GRADE CENTER CORRIDOR CL 3-14	5	0	0%	100%	08-Feb-19	15-Feb-19		08-Feb-19 A	15-Feb-19 A	\$25,000.00	\$25,000.00	\$0.00
200595	SLAB ON GRADE CENTER CORRIDOR CL 14-50	5	0	0%	100%	12-Feb-19	26-Feb-19		12-Feb-19 A	26-Feb-19 A	\$25,000.00	\$25,000.00	\$0.00
201020	IN-SLAB PLUMBING D 3RD LVL CL 14-29	5	0	0%	100%	18-Feb-19	21-Feb-19		18-Feb-19 A	21-Feb-19 A	\$50,000.00	\$50,000.00	\$0.00

<b>D/B New Correctional Facility Escambia Co., FL #1054</b>	ECCF16 28Feb19 Detailed Baseline Schedule Update	<b>ECCF16</b>	Page 1 of 4 01-Mar-19 08:09
<b>- Progress This Period: 28-Feb-19</b>			Data Date: 28-Feb-19

Activity ID	Activity Name	Orig Dur	Rem Dur	Prev Pct%	New Pct %	Actual Start	Actual Finish	Total Float	Early Start	Early Finish	Budgeted Cost	This Period Cost	Cost to Complete
201030	IN-SLAB PLUMBING D 3RD LVL CL 29-50	5	0	0%	100%	25-Feb-19	28-Feb-19		25-Feb-19 A	28-Feb-19 A	\$50,000.00	\$50,000.00	\$0.00
201220	IN-SLAB ELECTRICAL D 3RD LVL CL 14-29	5	0	0%	100%	18-Feb-19	19-Feb-19		18-Feb-19 A	19-Feb-19 A	\$50,000.00	\$50,000.00	\$0.00
201230	IN-SLAB ELECTRICAL D 3RD LVL CL 29-50	5	0	0%	100%	28-Feb-19	28-Feb-19		28-Feb-19 A	28-Feb-19 A	\$50,000.00	\$50,000.00	\$0.00
210000	PRECAST A (1/5)	15	0	33%	100%	21-Jan-19	06-Feb-19		21-Jan-19 A	06-Feb-19 A	\$200,000.00	\$134,000.00	\$0.00
210010	PRECAST A (2/5)	4	0	0%	100%	07-Feb-19	07-Feb-19		07-Feb-19 A	07-Feb-19 A	\$200,000.00	\$200,000.00	\$0.00
210120	STRUCTURAL STEEL D ELEV 115	5	0	40%	100%	22-Jan-19	15-Feb-19		22-Jan-19 A	15-Feb-19 A	\$50,000.00	\$30,000.00	\$0.00
210130	DETAIL STRUCTURAL STEEL D ELEV 115 (1/2)	13	0	0%	100%	11-Feb-19	15-Feb-19		11-Feb-19 A	15-Feb-19 A	\$10,000.00	\$10,000.00	\$0.00
210310	LARGE STAIR C A	6	0	0%	100%	01-Feb-19	28-Feb-19		01-Feb-19 A	28-Feb-19 A	\$4,900.00	\$4,900.00	\$0.00
211060	PRECAST D ELEV 100	9	0	77%	100%	15-Jan-19	30-Jan-19		15-Jan-19 A	30-Jan-19 A	\$175,000.00	\$40,250.00	\$0.00
<b>Change Original Duration</b>		106	99			18-Feb-19		-11	18-Feb-19 A	18-Jul-19	\$1,659,436.00	\$210,000.00	\$1,449,436.00
<b>CONSTRUCTION</b>		106	99			18-Feb-19		-11	18-Feb-19 A	18-Jul-19	\$1,659,436.00	\$210,000.00	\$1,449,436.00
<b>CORRECTIONAL FACILITY</b>		106	99			18-Feb-19		-11	18-Feb-19 A	18-Jul-19	\$1,659,436.00	\$210,000.00	\$1,449,436.00
200700	SLAB ON DECK D ELEV 115 - 3RD LVL (1/2)	6	0	0%	100%	18-Feb-19	23-Feb-19		18-Feb-19 A	23-Feb-19 A	\$200,000.00	\$200,000.00	\$0.00
201140	IN-SLAB PLUMBING B 2ND LVL	5	5	0%	0%			-4	06-May-19	10-May-19	\$50,000.00	\$0.00	\$50,000.00
201150	IN-SLAB PLUMBING B 3RD LVL	5	5	0%	0%			-22	14-Jun-19	20-Jun-19	\$50,000.00	\$0.00	\$50,000.00
201160	IN-SLAB PLUMBING B 4TH LVL	5	5	0%	0%			-21	12-Jul-19	18-Jul-19	\$50,000.00	\$0.00	\$50,000.00
201340	IN-SLAB ELECTRICAL B 2ND LVL	5	5	0%	0%			-4	06-May-19	10-May-19	\$50,000.00	\$0.00	\$50,000.00
201350	IN-SLAB ELECTRICAL B 3RD LVL	5	5	0%	0%			-22	14-Jun-19	20-Jun-19	\$50,000.00	\$0.00	\$50,000.00
201360	IN-SLAB ELECTRICAL B 4TH LVL	5	5	0%	0%			-21	12-Jul-19	18-Jul-19	\$50,000.00	\$0.00	\$50,000.00
210020	PRECAST A (3/5)	9	9	0%	0%			-22	14-Mar-19	26-Mar-19	\$200,000.00	\$0.00	\$200,000.00
210030	PRECAST ELEVATOR SHAFTS B	7	7	0%	0%			-22	24-Apr-19	02-May-19	\$66,109.00	\$0.00	\$66,109.00
210150	STRUCTURAL STEEL D LOW ROOF (1/3)	4	4	0%	0%			-7	28-Feb-19	05-Mar-19	\$50,000.00	\$0.00	\$50,000.00
210160	DETAIL STRUCTURAL STEEL D LOW ROOF (1/3)	5	5	0%	0%			-1	06-Mar-19	12-Mar-19	\$10,000.00	\$0.00	\$10,000.00
210170	DETAIL STRUCTURAL STEEL D ELEV 115 (2/2)	10	0	0%	100%	18-Feb-19	26-Feb-19		18-Feb-19 A	26-Feb-19 A	\$10,000.00	\$10,000.00	\$0.00
210360	PRECAST STAIR SHAFT B B	4	4	0%	0%			-22	22-May-19	28-May-19	\$66,109.00	\$0.00	\$66,109.00

Activity ID	Activity Name	Orig Dur	Rem Dur	Prev Pct%	New Pct %	Actual Start	Actual Finish	Total Float	Early Start	Early Finish	Budgeted Cost	This Period Cost	Cost to Complete
210370	PRECAST STAIR SHAFT B D	4	4	0%	0%			-22	22-May-19	28-May-19	\$66,109.00	\$0.00	\$66,109.00
210380	PRECAST STAIR SHAFT B C	4	4	0%	0%			-19	24-Apr-19	29-Apr-19	\$66,109.00	\$0.00	\$66,109.00
211090	PRECAST CENTER CORRIDOR CL 14-50	6	6	0%	0%			-22	06-Mar-19	13-Mar-19	\$200,000.00	\$0.00	\$200,000.00
211100	PRECAST SALLYPORT	5	5	0%	0%			8	14-Jun-19	20-Jun-19	\$125,000.00	\$0.00	\$125,000.00
211110	PRECAST D ELEV 115-137	6	6	0%	0%			-22	06-Mar-19	13-Mar-19	\$175,000.00	\$0.00	\$175,000.00
211130	PRECAST CONNECTOR	6	6	0%	0%			-22	27-Mar-19	03-Apr-19	\$125,000.00	\$0.00	\$125,000.00
<b>Logic Change</b>		167	134			08-Jan-19		39	08-Jan-19 A	06-Sep-19	\$1,560,000.00	\$155,000.00	\$1,325,000.00
<b>CONSTRUCTION</b>		167	134			08-Jan-19		39	08-Jan-19 A	06-Sep-19	\$1,560,000.00	\$155,000.00	\$1,325,000.00
<b>CORRECTIONAL FACILITY</b>		167	134			08-Jan-19		39	08-Jan-19 A	06-Sep-19	\$1,560,000.00	\$155,000.00	\$1,325,000.00
200500	SLAB ON GRADE A	10	10	0%	0%			69	05-Jul-19	18-Jul-19	\$50,000.00	\$0.00	\$50,000.00
200525	SLAB ON GRADE B	15	15	0%	0%			39	16-Aug-19	06-Sep-19	\$50,000.00	\$0.00	\$50,000.00
200550	SLAB ON GRADE C (1/2)	10	10	0%	0%			148	28-Feb-19	13-Mar-19	\$50,000.00	\$0.00	\$50,000.00
200575	SLAB ON GRADE D (1/2)	10	10	0%	0%			118	11-Apr-19	24-Apr-19	\$50,000.00	\$0.00	\$50,000.00
200770	TOPPING SLAB C 2ND LVL	10	10	0%	0%			88	04-Apr-19	17-Apr-19	\$150,000.00	\$0.00	\$150,000.00
200790	TOPPING SLAB C ROOF	10	10	0%	0%			40	07-Mar-19	20-Mar-19	\$150,000.00	\$0.00	\$150,000.00
200800	TOPPING SLAB A 2ND LVL	10	10	0%	0%			54	06-Jun-19	19-Jun-19	\$150,000.00	\$0.00	\$150,000.00
200810	TOPPING SLAB A 3RD LVL	10	10	0%	0%			29	22-May-19	05-Jun-19	\$150,000.00	\$0.00	\$150,000.00
200830	TOPPING SLAB A ROOF LVL	10	10	0%	0%			19	03-Apr-19	16-Apr-19	\$150,000.00	\$0.00	\$150,000.00
210210	STRUCTURAL STEEL B SEQ2	9	9	0%	0%			-3	18-Apr-19	30-Apr-19	\$25,000.00	\$0.00	\$25,000.00
210230	DETAIL STRUCTURAL STEEL B SEQ2	12	12	0%	0%			-6	06-May-19	21-May-19	\$10,000.00	\$0.00	\$10,000.00
210240	STRUCTURAL STEEL B SEQ3&4	12	12	0%	0%			-22	29-May-19	13-Jun-19	\$50,000.00	\$0.00	\$50,000.00
210270	STRUCTURAL STEEL D ELEV 137	3	3	0%	0%			-5	14-Mar-19	18-Mar-19	\$50,000.00	\$0.00	\$50,000.00
210390	PRECAST B ROOF	5	5	0%	0%			-22	21-May-19	28-May-19	\$100,000.00	\$0.00	\$100,000.00
211040	PRECAST C (3/3)	15	0	40%	100%	08-Jan-19	27-Feb-19		08-Jan-19 A	27-Feb-19 A	\$200,000.00	\$120,000.00	\$0.00
211070	PRECAST D EXTERIOR WALLS (1/2)	5	4	0%	20%	28-Feb-19		-22	28-Feb-19 A	05-Mar-19	\$175,000.00	\$35,000.00	\$140,000.00

Activity ID	Activity Name	Orig Dur	Rem Dur	Prev Pct%	New Pct %	Actual Start	Actual Finish	Total Float	Early Start	Early Finish	Budgeted Cost	This Period Cost	Cost to Complete
<b>Added Activity This Period / Modifications</b>		59	59			25-Feb-19		256	25-Feb-19 A	21-May-19	(\$5,000,000.00)	\$0.00	(\$5,000,000.00)
<b>CONSTRUCTION</b>		56	59			25-Feb-19		19	25-Feb-19 A	21-May-19	\$0.00	\$0.00	\$0.00
<b>CORRECTIONAL FACILITY</b>		56	59			25-Feb-19		19	25-Feb-19 A	21-May-19	\$0.00	\$0.00	\$0.00
200701	SLAB ON DECK D ELEV 115 - 3RD LVL (2/2)	6	2		66%	25-Feb-19		61	25-Feb-19 A	01-Mar-19	\$0.00	\$0.00	\$0.00
200785	TOPPING SLAB C 4TH LVL	10	10		0%			48	07-Mar-19	20-Mar-19	\$0.00	\$0.00	\$0.00
200905	SLAB ON DECK D ELEV 154 ROOF LVL	1	1		0%			22	16-May-19	16-May-19	\$0.00	\$0.00	\$0.00
210021	PRECAST A (4/5)	4	4		0%			-22	10-Apr-19	15-Apr-19	\$0.00	\$0.00	\$0.00
210022	PRECAST A (5/5)	9	9		0%			-22	09-May-19	21-May-19	\$0.00	\$0.00	\$0.00
210151	STRUCTURAL STEEL D LOW ROOF (2/3)	4	4		0%			-6	14-Mar-19	19-Mar-19	\$0.00	\$0.00	\$0.00
210152	STRUCTURAL STEEL D LOW ROOF (3/3)	4	4		0%			-5	20-Mar-19	25-Mar-19	\$0.00	\$0.00	\$0.00
210161	DETAIL STRUCTURAL STEEL D LOW ROOF (2/3)	5	5		0%			-6	20-Mar-19	26-Mar-19	\$0.00	\$0.00	\$0.00
210162	DETAIL STRUCTURAL STEEL D LOW ROOF (3/3)	5	5		0%			-6	27-Mar-19	02-Apr-19	\$0.00	\$0.00	\$0.00
211071	PRECAST D EXTERIOR WALLS (2/2)	4	4		0%			-22	04-Apr-19	09-Apr-19	\$0.00	\$0.00	\$0.00
211091	PRECAST CENTER CORRIDOR CL 14-50 / PRECAST D FL EV 154	6	6		0%			-22	16-Apr-19	23-Apr-19	\$0.00	\$0.00	\$0.00
<b>MODIFICATIONS</b>		1	1					314	28-Feb-19	28-Feb-19	(\$5,000,000.00)	\$0.00	(\$5,000,000.00)
<b>MODIFICATIONS</b>		1	1					314	28-Feb-19	28-Feb-19	(\$5,000,000.00)	\$0.00	(\$5,000,000.00)
900009	CHANGE ORDER NO.9	1	1		0%			314	28-Feb-19	28-Feb-19	(\$5,000,000.00)	\$0.00	(\$5,000,000.00)
<b>Delete Activity (Remove from Service)</b>		12	0			14-Feb-19	14-Feb-19		14-Feb-19 A	14-Feb-19 A	\$0.00	\$0.00	\$0.00
<b>CONSTRUCTION</b>		12	0			14-Feb-19	14-Feb-19		14-Feb-19 A	14-Feb-19 A	\$0.00	\$0.00	\$0.00
<b>CORRECTIONAL FACILITY</b>		12	0			14-Feb-19	14-Feb-19		14-Feb-19 A	14-Feb-19 A	\$0.00	\$0.00	\$0.00
200750	SLAB ON DECK D LOW ROOF (DELETE)	12	0	0%	100%	14-Feb-19	14-Feb-19		14-Feb-19 A	14-Feb-19 A	\$0.00	\$0.00	\$0.00

Activity ID	Activity Name	Orig Dur	Rem Dur	Early Start	Early Finish	Total Float	2019											
							Mar			Apr			May					
<b>ECCF16 28Feb19 Detailed Baseline Schedule Update</b>																		
<b>PRECONSTRUCTION</b>																		
<b>MILESTONES</b>																		
800017	PFRR BOARD MEETING - BCC RECOMMENDATION DEVELOPMENT WORKSHOP	0	0		01-Mar-19*	0	◆ PFRR BOARD MEETING - BCC RECOMMENDATION DEVELOPMENT WORKSHOP											
009999	OBTAIN LICENSES, FEES, PERMITS	0	0		09-Mar-19	165	◆ OBTAIN LICENSES, FEES, PERMITS											
001599	DESIGN COMPLETE	0	0		23-Mar-19	66	◆ DESIGN COMPLETE											
800018	QUARTERLY TOWN HALL PROGRESS MEETING (COC) 1ST WED OF QTR	0	0		03-Apr-19*	0	◆ QUARTERLY TOWN HALL PROGRESS MEETING (COC) 1ST WED OF QTR											
000629	APPROVE CONSTRUCTION SCHEDULE	0	0		06-Apr-19	52	◆ APPROVE CONSTRUCTION SCHEDULE											
800019	PFRR BOARD MEETING - BCC RECOMMENDATION PUBLIC Q&A	0	0		01-May-19*	0	◆ PFRR BOARD MEETING - BCC RECOMMENDATION PUBLIC Q&A											
119999	OTHER UTILITIES AVAILABLE	0	0		22-May-19	38	◆ OTHER UTILITIES											
<b>WEATHER</b>																		
890018	ANTICIPATED ADVERSE WEATHER - OCT19	3	3	28-Feb-19	04-Mar-19	312	[Green Bar] ANTICIPATED ADVERSE WEATHER - OCT19											
890019	ANTICIPATED ADVERSE WEATHER - NOV19	4	4	28-Feb-19	05-Mar-19	311	[Green Bar] ANTICIPATED ADVERSE WEATHER - NOV19											
890020	ANTICIPATED ADVERSE WEATHER - DEC19	5	5	28-Feb-19	06-Mar-19	310	[Green Bar] ANTICIPATED ADVERSE WEATHER - DEC19											
890021	ANTICIPATED ADVERSE WEATHER - JAN20	5	5	28-Feb-19	06-Mar-19	310	[Green Bar] ANTICIPATED ADVERSE WEATHER - JAN20											
890022	ANTICIPATED ADVERSE WEATHER - FEB20	5	5	28-Feb-19	06-Mar-19	310	[Green Bar] ANTICIPATED ADVERSE WEATHER - FEB20											
890023	ANTICIPATED ADVERSE WEATHER - MAR20	5	5	28-Feb-19	06-Mar-19	310	[Green Bar] ANTICIPATED ADVERSE WEATHER - MAR20											
890024	ANTICIPATED ADVERSE WEATHER - APR20	3	3	28-Feb-19	04-Mar-19	312	[Green Bar] ANTICIPATED ADVERSE WEATHER - APR20											
890025	ANTICIPATED ADVERSE WEATHER - MAY20	3	3	28-Feb-19	04-Mar-19	312	[Green Bar] ANTICIPATED ADVERSE WEATHER - MAY20											
<b>DESIGN</b>																		
001171	SITE/CIVIL DESIGN - FENCING/MISC. SITE ITEMS	30	1	25-Jul-18 A	28-Feb-19	89	[Blue Bar] SITE/CIVIL DESIGN - FENCING/MISC. SITE ITEMS											
001420	EC REVIEW - FF&E DESIGN (100% DESIGN)	14	1	10-Oct-18 A	28-Feb-19	75	[Blue Bar] EC REVIEW - FF&E DESIGN (100% DESIGN)											
001500	CONSOLIDATED CONSTRUCTION SET (100% CD)	14	14	10-Mar-19	23-Mar-19	66	[Green Bar] CONSOLIDATED CONSTRUCTION SET (100% CD)											
<b>PERMITS</b>																		
009020	PERMITS - BUILDING	60	10	13-Mar-18 A	09-Mar-19	66	[Blue Bar] PERMITS - BUILDING											
<b>PRECONSTRUCTION SUBMITTALS</b>																		
000620	SUBMIT FINAL BASELINE DESIGN/CONSTRUCTION SCHEDULE	90	17	30-Jan-18 A	16-Mar-19	52	[Blue Bar] SUBMIT FINAL BASELINE DESIGN/CONSTRUCTION SCHEDULE											
000600	PREPARE & SUBMIT LOD 300/400 FEDERATED MODEL	143	59	07-Nov-18 A	27-Apr-19	31	[Blue Bar] PREPARE & SUBMIT LOD 300/400 FEDERATED MODEL											
000625	APPROVE FINAL BASELINE DESIGN/CONSTRUCTION SCHEDULE	21	21	17-Mar-19	06-Apr-19	52	[Green Bar] APPROVE FINAL BASELINE DESIGN/CONSTRUCTION SCHEDULE											
<b>PROCUREMENT</b>																		
010000	PROCUREMENT OF LONG-LEAD ITEMS	450	76	02-Jan-18 A	14-May-19	64	[Blue Bar] PROCUREMENT OF LONG-LEAD ITEMS											
010031	PRECAST PROCUREMENT - MATERIAL COST	1	1	26-Sep-18 A	28-Feb-19	124	[Blue Bar] PRECAST PROCUREMENT - MATERIAL COST											

Activity ID	Activity Name	Orig Dur	Rem Dur	Early Start	Early Finish	Total Float	2019											
							Mar			Apr			May					
010061	STEEL PROCUREMENT (STR & MISC) - MATERIAL COST	1	1	07-Nov-18 A	28-Feb-19	74	STEEL PROCUREMENT (STR & MISC) - MATERIAL COST											
<b>CONSTRUCTION</b>																		
<b>ADMINISTRATION</b>																		
700031	EXTERIOR IMPROVEMENTS	418	205	06-Apr-18 A	19-Dec-19	40												
700004	MASONRY	519	337	11-Jun-18 A	29-Jun-20	-22												
700006	ROUGH CARPENTRY	519	337	11-Jun-18 A	29-Jun-20	-22												
700007	FINISH CARPENTRY & CASEWORK	519	337	11-Jun-18 A	29-Jun-20	-22												
700008	WATERPROOFING, JOINT SEALANTS, AIR BARRIER, EXP. JTS.	519	337	11-Jun-18 A	29-Jun-20	-22												
700010	STEEL DOORS & FRAMES, WOOD DOORS, HARDWARE	519	337	11-Jun-18 A	29-Jun-20	-22												
700011	ALUMINUM ENTRANCES, DOORS, FRAMES, GLASS & GLAZING	519	337	11-Jun-18 A	29-Jun-20	-22												
700012	OVERHEAD COILING DOORS, VEHICLE SALLYPORT DOORS	519	337	11-Jun-18 A	29-Jun-20	-22												
700013	GYPSUM BOARD, METAL FRAMING, ACOUSTICAL TREATMENTS	519	337	11-Jun-18 A	29-Jun-20	-22												
700014	FLOORING & PAINTING	519	337	11-Jun-18 A	29-Jun-20	-22												
700015	SPECIALTIES	519	337	11-Jun-18 A	29-Jun-20	-22												
700017	MISCELLANEOUS EQUIPMENT	519	337	11-Jun-18 A	29-Jun-20	-22												
700018	DETENTION HOLLOW METAL DOORS, FRAMES, GLAZING	519	337	11-Jun-18 A	29-Jun-20	-22												
700019	MODULAR STEEL CELLS, STEEL PANELS, DETENTION CEILINGS	519	337	11-Jun-18 A	29-Jun-20	-22												
700020	DETENTION FURNISHINGS & EQUIPMENT	519	337	11-Jun-18 A	29-Jun-20	-22												
700021	FURNISHINGS	519	337	11-Jun-18 A	29-Jun-20	-22												
700022	SPECIAL CONSTRUCTION	519	337	11-Jun-18 A	29-Jun-20	-22												
700024	FIRE SUPPRESSION	519	337	11-Jun-18 A	29-Jun-20	-22												
700025	PLUMBING	519	337	11-Jun-18 A	29-Jun-20	-22												
700026	HEATING, VENTILATING, AND AIR CONDITIONING	519	337	11-Jun-18 A	29-Jun-20	-22												
700027	ELECTRICAL	519	337	11-Jun-18 A	29-Jun-20	-22												
700028	COMMUNICATIONS	519	337	11-Jun-18 A	29-Jun-20	-22												
700029	ELECTRONIC SECURITY SYSTEMS	519	337	11-Jun-18 A	29-Jun-20	-22												
700016	FOOD SERVICE & LAUNDRY EQUIPMENT	513	337	18-Jun-18 A	29-Jun-20	-22												
700003	PRECAST CONCRETE	243	80	22-Jun-18 A	20-Jun-19	8												
700002	CAST-IN-PLACE CONCRETE	262	134	20-Aug-18 A	06-Sep-19	39												
700030	EARTHWORK	356	162	20-Aug-18 A	17-Oct-19	79												
700001	BUILDING & SITE DEMOLITION	56	10	24-Aug-18 A	13-Mar-19	3	BUILDING & SITE DEMOLITION											
700032	UTILITIES	103	60	06-Sep-18 A	22-May-19	38	UTILITIES											



Activity ID	Activity Name	Orig Dur	Rem Dur	Early Start	Early Finish	Total Float	2019															
							Mar				Apr				May							
700005	METALS	145	99	14-Nov-18 A	18-Jul-19	-21																
401000	ALTERNATE 01 - FULL EMERGENCY POWER	1	1	28-Feb-19	28-Feb-19	314																
402000	ALTERNATE 02 - DOMESTIC HOT WATER, CHILLED WATER, & HEATING	1	1	28-Feb-19	28-Feb-19	314																
403000	ALTERNATE 03 - INMATE PLUMBING CONTROL SYSTEM	1	1	28-Feb-19	28-Feb-19	314																
405000	ALTERNATE 05 - FULL OPERABLE SLIDER DOORS	1	1	28-Feb-19	28-Feb-19	314																
409000	ALTERNATE 09 - EXACQ VISION VMS	1	1	28-Feb-19	28-Feb-19	314																
410000	ALTERNATE 10 - PERVIOUS CONCRETE PAVING	1	1	28-Feb-19	28-Feb-19	314																
414000	ALTERNATE 14 - SECOND BUNK FOR CELLS	1	1	28-Feb-19	28-Feb-19	314																
700009	ROOFING & INSULATED METAL PANELS	124	124	21-Mar-19	13-Sep-19	-21																
<b>DESIGN</b>																						
003000	A/E CONSTRUCTION ADMINISTRATION SERVICES (25 MONTHS)	25	18	05-Sep-18 A	17-Mar-19	438																
<b>SITWORK</b>																						
100002	MAINTAIN EROSION CONTROLS (25 MONTHS)	25	17	16-Jul-18 A	22-Mar-19	183																
101400	UTILITY DEMOLITION - CONNECTOR/CORRIDOR AREA	15	2	13-Sep-18 A	15-Mar-19	11																
112300	SITE UTILITIES - U/G ELECTRIC FOR SITE LIGHTING WEST	10	10	22-Oct-18 A	10-Apr-19	45																
100100	SITE GRADING - STORMWATER POND (EXIST SE JUV PLOT)	10	2	21-Jan-19 A	01-Mar-19	46																
112000	SITE UTILITIES - WATER WEST/NORTH (INCL CONNECTOR/CORRIDOR)	10	2	09-Feb-19 A	12-Apr-19	66																
101200	SITE & UTILITY DEMOLITION - REMAINING SITE	10	10	28-Feb-19	13-Mar-19	3																
101110	SITE & UTILITY DEMOLITION - EXISTING SE JUVENILE PARKING LOT 2 OF 2 (DELETE)	0	0	28-Feb-19	28-Feb-19	315																
100110	SITE GRADING - STORMWATER POND (EXIST SE JUV PLOT) 2 OF 2 (DELETE)	0	0	28-Feb-19	28-Feb-19	315																
110000	SITE UTILITIES - STORMWATER POND	10	10	04-Mar-19	15-Mar-19	46																
100200	SITE GRADING - REMAINING SITE	10	10	14-Mar-19	27-Mar-19	3																
151010	GRAVEL - STORMWATER POND	5	5	18-Mar-19	22-Mar-19	173																
152000	DECORATIVE FENCE/GATE - RETENTION POND	10	10	25-Mar-19	05-Apr-19	173																
159300	LANDSCAPING - NE JUVENILE PARKING LOT	5	5	25-Mar-19	29-Mar-19	293																
100400	SITE GRADING - CONNECTOR/CORRIDOR AREA	10	10	28-Mar-19	10-Apr-19	3																
111000	SITE UTILITIES - SANITARY SOUTH	10	10	28-Mar-19	10-Apr-19	40																
110010	SITE UTILITIES - STORM SOUTH 1 OF 2	10	10	28-Mar-19	10-Apr-19	38																
113000	SITE UTILITIES - GAS EAST	10	10	28-Mar-19	10-Apr-19	68																
112400	SITE UTILITIES - TELECOM NORTH (INCL CONNECTOR/CORRIDOR)	10	10	11-Apr-19	24-Apr-19	58																
112310	SITE UTILITIES - U/G ELECTRIC FOR SITE LIGHTING EAST	10	10	11-Apr-19	24-Apr-19	45																
112380	SITE UTILITIES - U/G ELECTRIC NORTH (BY GULF POWER)	20	20	11-Apr-19	08-May-19	3																







Activity ID	Activity Name	Orig Dur	Rem Dur	Early Start	Early Finish	Total Float	2019															
							Mar				Apr				May							
201090	IN-SLAB PLUMBING C ROOF	5	5	28-Feb-19	06-Mar-19	40																
200480	UNDER SLAB ELECTRICAL D (1/2)	10	10	28-Feb-19	13-Mar-19	138																
200465	UNDER SLAB ELECTRICAL C (2/2)	10	10	28-Feb-19	13-Mar-19	148																
200430	UNDER SLAB ELECTRICAL B	10	10	28-Feb-19	13-Mar-19	148																
201240	IN-SLAB ELECTRICAL D 4TH LVL & HIGH ROOF	5	5	28-Feb-19	06-Mar-19	72																
201290	IN-SLAB ELECTRICAL C ROOF	5	5	28-Feb-19	06-Mar-19	40																
211090	PRECAST CENTER CORRIDOR CL 14-50	6	6	06-Mar-19	13-Mar-19	-22																
211110	PRECAST D ELEV 115-137	6	6	06-Mar-19	13-Mar-19	-22																
210160	DETAIL STRUCTURAL STEEL D LOW ROOF (1/3)	5	5	06-Mar-19	12-Mar-19	-1																
201050	IN-SLAB PLUMBING D LOW ROOF CL 14-29	5	5	06-Mar-19	12-Mar-19	38																
201250	IN-SLAB ELECTRICAL D LOW ROOF CL 14-29	5	5	06-Mar-19	12-Mar-19	38																
200790	TOPPING SLAB C ROOF	10	10	07-Mar-19	20-Mar-19	40																
201080	IN-SLAB PLUMBING C 3RD LVL	5	5	07-Mar-19	13-Mar-19	78																
201280	IN-SLAB ELECTRICAL C 3RD LVL	5	5	07-Mar-19	13-Mar-19	78																
200785	TOPPING SLAB C 4TH LVL	10	10	07-Mar-19	20-Mar-19	48																
210320	MEZZANINE STAIR C	6	6	13-Mar-19	20-Mar-19	80																
201060	IN-SLAB PLUMBING D LOW ROOF CL 29-50	5	5	13-Mar-19	19-Mar-19	38																
201260	IN-SLAB ELECTRICAL D LOW ROOF CL 29-50	5	5	13-Mar-19	19-Mar-19	38																
220000	EXTERIOR BUILDING FINISHES (PCST/MTL PNL/C.WALL)	140	140	14-Mar-19	30-Sep-19	52																
200560	SLAB ON GRADE C (2/2)	10	10	14-Mar-19	27-Mar-19	148																
210020	PRECASTA (3/5)	9	9	14-Mar-19	26-Mar-19	-22																
210270	STRUCTURAL STEEL D ELEV 137	3	3	14-Mar-19	18-Mar-19	-5																
200475	UNDER SLAB PLUMBING D (2/2)	10	10	14-Mar-19	27-Mar-19	138																
201070	IN-SLAB PLUMBING C 2ND LVL	5	5	14-Mar-19	20-Mar-19	98																
200485	UNDER SLAB ELECTRICAL D (2/2)	10	10	14-Mar-19	27-Mar-19	138																
201270	IN-SLAB ELECTRICAL C 2ND LVL	5	5	14-Mar-19	20-Mar-19	98																
210151	STRUCTURAL STEEL D LOW ROOF (2/3)	4	4	14-Mar-19	19-Mar-19	-6																
210280	DETAIL STRUCTURAL STEEL D ELEV 137	9	9	19-Mar-19	29-Mar-19	-5																
210152	STRUCTURAL STEEL D LOW ROOF (3/3)	4	4	20-Mar-19	25-Mar-19	-5																
210161	DETAIL STRUCTURAL STEEL D LOW ROOF (2/3)	5	5	20-Mar-19	26-Mar-19	-6																
260000	INTERIOR PARTITIONS/CONSTRUCTION C4	35	35	21-Mar-19	08-May-19	48																
200780	TOPPING SLAB C 3RD LVL	10	10	21-Mar-19	03-Apr-19	73																

Activity ID	Activity Name	Orig Dur	Rem Dur	Early Start	Early Finish	Total Float	2019															
							Mar			Apr			May									
200940	POUR SWITCHBACK STAIRS C	3	3	21-Mar-19	25-Mar-19	80																
200950	POUR LARGE STAIR C A	3	3	21-Mar-19	25-Mar-19	80																
200960	POUR MEZZANINE STAIR C	3	3	21-Mar-19	25-Mar-19	80																
230000	ROOF SYSTEM C	20	20	21-Mar-19	17-Apr-19	40																
211130	PRECAST CONNECTOR	6	6	27-Mar-19	03-Apr-19	-22																
210330	SWITCHBACK STAIRS A	15	15	27-Mar-19	16-Apr-19	36																
201130	IN-SLAB PLUMBING A ROOF LVL	5	5	27-Mar-19	02-Apr-19	19																
201330	IN-SLAB ELECTRICAL A ROOF LVL	5	5	27-Mar-19	02-Apr-19	19																
210162	DETAIL STRUCTURAL STEEL D LOW ROOF (3/3)	5	5	27-Mar-19	02-Apr-19	-6																
200890	SLAB ON DECK D ELEV 137 - 4TH LVL	3	3	01-Apr-19	03-Apr-19	-5																
200830	TOPPING SLAB A ROOF LVL	10	10	03-Apr-19	16-Apr-19	19																
200900	SLAB ON DECK D ELEV 102 - 2ND LVL	6	6	03-Apr-19	10-Apr-19	28																
210200	STRUCTURAL STEEL B SEQ1	11	11	03-Apr-19	17-Apr-19	-6																
201120	IN-SLAB PLUMBING A 4TH LVL	5	5	03-Apr-19	09-Apr-19	24																
201320	IN-SLAB ELECTRICAL A 4TH LVL	5	5	03-Apr-19	09-Apr-19	24																
200770	TOPPING SLAB C 2ND LVL	10	10	04-Apr-19	17-Apr-19	88																
211080	PRECAST D ELEV 157	4	4	04-Apr-19	09-Apr-19	-5																
211071	PRECAST D EXTERIOR WALLS (2/2)	4	4	04-Apr-19	09-Apr-19	-22																
201110	IN-SLAB PLUMBING A 3RD LVL	5	5	10-Apr-19	16-Apr-19	54																
201310	IN-SLAB ELECTRICAL A 3RD LVL	5	5	10-Apr-19	16-Apr-19	54																
210021	PRECAST A (4/5)	4	4	10-Apr-19	15-Apr-19	-22																
200575	SLAB ON GRADE D (1/2)	10	10	11-Apr-19	24-Apr-19	118																
231000	ROOF SYSTEM D LOW ROOF	20	20	11-Apr-19	08-May-19	28																
211091	PRECAST CENTER CORRIDOR CL 14-50 / PRECAST D ELEV 154	6	6	16-Apr-19	23-Apr-19	-22																
200820	TOPPING SLAB A 4TH LVL	10	10	17-Apr-19	30-Apr-19	19																
200970	POUR SWITCHBACK STAIRS A	3	3	17-Apr-19	19-Apr-19	61																
210340	MECHANICAL STAIRS A	10	10	17-Apr-19	30-Apr-19	36																
232000	ROOF SYSTEM A	20	20	17-Apr-19	06-May-19	72																
201100	IN-SLAB PLUMBING A 2ND LVL	5	5	17-Apr-19	23-Apr-19	84																
201300	IN-SLAB ELECTRICAL A 2ND LVL	5	5	17-Apr-19	23-Apr-19	84																
210210	STRUCTURAL STEEL B SEQ2	9	9	18-Apr-19	30-Apr-19	-3																
210220	DETAIL STRUCTURAL STEEL B SEQ1	12	12	18-Apr-19	03-May-19	-6																



Activity ID	Activity Name	Orig Dur	Rem Dur	Early Start	Early Finish	Total Float	2019															
							Mar			Apr			May									
<b>MODIFICATIONS</b>																						
900006	CHANGE ORDER NO.6	1	0	01-Dec-18 A	28-Feb-19	315																
900008	CHANGE ORDER NO.8	1	1	28-Feb-19	28-Feb-19	314																
900009	CHANGE ORDER NO.9	1	1	28-Feb-19	28-Feb-19	314																

 Actual Work  
 Remaining Work  
 Critical Remaining Work  
 Milestone

D/B New Escambia County Correctional Facility  
Pensacola, FL

**ECCF16** ECCF16 28Feb19 Detailed Baseline Schedule Update  
- 90-Day Schedule 11x17

Page 8 of 8  
01-Mar-19 08:03  
Data Date: 28-Feb-19

Caddell - WGI  
#1054



## Daily Log: Friday 2/1/2019

**Daily Log Completed**  
 The Daily Log was completed by Donald Shelton on Mon Feb 4, 2019 at 10:41 am CST.

### WEATHER REPORT

Temperature			Precipitation Since			Humidity				Windspeed		
Low	High	Avg	Midnight	2 Days Ago	3 Days Ago	Low	Avg	High	Dew	Avg	Max	Gust
45°F	59°F	51°F	0.02 in.	0.02 in.	0.02 in.	56%	67%	98%	40°F	6.2 mph	9 mph	16 mph

### DAILY SNAPSHOT

06:00 AM	09:00 AM	12:00 PM	03:00 PM	06:00 PM	09:00 PM
partly-cloudy-night 46°F	partly-cloudy-day 49°F	partly-cloudy-day 55°F	partly-cloudy-day 59°F	partly-cloudy-night 57°F	partly-cloudy-night 54°F

### OBSERVED WEATHER CONDITIONS

No.	Weather Delay	Sky	Temp	Average	Precipitation	Wind	Ground/Sea
1	No	Cloudy	Cold	51	0	Calm	Dry

### MANPOWER LOG

59 Workers | 568.5 Man Hours

No.	Contact/Company	Cost Code	Workers	# Hours	Man Hours	Location
1	A&B Electric Co., Inc.		6	10.0	60.0	Building>C
<b>Notes:</b> Working on underground conduits in section "C", Start Backfill and tamp dirt for compaction test.						
2	Bayside Structures, LLC		3	8.0	24.0	Site
<b>Notes:</b> Worked on connector rebar and forms at existing building.						
3	Caddell Construction Co. (DE), LLC		9	11.75	105.75	Site
<b>Notes:</b> WGI/Caddell supervision, quality control and safety onsite.						
4	Chavers Construction Inc.		5	11.75	58.75	Site>Stormwater Pond
<b>Notes:</b> Back-fill Stormwater Pipe connected to S23						
5	Ed Emmons Steel Erectors, Inc.		8	8.0	64.0	Building>C
<b>Notes:</b> Framed first landing, set first stringer and first handrail. Installed header at second landing.						
6	Larry M. Jacobs & Associates, Inc.		1	2.0	2.0	Site>Stormwater Pond
<b>Notes:</b> Conducted Density test In Stormwater Pond Area						

**MANPOWER LOG**

**59 Workers | 568.5 Man Hours**

No.	Contact/Company	Cost Code	Workers	# Hours	Man Hours	Location
7	Nash Plumbing and Mechanical, LLC		8	8.0	64.0	Building>C
<b>Notes:</b> Underground rough-in plumbing in Area C						
8	Tindall Corporation		19	10.0	190.0	Building
<b>Notes:</b> **Erecting last panel for this phase in area D on line 50, moved crane back to area A **Grouting and welding in roof level of corridor and D. **Erecting in area A near line 6.						
			<b>59</b>		<b>568.5</b>	

**Manpower Log's Attachments:**

1. A&B Electric Co., Inc.



[Daily Construction Report - - 2-1-19.pdf](#)

2. Bayside Structures, LLC



[Bayside Daily 2-1-2019.PDF](#)



4. Chavers Construction Inc.

[Chaver Daily 2-1-2019.PDF](#)

5. Ed Emmons Steel Erectors, Inc.

[New Doc 2019-02-01 15.10.15.pdf](#)

7. Nash Plumbing and Mechanical, LLC

[Nash Daily 2-1-2019.xlsx](#)

8. Tindall Corporation

[Tindall Escambia Daily 2-1-2019.xlsx](#)

**EQUIPMENT LOG**

No.	Equipment Name	Cost Code	Hrs Operating	Hrs Idle	Inspected?	Inspection Time	Location
1	Kobelco Crane CKE2500				No	07:00 AM	Building>A
	<b>Notes:</b>						
2	Genie Lift S85				No	07:00 AM	Building>A
	<b>Notes:</b>						
3	JLG Lift 860SJ				No	07:00 AM	Building>A
	<b>Notes:</b>						
4	JLG Lift 660SJ				No	07:00 AM	Building>D
	<b>Notes:</b>						
5	JLG Lift 660SJ				No	07:00 AM	Building>D
	<b>Notes:</b>						
6	Grove Crane AT700D				No	07:00 AM	Site
	<b>Notes:</b>						

## EQUIPMENT LOG

No.	Equipment Name	Cost Code	Hrs Operating	Hrs Idle	Inspected?	Inspection Time	Location
7	Bobcat Skidsteer				No	07:00 AM	Site
	<b>Notes:</b>						
8	Cat Telehandler				No	07:00 AM	Site
	<b>Notes:</b>						
9	JLG Skytrak Telehandler				No	07:00 AM	Site
	<b>Notes:</b>						
10	JLG Skytrak Telehandler				No	07:00 AM	Site
	<b>Notes:</b>						
11	Volvo 330 Excavator				No	07:00 AM	Site>Stormwater Pond
	<b>Notes:</b>						

---

By

---

Date

---

Copies To



**Whitesell Green / Caddell, a Joint Venture**  
 2700 Lagoon Park Drive  
 Montgomery, Alabama 36109  
 P: (334) 272-7723  
 F: (334) 394-0193

**Project: 1054 - Escambia County Correctional Facility**  
 3080 N. Pace Boulevard  
 Pensacola, Florida 32501

## Daily Log: Saturday 2/2/2019

**Daily Log Completed**  
 The Daily Log was completed by Donald Shelton on Mon Feb 4, 2019 at 11:00 am CST.

### WEATHER REPORT

Temperature			Precipitation Since			Humidity				Windspeed		
Low	High	Avg	Midnight	2 Days Ago	3 Days Ago	Low	Avg	High	Dew	Avg	Max	Gust
50°F	64°F	57°F	0.00 in.	0.02 in.	0.02 in.	82%	91%	100%	55°F	4.3 mph	6 mph	6 mph

### DAILY SNAPSHOT

06:00 AM	09:00 AM	12:00 PM	03:00 PM	06:00 PM	09:00 PM
cloudy 52°F	cloudy 55°F	cloudy 62°F	cloudy 64°F	cloudy 62°F	cloudy 61°F

### OBSERVED WEATHER CONDITIONS

No.	Weather Delay	Sky	Temp	Average	Precipitation	Wind	Ground/Sea
1	No	Cloudy	Mild	57	0	Calm	Wet/Muddy

### MANPOWER LOG

24 Workers | 222.5 Man Hours

No.	Contact/Company	Cost Code	Workers	# Hours	Man Hours	Location
1	Caddell Construction Co. (DE), LLC		1	10.0	10.0	Site
<b>Notes:</b> WGI/Caddell supervision, quality control and safety onsite.						
2	Chavers Construction Inc.		5	6.5	32.5	Site>Stormwater Pond
<b>Notes:</b> Back-filled and compacted stormwater pipe connected to S23						
3	Tindall Corporation		18	10.0	180.0	Building>A
<b>Notes:</b> **Grouting and welding in roof level of corridor and D. **Erecting in area A near line 6.						
			<b>24</b>	<b>222.5</b>		

#### Manpower Log's Attachments:

2. Chavers Construction Inc.

[Chaver Daily 2-2-2019.PDF](#)

3. Tindall Corporation

[Tindall Escambia Daily 2-2-2019.xlsx](#)

**EQUIPMENT LOG**

No.	Equipment Name	Cost Code	Hrs Operating	Hrs Idle	Inspected?	Inspection Time	Location
1	Kobelco Crane CKE2500				No	07:00 AM	Building>A
	<b>Notes:</b>						
2	JLG Lift 860SJ				No	07:00 AM	Building>A
	<b>Notes:</b>						
3	JLG Lift 660SJ				No	07:00 AM	Building>A
	<b>Notes:</b>						
4	Genie Lift S85				No	07:00 AM	Building>A
	<b>Notes:</b>						
5	JLG Skytrak Telehandler				No	07:00 AM	Site
	<b>Notes:</b>						
6	Volvo 330 Excavator				No	07:00 AM	Site>Stormwater Pond
	<b>Notes:</b>						
7	John Deere 85G Excavator				No	07:00 AM	Site>Stormwater Pond
	<b>Notes:</b>						
8	Vibratory Roller				No	07:00 AM	Site>Stormwater Pond
	<b>Notes:</b>						

By \_\_\_\_\_

Date \_\_\_\_\_

Copies To \_\_\_\_\_



Whitesell Green / Caddell, a Joint Venture  
 2700 Lagoon Park Drive  
 Montgomery, Alabama 36109  
 P: (334) 272-7723  
 F: (334) 394-0193

Project: 1054 - Escambia County Correctional  
**Facility**  
 3080 N. Pace Boulevard  
 Pensacola, Florida 32501

## Daily Log: Sunday 2/3/2019

### WEATHER REPORT

Temperature			Precipitation Since			Humidity				Windspeed		
Low	High	Avg	Midnight	2 Days Ago	3 Days Ago	Low	Avg	High	Dew	Avg	Max	Gust
57°F	68°F	61°F	0.00 in.	0.00 in.	0.02 in.	77%	92%	100%	58°F	2.8 mph	4 mph	7 mph

### DAILY SNAPSHOT

06:00 AM	09:00 AM	12:00 PM	03:00 PM	06:00 PM	09:00 PM
cloudy 58°F	cloudy 60°F	cloudy 65°F	cloudy 68°F	partly-cloudy-night 62°F	partly-cloudy-night 59°F

### OBSERVED WEATHER CONDITIONS

No.	Weather Delay	Sky	Temp	Average	Precipitation	Wind	Ground/Sea
1	No						

By \_\_\_\_\_ Date \_\_\_\_\_ Copies To \_\_\_\_\_



## Daily Log: Monday 2/4/2019

**Daily Log Completed**  
 The Daily Log was completed by Donald Shelton on Fri Feb 8, 2019 at 07:46 am CST.

### WEATHER REPORT

Temperature			Precipitation Since			Humidity				Windspeed		
Low	High	Avg	Midnight	2 Days Ago	3 Days Ago	Low	Avg	High	Dew	Avg	Max	Gust
55°F	66°F	62°F	0.00 in.	0.00 in.	0.00 in.	83%	93%	100%	60°F	4.2 mph	7 mph	9 mph

### DAILY SNAPSHOT

06:00 AM	09:00 AM	12:00 PM	03:00 PM	06:00 PM	09:00 PM
cloudy 59°F	partly-cloudy-day 62°F	cloudy 67°F	cloudy 66°F	cloudy 64°F	cloudy 63°F

### OBSERVED WEATHER CONDITIONS

No.	Weather Delay	Sky	Temp	Average	Precipitation	Wind	Ground/Sea
1	No	Cloudy	Mild	61	0	Calm	Dry

### MANPOWER LOG

71 Workers | 654.0 Man Hours

No.	Contact/Company	Cost Code	Workers	# Hours	Man Hours	Location
1	A&B Electric Co., Inc.		9	10.0	90.0	Building>C
<b>Notes:</b> Working on underground conduit in section "C", Working on temporary lights in main corridor.						
2	Bayside Structures, LLC		11	9.0	99.0	Site
<b>Notes:</b> Set forms at connector north end at existing jail. Tied grade beam rebar at connector north end at existing jail. Cleaned footer GB6 at connector and started stem wall lay out and rebar						
3	Caddell Construction Co. (DE), LLC		9	10.0	90.0	Site
<b>Notes:</b> WGI/Caddell supervision, quality control and safety onsite.						
4	Chavers Construction Inc.		4	10.0	40.0	Site>Stormwater Pond
<b>Notes:</b> Installed 36 inch rcp south from S23 towards retention pond. Backfill from S23 to retention pond.						
5	Ed Emmons Steel Erectors, Inc.		8	8.0	64.0	Building
<b>Notes:</b> Installed and completed landing at 2nd floor Stair A. Set 2nd stringer and handrail.						


**MANPOWER LOG**

71 Workers | 654.0 Man Hours

No.	Contact/Company	Cost Code	Workers	# Hours	Man Hours	Location
6	Larry M. Jacobs & Associates, Inc.		1	1.0	1.0	Site>Stormwater Pond
<b>Notes:</b> Conducted Density Test in Stormwater Pond Area.						
7	Nash Plumbing and Mechanical, LLC		6	8.0	48.0	Building>C
<b>Notes:</b> Roughed -in underground plumbing north end of Area C						
8	Tindall Corporation		19	10.0	190.0	Building>A
<b>Notes:</b> **Grouting and welding. **Erecting in area A near line 6. **Misc. patching						
9	EAA Site Contractors LLC		4	8.0	32.0	Site
<b>Notes:</b> Total man hours 32. EAA continued to dig retention pond. Also continued to place dirt in section B and outside electrical room in section D. Surveyors set stakes to identify the pond corners. In order for EAA to complete back filling and compaction on the bldg pad in section A, B and D we need better access to those areas. These areas need to be free of all equipment and materials. EAA's ability to complete this task in a timely manner is being hampered by this lack of access.						
			<b>71</b>	<b>654.0</b>		


**Manpower Log's Attachments:**

1. A&B Electric Co., Inc.

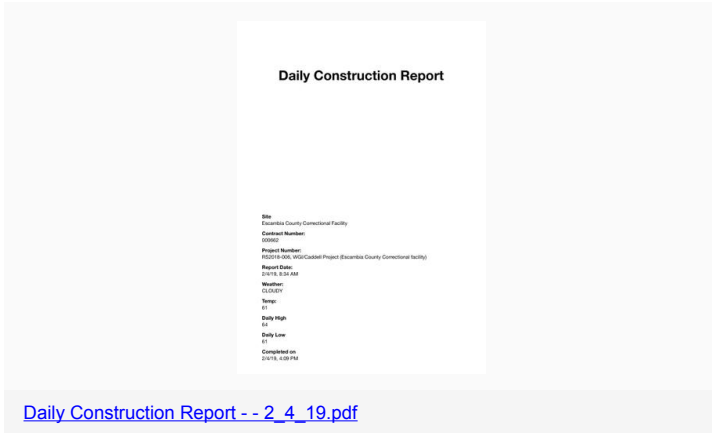


[Daily Construction Report -- 2\\_4\\_19.pdf](#)

2. Bayside Structures, LLC

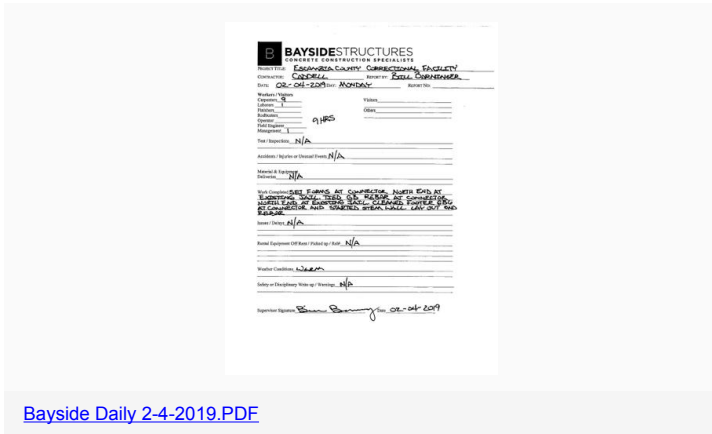


[Bayside Daily 2-4-2019.PDF](#)

4. Chavers Construction Inc.

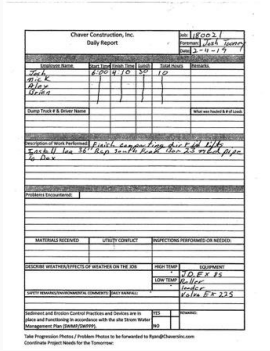

[Chaver Daily 2-4-2019.PDF](#)

5. Ed Emmons Steel Erectors, Inc.



[New Doc 2019-02-04 15.59.28.pdf](#)

7. Nash Plumbing and Mechanical, LLC

[Nash Daily 2-4-2019.xlsx](#)

8. Tindall Corporation

[Tindall Escambia Daily 2-4-2019.xlsx](#)

**NOTES LOG**

No.	Issue?	Location	Comments
1	No	Building>B	AllStop Waterproof has completed damp proofing on single elevator pit

**EQUIPMENT LOG**

No.	Equipment Name	Cost Code	Hrs Operating	Hrs Idle	Inspected?	Inspection Time	Location
1	Kobelco Crane CKE2500				No	07:00 AM	Building>A
	<b>Notes:</b>						
2	JLG Lift 860SJ				No	07:00 AM	Building>A
	<b>Notes:</b>						
3	Genie Lift S85				No	07:00 AM	Building>A
	<b>Notes:</b>						
4	Cat Skidsteer				No	07:00 AM	Building>B
	<b>Notes:</b>						



**EQUIPMENT LOG**

No.	Equipment Name	Cost Code	Hrs Operating	Hrs Idle	Inspected?	Inspection Time	Location
5	Bobcat Miniexcavator				No	07:00 AM	Building>C
	<b>Notes:</b>						
6	Scissor Lift				No	07:00 AM	Building>D
	<b>Notes:</b>						
7	Scissor Lift				No	07:00 AM	Building>D
	<b>Notes:</b>						
8	Scissor Lift				No	07:00 AM	Building>D
	<b>Notes:</b>						
9	Scissor Lift				No	07:00 AM	Building
	<b>Notes:</b>						
10	Grove Crane AT700D				No	07:00 AM	Site
	<b>Notes:</b>						
11	JLG Skytrak Telehandler				No	07:00 AM	Site
	<b>Notes:</b>						
12	John Deere 750 Dozer				No	07:00 AM	Site>Stormwater Pond
	<b>Notes:</b>						
13	Komatsu 320 PT Loader				No	07:00 AM	Site>Stormwater Pond
	<b>Notes:</b>						
14	Volvo 330 Excavator				No	07:00 AM	Site>Stormwater Pond
	<b>Notes:</b>						
15	John Deere 85G Excavator				No	07:00 AM	Site>Stormwater Pond
	<b>Notes:</b>						
16	Vibratory Roller				No	07:00 AM	Site>Stormwater Pond
	<b>Notes:</b>						
17	CAT Miniexcavator				No	07:00 AM	Building>C
	<b>Notes:</b>						
18	CAT Miniexcavator				No	07:00 AM	Building>C
	<b>Notes:</b>						

By \_\_\_\_\_

Date \_\_\_\_\_

Copies To \_\_\_\_\_



## Daily Log: Tuesday 2/5/2019

**Daily Log Completed**  
 The Daily Log was completed by Donald Shelton on Fri Feb 8, 2019 at 07:47 am CST.

### WEATHER REPORT

Temperature			Precipitation Since			Humidity				Windspeed		
Low	High	Avg	Midnight	2 Days Ago	3 Days Ago	Low	Avg	High	Dew	Avg	Max	Gust
62°F	70°F	65°F	0.00 in.	0.00 in.	0.01 in.	82%	95%	100%	63°F	4.3 mph	8 mph	11 mph

### DAILY SNAPSHOT

06:00 AM	09:00 AM	12:00 PM	03:00 PM	06:00 PM	09:00 PM
fog 63°F	fog 64°F	cloudy 70°F	cloudy 68°F	cloudy 65°F	cloudy 65°F

### OBSERVED WEATHER CONDITIONS

No.	Weather Delay	Sky	Temp	Average	Precipitation	Wind	Ground/Sea
1	No	Cloudy	Mild	64	0	Calm	Dry

### MANPOWER LOG

70 Workers | 625.0 Man Hours

No.	Contact/Company	Cost Code	Workers	# Hours	Man Hours	Location
1	A&B Electric Co., Inc.		10	10.0	100.0	Building>C
<b>Notes:</b> Rough in underground conduits in section "C", Installing temporary lights in main corridor, Backfill of Main Electrical room.						
2	Bayside Structures, LLC		8	9.0	72.0	Site
<b>Notes:</b> Finished form work for grade beam north end of connector. Continued working on stem walls at connector.						
3	Caddell Construction Co. (DE), LLC		9	10.0	90.0	Site
<b>Notes:</b> WGI/Caddell supervision, quality control and safety onsite.						
4	Chavers Construction Inc.		4	4.0	16.0	Site>Stormwater Pond
<b>Notes:</b> Set S23 Man hole top and back-fill						
5	Ed Emmons Steel Erectors, Inc.		8	8.0	64.0	Building>D
<b>Notes:</b> Moved crane Hung elevation 100 beams at South end of Area D and Connect to new precast.						
6	Larry M. Jacobs & Associates, Inc.		1	3.0	3.0	Building>D
<b>Notes:</b> Conducted structural erection steel test in Area D at elevation 115.						


**MANPOWER LOG**

70 Workers | 625.0 Man Hours

No.	Contact/Company	Cost Code	Workers	# Hours	Man Hours	Location
7	Nash Plumbing and Mechanical, LLC		6	8.0	48.0	Building>C
<b>Notes:</b> Roughed-in South End of Area C						
8	Tindall Corporation		20	10.0	200.0	Building>A
<b>Notes:</b> **Grouting and welding. **Erecting in area A near line 6. **Misc. patching						
9	EAA Site Contractors LLC		4	8.0	32.0	Site
<b>Notes:</b> Total man hours 37.5. EAA continued to dig retention pond. We helped A&B Electric place dirt in the electrical room in section D. Also continued to place dirt in section B.						
			<b>70</b>		<b>625.0</b>	


**Manpower Log's Attachments:**

- 1. A&B Electric Co., Inc.

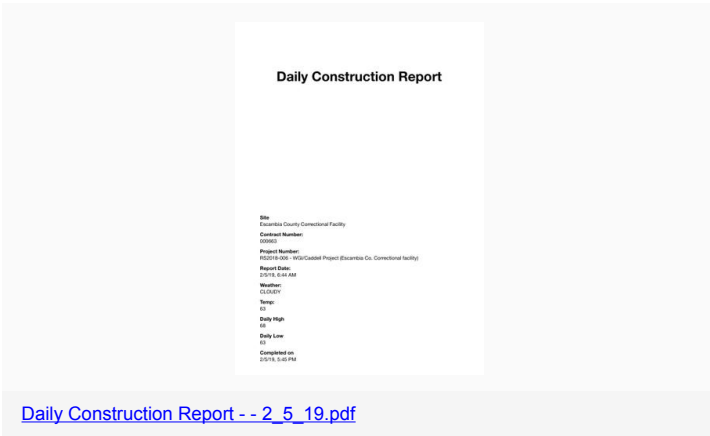

[Daily Construction Report -- 2\\_5\\_19.pdf](#)

- 2. Bayside Structures, LLC

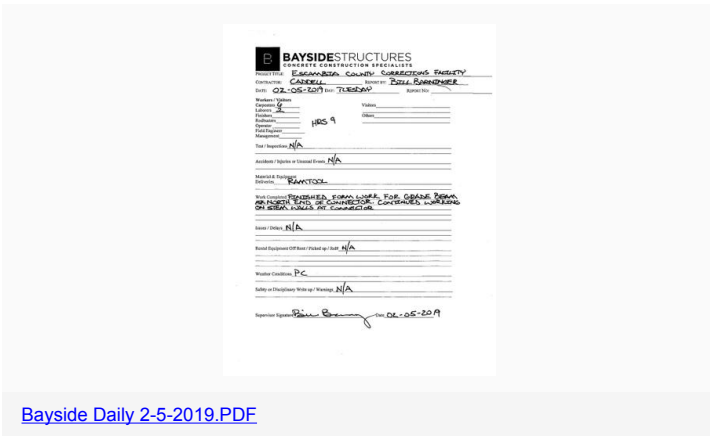

[Bayside Daily 2-5-2019.PDF](#)



## EQUIPMENT LOG

No.	Equipment Name	Cost Code	Hrs Operating	Hrs Idle	Inspected?	Inspection Time	Location
7	CAT Miniexcavator				No	07:00 AM	Building>C
	<b>Notes:</b>						
8	Grove Crane AT700D				No	07:00 AM	Building>D
	<b>Notes:</b>						
9	Genie Lift S80				No	07:00 AM	Building>D
	<b>Notes:</b>						
10	CAT Miniexcavator				No	07:00 AM	Building>D
	<b>Notes:</b>						
11	JLG Skytrak Telehandler				No	07:00 AM	Site
	<b>Notes:</b>						
12	Bobcat Miniexcavator				No	07:00 AM	Site
	<b>Notes:</b>						
13	Doosan Loader				No	07:00 AM	Site>Stormwater Pond
	<b>Notes:</b>						
14	Komatsu 320 PT Loader				No	07:00 AM	Site>Stormwater Pond
	<b>Notes:</b>						
15	Vibratory Roller				No	07:00 AM	Site>Stormwater Pond
	<b>Notes:</b>						
16	John Deere 750 Dozer				No	07:00 AM	Site>Stormwater Pond
	<b>Notes:</b>						
17	Terex Articulated Dump Truck				No	07:00 AM	Site>Stormwater Pond
	<b>Notes:</b>						
18	Cat Telehandler				No	07:00 AM	Site
	<b>Notes:</b>						

## INSPECTION LOG

No.	Start Time	End Time	Inspection Type	Inspecting Entity	Inspector Name	Location	Area
1	08:00 AM	11:00 AM	Third Party	Mott MacDonald	Mike Tugwell	Building	D
	<b>Comments:</b> Conducted Threshold Inspection in Area D elevation 115.						

By \_\_\_\_\_

Date \_\_\_\_\_

Copies To \_\_\_\_\_



## Daily Log: Wednesday 2/6/2019

**Daily Log Completed**  
 The Daily Log was completed by Donald Shelton on Fri Feb 8, 2019 at 07:35 am CST.

### WEATHER REPORT

Temperature			Precipitation Since			Humidity				Windspeed		
Low	High	Avg	Midnight	2 Days Ago	3 Days Ago	Low	Avg	High	Dew	Avg	Max	Gust
64°F	72°F	67°F	0.00 in.	0.00 in.	0.00 in.	81%	93%	99%	65°F	5.8 mph	8 mph	13 mph

### DAILY SNAPSHOT

06:00 AM	09:00 AM	12:00 PM	03:00 PM	06:00 PM	09:00 PM
fog 66°F	fog 67°F	cloudy 71°F	cloudy 72°F	cloudy 68°F	partly-cloudy-night 66°F

### OBSERVED WEATHER CONDITIONS

No.	Weather Delay	Sky	Temp	Average	Precipitation	Wind	Ground/Sea
1	No	Cloudy	Mild	66	0	Calm	Dry

### MANPOWER LOG

71 Workers | 650.0 Man Hours

No.	Contact/Company	Cost Code	Workers	# Hours	Man Hours	Location
1	A&B Electric Co., Inc.		10	10.0	100.0	Building
<b>Notes:</b> Working on temporary lights in section "C" & "D", Working on backfill of Main Electrical room. Working on temporary panels.						
2	Bayside Structures, LLC		10	9.0	90.0	Site
<b>Notes:</b> Started fine grading corridor at elevation 83. Finished rebar for connector stem walls. Finished forming one side of stem wall.						
3	Caddell Construction Co. (DE), LLC		9	10.0	90.0	Site
<b>Notes:</b> WGI/Caddell supervision, quality control and safety onsite.						
4	Ed Emmons Steel Erectors, Inc.		9	8.0	72.0	Building>D
<b>Notes:</b> Hung remaining beams of elevations 100 and 115 at south connection point to precast in Area D. Continued hanging beams at elevation 115 and repaired welds.						
5	Larry M. Jacobs & Associates, Inc.		1	2.0	2.0	Building
<b>Notes:</b> Conducted Density Test in Area C and D.						
6	Nash Plumbing and Mechanical, LLC		6	8.0	48.0	Building>C
<b>Notes:</b> Continued with underground plumbing rough-in in Area C						


**MANPOWER LOG**

71 Workers | 650.0 Man Hours

No.	Contact/Company	Cost Code	Workers	# Hours	Man Hours	Location
7	Tindall Corporation		20	10.0	200.0	Building>A
<b>Notes:</b> **Grouting and welding. **Erecting in area A near line 6. Move crane to area C. **Misc. patching						
8	EAA Site Contractors LLC		6	8.0	48.0	Site
<b>Notes:</b> Total man hours 60. EAA continued to dig retention pond. Continued to place dirt in section B for the final lift. Started placing dirt in section A also for the final lift.						
			<b>71</b>		<b>650.0</b>	


**Manpower Log's Attachments:**

1. A&B Electric Co., Inc.

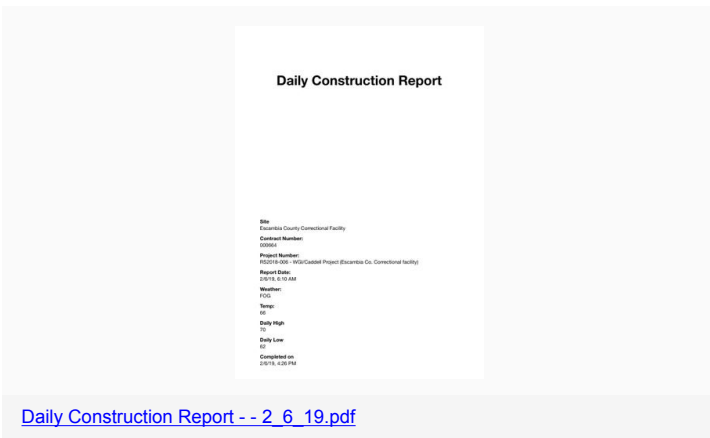


[Daily Construction Report -- 2\\_6\\_19.pdf](#)

2. Bayside Structures, LLC

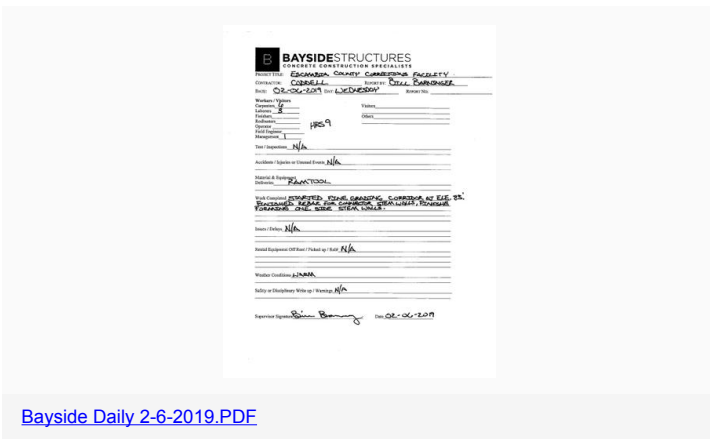

[Bayside Daily 2-6-2019.PDF](#)

4. Ed Emmons Steel Erectors, Inc.

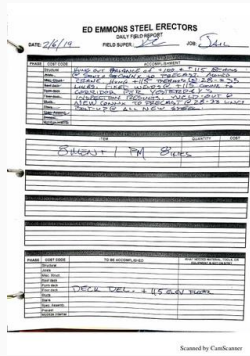

[New Doc 2019-02-06 15.03.05.pdf](#)

6. Nash Plumbing and Mechanical, LLC

[Nash Daily 2-6-2019.xlsx](#)

7. Tindall Corporation

[Tindall Escambia Daily 2-6-2019.xlsx](#)

**EQUIPMENT LOG**

No.	Equipment Name	Cost Code	Hrs Operating	Hrs Idle	Inspected?	Inspection Time	Location
1	Kobelco Crane CKE2500				No	07:00 AM	Building>A
	<b>Notes:</b>						
2	JLG Lift 860SJ				No	07:00 AM	Building>A
	<b>Notes:</b>						
3	Genie Lift S85				No	07:00 AM	Building>A
	<b>Notes:</b>						
4	John Deere 550H Dozer				No	07:00 AM	Building>B
	<b>Notes:</b>						
5	Vibratory Roller				No	07:00 AM	Building>B
	<b>Notes:</b>						
6	John Deere Skidsteer				No	07:00 AM	Building>B
	<b>Notes:</b>						
7	CAT Miniexcavator				No	07:00 AM	Building>C
	<b>Notes:</b>						
8	Genie Lift S80				No	07:00 AM	Building>D
	<b>Notes:</b>						
9	Grove Crane AT700D				No	07:00 AM	Building>D
	<b>Notes:</b>						
10	Scissor Lift				No	07:00 AM	Building>D
	<b>Notes:</b>						
11	Scissor Lift				No	07:00 AM	Building>D
	<b>Notes:</b>						
12	Scissor Lift				No	07:00 AM	Building>D
	<b>Notes:</b>						



## EQUIPMENT LOG

No.	Equipment Name	Cost Code	Hrs Operating	Hrs Idle	Inspected?	Inspection Time	Location
13	Vibratory Roller				No	07:00 AM	Building>D
	<b>Notes:</b>						
14	JLG Skytrak Telehandler				No	07:00 AM	Site
	<b>Notes:</b>						
15	JLG Skytrak Telehandler				No	07:00 AM	Site
	<b>Notes:</b>						
16	Cat Telehandler				No	07:00 AM	Site
	<b>Notes:</b>						
17	Bobcat Skidsteer				No	07:00 AM	Site
	<b>Notes:</b>						
18	Bobcat Miniexcavator				No	07:00 AM	Site
	<b>Notes:</b>						
19	Volvo 330 Excavator				No	07:00 AM	Site>Stormwater Pond
	<b>Notes:</b>						
20	Terex Articulated Dump Truck				No	07:00 AM	Site>Stormwater Pond
	<b>Notes:</b>						
21	John Deere 750 Dozer				No	07:00 AM	Site>Stormwater Pond
	<b>Notes:</b>						
22	Komatsu 320 PT Loader				No	07:00 AM	Site>Stormwater Pond
	<b>Notes:</b>						
23	Komatsu 78MR Excavator				No	07:00 AM	Building>D
	<b>Notes:</b>						

By \_\_\_\_\_

Date \_\_\_\_\_

Copies To \_\_\_\_\_



## Daily Log: Thursday 2/7/2019

**Daily Log Completed**  
 The Daily Log was completed by Donald Shelton on Mon Feb 11, 2019 at 07:44 am CST.

### WEATHER REPORT

Temperature			Precipitation Since			Humidity				Windspeed		
Low	High	Avg	Midnight	2 Days Ago	3 Days Ago	Low	Avg	High	Dew	Avg	Max	Gust
64°F	75°F	68°F	0.00 in.	0.00 in.	0.00 in.	76%	92%	100%	66°F	7.2 mph	11 mph	15 mph

### DAILY SNAPSHOT

06:00 AM	09:00 AM	12:00 PM	03:00 PM	06:00 PM	09:00 PM
<b>fog</b> 65°F	<b>cloudy</b> 68°F	<b>partly-cloudy-day</b> 74°F	<b>partly-cloudy-day</b> 74°F	<b>partly-cloudy-night</b> 69°F	<b>cloudy</b> 68°F

### OBSERVED WEATHER CONDITIONS

No.	Weather Delay	Sky	Temp	Average	Precipitation	Wind	Ground/Sea
1	No	Clear	Hot	68	0	Light Wind	Dry

### MANPOWER LOG

**48 Workers | 415.52 Man Hours**

No.	Contact/Company	Cost Code	Workers	# Hours	Man Hours	Location
1	EAA Site Contractors LLC		8	8.0	64.0	Site
<b>Notes:</b> Total man hours 60. EAA continued to dig retention pond today. Placed dirt in section A and B. The compaction test for section B (the final lift) passed today. Also the loading dock area passed the compaction test as well today.						
2	A&B Electric Co., Inc.		10	10.0	100.0	Site>C
<b>Notes:</b> Working on temporary panels and temporary lights, Working on underground in section "C"						
3	Bayside Structures, LLC		6	9.0	54.0	Site
<b>Notes:</b> Regrade and tamp corridor at elevation 83. closed up west side of connector stem wall. Made corrections in rebar for GB6 on north end. Moved GB pour for connector to Thursday next week. Installed vapor barrier in corridor elevation 83.						
4	Caddell Construction Co. (DE), LLC		9	10.0	90.0	Site
<b>Notes:</b> WGI/Caddell supervision, quality control and safety onsite.						
5	Larry M. Jacobs & Associates, Inc.		1	1.0	1.0	Site
<b>Notes:</b> Conducted Density Test in Area B and Loading Dock.						
6	Nash Plumbing and Mechanical, LLC		1	8.0	8.0	Building>C
<b>Notes:</b> Continued with plumbing underground rough-in in Area C						

**MANPOWER LOG**

**48 Workers | 415.52 Man Hours**

No.	Contact/Company	Cost Code	Workers	# Hours	Man Hours	Location
7	Ed Emmons Steel Erectors, Inc.		9	8.0	72.0	Building>D
<b>Notes:</b> Continued erecting beams in Area D elevation 115.						
8	Chavers Construction Inc.		4	6.63	26.52	Site>Stormwater Pond
<b>Notes:</b> Demob 202 feet of 36x28 existing storm pipe. Demob 4 storm boxes.						
			<b>48</b>		<b>415.52</b>	

**Manpower Log's Attachments:**

2. A&B Electric Co., Inc.



[Daily Construction Report -- 2\\_7\\_19.pdf](#)

3. Bayside Structures, LLC




[Bayside Daily 2-7-2019.PDF](#)

6. Nash Plumbing and Mechanical, LLC


[Nash Daily 2-7-2019.xlsx](#)

7. Ed Emmons Steel Erectors, Inc.

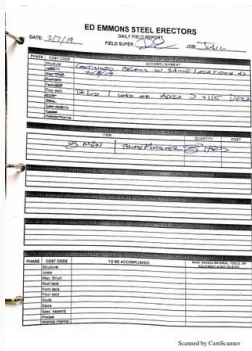

[New Doc 2019-02-07 16.35.30.pdf](#)

8. Chavers Construction Inc.

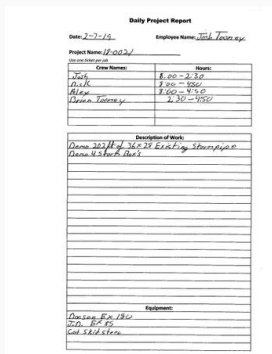

[Chaver Daily 2-7-2019.PDF](#)

**EQUIPMENT LOG**

No.	Equipment Name	Cost Code	Hrs Operating	Hrs Idle	Inspected?	Inspection Time	Location
1	John Deere 550H Dozer				No	07:00 AM	Building>A
	<b>Notes:</b>						
2	Vibratory Roller				No	07:00 AM	Building>A
	<b>Notes:</b>						
3	John Deere Skidsteer				No	07:00 AM	Building>A
	<b>Notes:</b>						
4	CAT Miniexcavator				No	07:00 AM	Building>C
	<b>Notes:</b>						
5	Grove Crane AT700D				No	07:00 AM	Building>D
	<b>Notes:</b>						
6	Genie Lift S80				No	07:00 AM	Building>D
	<b>Notes:</b>						
7	Scissor Lift				No	07:00 AM	Building>D
	<b>Notes:</b>						
8	Scissor Lift				No	07:00 AM	Building>D
	<b>Notes:</b>						

**EQUIPMENT LOG**

No.	Equipment Name	Cost Code	Hrs Operating	Hrs Idle	Inspected?	Inspection Time	Location
9	Cat Telehandler				No	07:00 AM	Site
	<b>Notes:</b>						
10	JLG Skytrak Telehandler				No	07:00 AM	Site
	<b>Notes:</b>						
11	Terex Articulated Dump Truck				No	07:45 AM	Site>Stormwater Pond
	<b>Notes:</b>						
12	Volvo 330 Excavator				No	07:00 AM	Site>Stormwater Pond
	<b>Notes:</b>						
13	John Deere 750 Dozer				No	07:00 AM	Site>Stormwater Pond
	<b>Notes:</b>						
14	Komatsu 320 PT Loader				No	07:00 AM	Site>Stormwater Pond
	<b>Notes:</b>						
15	Doosan Loader				No	07:00 AM	Site>Stormwater Pond
	<b>Notes:</b>						
16	Volvo 330 Excavator				No	07:00 AM	Site>Stormwater Pond
	<b>Notes:</b>						

**INSPECTION LOG**

No.	Start Time	End Time	Inspection Type	Inspecting Entity	Inspector Name	Location	Area
1	02:40 PM	03:10 AM	Third Party	Mott MacDonald	Mike Tugwell	Site	
	<b>Comments:</b> Threshold inspection on corridor connecting the existing jail to new construction.						

By \_\_\_\_\_

Date \_\_\_\_\_

Copies To \_\_\_\_\_



## Daily Log: Friday 2/8/2019

**Daily Log Completed**  
 The Daily Log was completed by Donald Shelton on Mon Feb 11, 2019 at 07:37 am CST.

### WEATHER REPORT

Temperature			Precipitation Since			Humidity				Windspeed		
Low	High	Avg	Midnight	2 Days Ago	3 Days Ago	Low	Avg	High	Dew	Avg	Max	Gust
45°F	68°F	57°F	0.00 in.	0.00 in.	0.00 in.	39%	63%	97%	44°F	11.0 mph	15 mph	26 mph

### DAILY SNAPSHOT

06:00 AM	09:00 AM	12:00 PM	03:00 PM	06:00 PM	09:00 PM
partly-cloudy-night 59°F	partly-cloudy-day 56°F	cloudy 57°F	cloudy 59°F	cloudy 58°F	partly-cloudy-night 50°F

### OBSERVED WEATHER CONDITIONS

No.	Weather Delay	Sky	Temp	Average	Precipitation	Wind	Ground/Sea
1	No	Cloudy	Mild	57	0	Light Wind	Dry

### MANPOWER LOG

47 Workers | 379.0 Man Hours

No.	Contact/Company	Cost Code	Workers	# Hours	Man Hours	Location
1	A&B Electric Co., Inc.		7	8.0	56.0	Building
<b>Notes:</b> Worked on temp lighting, finished underground rough in for armory, installed pull box at finish floor level in day room B chase, built up boxes and conduit for Moss Point, received materials and ice machine and ice.						
2	Bayside Structures, LLC		10	9.0	90.0	Site
<b>Notes:</b> Placed reinforcement slab on grade in corridor. Continued forming connector.						
3	Caddell Construction Co. (DE), LLC		9	8.0	72.0	Site
<b>Notes:</b> WGI/Caddell supervision, quality control and safety onsite.						
4	EAA Site Contractors LLC		4	8.0	32.0	Site
<b>Notes:</b> Total man hours 22.5. EAA completed the third lift on the loading dock in section D. The loading dock area is ready for the next compaction test on Monday. Set grades in section A today						
5	Ed Emmons Steel Erectors, Inc.		9	8.0	72.0	Building>D
<b>Notes:</b> Continued erecting beams in Area D at elevation 115.						


**MANPOWER LOG**

47 Workers | 379.0 Man Hours

No.	Contact/Company	Cost Code	Workers	# Hours	Man Hours	Location
6	Nash Plumbing and Mechanical, LLC		7	8.0	56.0	Building>C
<b>Notes:</b> Back-filled after plumbing underground inspection in Area C.						
7	Larry M. Jacobs & Associates, Inc.		1	1.0	1.0	Site>D
<b>Notes:</b> Conducted Density Test in Area D						
			<b>47</b>		<b>379.0</b>	


**Manpower Log's Attachments:**

- 1. A&B Electric Co., Inc.

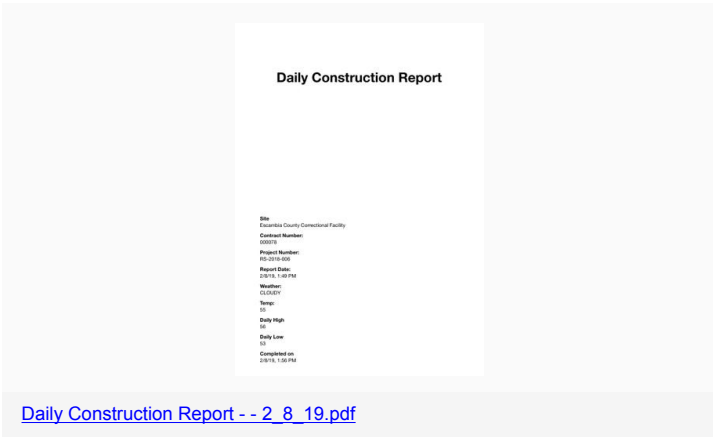


[Daily Construction Report - - 2\\_8\\_19.pdf](#)

- 2. Bayside Structures, LLC

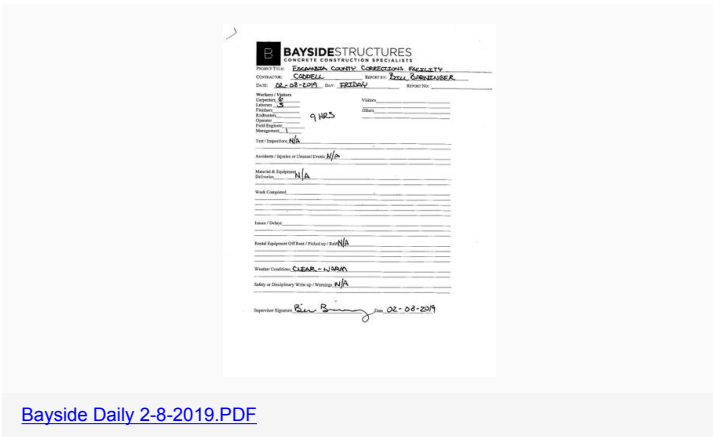

[Bayside Daily 2-8-2019.PDF](#)

5. Ed Emmons Steel Erectors, Inc.



[New Doc 2019-02-08 16.16.15.pdf](#)

6. Nash Plumbing and Mechanical, LLC

[Nash Daily 2-8-2019.xlsx](#)

**EQUIPMENT LOG**

No.	Equipment Name	Cost Code	Hrs Operating	Hrs Idle	Inspected?	Inspection Time	Location
1	CAT Miniexcavator				No	07:00 AM	Building>C
	<b>Notes:</b>						
2	Cat Skidsteer				No	07:00 AM	Building>C
	<b>Notes:</b>						
3	Grove Crane AT700D				No	07:00 AM	Building>D
	<b>Notes:</b>						
4	Vibratory Roller				No	07:00 AM	Building>D
	<b>Notes:</b>						
5	Scissor Lift				No	07:00 AM	Building>D
	<b>Notes:</b>						
6	Scissor Lift				No	07:00 AM	Building>D
	<b>Notes:</b>						
7	Scissor Lift				No	07:00 AM	Building>D
	<b>Notes:</b>						
8	JLG Skytrak Telehandler				No	07:00 AM	Site
	<b>Notes:</b>						
9	Cat Telehandler				No	07:00 AM	Site
	<b>Notes:</b>						
10	Bobcat Skidsteer				No	07:00 AM	Site
	<b>Notes:</b>						
11	Komatsu 320 PT Loader				No	07:00 AM	Site>Stormwater Pond
	<b>Notes:</b>						

By \_\_\_\_\_

Date \_\_\_\_\_

Copies To \_\_\_\_\_





**Whitesell Green / Caddell, a Joint Venture**  
 2700 Lagoon Park Drive  
 Montgomery, Alabama 36109  
 P: (334) 272-7723  
 F: (334) 394-0193

**Project: 1054 - Escambia County Correctional Facility**  
 3080 N. Pace Boulevard  
 Pensacola, Florida 32501

## Daily Log: Saturday 2/9/2019

**Daily Log Completed**  
 The Daily Log was completed by Donald Shelton on Mon Feb 11, 2019 at 07:09 am CST.

### WEATHER REPORT

Temperature			Precipitation Since			Humidity				Windspeed		
Low	High	Avg	Midnight	2 Days Ago	3 Days Ago	Low	Avg	High	Dew	Avg	Max	Gust
42°F	62°F	51°F	0.00 in.	0.00 in.	0.00 in.	33%	46%	54%	30°F	7.8 mph	11 mph	19 mph

### DAILY SNAPSHOT

06:00 AM	09:00 AM	12:00 PM	03:00 PM	06:00 PM	09:00 PM
partly-cloudy-night 43°F	cloudy 46°F	cloudy 55°F	partly-cloudy-day 62°F	partly-cloudy-night 57°F	clear-night 54°F

### OBSERVED WEATHER CONDITIONS

No.	Weather Delay	Sky	Temp	Average	Precipitation	Wind	Ground/Sea
1	No	Cloudy	Mild	51	0	Calm	Dry

### MANPOWER LOG

**4 Workers | 20.0 Man Hours**

No.	Contact/Company	Cost Code	Workers	# Hours	Man Hours	Location
1	Caddell Construction Co. (DE), LLC		1	5.0	5.0	Site
<b>Notes:</b> WGI/Caddell supervision, quality control and safety onsite.						
2	Chavers Construction Inc.		3	5.0	15.0	Site>Stormwater Pond
<b>Notes:</b> Installing domestic water from the connector to the corner of the site.						
			<b>4</b>	<b>20.0</b>		

### EQUIPMENT LOG

No.	Equipment Name	Cost Code	Hrs Operating	Hrs Idle	Inspected?	Inspection Time	Location
1	Excavator				No	07:00 AM	Site>Stormwater Pond
<b>Notes:</b>							

By \_\_\_\_\_ Date \_\_\_\_\_ Copies To \_\_\_\_\_



Whitesell Green / Caddell, a Joint Venture  
 2700 Lagoon Park Drive  
 Montgomery, Alabama 36109  
 P: (334) 272-7723  
 F: (334) 394-0193

Project: 1054 - Escambia County Correctional  
**Facility**  
 3080 N. Pace Boulevard  
 Pensacola, Florida 32501

## Daily Log: Sunday 2/10/2019

### WEATHER REPORT

Temperature			Precipitation Since			Humidity				Windspeed		
Low	High	Avg	Midnight	2 Days Ago	3 Days Ago	Low	Avg	High	Dew	Avg	Max	Gust
53°F	64°F	59°F	0.01 in.	0.01 in.	0.01 in.	48%	72%	98%	49°F	7.1 mph	9 mph	15 mph

### DAILY SNAPSHOT

06:00 AM	09:00 AM	12:00 PM	03:00 PM	06:00 PM	09:00 PM
cloudy 55°F	cloudy 59°F	cloudy 63°F	cloudy 65°F	cloudy 62°F	partly-cloudy-night 61°F

### OBSERVED WEATHER CONDITIONS

No.	Weather Delay	Sky	Temp	Average	Precipitation	Wind	Ground/Sea
1	No						

By \_\_\_\_\_

Date \_\_\_\_\_

Copies To \_\_\_\_\_



## Daily Log: Monday 2/11/2019

**Daily Log Completed**  
 The Daily Log was completed by Donald Shelton on Fri Feb 15, 2019 at 03:56 pm CST.

### WEATHER REPORT

Temperature			Precipitation Since			Humidity				Windspeed		
Low	High	Avg	Midnight	2 Days Ago	3 Days Ago	Low	Avg	High	Dew	Avg	Max	Gust
56°F	69°F	63°F	0.01 in.	0.02 in.	0.02 in.	83%	95%	100%	62°F	7.3 mph	11 mph	17 mph

### DAILY SNAPSHOT

06:00 AM	09:00 AM	12:00 PM	03:00 PM	06:00 PM	09:00 PM
cloudy 59°F	cloudy 62°F	cloudy 68°F	cloudy 70°F	cloudy 68°F	cloudy 67°F

### OBSERVED WEATHER CONDITIONS

No.	Weather Delay	Sky	Temp	Average	Precipitation	Wind	Ground/Sea
1	No	Overcast	Mild	63	0	Calm	Dry

### MANPOWER LOG

74 Workers | 678.5 Man Hours

No.	Contact/Company	Cost Code	Workers	# Hours	Man Hours	Location
1	A&B Electric Co., Inc.		11	10.0	110.0	Building
<b>Notes:</b> Working on temporary panels and temporary lights, Working on fabbing conduit for underground. Stub conduits out from under 12" water pipe installed Saturday, Finish Backfill of Main Electrical room.						
2	Bayside Structures, LLC		8	10.0	80.0	Building
<b>Notes:</b> Tied rebar corridor at elevation 83 in Area C and D.						
3	Caddell Construction Co. (DE), LLC		9	10.0	90.0	Site
<b>Notes:</b> WGI/Caddell supervision, quality control and safety onsite.						
4	Chavers Construction Inc.		2	8.25	16.5	Site
<b>Notes:</b> Installed 200' of 8" water main Hauled off last load of concrete pipe Spot existing utility						
5	Ed Emmons Steel Erectors, Inc.		9	8.0	72.0	Building>D
<b>Notes:</b> Set up crane between Area C and D. Laid composite deck and hung beams.						


**MANPOWER LOG**

**74 Workers | 678.5 Man Hours**

No.	Contact/Company	Cost Code	Workers	# Hours	Man Hours	Location
6	Larry M. Jacobs & Associates, Inc.		1	2.0	2.0	Site
	<b>Notes:</b> Conducted Density Tests in Loading Dock, Area A, and B.					
7	Nash Plumbing and Mechanical, LLC		7	8.0	56.0	Building>A
	<b>Notes:</b> Installed plumbing underground rough-in in Area A.					
8	Tindall Corporation		18	10.0	180.0	Building>C
	<b>Notes:</b> **Erecting in area C from J to M line **Welding and grouting **Misc. patching 185 Total Man Hold					
9	EAA Site Contractors LLC		9	8.0	72.0	Site
	<b>Notes:</b> Total man hours 90. EAA continued to dig retention pond. Hauled dirt to A&B electric for backfill in the eclectic room of section D. Also continued to place dirt in section A and B. The compaction test for the loading dock in section D passed the third lift. Also passed 2 of 3 compaction test for section A.					
			<b>74</b>	<b>678.5</b>		


**Manpower Log's Attachments:**

- 1. A&B Electric Co., Inc.

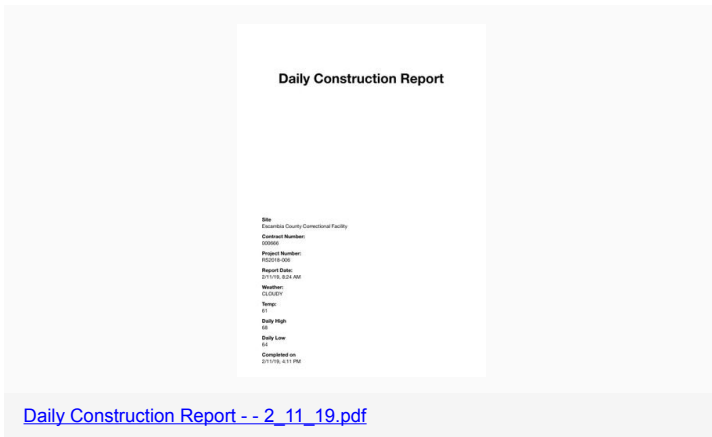

[Daily Construction Report -- 2\\_11\\_19.pdf](#)

- 2. Bayside Structures, LLC

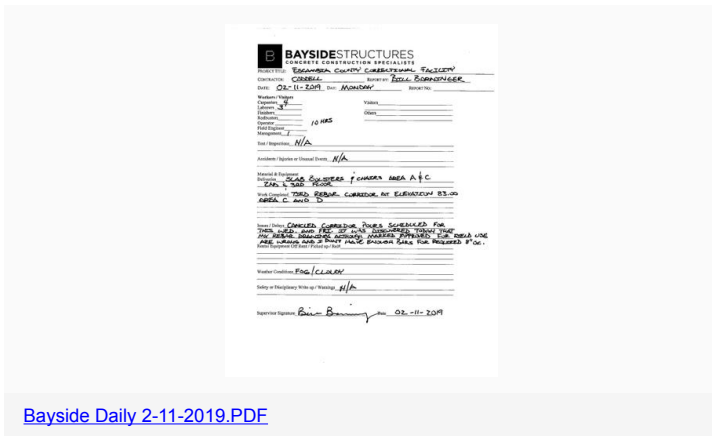

[Bayside Daily 2-11-2019.PDF](#)

4. Chavers Construction Inc.

[Chaver Daily 2-11-2019.PDF](#)

5. Ed Emmons Steel Erectors, Inc.

[New Doc 2019-02-11 15.17.37.pdf](#)

7. Nash Plumbing and Mechanical, LLC

[Nash Daily 2-11-2019.xlsx](#)

8. Tindall Corporation

[Tindall Escambia Daily 2-11-2019.xlsx](#)

**EQUIPMENT LOG**

No.	Equipment Name	Cost Code	Hrs Operating	Hrs Idle	Inspected?	Inspection Time	Location
1	Cat Skidsteer				No	07:00 AM	Building>A
	<b>Notes:</b>						
2	Vibratory Roller				No	07:00 AM	Building>B
	<b>Notes:</b>						
3	Komatsu 78MR Excavator				No	07:00 AM	Building>B
	<b>Notes:</b>						
4	Kobelco Crane CKE2500				No	07:00 AM	Building>C
	<b>Notes:</b>						
5	JLG Lift 660SJ				No	07:00 AM	Building>C
	<b>Notes:</b>						
6	Genie Lift S85				No	07:00 AM	Building>C
	<b>Notes:</b>						

## EQUIPMENT LOG

No.	Equipment Name	Cost Code	Hrs Operating	Hrs Idle	Inspected?	Inspection Time	Location
7	Grove Crane AT700D				No	07:00 AM	Building>D
	<b>Notes:</b>						
8	Genie Lift S80				No	07:00 AM	Building>D
	<b>Notes:</b>						
9	JLG Skytrak Telehandler				No	07:00 AM	Site
	<b>Notes:</b>						
10	JLG Skytrak Telehandler				No	07:00 AM	Site
	<b>Notes:</b>						
11	John Deere 85G Excavator				No	07:00 AM	Site
	<b>Notes:</b>						
12	Volvo 330 Excavator				No	07:00 AM	Site>Stormwater Pond
	<b>Notes:</b>						
13	Doosan Excavator				No	07:00 AM	Site>Stormwater Pond
	<b>Notes:</b>						
14	Komatsu 320 PT Loader				No	07:00 AM	Site>Stormwater Pond
	<b>Notes:</b>						
15	Terex Articulated Dump Truck				No	07:00 AM	Site>Stormwater Pond
	<b>Notes:</b>						

By \_\_\_\_\_

Date \_\_\_\_\_

Copies To \_\_\_\_\_



## Daily Log: Tuesday 2/12/2019

**Daily Log Completed**  
 The Daily Log was completed by Donald Shelton on Mon Feb 18, 2019 at 03:29 pm CST.

### WEATHER REPORT

Temperature			Precipitation Since			Humidity				Windspeed		
Low	High	Avg	Midnight	2 Days Ago	3 Days Ago	Low	Avg	High	Dew	Avg	Max	Gust
51°F	76°F	65°F	0.16 in.	0.16 in.	0.18 in.	76%	89%	98%	62°F	9.0 mph	16 mph	23 mph

### DAILY SNAPSHOT

06:00 AM	09:00 AM	12:00 PM	03:00 PM	06:00 PM	09:00 PM
cloudy 68°F	partly-cloudy-day 73°F	rain 67°F	cloudy 64°F	rain 58°F	partly-cloudy-night 57°F

### OBSERVED WEATHER CONDITIONS

No.	Weather Delay	Sky	Temp	Average	Precipitation	Wind	Ground/Sea
1	No	Overcast	Mild	65	0	Light Wind	Dry

### MANPOWER LOG

64 Workers | 477.0 Man Hours

No.	Contact/Company	Cost Code	Workers	# Hours	Man Hours	Location
1	A&B Electric Co., Inc.		11	10.0	110.0	Building>D
<b>Notes:</b> Fab conduits and 90's for Rough in, Backfill of Main Electrical room.						
2	Bayside Structures, LLC		9	8.0	72.0	Site
<b>Notes:</b> Finished tying rebar mats and fine grading in corridor, marked FF 83 in Area D and started building boxes for column slabs.						
3	Caddell Construction Co. (DE), LLC		9	10.0	90.0	Site
<b>Notes:</b> WGI/Caddell supervision, quality control and safety onsite.						
4	Chavers Construction Inc.		1	8.0	8.0	Site
<b>Notes:</b> Installed 180' of domestic water main. Back filled trench in first lift. Passed inspection by county inspector.						
5	Ed Emmons Steel Erectors, Inc.		9	5.0	45.0	Building
<b>Notes:</b> Started installing perimeter safety cables at elevator shaft. Rain out at 11:15/11:30.						

**MANPOWER LOG**

**64 Workers | 477.0 Man Hours**

No.	Contact/Company	Cost Code	Workers	# Hours	Man Hours	Location
6	Larry M. Jacobs & Associates, Inc.		2	3.0	6.0	Site
	<b>Notes:</b> Conducted Density Test in Area A and D. Conducted Steel inspection in Area D					
7	Nash Plumbing and Mechanical, LLC		4	8.0	32.0	Site
	<b>Notes:</b> Received and organized materials					
8	Tindall Corporation		19	6.0	114.0	Building>C
	<b>Notes:</b> **Erecting in area C from J to M line **Welding and grouting **Misc. patching Total of 106 Man Hours					
			<b>64</b>		<b>477.0</b>	

**Manpower Log's Attachments:**

- 1. A&B Electric Co., Inc.

**Daily Construction Report**

**Site:** Escambia County Correctional Facility  
**Contract Number:** 000007  
**Project Number:** 00000000-1000-Correctional Project (Escambia Co. Correctional Facility)  
**Report Date:** 2/12/19, 08:17 AM  
**Weather:** CLEAR  
**Temp:** 73  
**Wind:** 73  
**Wind Dir:** 73  
**Wind Line:** 43  
**Completed on:** 2/12/19, 4:55 PM

[Daily Construction Report -- 2\\_12\\_19.pdf](#)

- 2. Bayside Structures, LLC

**BAYSIDE STRUCTURES**  
 10000 BAYSIDE DRIVE, SUITE 100, JACKSONVILLE, FL 32216  
 PHONE: 904.250.1234 FAX: 904.250.1235  
 WWW.BAYSIDESTRUCTURES.COM

**Project Title:** Escambia County Correctional Facility  
**Location:** Caddell  
**City:** Jacksonville, FL  
**Contract No.:** 00000000-1000-Correctional Project (Escambia Co. Correctional Facility)  
**Report Date:** 2/12/19, 08:17 AM  
**Weather:** CLEAR  
**Temp:** 73  
**Wind:** 73  
**Wind Dir:** 73  
**Wind Line:** 43  
**Completed on:** 2/12/19, 4:55 PM

[Bayside Daily 2-12-2019.PDF](#)





## EQUIPMENT LOG

No.	Equipment Name	Cost Code	Hrs Operating	Hrs Idle	Inspected?	Inspection Time	Location
7	JLG Lift 660SJ				No	07:00 AM	Building>C
<b>Notes:</b>							
8	JLG Skytrak Telehandler				No	07:00 AM	Site
<b>Notes:</b>							
9	JLG Skytrak Telehandler				No	07:00 AM	Site
<b>Notes:</b>							

---

By

---

Date

---

Copies To



## Daily Log: Wednesday 2/13/2019

**Daily Log Completed**  
 The Daily Log was completed by Donald Shelton on Mon Feb 18, 2019 at 01:35 pm CST.

### WEATHER REPORT

Temperature			Precipitation Since			Humidity				Windspeed		
Low	High	Avg	Midnight	2 Days Ago	3 Days Ago	Low	Avg	High	Dew	Avg	Max	Gust
39°F	63°F	50°F	0.00 in.	0.16 in.	0.17 in.	30%	61%	92%	35°F	6.7 mph	12 mph	19 mph

### DAILY SNAPSHOT

06:00 AM	09:00 AM	12:00 PM	03:00 PM	06:00 PM	09:00 PM
clear-night 41°F	clear-day 50°F	clear-day 59°F	clear-day 63°F	clear-night 56°F	clear-night 42°F

### OBSERVED WEATHER CONDITIONS

No.	Weather Delay	Sky	Temp	Average	Precipitation	Wind	Ground/Sea
1	No	Clear	Mild	50	0	Light Wind	Dry


### MANPOWER LOG

52 Workers | 484.0 Man Hours

No.	Contact/Company	Cost Code	Workers	# Hours	Man Hours	Location
1	A&B Electric Co., Inc.		11	10.0	110.0	Site>Stormwater Pond
<b>Notes:</b> Remove existing service pole in old Juvenile parking, Bend 90's and fab nipples for rough in, Backfill of Main Electrical room.						
2	Bayside Structures, LLC		7	10.0	70.0	Building>D
<b>Notes:</b> Laid out Tindall Dowels and installed stemwall at connector. Worked on forming column isolation in Area D. Elevation 83.						
3	Caddell Construction Co. (DE), LLC		1	8.0	8.0	Site
<b>Notes:</b> WGI/Caddell supervision, quality control and safety onsite.						
4	Chavers Construction Inc.		1	8.0	8.0	Site
<b>Notes:</b> Back filled trench for second and third lift.						
5	Ed Emmons Steel Erectors, Inc.		1	8.0	8.0	Building
<b>Notes:</b> Installed perimeter cables. Cut in fillers at deck edges. Laid out shear studs. Installed shear studs.						
6	Larry M. Jacobs & Associates, Inc.		2	4.0	8.0	Site
<b>Notes:</b> Conducted Density Test in Area D and 8' Plan North side of Area D. Conducted Steel inspection in Area D.						



5. Ed Emmons Steel Erectors, Inc.

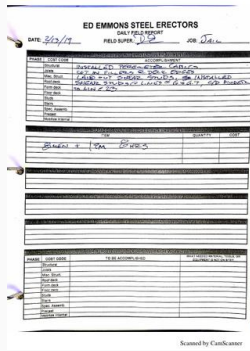

[New Doc 2019-02-13 15.12.40.pdf](#)

7. Nelson Plumbing Contractors, Inc.

[Nash Daily 2-13-2019.xlsx](#)

8. Tindall Corporation

[Tindall Escambia Daily 2-13-2019.xlsx](#)

**EQUIPMENT LOG**

No.	Equipment Name	Cost Code	Hrs Operating	Hrs Idle	Inspected?	Inspection Time	Location
1	John Deere 50G Miniexcavator				No	07:00 AM	Building>B
	<b>Notes:</b>						
2	Kobelco Crane CKE2500				No	07:00 AM	Building>C
	<b>Notes:</b>						
3	JLG Lift 660SJ				No	07:00 AM	Building>C
	<b>Notes:</b>						
4	Grove Crane AT700D				No	07:00 AM	Building>D
	<b>Notes:</b>						
5	Genie Lift S80				No	07:00 AM	Building>D
	<b>Notes:</b>						
6	JLG Skytrak Telehandler				No	07:00 AM	Site
	<b>Notes:</b>						
7	JLG Skytrak Telehandler				No	07:00 AM	Site
	<b>Notes:</b>						
8	Cat Telehandler				No	07:00 AM	Site
	<b>Notes:</b>						
9	Cat Skidsteer				No	07:00 AM	Site
	<b>Notes:</b>						
10	John Deere 85G Excavator				No	07:00 AM	Site
	<b>Notes:</b>						
11	Volvo 330 Excavator				No	07:00 AM	Site>Stormwater Pond
	<b>Notes:</b>						

## EQUIPMENT LOG

No.	Equipment Name	Cost Code	Hrs Operating	Hrs Idle	Inspected?	Inspection Time	Location
12	Terex Articulated Dump Truck				No	07:00 AM	Site>Stormwater Pond

**Notes:**

---

---

By

---

Date

---

Copies To



## Daily Log: Thursday 2/14/2019

**Daily Log Completed**  
 The Daily Log was completed by Donald Shelton on Mon Feb 18, 2019 at 03:26 pm CST.

### WEATHER REPORT

Temperature			Precipitation Since			Humidity				Windspeed		
Low	High	Avg	Midnight	2 Days Ago	3 Days Ago	Low	Avg	High	Dew	Avg	Max	Gust
37°F	67°F	54°F	0.00 in.	0.00 in.	0.16 in.	53%	81%	100%	47°F	6.4 mph	13 mph	14 mph

### DAILY SNAPSHOT

06:00 AM	09:00 AM	12:00 PM	03:00 PM	06:00 PM	09:00 PM
clear-night 39°F	partly-cloudy-day 58°F	partly-cloudy-day 66°F	partly-cloudy-day 67°F	partly-cloudy-night 61°F	partly-cloudy-night 59°F

### OBSERVED WEATHER CONDITIONS

No.	Weather Delay	Sky	Temp	Average	Precipitation	Wind	Ground/Sea
1	No	Clear	Mild	53	0	Light Wind	Dry

### MANPOWER LOG

72 Workers | 654.0 Man Hours

No.	Contact/Company	Cost Code	Workers	# Hours	Man Hours	Location
1	A&B Electric Co., Inc.		2	10.0	20.0	Building
<b>Notes:</b> Working on temporary lights, Fab nipples and boxes for rough in.						
2	Bayside Structures, LLC		11	10.0	110.0	Site
<b>Notes:</b> Worked on installing rebar in corridor. Installed rebar in GB at connector that we were shorted for GB change. Formed GB at connector or after rebar was installed.						
3	Caddell Construction Co. (DE), LLC		9	10.0	90.0	Site
<b>Notes:</b> WGI/Caddell supervision, quality control and safety onsite.						
4	Chavers Construction Inc.		3	8.0	24.0	Site
<b>Notes:</b> Installed domestic water main.						
5	Ed Emmons Steel Erectors, Inc.		9	8.0	72.0	Building>D
<b>Notes:</b> Shot shear studs						
6	Larry M. Jacobs & Associates, Inc.		1	2.0	2.0	Site
<b>Notes:</b> Conducted Density Test in Area A, B, and North side of site.						

**MANPOWER LOG**

72 Workers | 654.0 Man Hours

No.	Contact/Company	Cost Code	Workers	# Hours	Man Hours	Location
7	Nash Plumbing and Mechanical, LLC		7	8.0	56.0	Building
<b>Notes:</b> Plumbing: layout holes in corridor walls to be core drilled Mechanical: build block outs for 115' elevation pour.						
8	Tindall Corporation		20	10.0	200.0	Building>C
<b>Notes:</b> **Erecting in area C from J to M line **Welding and grouting **Misc. patching 202.5 Total Man Hours						
9	EAA Site Contractors LLC		10	8.0	80.0	Site
<b>Notes:</b> Total man hours 70. EAA continued to dig retention pond today. The structural fill for section A 100% complete. Both to grade and compaction. Pete from Caddell has accepted section A as complete. In addition all areas of section B have passed density test.						
			<b>72</b>		<b>654.0</b>	

**Manpower Log's Attachments:**

1. A&B Electric Co., Inc.



[Daily Construction Report - - 2\\_14\\_19.pdf](#)


2. Bayside Structures, LLC



[Bayside Daily 2-14-2019.PDF](#)



5. Ed Emmons Steel Erectors, Inc.

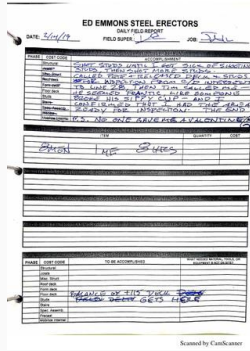

[New Doc 2019-02-14 15.16.37.pdf](#)

7. Nash Plumbing and Mechanical, LLC

[Nash Daily 2-14-2019.xlsx](#)

8. Tindall Corporation

[Tindall Escambia Daily 2-14-2019.xlsx](#)

**EQUIPMENT LOG**

No.	Equipment Name	Cost Code	Hrs Operating	Hrs Idle	Inspected?	Inspection Time	Location
1	John Deere 550H Dozer				No	07:00 AM	Building>A
	<b>Notes:</b>						
2	JLG Lift 860SJ				No	07:00 AM	Building>A
	<b>Notes:</b>						
3	Kobelco Crane CKE2500				No	07:00 AM	Building>C
	<b>Notes:</b>						
4	JLG Lift 660SJ				No	07:00 AM	Building>C
	<b>Notes:</b>						
5	JLG Lift 660SJ				No	07:00 AM	Building>C
	<b>Notes:</b>						
6	Genie Lift S85				No	07:00 AM	Building>C
	<b>Notes:</b>						
7	Grove Crane AT700D				No	07:00 AM	Building>D
	<b>Notes:</b>						
8	Genie Lift S85				No	07:00 AM	Building>D
	<b>Notes:</b>						
9	John Deere 85G Excavator				No	07:00 AM	Site
	<b>Notes:</b>						
10	Cat Skidsteer				No	07:00 AM	Site
	<b>Notes:</b>						
11	JLG Skytrak Telehandler				No	07:00 AM	Site
	<b>Notes:</b>						
12	JLG Skytrak Telehandler				No	07:00 AM	Site
	<b>Notes:</b>						

## EQUIPMENT LOG

No.	Equipment Name	Cost Code	Hrs Operating	Hrs Idle	Inspected?	Inspection Time	Location
13	Cat Telehandler				No	07:00 AM	Site
	<b>Notes:</b>						
14	Volvo 330 Excavator				No	07:00 AM	Site>Stormwater Pond
	<b>Notes:</b>						
15	Terex Articulated Dump Truck				No	07:00 AM	Site>Stormwater Pond
	<b>Notes:</b>						
16	Vibratory Roller				No	07:00 AM	Site
	<b>Notes:</b>						

---

By

---

Date

---

Copies To



## Daily Log: Friday 2/15/2019

**Daily Log Completed**  
 The Daily Log was completed by Donald Shelton on Mon Feb 18, 2019 at 03:31 pm CST.

### WEATHER REPORT

Temperature			Precipitation Since			Humidity				Windspeed		
Low	High	Avg	Midnight	2 Days Ago	3 Days Ago	Low	Avg	High	Dew	Avg	Max	Gust
54°F	74°F	64°F	0.01 in.	0.01 in.	0.01 in.	61%	84%	100%	59°F	6.7 mph	13 mph	21 mph

### DAILY SNAPSHOT

06:00 AM	09:00 AM	12:00 PM	03:00 PM	06:00 PM	09:00 PM
cloudy 57°F	partly-cloudy-day 67°F	partly-cloudy-day 74°F	partly-cloudy-day 73°F	partly-cloudy-night 66°F	partly-cloudy-night 65°F

### OBSERVED WEATHER CONDITIONS

No.	Weather Delay	Sky	Temp	Average	Precipitation	Wind	Ground/Sea
1	No	Cloudy	Mild	64	0	Light Wind	Dry


### MANPOWER LOG

58 Workers | 518.0 Man Hours

No.	Contact/Company	Cost Code	Workers	# Hours	Man Hours	Location
1	EAA Site Contractors LLC		3	8.0	24.0	Site
	<b>Notes:</b> Total man hours 20. EAA continued to dig retention pond today. Also we built a dirt ramp into section D from the east side. Starting to bring structural fill into the north end of section D. Section B of the bldg pad is 100% complete and has been accepted by Pete.					
2	A&B Electric Co., Inc.		1	10.0	10.0	Building
	<b>Notes:</b> Repair temporary lights					
3	Bayside Structures, LLC		8	8.0	64.0	
	<b>Notes:</b> Finished rebar at connector and worked on corridor rebar.					
4	Caddell Construction Co. (DE), LLC		9	10.0	90.0	Site
	<b>Notes:</b> WGI/Caddell supervision, quality control and safety onsite.					
5	Chavers Construction Inc.		3	8.0	24.0	Site
	<b>Notes:</b> Back filled trench in first and second and third lift					
6	Ed Emmons Steel Erectors, Inc.		9	8.0	72.0	Building>D
	<b>Notes:</b> Installed decking at elevation 115					
7	Larry M. Jacobs & Associates, Inc.		1	2.0	2.0	Site
	<b>Notes:</b> Conducted Density Test North of Area C.					



6. Ed Emmons Steel Erectors, Inc.



[New Doc 2019-02-15 14.59.23.pdf](#)

8. Nash Plumbing and Mechanical, LLC

[Nash Daily 2-15-2019.xlsx](#)

9. Tindall Corporation

[Tindall Escambia Daily 2-15-2019.xlsx](#)

**EQUIPMENT LOG**

No.	Equipment Name	Cost Code	Hrs Operating	Hrs Idle	Inspected?	Inspection Time	Location
1	John Deere 550H Dozer				No	07:00 AM	Building>B
	<b>Notes:</b>						
2	Kobelco Crane CKE2500				No	07:00 AM	Building>C
	<b>Notes:</b>						
3	Genie Lift S85				No	07:00 AM	Building>C
	<b>Notes:</b>						
4	JLG Lift 660SJ				No	07:00 AM	Building>C
	<b>Notes:</b>						
5	JLG Lift 660SJ				No	07:00 AM	Building>C
	<b>Notes:</b>						
6	Grove Crane AT700D				No	07:00 AM	Building>D
	<b>Notes:</b>						
7	Scissor Lift				No	07:00 AM	Building>D
	<b>Notes:</b>						
8	JLG Skytrak Telehandler				No	07:00 AM	Site
	<b>Notes:</b>						
9	JLG Skytrak Telehandler				No	07:00 AM	Site
	<b>Notes:</b>						
10	Cat Telehandler				No	07:00 AM	Site
	<b>Notes:</b>						
11	John Deere 85G Excavator				No	07:00 AM	Site
	<b>Notes:</b>						
12	Cat Skidsteer				No	07:00 AM	Site
	<b>Notes:</b>						

## EQUIPMENT LOG

No.	Equipment Name	Cost Code	Hrs Operating	Hrs Idle	Inspected?	Inspection Time	Location
13	Volvo 330 Excavator				No	07:00 AM	Site>Stormwater Pond

Notes:

## INSPECTION LOG

No.	Start Time	End Time	Inspection Type	Inspecting Entity	Inspector Name	Location	Area
1	01:30 PM	02:30 PM	Third Party	Mott MacDonald	Mike Tugwell	Site	

Comments: Threshold inspection on connector section

## PHOTOS



[DJI\\_0330.jpg](#)



[DJI\\_0340.jpg](#)



[DJI\\_0339.jpg](#)



[DJI\\_0290.jpg](#)



[DJI\\_0332.jpg](#)



[DJI\\_0331.jpg](#)



[DJI\\_0292.jpg](#)



[DJI\\_0333.jpg](#)



[DJI\\_0293.jpg](#)



[DJI\\_0335.jpg](#)



[DJI\\_0291.jpg](#)



[DJI\\_0337.jpg](#)



[DJI\\_0338.jpg](#)



[DJI\\_0299.jpg](#)



[DJI\\_0336.jpg](#)



[DJI\\_0294.jpg](#)



[DJI\\_0296.jpg](#)



[DJI\\_0334.jpg](#)



[DJI\\_0295.jpg](#)



[DJI\\_0300.jpg](#)



[DJI\\_0297.jpg](#)



[DJI\\_0301.jpg](#)





[DJI\\_0302.jpg](#)



[DJI\\_0304.jpg](#)



[DJI\\_0303.jpg](#)



[DJI\\_0309.jpg](#)



[DJI\\_0311.jpg](#)



[DJI\\_0310.jpg](#)



[DJI\\_0313.jpg](#)



[DJI\\_0312.jpg](#)



[DJI\\_0315.jpg](#)



[DJI\\_0316.jpg](#)



[DJI\\_0318.jpg](#)



[DJI\\_0317.jpg](#)



[DJI\\_0319.jpg](#)



[DJI\\_0321.jpg](#)



[DJI\\_0324.jpg](#)



[DJI\\_0320.jpg](#)



[DJI\\_0307.jpg](#)



[DJI\\_0323.jpg](#)



[DJI\\_0325.jpg](#)



[DJI\\_0328.jpg](#)



[DJI\\_0308.jpg](#)



[DJI\\_0305.jpg](#)



[DJI\\_0329.jpg](#)



[DJI\\_0326.jpg](#)



[DJI\\_0327.jpg](#)



[DJI\\_0322.jpg](#)

---

By

Date

Copies To



## Daily Log: Saturday 2/16/2019

**Daily Log Completed**  
 The Daily Log was completed by Donald Shelton on Mon Feb 18, 2019 at 12:31 pm CST.

### WEATHER REPORT

Temperature			Precipitation Since			Humidity				Windspeed		
Low	High	Avg	Midnight	2 Days Ago	3 Days Ago	Low	Avg	High	Dew	Avg	Max	Gust
62°F	76°F	67°F	0.00 in.	0.01 in.	0.01 in.	68%	88%	100%	64°F	6.1 mph	9 mph	14 mph

### DAILY SNAPSHOT

06:00 AM	09:00 AM	12:00 PM	03:00 PM	06:00 PM	09:00 PM
cloudy 66°F	cloudy 68°F	partly-cloudy-day 77°F	partly-cloudy-day 74°F	clear-night 66°F	partly-cloudy-night 63°F

### OBSERVED WEATHER CONDITIONS

No.	Weather Delay	Sky	Temp	Average	Precipitation	Wind	Ground/Sea
1	No	Cloudy	Mild	67	0	Light Wind	Dry

### MANPOWER LOG

17 Workers | 170.0 Man Hours

No.	Contact/Company	Cost Code	Workers	# Hours	Man Hours	Location
1	Caddell Construction Co. (DE), LLC		1	10.0	10.0	Site
<b>Notes:</b> WGI/Caddell supervision, quality control and safety onsite.						
2	Tindall Corporation		16	10.0	160.0	Building>C
<b>Notes:</b> **Erecting in area C from J to M line **Welding and grouting						
			<b>17</b>	<b>170.0</b>		

2. Tindall Corporation

[Tindall Escambia Daily 2-16-2019.xlsx](#)

### EQUIPMENT LOG

No.	Equipment Name	Cost Code	Hrs Operating	Hrs Idle	Inspected?	Inspection Time	Location
1	Kobelco Crane CKE2500				No	07:00 AM	Building>C
<b>Notes:</b>							
2	JLG Lift 660SJ				No	07:00 AM	Building>C
<b>Notes:</b>							

## EQUIPMENT LOG

No.	Equipment Name	Cost Code	Hrs Operating	Hrs Idle	Inspected?	Inspection Time	Location
3	JLG Lift 660SJ				No	07:00 AM	Building>C
<b>Notes:</b>							
4	JLG Skytrak Telehandler				No	07:00 AM	Site
<b>Notes:</b>							

---

By

---

Date

---

Copies To



Whitesell Green / Caddell, a Joint Venture  
 2700 Lagoon Park Drive  
 Montgomery, Alabama 36109  
 P: (334) 272-7723  
 F: (334) 394-0193

Project: 1054 - Escambia County Correctional  
**Facility**  
 3080 N. Pace Boulevard  
 Pensacola, Florida 32501

## Daily Log: Sunday 2/17/2019

### WEATHER REPORT

Temperature			Precipitation Since			Humidity				Windspeed		
Low	High	Avg	Midnight	2 Days Ago	3 Days Ago	Low	Avg	High	Dew	Avg	Max	Gust
64°F	77°F	70°F	0.00 in.	0.00 in.	0.01 in.	78%	92%	100%	67°F	8.1 mph	11 mph	16 mph

### DAILY SNAPSHOT

06:00 AM	09:00 AM	12:00 PM	03:00 PM	06:00 PM	09:00 PM
cloudy 66°F	cloudy 71°F	cloudy 77°F	cloudy 76°F	cloudy 71°F	cloudy 70°F

### OBSERVED WEATHER CONDITIONS

No.	Weather Delay	Sky	Temp	Average	Precipitation	Wind	Ground/Sea
1	No						

By \_\_\_\_\_ Date \_\_\_\_\_ Copies To \_\_\_\_\_



## Daily Log: Monday 2/18/2019

**Daily Log Completed**  
 The Daily Log was completed by Donald Shelton on Mon Feb 25, 2019 at 11:19 am CST.

### WEATHER REPORT

Temperature			Precipitation Since			Humidity				Windspeed		
Low	High	Avg	Midnight	2 Days Ago	3 Days Ago	Low	Avg	High	Dew	Avg	Max	Gust
55°F	68°F	58°F	0.01 in.	0.01 in.	0.01 in.	59%	78%	100%	50°F	9.5 mph	12 mph	22 mph

### DAILY SNAPSHOT

06:00 AM	09:00 AM	12:00 PM	03:00 PM	06:00 PM	09:00 PM
cloudy 56°F	cloudy 56°F	cloudy 58°F	cloudy 58°F	cloudy 56°F	cloudy 56°F

### OBSERVED WEATHER CONDITIONS

No.	Weather Delay	Sky	Temp	Average	Precipitation	Wind	Ground/Sea
1	No	Cloudy	Mild	58	0	Light Wind	Dry

### MANPOWER LOG



79 Workers | 697.5 Man Hours

No.	Contact/Company	Cost Code	Workers	# Hours	Man Hours	Location
1	A&B Electric Co., Inc.		11	10.0	110.0	Site
<b>Notes:</b> Fab nipples and conduit for rough in, fab boxes for rough in.						
2	Bayside Structures, LLC		8	9.0	72.0	Site
<b>Notes:</b> Poured 46 yards at the connector. Poured remaining of grade beams at the existing jail and stem walls. Worked on corridor pour set up.						
3	Caddell Construction Co. (DE), LLC		9	10.0	90.0	Site
<b>Notes:</b> WGI/Caddell supervision, quality control and safety onsite.						
4	Chavers Construction Inc.		3	3.5	10.5	Site
<b>Notes:</b> Filled and compacted 3 lifts for water main at NE corner of site. Laid 120' of 8" fire main.						
5	Ed Emmons Steel Erectors, Inc.		8	8.0	64.0	Building>D
<b>Notes:</b> Shut down crane due to high winds						
6	EAA Site Contractors LLC		9	8.0	72.0	Site
<b>Notes:</b> Total man hours 90. EAA continued to dig retention pond today. Started the final lift of section D today						




**MANPOWER LOG**

**79 Workers | 697.5 Man Hours**

No.	Contact/Company	Cost Code	Workers	# Hours	Man Hours	Location
7	Larry M. Jacobs & Associates, Inc.		2	1.5	3.0	Site
<b>Notes:</b> Conducted Concrete testing for connector pour and density test north entrance off of Fairfield Blvd.						
8	Nelson Plumbing Contractors, Inc.		7	8.0	56.0	Building>D 
<b>Notes:</b> Mechanical- set block out and sleeves at elevation 115 Plumbing- set floor drains and sleeves at elevation 115						
9	Tindall Corporation		22	10.0	220.0	Building>C 
<b>Notes:</b> Erecting in area C about M line **Welding and grouting **Patching various						
			<b>79</b>	<b>697.5</b>		

**Manpower Log's Attachments:**

1. A&B Electric Co., Inc.

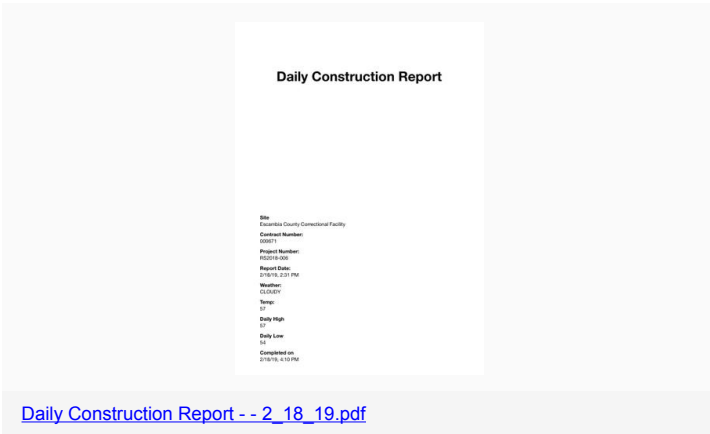


[Daily Construction Report -- 2\\_18\\_19.pdf](#)

2. Bayside Structures, LLC




[Bayside Daily 2-18-2019.PDF](#)

4. Chavers Construction Inc.

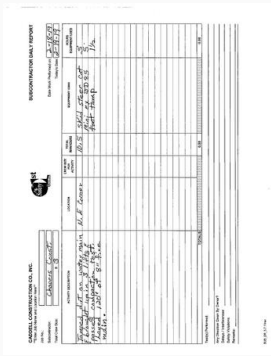

[Chaver Daily 2-18-2019.PDF](#)

5. Ed Emmons Steel Erectors, Inc.

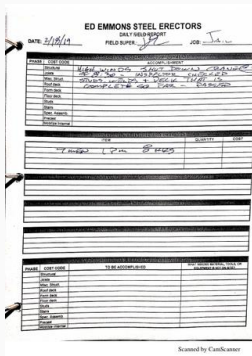

[New Doc 2019-02-18 20.01.50.pdf](#)

8. Nelson Plumbing Contractors, Inc.

[Nash Daily 2-18-2019.xlsx](#)

9. Tindall Corporation

[Tindall Escambia Daily 2-18-2019.xlsx](#)

**EQUIPMENT LOG**

No.	Equipment Name	Cost Code	Hrs Operating	Hrs Idle	Inspected?	Inspection Time	Location
1	Kobelco Crane CKE2500				No	07:00 AM	Building>C
	<b>Notes:</b>						
2	Genie Lift S85				No	07:00 AM	Building>C
	<b>Notes:</b>						
3	JLG Lift 660SJ				No	07:00 AM	Building>C
	<b>Notes:</b>						
4	John Deere 550H Dozer				No	07:00 AM	Building>D
	<b>Notes:</b>						
5	Komatsu 320 PT Loader				No	07:00 AM	Building>D
	<b>Notes:</b>						
6	Cat Skidsteer				No	07:00 AM	Building>D
	<b>Notes:</b>						

## EQUIPMENT LOG

No.	Equipment Name	Cost Code	Hrs Operating	Hrs Idle	Inspected?	Inspection Time	Location
7	Komatsu 78MR Excavator				No	07:00 AM	Building>D
	<b>Notes:</b>						
8	Terex Articulated Dump Truck				No	07:00 AM	Site>Stormwater Pond
	<b>Notes:</b>						
9	Volvo 330 Excavator				No	07:00 AM	Site>Stormwater Pond
	<b>Notes:</b>						
10	Cat Telehandler				No	07:00 AM	Site
	<b>Notes:</b>						
11	JLG Skytrak Telehandler				No	07:00 AM	Site
	<b>Notes:</b>						
12	JLG Skytrak Telehandler				No	07:00 AM	Site
	<b>Notes:</b>						

---

By

---

Date

---

Copies To



## Daily Log: Tuesday 2/19/2019

**Daily Log Completed**  
 The Daily Log was completed by Donald Shelton on Mon Feb 25, 2019 at 11:17 am CST.

### WEATHER REPORT

Temperature			Precipitation Since			Humidity				Windspeed		
Low	High	Avg	Midnight	2 Days Ago	3 Days Ago	Low	Avg	High	Dew	Avg	Max	Gust
52°F	66°F	60°F	0.07 in.	0.08 in.	0.08 in.	54%	76%	97%	52°F	10.4 mph	14 mph	20 mph

### DAILY SNAPSHOT

06:00 AM	09:00 AM	12:00 PM	03:00 PM	06:00 PM	09:00 PM
cloudy 57°F	cloudy 54°F	cloudy 62°F	cloudy 66°F	cloudy 65°F	cloudy 66°F

### OBSERVED WEATHER CONDITIONS

No.	Weather Delay	Sky	Temp	Average	Precipitation	Wind	Ground/Sea
1	No	Cloudy	Mild	60	0	Light Wind	Dry

### MANPOWER LOG

93 Workers | 1003.0 Man Hours

No.	Contact/Company	Cost Code	Workers	# Hours	Man Hours	Location
1	EAA Site Contractors LLC		11	8.0	88.0	Site
<b>Notes:</b> Total man hours 110. EAA continued to dig retention pond today. We placed dirt in the north part of section D and continued working south in section D. We have scheduled a compaction test for 8 am tomorrow.						
2	A&B Electric Co., Inc.		11	10.0	110.0	Site
<b>Notes:</b> Fabricate boxes and nipples for rough in, Fab 4" 90's for rough in, Repair and Check out Temporary lights. Repair conduit dug up and damaged by chavers Installing 12" water main.						
3	Bayside Structures, LLC		16	15.0	240.0	Site
<b>Notes:</b> Poured 225 LN FT. corridor at elevation 83. 45 yards cured and saw cut. Started placing WWM at elevation 115.						
4	Caddell Construction Co. (DE), LLC		9	15.0	135.0	Site
<b>Notes:</b> WGI/Caddell supervision, quality control and safety onsite.						
5	Chavers Construction Inc.		3	10.0	30.0	Site
<b>Notes:</b> Laid 150' of 8" fire main with 2 each 8" 45 degrees.						

**MANPOWER LOG**

**93 Workers | 1003.0 Man Hours**

No.	Contact/Company	Cost Code	Workers	# Hours	Man Hours	Location
6	Ed Emmons Steel Erectors, Inc.		9	10.0	90.0	Building>D
<b>Notes:</b> Finish elevation 100 floor deck at G-H.7, 46-50.						
7	Larry M. Jacobs & Associates, Inc.		1	2.0	2.0	Site
<b>Notes:</b> Conducted Density tests in Area D and Northeast corner of site for water main.						
8	Nash Plumbing and Mechanical, LLC		11	8.0	88.0	Building
<b>Notes:</b> Mechanical- safety training Plumbing- located penetrations in corridor walls, sleeves, floor drains, and roof drains at elevation 115.						
9	Tindall Corporation		22	10.0	220.0	Building>C
<b>Notes:</b> **Erecting east edge of arc C. **Welding and grouting **Patching various						
			<b>93</b>	<b>1003.0</b>		

**Manpower Log's Attachments:**

2. A&B Electric Co., Inc.




[Daily Construction Report -- 2\\_19\\_19.pdf](#)

3. Bayside Structures, LLC




[Bayside Daily 2-19-2019.PDF](#)

5. Chavers Construction Inc.

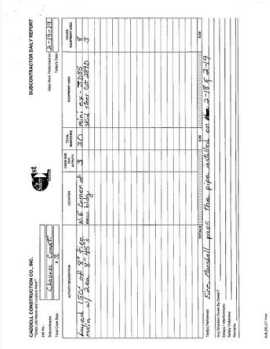

[Chaver Daily 2-19-2019.PDF](#)

6. Ed Emmons Steel Erectors, Inc.



[New Doc 2019-02-219 06.25.11.pdf](#)

8. Nash Plumbing and Mechanical, LLC

[Nash Daily 2-19-2019.xlsx](#)

9. Tindall Corporation

[Tindall Escambia daily 2-19-19.xlsx](#)

**EQUIPMENT LOG**

No.	Equipment Name	Cost Code	Hrs Operating	Hrs Idle	Inspected?	Inspection Time	Location
1	John Deere 750 Dozer				No	07:00 AM	Building>A
	<b>Notes:</b>						
2	Kobelco Crane CKE2500				No	07:00 AM	Building>C
	<b>Notes:</b>						
3	Genie Lift S85				No	07:00 AM	Building>C
	<b>Notes:</b>						
4	JLG Lift 660SJ				No	07:00 AM	Building>C
	<b>Notes:</b>						
5	JLG Lift 660SJ				No	07:00 AM	Building>C
	<b>Notes:</b>						
6	Grove Crane AT700D				No	07:00 AM	Building>D
	<b>Notes:</b>						

## EQUIPMENT LOG

No.	Equipment Name	Cost Code	Hrs Operating	Hrs Idle	Inspected?	Inspection Time	Location
7	Scissor Lift				No	07:00 AM	Building>D
	<b>Notes:</b>						
8	John Deere 550H Dozer				No	07:00 AM	Building>D
	<b>Notes:</b>						
9	Vibratory Roller				No	07:00 AM	Building>D
	<b>Notes:</b>						
10	Cat Skidsteer				No	07:00 AM	Building>D
	<b>Notes:</b>						
11	Komatsu 78MR Excavator				No	07:00 AM	Building>D
	<b>Notes:</b>						
12	Komatsu 320 PT Loader				No	07:00 AM	Building>D
	<b>Notes:</b>						
13	JLG Skytrak Telehandler				No	07:00 AM	Site
	<b>Notes:</b>						
14	JLG Skytrak Telehandler				No	07:00 AM	Site
	<b>Notes:</b>						
15	Cat Telehandler				No	07:00 AM	Site
	<b>Notes:</b>						
16	Bobcat Miniexcavator				No	07:00 AM	Site
	<b>Notes:</b>						
17	Cat Skidsteer				No	07:00 AM	Site
	<b>Notes:</b>						
18	John Deere 85G Excavator				No	07:00 AM	Site
	<b>Notes:</b>						
19	Volvo 330 Excavator				No	07:00 AM	Site>Stormwater Pond
	<b>Notes:</b>						
20	Terex Articulated Dump Truck				No	07:00 AM	Site>Stormwater Pond
	<b>Notes:</b>						

By \_\_\_\_\_

Date \_\_\_\_\_

Copies To \_\_\_\_\_



## Daily Log: Wednesday 2/20/2019

**Daily Log Completed**  
 The Daily Log was completed by Donald Shelton on Mon Feb 25, 2019 at 11:17 am CST.

### WEATHER REPORT

Temperature			Precipitation Since			Humidity				Windspeed		
Low	High	Avg	Midnight	2 Days Ago	3 Days Ago	Low	Avg	High	Dew	Avg	Max	Gust
61°F	74°F	67°F	0.00 in.	0.07 in.	0.08 in.	83%	94%	100%	65°F	11.3 mph	14 mph	26 mph

### DAILY SNAPSHOT

06:00 AM	09:00 AM	12:00 PM	03:00 PM	06:00 PM	09:00 PM
fog 62°F	fog 64°F	cloudy 71°F	fog 73°F	fog 71°F	fog 70°F

### OBSERVED WEATHER CONDITIONS

No.	Weather Delay	Sky	Temp	Average	Precipitation	Wind	Ground/Sea
1	No	Cloudy	Mild	67	0	Light Wind	Dry

### MANPOWER LOG

89 Workers | 806.0 Man Hours

No.	Contact/Company	Cost Code	Workers	# Hours	Man Hours	Location
1	EAA Site Contractors LLC		11	8.0	88.0	Site
<b>Notes:</b> Total man hours 110. We placed dirt in section D. All required compaction test for section D passed today. EAA will finalize the grade in section D tomorrow						
2	A&B Electric Co., Inc.		14	10.0	140.0	Site
<b>Notes:</b> Fab boxes and nipples for rough in, Fab 90's for underground rough in.						
3	Bayside Structures, LLC		12	10.0	120.0	Building>D
<b>Notes:</b> Completed placing WWM 4x4 for first pour at 115. Placed all 12' girder #4 bars and all 3' beam #4 rebar. Installed buck head at center line G. 112' LN FT. Installed buck head for next corridor pour at elevation 85. Excavated and poured 124 LN FT of dead men for Tindall.						
4	Caddell Construction Co. (DE), LLC		9	10.0	90.0	Site
<b>Notes:</b> WGI/Caddell supervision, quality control and safety onsite.						
5	Chavers Construction Inc.		4	10.0	40.0	Site
<b>Notes:</b> Laid 8" fire main. Filled and compacted all three lifts.						




**MANPOWER LOG**

**89 Workers | 806.0 Man Hours**

No.	Contact/Company	Cost Code	Workers	# Hours	Man Hours	Location
6	Ed Emmons Steel Erectors, Inc.		9	6.0	54.0	Building>D
<b>Notes:</b> Hung remaining steel at elevation 115. Hand welded studs at elevation 115 and 100.						
7	Larry M. Jacobs & Associates, Inc.		2	3.0	6.0	Site
<b>Notes:</b> Conducted Density Test in Area D And Fire Main installation NE corner of site. Conducted Flat surface Test in Corridor (1st Pour)						
8	Nash Plumbing and Mechanical, LLC		6	8.0	48.0	Building
<b>Notes:</b> Mechanical- locating penetrations for piping Plumbing- sleeves, floor drains, roof drains 115' elevation						
9	Tindall Corporation		22	10.0	220.0	Building>C
<b>Notes:</b> **Erecting east edge of are C. **Welding and grouting **Patching various						
			<b>89</b>		<b>806.0</b>	

**Manpower Log's Attachments:**

2. A&B Electric Co., Inc.

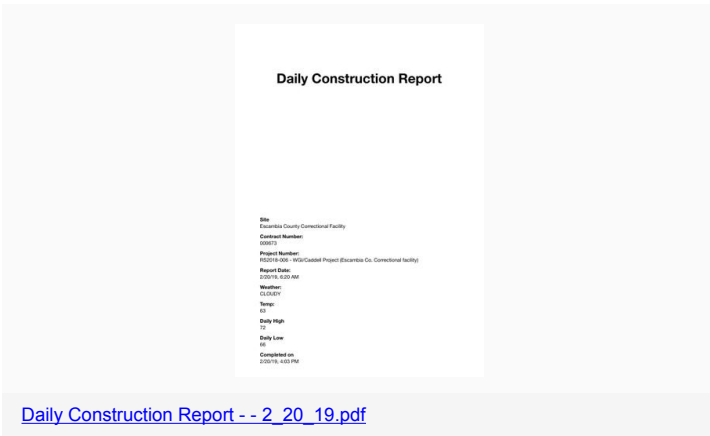

[Daily Construction Report -- 2\\_20\\_19.pdf](#)

3. Bayside Structures, LLC



[Bayside Daily 2-20-2019.PDF](#)

5. Chavers Construction Inc.

[Chaver Daily 2-20-2019.PDF](#)

6. Ed Emmons Steel Erectors, Inc.

[New Doc 2019-02-20 18.21.46.pdf](#)

8. Nash Plumbing and Mechanical, LLC

[Nash Daily 2-20-2019.xlsx](#)

9. Tindall Corporation

[Tindall Escambia Daily 2-20-2019.xlsx](#)

**EQUIPMENT LOG**

No.	Equipment Name	Cost Code	Hrs Operating	Hrs Idle	Inspected?	Inspection Time	Location
1	John Deere 750 Dozer				No	07:00 AM	Building>A
	<b>Notes:</b>						
2	Kobelco Crane CKE2500				No	07:00 AM	Building>C
	<b>Notes:</b>						
3	Genie Lift S85				No	07:00 AM	Building>C
	<b>Notes:</b>						
4	JLG Lift 660SJ				No	07:00 AM	Building>C
	<b>Notes:</b>						
5	JLG Lift 660SJ				No	07:00 AM	Building>C
	<b>Notes:</b>						
6	Grove Crane AT700D				No	07:00 AM	Building>D
	<b>Notes:</b>						

## EQUIPMENT LOG

No.	Equipment Name	Cost Code	Hrs Operating	Hrs Idle	Inspected?	Inspection Time	Location
7	John Deere 550H Dozer				No	07:00 AM	Building>D
	<b>Notes:</b>						
8	Vibratory Roller				No	07:00 AM	Building>D
	<b>Notes:</b>						
9	Cat Skidsteer				No	07:00 AM	Building>D
	<b>Notes:</b>						
10	Komatsu 320 PT Loader				No	07:00 AM	Building>D
	<b>Notes:</b>						
11	Komatsu 78MR Excavator				No	07:00 AM	Building>D
	<b>Notes:</b>						
12	JLG Skytrak Telehandler				No	07:00 AM	Site
	<b>Notes:</b>						
13	JLG Skytrak Telehandler				No	07:00 AM	Site
	<b>Notes:</b>						
14	Cat Telehandler				No	07:00 AM	Site
	<b>Notes:</b>						
15	John Deere 85G Excavator				No	07:00 AM	Site
	<b>Notes:</b>						
16	Cat Skidsteer				No	07:00 AM	Site
	<b>Notes:</b>						
17	Bobcat Miniexcavator				No	07:00 AM	Building>D
	<b>Notes:</b>						
18	Volvo 330 Excavator				No	07:00 AM	Site>Stormwater Pond
	<b>Notes:</b>						

By \_\_\_\_\_

Date \_\_\_\_\_

Copies To \_\_\_\_\_



## Daily Log: Thursday 2/21/2019

**Daily Log Completed**  
 The Daily Log was completed by Donald Shelton on Mon Feb 25, 2019 at 11:31 am CST.

### WEATHER REPORT

Temperature			Precipitation Since			Humidity				Windspeed		
Low	High	Avg	Midnight	2 Days Ago	3 Days Ago	Low	Avg	High	Dew	Avg	Max	Gust
67°F	75°F	70°F	0.02 in.	0.02 in.	0.09 in.	83%	95%	100%	68°F	6.2 mph	8 mph	16 mph

### DAILY SNAPSHOT

06:00 AM	09:00 AM	12:00 PM	03:00 PM	06:00 PM	09:00 PM
fog 68°F	fog 72°F	cloudy 74°F	cloudy 75°F	cloudy 70°F	partly-cloudy-night 69°F

### OBSERVED WEATHER CONDITIONS

No.	Weather Delay	Sky	Temp	Average	Precipitation	Wind	Ground/Sea
1	No	Cloudy	Mild	70	0	Calm	Dry



### MANPOWER LOG

85 Workers | 765.0 Man Hours

No.	Contact/Company	Cost Code	Workers	# Hours	Man Hours	Location
1	A&B Electric Co., Inc.		14	10.0	140.0	Site
<b>Notes:</b> Fab boxes and nipples for block rough in, Fab 4" 90's for underground Rough in, Working on temporary lights.						
2	Bayside Structures, LLC		8	8.0	64.0	Building>D
<b>Notes:</b> Unloaded rebar truck, worked on stripping connector stem wall and GB, and worked on wwm at elevation 115 from line 17 to 28.						
3	Caddell Construction Co. (DE), LLC		9	10.0	90.0	Site
<b>Notes:</b> WGI/Caddell supervision, quality control and safety onsite.						
4	Chavers Construction Inc.		3	8.0	24.0	Site
<b>Notes:</b> Laid 8" fire main at NE corner of site.						
5	Ed Emmons Steel Erectors, Inc.		8	8.0	64.0	Building>D
<b>Notes:</b> Stick welded rest of elevation 100 studs. Lay out						
6	Larry M. Jacobs & Associates, Inc.		1	3.0	3.0	Site
<b>Notes:</b> Conducted Density Tests Area D and North East of site for Firewater Main.						

**MANPOWER LOG**

**85 Workers | 765.0 Man Hours**

No.	Contact/Company	Cost Code	Workers	# Hours	Man Hours	Location
7	Nash Plumbing and Mechanical, LLC		9	8.0	72.0	Building 
<p><b>Notes:</b> Mechanical- laid out penetrations for piping in precast walls. Plumbing- laid out penetrations for piping in precast walls.</p>						
8	Tindall Corporation		22	10.0	220.0	Building>C 
<p><b>Notes:</b> **Erecting east edge of area C. **Welding and grouting **Patching various</p>						
9	EAA Site Contractors LLC		11	8.0	88.0	Site
<p><b>Notes:</b> Total man hours 105. EAA continued to dig retention pond today. We continued to place dirt in section D and outside of section A and B for future parking lot. Section D is 100% complete. Both to grade and compaction.</p>						
			<b>85</b>		<b>765.0</b>	


**Manpower Log's Attachments:**

1. A&B Electric Co., Inc.




[Daily Construction Report -- 2\\_21\\_19.pdf](#)

2. Bayside Structures, LLC

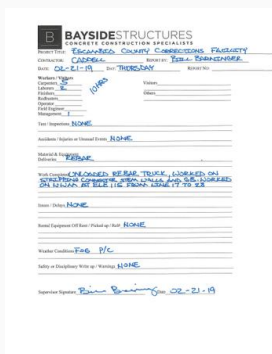

[Bayside Daily 2-21-2019.PDF](#)

5. Ed Emmons Steel Erectors, Inc.

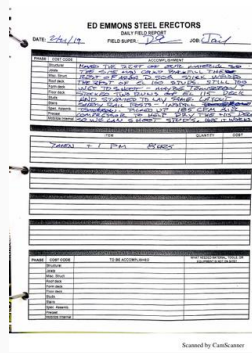

[New Doc 2019-02-21 15.00.58.pdf](#)

7. Nash Plumbing and Mechanical, LLC

[Nash Daily 2-21-2019.xlsx](#)

8. Tindall Corporation

[Tindall Escambia Daily 2-21-2019.xlsx](#)

**EQUIPMENT LOG**

No.	Equipment Name	Cost Code	Hrs Operating	Hrs Idle	Inspected?	Inspection Time	Location
1	Kobelco Crane CKE2500				No	07:00 AM	Building>C
	<b>Notes:</b>						
2	Genie Lift S85				No	07:00 AM	Building>C
	<b>Notes:</b>						
3	JLG Lift 660SJ				No	07:00 AM	Building>C
	<b>Notes:</b>						
4	Sky Power Lift 600AJ				No	07:00 AM	Building>C
	<b>Notes:</b>						
5	Grove Crane AT700D				No	07:00 AM	Building>D
	<b>Notes:</b>						
6	Scissor Lift				No	07:00 AM	Building>D
	<b>Notes:</b>						
7	JLG Skytrak Telehandler				No	07:00 AM	Site
	<b>Notes:</b>						
8	JLG Skytrak Telehandler				No	07:00 AM	Site
	<b>Notes:</b>						
9	Cat Telehandler				No	07:00 AM	Site
	<b>Notes:</b>						
10	Volvo 330 Excavator				No	07:00 AM	Site>Stormwater Pond
	<b>Notes:</b>						
11	Terex Articulated Dump Truck				No	07:00 AM	Site>Stormwater Pond
	<b>Notes:</b>						

## EQUIPMENT LOG

No.	Equipment Name	Cost Code	Hrs Operating	Hrs Idle	Inspected?	Inspection Time	Location
12	Komatsu 320 PT Loader				No	07:00 AM	Site>Stormwater Pond
<b>Notes:</b>							
13	John Deere 750 Dozer				No	07:00 AM	Site>Stormwater Pond
<b>Notes:</b>							

---

By

---

Date

---

Copies To



## Daily Log: Friday 2/22/2019

**Daily Log Completed**  
 The Daily Log was completed by Donald Shelton on Mon Feb 25, 2019 at 11:30 am CST.

### WEATHER REPORT

Temperature			Precipitation Since			Humidity				Windspeed		
Low	High	Avg	Midnight	2 Days Ago	3 Days Ago	Low	Avg	High	Dew	Avg	Max	Gust
66°F	75°F	69°F	0.02 in.	0.04 in.	0.04 in.	78%	91%	100%	67°F	7.6 mph	10 mph	19 mph

### DAILY SNAPSHOT

06:00 AM	09:00 AM	12:00 PM	03:00 PM	06:00 PM	09:00 PM
<b>fog</b> 66°F	<b>cloudy</b> 70°F	<b>cloudy</b> 75°F	<b>partly-cloudy-day</b> 75°F	<b>partly-cloudy-night</b> 70°F	<b>partly-cloudy-night</b> 68°F

### OBSERVED WEATHER CONDITIONS

No.	Weather Delay	Sky	Temp	Average	Precipitation	Wind	Ground/Sea
1	No	Cloudy	Mild	69	0	Light Wind	Dry

### MANPOWER LOG


**67 Workers | 634.0 Man Hours**

No.	Contact/Company	Cost Code	Workers	# Hours	Man Hours	Location
1	A&B Electric Co., Inc.		10	10.0	100.0	Site
<b>Notes:</b> Working on temporary lights, Fab boxes and nipples for block rough in.						
2	Bayside Structures, LLC		9	10.0	90.0	Site
<b>Notes:</b> Finish wwm and rebar on elevation 115. Installed precast embeds on G.7 elevation 115. Installed bulk head on elevation 115 G.7. Installed all rebar over beams and girders.						
3	Caddell Construction Co. (DE), LLC		9	10.0	90.0	Site
<b>Notes:</b> WGI/Caddell supervision, quality control and safety onsite.						
4	Chavers Construction Inc.		3	8.0	24.0	Site
<b>Notes:</b> Laid 8" fire main at NE corner of site.						
5	Ed Emmons Steel Erectors, Inc.		9	8.0	72.0	Building>D
<b>Notes:</b> Laid out and shot studs 28-32.9, H.7-J						
6	Nash Plumbing and Mechanical, LLC		6	8.0	48.0	Building
<b>Notes:</b> Hole layout for penetrations in precast corridor walls						





5. Ed Emmons Steel Erectors, Inc.



[New Doc 2019-02-22 15.15.36.pdf](#)

6. Nash Plumbing and Mechanical, LLC

[Nash Daily 2-22-2019.xlsx](#)

7. Tindall Corporation

[Tindall Escambia Daily 2-22-2019.xlsx](#)

**EQUIPMENT LOG**

No.	Equipment Name	Cost Code	Hrs Operating	Hrs Idle	Inspected?	Inspection Time	Location
1	Kobelco Crane CKE2500				No	07:00 AM	Building>C
	<b>Notes:</b>						
2	Genie Lift S85				No	07:00 AM	Building>C
	<b>Notes:</b>						
3	JLG Lift 660SJ				No	07:00 AM	Building>C
	<b>Notes:</b>						
4	Sky Power Lift 600AJ				No	07:00 AM	Building>C
	<b>Notes:</b>						
5	Grove Crane AT700D				No	07:00 AM	Building>D
	<b>Notes:</b>						
6	Genie Lift S80				No	07:00 AM	Building>D
	<b>Notes:</b>						
7	Scissor Lift				No	07:00 AM	Building>D
	<b>Notes:</b>						
8	JLG Skytrak Telehandler				No	07:00 AM	Site
	<b>Notes:</b>						
9	JLG Skytrak Telehandler				No	07:00 AM	Site
	<b>Notes:</b>						
10	Cat Telehandler				No	07:00 AM	Site
	<b>Notes:</b>						

By \_\_\_\_\_

Date \_\_\_\_\_

Copies To \_\_\_\_\_



## Daily Log: Saturday 2/23/2019

**Daily Log Completed**  
 The Daily Log was completed by Donald Shelton on Mon Feb 25, 2019 at 11:30 am CST.

### WEATHER REPORT

Temperature			Precipitation Since			Humidity				Windspeed		
Low	High	Avg	Midnight	2 Days Ago	3 Days Ago	Low	Avg	High	Dew	Avg	Max	Gust
67°F	78°F	71°F	0.00 in.	0.02 in.	0.04 in.	77%	93%	100%	69°F	9.0 mph	11 mph	21 mph

### DAILY SNAPSHOT

06:00 AM	09:00 AM	12:00 PM	03:00 PM	06:00 PM	09:00 PM
<b>fog</b> 69°F	<b>cloudy</b> 71°F	<b>cloudy</b> 79°F	<b>cloudy</b> 77°F	<b>cloudy</b> 72°F	<b>cloudy</b> 71°F

### OBSERVED WEATHER CONDITIONS

No.	Weather Delay	Sky	Temp	Average	Precipitation	Wind	Ground/Sea
1	No	Cloudy	Mild	71	0	Light Wind	Dry

### MANPOWER LOG

47 Workers | 452.0 Man Hours

No.	Contact/Company	Cost Code	Workers	# Hours	Man Hours	Location
1	Bayside Structures, LLC		22	10.0	220.0	Building>D
<b>Notes:</b> Poured elevation 115 from line 17-28, 100 yards. Installed wwm at elevation 100 south-end last pour. Installed 7 embeds on center line 7 elevation 100. Install rebar over beams and girders.						
2	Caddell Construction Co. (DE), LLC		3	10.0	30.0	Site
<b>Notes:</b> WGI/Caddell supervision, quality control and safety onsite.						
3	Nelson Plumbing Contractors, Inc.		2	8.0	16.0	Building>D
<b>Notes:</b> Plumbing- observed 1st pour of elevation 115						
4	Tindall Corporation		18	10.0	180.0	Building>C
<b>Notes:</b> **Erecting east edge of area C. **Welding and grouting **Patching various						
5	Larry M. Jacobs & Associates, Inc.		2	3.0	6.0	Building>D
<b>Notes:</b> Conducted tests for concrete pour.						
			<b>47</b>	<b>452.0</b>		

#### Manpower Log's Attachments:

1. Bayside Structures, LLC



[Bayside Daily 2-23-2019.PDF](#)

3. Nelson Plumbing Contractors, Inc.

[Nash Daily 2-23-2019.xlsx](#)

4. Tindall Corporation

[Tindall Escambia Daily 2-23-2019.xlsx](#)

**EQUIPMENT LOG**

No.	Equipment Name	Cost Code	Hrs Operating	Hrs Idle	Inspected?	Inspection Time	Location
1	Kobelco Crane CKE2500				No	07:00 AM	Building>C
	<b>Notes:</b>						
2	Genie Lift S85				No	07:00 AM	Building>C
	<b>Notes:</b>						
3	JLG Lift 660SJ				No	07:05 AM	Building>C
	<b>Notes:</b>						
4	Sky Power Lift 600AJ				No	07:00 AM	Building>C
	<b>Notes:</b>						
5	Pump Truck				No	07:00 AM	Building>D
	<b>Notes:</b>						
6	JLG Skytrak Telehandler				No	07:00 AM	Site
	<b>Notes:</b>						

By \_\_\_\_\_

Date \_\_\_\_\_

Copies To \_\_\_\_\_



Whitesell Green / Caddell, a Joint Venture  
 2700 Lagoon Park Drive  
 Montgomery, Alabama 36109  
 P: (334) 272-7723  
 F: (334) 394-0193

Project: 1054 - Escambia County Correctional  
**Facility**  
 3080 N. Pace Boulevard  
 Pensacola, Florida 32501

## Daily Log: Sunday 2/24/2019

### WEATHER REPORT

Temperature			Precipitation Since			Humidity				Windspeed		
Low	High	Avg	Midnight	2 Days Ago	3 Days Ago	Low	Avg	High	Dew	Avg	Max	Gust
50°F	72°F	65°F	0.14 in.	0.14 in.	0.16 in.	30%	60%	99%	49°F	9.8 mph	14 mph	23 mph

### DAILY SNAPSHOT

06:00 AM	09:00 AM	12:00 PM	03:00 PM	06:00 PM	09:00 PM
cloudy 63°F	clear-day 65°F	clear-day 71°F	clear-day 72°F	clear-night 63°F	clear-night 52°F

### OBSERVED WEATHER CONDITIONS

No.	Weather Delay	Sky	Temp	Average	Precipitation	Wind	Ground/Sea
1	No						

By \_\_\_\_\_

Date \_\_\_\_\_

Copies To \_\_\_\_\_



## Daily Log: Monday 2/25/2019

**Daily Log Completed**  
 The Daily Log was completed by Donald Shelton on Mon Mar 4, 2019 at 07:56 am CST.

### WEATHER REPORT

Temperature			Precipitation Since			Humidity				Windspeed		
Low	High	Avg	Midnight	2 Days Ago	3 Days Ago	Low	Avg	High	Dew	Avg	Max	Gust
42°F	66°F	54°F	0.01 in.	0.15 in.	0.15 in.	23%	46%	68%	33°F	8.4 mph	11 mph	23 mph

### DAILY SNAPSHOT

06:00 AM	09:00 AM	12:00 PM	03:00 PM	06:00 PM	09:00 PM
clear-night 43°F	clear-day 53°F	partly-cloudy-day 64°F	cloudy 66°F	partly-cloudy-night 61°F	partly-cloudy-night 56°F

### OBSERVED WEATHER CONDITIONS

No.	Weather Delay	Sky	Temp	Average	Precipitation	Wind	Ground/Sea
1	No	Cloudy	Cold	54	0	Light Wind	Dry

### MANPOWER LOG

75 Workers | 708.0 Man Hours

No.	Contact/Company	Cost Code	Workers	# Hours	Man Hours	Location
1	EAA Site Contractors LLC		4	10.0	40.0	Site>Stormwater Pond
<b>Notes:</b> Total man hours 28. EAA continued to dig retention pond today.						
2	A&B Electric Co., Inc.		10	10.0	100.0	Building
<b>Notes:</b> Inspect light fixtures and rework whips on fixtures, Start installing temporary fixtures in "D" area, 2nd Elev. Build up brackets for light fixtures going in area "C" 2nd, 3rd and 4th floors.						
3	Bayside Structures, LLC		11	10.0	110.0	Building
<b>Notes:</b> Poured 27 yards at elevation 100. Stripped and cleaned bulkhead and embeds at elevation 115. Did final preparation for second corridor. Pour in the morning. Sprayed cure compound on slab.						
4	Caddell Construction Co. (DE), LLC		9	10.0	90.0	Site
<b>Notes:</b> WGI/Caddell supervision, quality control and safety onsite.						
5	Chavers Construction Inc.		4	8.0	32.0	Site
<b>Notes:</b> Installed 140 feet of 8 inch water main.						


**MANPOWER LOG**

**75 Workers | 708.0 Man Hours**

No.	Contact/Company	Cost Code	Workers	# Hours	Man Hours	Location
6	Ed Emmons Steel Erectors, Inc.		8	8.0	64.0	Building>D
<b>Notes:</b> Shot studs at elevation 115, stocked deck at elevation 115, and ran perimeter angle at same elevation.						
7	Nash Plumbing and Mechanical, LLC		9	8.0	72.0	Building
<b>Notes:</b> Finished decking 115' elevation, break test south end of corridor						
8	Tindall Corporation		20	10.0	200.0	Building>C
<b>Notes:</b> **Erecting east edge of area C. **Welding and grouting **Patching various 208.5 Total Man Hours						
			<b>75</b>		<b>708.0</b>	

**Manpower Log's Attachments:**

2. A&B Electric Co., Inc.

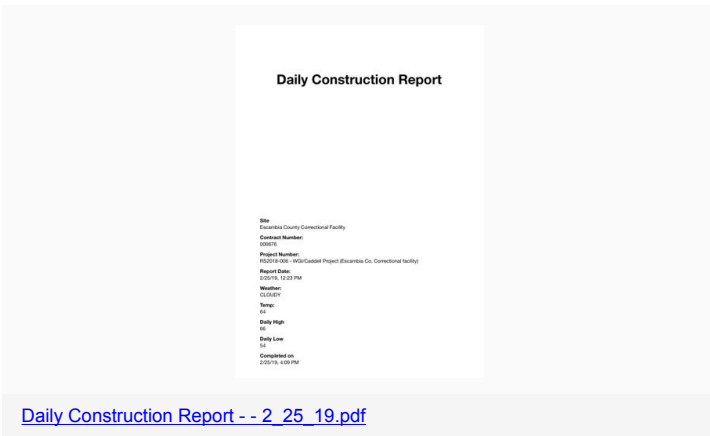


[Daily Construction Report -- 2\\_25\\_19.pdf](#)

3. Bayside Structures, LLC




[Bayside Daily 2-25-2019.PDF](#)

5. Chavers Construction Inc.

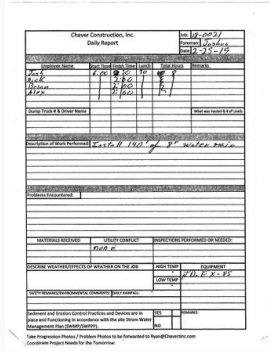

[Chaver Daily 2-25-2019.PDF](#)

6. Ed Emmons Steel Erectors, Inc.

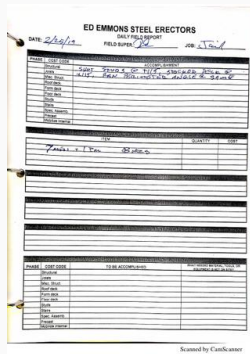

[New Doc 2019-02-25 14.59.01.pdf](#)

7. Nash Plumbing and Mechanical, LLC

[Nash Daily 2-25-2019.xlsx](#)

8. Tindall Corporation

[Tindall Escambia Daily 2-25-2019.xlsx](#)

**EQUIPMENT LOG**

No.	Equipment Name	Cost Code	Hrs Operating	Hrs Idle	Inspected?	Inspection Time	Location
1	Kobelco Crane CKE2500				No	07:00 AM	Building>C
	<b>Notes:</b>						
2	Genie Lift S85				No	07:00 AM	Building>C
	<b>Notes:</b>						
3	JLG Lift 660SJ				No	07:00 AM	Building>C
	<b>Notes:</b>						
4	Sky Power Lift 600AJ				No	07:00 AM	Building>C
	<b>Notes:</b>						
5	Grove Crane AT700D				No	07:00 AM	Building>D
	<b>Notes:</b>						
6	Genie Lift S80				No	07:25 AM	Building>D
	<b>Notes:</b>						



## EQUIPMENT LOG

No.	Equipment Name	Cost Code	Hrs Operating	Hrs Idle	Inspected?	Inspection Time	Location
7	Scissor Lift				No	07:00 AM	Building
	<b>Notes:</b>						
8	JLG Skytrak Telehandler				No	07:00 AM	Site
	<b>Notes:</b>						
9	JLG Skytrak Telehandler				No	07:00 AM	Site
	<b>Notes:</b>						
10	Cat Telehandler				No	07:00 AM	Site
	<b>Notes:</b>						
11	Bobcat Miniexcavator				No	07:00 AM	Site
	<b>Notes:</b>						
12	John Deere 85G Excavator				No	07:00 AM	Site
	<b>Notes:</b>						
13	Volvo 330 Excavator				No	07:00 AM	Site>Stormwater Pond
	<b>Notes:</b>						
14	Terex Articulated Dump Truck				No	07:00 AM	Site>Stormwater Pond
	<b>Notes:</b>						
15	Komatsu 320 PT Loader				No	07:00 AM	Site>Stormwater Pond
	<b>Notes:</b>						
16	John Deere 750 Dozer				No	07:00 AM	Site>Stormwater Pond
	<b>Notes:</b>						

By \_\_\_\_\_

Date \_\_\_\_\_

Copies To \_\_\_\_\_



## Daily Log: Tuesday 2/26/2019

**Daily Log Completed**  
 The Daily Log was completed by Donald Shelton on Mon Mar 4, 2019 at 10:33 am CST.

### WEATHER REPORT

Temperature			Precipitation Since			Humidity				Windspeed		
Low	High	Avg	Midnight	2 Days Ago	3 Days Ago	Low	Avg	High	Dew	Avg	Max	Gust
52°F	68°F	61°F	0.01 in.	0.02 in.	0.16 in.	57%	78%	100%	54°F	6.1 mph	10 mph	14 mph

### DAILY SNAPSHOT

06:00 AM	09:00 AM	12:00 PM	03:00 PM	06:00 PM	09:00 PM
clear-night 56°F	partly-cloudy-day 63°F	partly-cloudy-day 68°F	partly-cloudy-day 68°F	partly-cloudy-night 63°F	partly-cloudy-night 62°F

### OBSERVED WEATHER CONDITIONS

No.	Weather Delay	Sky	Temp	Average	Precipitation	Wind	Ground/Sea
1	No	Cloudy	Mild	61	0	Light Wind	Dry

### MANPOWER LOG

81 Workers | 728.0 Man Hours

No.	Contact/Company	Cost Code	Workers	# Hours	Man Hours	Location
1	EAA Site Contractors LLC		1	5.0	5.0	Site
<b>Notes:</b> Total man hours 5. EAA continued to dig retention pond today. Only worked on site until lunch.						
2	A&B Electric Co., Inc.		7	10.0	70.0	Building
<b>Notes:</b> Working on temporary lighting on 2nd floor section "D", Working on temporary lights check out and replace whips, Working on temporary lights in 2nd floor corridor.						
3	Bayside Structures, LLC		18	9.5	171.0	Site
<b>Notes:</b> Poured 40 yards in corridor Area D. Cured and cut control joints. Worked on supplemental Grade Beam at H.5/37. Started PC excavation at west side of connector. Excavated and poured 140 LN FT of dead men in Area D.						
4	Caddell Construction Co. (DE), LLC		9	10.0	90.0	Site
<b>Notes:</b> WGI/Caddell supervision, quality control and safety onsite.						
5	Chavers Construction Inc.		4	9.0	36.0	Site
<b>Notes:</b> Laid 100 feet of fire main, compacted 140 feet water main in lifts and 100 feet fire main.						


**MANPOWER LOG**

81 Workers | 728.0 Man Hours

No.	Contact/Company	Cost Code	Workers	# Hours	Man Hours	Location
6	Ed Emmons Steel Erectors, Inc.		9	8.0	72.0	Building>D
<b>Notes:</b> Laid out and shot studs at elevation 115 G-G.7, 32.9-35/36. Laid deck h.7-M. Deck and studs will be finish tomorrow. Moved crane to Stair A.						
7	Larry M. Jacobs & Associates, Inc.		2	4.0	8.0	Site
<b>Notes:</b> Conducted tests for concrete pour and density.						
8	Nash Plumbing and Mechanical, LLC		9	8.0	72.0	Building
<b>Notes:</b> pipe penetration layout						
9	Ruben Surveying		2	2.0	4.0	Building
<b>Notes:</b> Conducting floor flatness test						
10	Tindall Corporation		20	10.0	200.0	Building>C
<b>Notes:</b> **Erecting east edge of area C. **Welding and grouting **Patching various						
			<b>81</b>		<b>728.0</b>	


**Manpower Log's Attachments:**

2. A&B Electric Co., Inc.

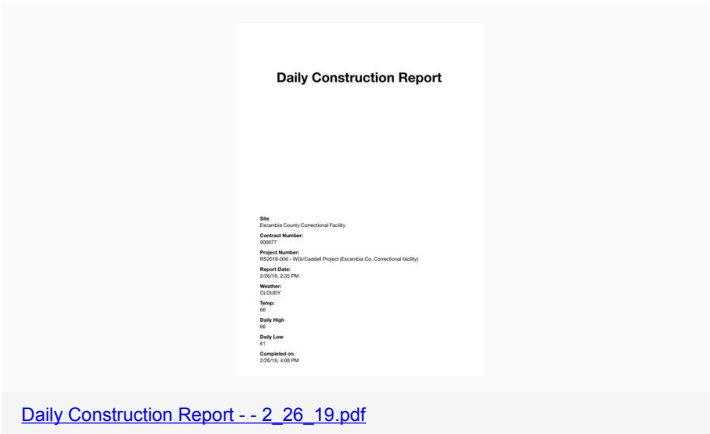

[Daily Construction Report -- 2\\_26\\_19.pdf](#)

3. Bayside Structures, LLC

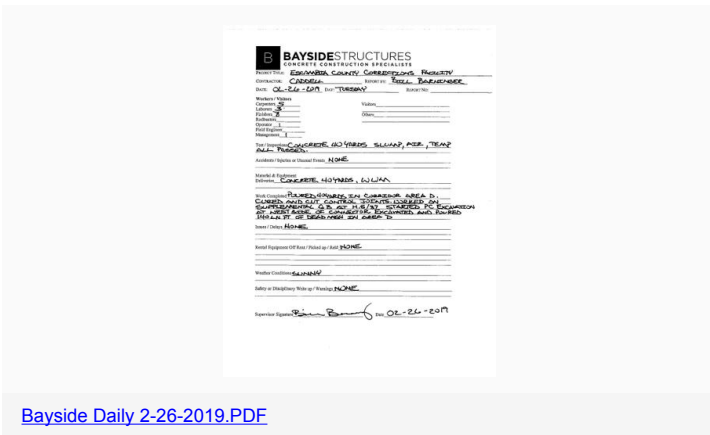

[Bayside Daily 2-26-2019.PDF](#)



## EQUIPMENT LOG

No.	Equipment Name	Cost Code	Hrs Operating	Hrs Idle	Inspected?	Inspection Time	Location
7	JLG Lift 660SJ				No	07:00 AM	Building>C
<b>Notes:</b>							
8	Sky Power Lift 600AJ				No	07:00 AM	Building>C
<b>Notes:</b>							
9	JLG Skytrak Telehandler				No	07:00 AM	Site
<b>Notes:</b>							
10	JLG Skytrak Telehandler				No	07:00 AM	Site
<b>Notes:</b>							
11	Cat Telehandler				No	07:00 AM	Site
<b>Notes:</b>							
12	Pump Truck				No	07:00 AM	Site
<b>Notes:</b>							
13	Volvo 330 Excavator				No	07:00 AM	Site>Stormwater Pond
<b>Notes:</b>							

## INSPECTION LOG

No.	Start Time	End Time	Inspection Type	Inspecting Entity	Inspector Name	Location	Area
1	09:00 AM	11:00 AM	Third Party	Mott MacDonald	Mike Tugwell	Building	
<b>Comments:</b> Threshold inspection							

By \_\_\_\_\_

Date \_\_\_\_\_

Copies To \_\_\_\_\_

## Daily Log: Wednesday 2/27/2019

**Daily Log Completed**

The Daily Log was completed by Donald Shelton on Mon Mar 4, 2019 at 11:00 am CST.

### WEATHER REPORT

Temperature			Precipitation Since			Humidity				Windspeed		
Low	High	Avg	Midnight	2 Days Ago	3 Days Ago	Low	Avg	High	Dew	Avg	Max	Gust
60°F	75°F	65°F	0.38 in.	0.39 in.	0.40 in.	66%	89%	100%	62°F	4.8 mph	9 mph	15 mph

### DAILY SNAPSHOT


06:00 AM	09:00 AM	12:00 PM	03:00 PM	06:00 PM	09:00 PM
rain 62°F	cloudy 65°F	partly-cloudy-day 74°F	clear-day 75°F	partly-cloudy-night 67°F	partly-cloudy-night 62°F

### OBSERVED WEATHER CONDITIONS

No.	Weather Delay	Sky	Temp	Average	Precipitation	Wind	Ground/Sea
1	No	Cloudy	Mild	65	1 inch	Light Wind	Wet/Muddy

#### Observed Weather Conditions' Attachments:

1 \_\_\_\_\_

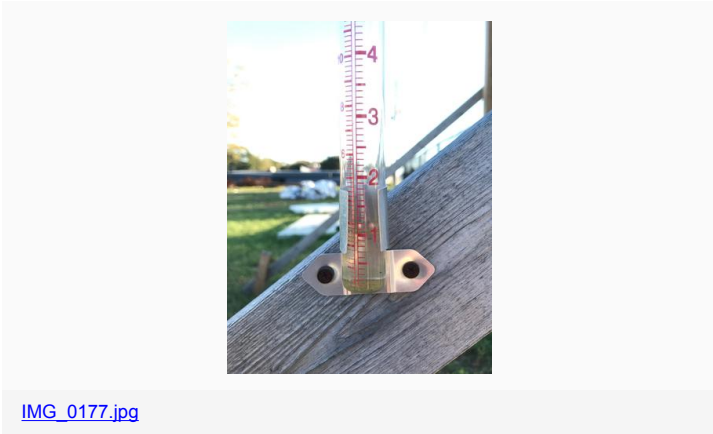

### MANPOWER LOG






**51 Workers | 438.0 Man Hours**

No.	Contact/Company	Cost Code	Workers	# Hours	Man Hours	Location
1	A&B Electric Co., Inc.		10	10.0	100.0	Building

**Notes:** Working on temporary lights, replace cords on lights, Build brackets for temporary lights. Installing temporary lights on 2nd floor corridor and section "D" on 2nd floor. Start installing temporary power packs (Turtles) on 1st and 2nd Floor, Pulling new cable for temporary

**MANPOWER LOG**

51 Workers | 438.0 Man Hours

No.	Contact/Company	Cost Code	Workers	# Hours	Man Hours	Location
	power packs, Will have outages on temporary lights to install new circuits in 400 amp power panel.					
2	Bayside Structures, LLC		12	8.0	96.0	Building 
	<b>Notes:</b> Demucked supplemental GB H.7/37. Finished drilling dowel holes H.7/37 GB. Installed #7 rebar dowels H.7/37. Started placing W.W.M. at elevation 115. Installed column block outs in Area D elevation 83.					
3	Caddell Construction Co. (DE), LLC		9	10.0	90.0	Site
	<b>Notes:</b> WGI/Caddell supervision, quality control and safety onsite.					
4	Ed Emmons Steel Erectors, Inc.		8	7.0	56.0	Building>D 
	<b>Notes:</b> Lost two hours due to rain. Started at 8:30 am. Dried of deck at elevation 115. Shot studs on all possible decks. Installed flashing at areas that received studs.					
5	Chavers Construction Inc.		4	10.0	40.0	Site 
	<b>Notes:</b> Installed 60' Fire main and compacted lifts. Dug up right-away for 8" water taps. Installed saddle and tapping values.					
6	Nash Plumbing and Mechanical, LLC		6	8.0	48.0	Building 
	<b>Notes:</b> Checked material inventory until rain stopped. Continued hole layout in corridor.					
7	Tindall Corporation		2	4.0	8.0	Building 
	<b>Notes:</b> **Patching various					
			<b>51</b>	<b>438.0</b>		

**Manpower Log's Attachments:**

- 1. A&B Electric Co., Inc.



[Daily Construction Report -- 2\\_27\\_19.pdf](#)

2. Bayside Structures, LLC

**BAYSIDESTRUCTURES**  
 ESCAMBIA COUNTY COMMERCIAL, FLORIDA  
 PROJECT: 02-27-2019 LOCATION: WILKINSON  
 DATE: 02-27-2019 TIME: 08:00  
 OPERATOR: [Signature]  
 SUPERVISOR: [Signature]  
 EQUIPMENT: [List]  
 MATERIALS: [List]  
 COMMENTS: REMOVED CONCRETE ON SITE - EXPOSED  
REINFORCING BARS WERE FOUND IN AREA TO BE EXCAVATED  
REINFORCING BARS WERE FOUND IN AREA TO BE EXCAVATED  
REINFORCING BARS WERE FOUND IN AREA TO BE EXCAVATED  
 REPORTER: [Signature] DATE: 02-27-2019

[Bayside Daily 2-27-2019.PDF](#)

4. Ed Emmons Steel Erectors, Inc.

**ED EMMONS STEEL ERECTORS**  
 PROJECT: [Signature] DATE: 2/27/19  
 LOCATION: [Signature]  
 TIME: [Signature]  
 OPERATOR: [Signature]  
 SUPERVISOR: [Signature]  
 EQUIPMENT: [List]  
 MATERIALS: [List]  
 COMMENTS: [Handwritten notes]  
 REPORTER: [Signature] DATE: 2-27-2019

[New Doc 2019-02-27 16.38.39.pdf](#)

5. Chavers Construction Inc.

**Chavers Construction, Inc.**  
 Daily Report  
 PROJECT: [Signature] DATE: 2-27-19  
 LOCATION: [Signature]  
 TIME: [Signature]  
 OPERATOR: [Signature]  
 SUPERVISOR: [Signature]  
 EQUIPMENT: [List]  
 MATERIALS: [List]  
 COMMENTS: [Handwritten notes]  
 REPORTER: [Signature] DATE: 2-27-2019

[Chaver Daily 2-27-2019.PDF](#)

6. Nash Plumbing and Mechanical, LLC

[Nash Daily 2-26-2019.xlsx](#)

7. Tindall Corporation

[Tindall Escambia daily 2-27-19.xlsx](#)



## EQUIPMENT LOG

No.	Equipment Name	Cost Code	Hrs Operating	Hrs Idle	Inspected?	Inspection Time	Location
1	Scissor Lift				No	07:00 AM	Building
	<b>Notes:</b>						
2	John Deere 85G Excavator				No	07:00 AM	Site
	<b>Notes:</b>						
3	JLG Skytrak Telehandler				No	07:00 AM	Site
	<b>Notes:</b>						
4	JLG Skytrak Telehandler				No	07:00 AM	Site
	<b>Notes:</b>						
5	Sky Power Lift 600AJ				No	07:00 AM	Site
	<b>Notes:</b>						

## PHOTOS



[DJI\\_0355.jpg](#)



[DJI\\_0363.jpg](#)



[DJI\\_0354.jpg](#)



[DJI\\_0361.jpg](#)



[DJI\\_0364.jpg](#)



[DJI\\_0366.jpg](#)



[DJI\\_0360.jpg](#)



[DJI\\_0367.jpg](#)

Excavation of Stormwater Pond



[DJI\\_0365.jpg](#)

Grade Beams at Connector Corridor.



[DJI\\_0356.jpg](#)



[DJI\\_0358.jpg](#)

Area's C and D



[DJI\\_0359.jpg](#)



[DJI\\_0368.jpg](#)



[DJI\\_0362.jpg](#)



[DJI\\_0369.jpg](#)



[DJI\\_0371.jpg](#)



[DJI\\_0370.jpg](#)



[DJI\\_0349.jpg](#)



[DJI\\_0350.jpg](#)



[DJI\\_0353.jpg](#)

Job East view of building



[DJI\\_0352.jpg](#)



[DJI\\_0351.jpg](#)

By

Date

Copies To



## Daily Log: Thursday 2/28/2019

**Daily Log Completed**  
 The Daily Log was completed by Donald Shelton on Mon Mar 4, 2019 at 10:30 am CST.

### WEATHER REPORT

Temperature			Precipitation Since			Humidity				Windspeed		
Low	High	Avg	Midnight	2 Days Ago	3 Days Ago	Low	Avg	High	Dew	Avg	Max	Gust
56°F	73°F	65°F	0.34 in.	0.72 in.	0.73 in.	82%	94%	100%	63°F	3.9 mph	9 mph	18 mph

### DAILY SNAPSHOT

06:00 AM	09:00 AM	12:00 PM	03:00 PM	06:00 PM	09:00 PM
cloudy 64°F	cloudy 68°F	cloudy 70°F	cloudy 72°F	cloudy 67°F	rain 67°F

### OBSERVED WEATHER CONDITIONS

No.	Weather Delay	Sky	Temp	Average	Precipitation	Wind	Ground/Sea
1	No	Overcast	Mild	65	0	Light Wind	Wet/Muddy

### MANPOWER LOG

55 Workers | 502.0 Man Hours

No.	Contact/Company	Cost Code	Workers	# Hours	Man Hours	Location
1	EAA Site Contractors LLC		3	8.0	24.0	Site
<b>Notes:</b> Total man hours 25. EAA continued to dig retention pond today. We also took out the topsoil ramp going into section D. We are replacing the topsoil ramp with structural fill.						
2	A&B Electric Co., Inc.		10	10.0	100.0	Building
<b>Notes:</b> Working on temporary power panels and temporary lights, 2nd floor section "D" & 2nd floor corridor, also installing power pack on first floor corridor.						
3	Bayside Structures, LLC		10	9.0	90.0	Building
<b>Notes:</b> Continued installing W.W.M. at elevation 115 Area D. Finished installing #7 dowels at H.7/37 worked on tying rebar in GB (supplemental) H.7/37. Finished cleaning deck at elevation 115 for second pour. Started installing rebar at floor openings on deck elevation 115. Set slab bolster for W.W.M. at elevation 115 Area D						
4	Caddell Construction Co. (DE), LLC		9	10.0	90.0	Site
<b>Notes:</b> WGI/Caddell supervision, quality control and safety onsite.						
5	Chavers Construction Inc.		4	10.0	40.0	Site
<b>Notes:</b> Made (2) 8x8 Hot water tap's for Domestic water and fire main. 40.5 Total Man Hours						


**MANPOWER LOG**

**55 Workers | 502.0 Man Hours**

No.	Contact/Company	Cost Code	Workers	# Hours	Man Hours	Location
6	Ed Emmons Steel Erectors, Inc.		6	8.0	48.0	Building>C
<b>Notes:</b> Cleaned deck at elevation 115 Area D. Framed one landing and set one stringer in Stairwell A.						
7	Nash Plumbing and Mechanical, LLC		10	8.0	80.0	Building>D
<b>Notes:</b> Mechanical- finished marking pipe penetrations, performed anchor load test. Plumbing- set sleeves at elevation 115.						
8	Tindall Corporation		3	10.0	30.0	Building
<b>Notes:</b> **Patching various						
			<b>55</b>		<b>502.0</b>	


**Manpower Log's Attachments:**

2. A&B Electric Co., Inc.

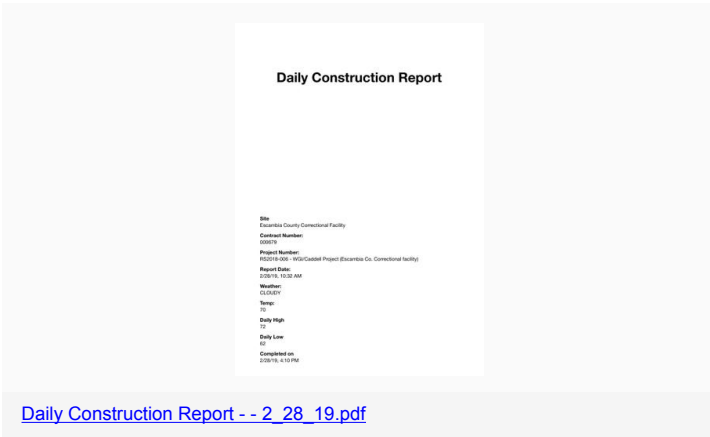


[Daily Construction Report -- 2\\_28\\_19.pdf](#)

3. Bayside Structures, LLC

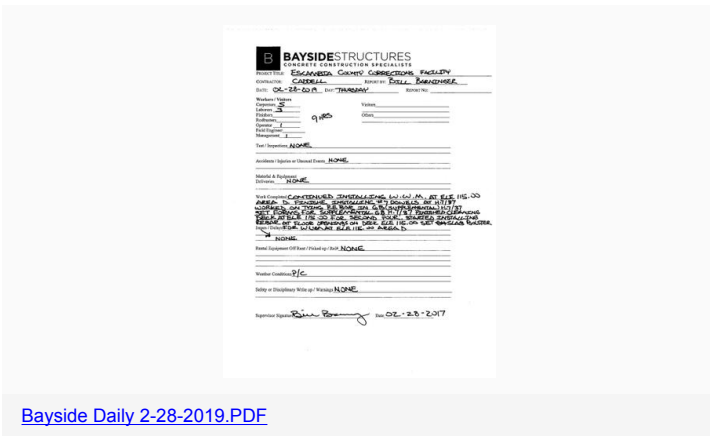


[Bayside Daily 2-28-2019.PDF](#)

5. Chavers Construction Inc.

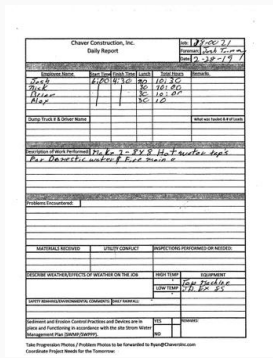

[Chaver Daily 2-28-2019.PDF](#)

6. Ed Emmons Steel Erectors, Inc.



[New Doc 2019-02-28 15.21.05.pdf](#)

7. Nash Plumbing and Mechanical, LLC

[Nash Daily 2-28-2019.xlsx](#)

8. Tindall Corporation

[Tindall Escambia daily 2-28-19.xlsx](#)

**EQUIPMENT LOG**

No.	Equipment Name	Cost Code	Hrs Operating	Hrs Idle	Inspected?	Inspection Time	Location
1	Grove Crane AT700D				No	07:00 AM	Building>C
	<b>Notes:</b>						
2	Bobcat Miniexcavator				No	07:00 AM	Building>D
	<b>Notes:</b>						
3	John Deere 85G Excavator				No	07:00 AM	Site
	<b>Notes:</b>						
4	JLG Skytrak Telehandler				No	07:00 AM	Site
	<b>Notes:</b>						
5	JLG Skytrak Telehandler				No	07:00 AM	Site
	<b>Notes:</b>						
6	Cat Telehandler				No	07:00 AM	Site
	<b>Notes:</b>						

## EQUIPMENT LOG

No.	Equipment Name	Cost Code	Hrs Operating	Hrs Idle	Inspected?	Inspection Time	Location
7	Terex Articulated Dump Truck				No	07:00 AM	Site>Stormwater Pond
<b>Notes:</b>							
8	Volvo 330 Excavator				No	07:00 AM	Site>Stormwater Pond
<b>Notes:</b>							
9	Komatsu 320 PT Loader				No	07:00 AM	Site>Stormwater Pond
<b>Notes:</b>							

---

By

---

Date

---

Copies To

**Committee of the Whole**

6.

**Meeting Date:** 03/14/2019

**Issue:** American Red Cross Shelter Staffing

**From:** AMY LOVOY, Interim County Administrator

---

**Information**

**Recommendation:**

American Red Cross Shelter Staffing  
(John Dosh, Public Safety - 15 min)

- A. Board Discussion
  - B. Board Direction
- 

**Attachments**

Shelter Briefing


---





## 2019 General Population Hurricane Shelter locations:

- Shelter space needed 20 sq. ft. per person.
- Provide feeding to those sheltering.
- 2020 Sheltering space estimates are 11,757.

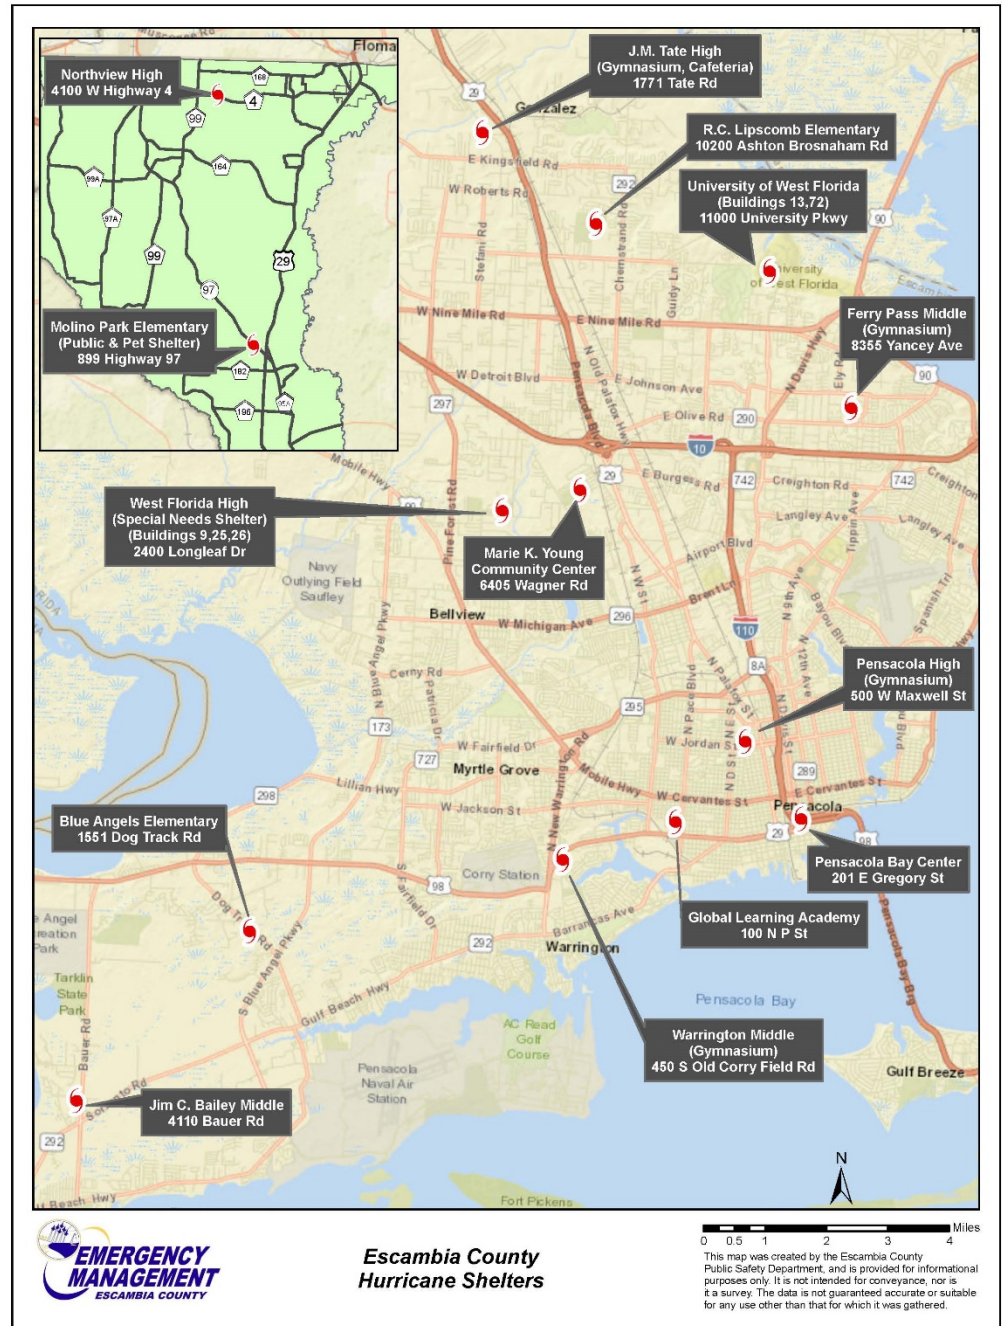



**American  
Red Cross**

## PREVIOUS SUPPORT PROVIDED

- All Volunteer supported
- Shelter Management and Operations
- Feeding of the sheltering population
- Support was provided by hosting facility staff (Principles, Food Service staff, Janitorial Staff, etc.)
- Cleanup after closing of shelter
- Will continue to provide some levels of post event support



**This years sheltering Gaps include :**

**Staffing (1 per 150) to run the 14 Hurricane Shelters & provide feeding to those being sheltered.**

**11 of those shelters are located in Escambia County Schools- Suggested solution is to ask the ECSD to provide shelter staffing and feeding as suggest in Florida Statute 252.38 (d)**

**2 of those shelters are located in County owned Community Centers- Suggested solution is to use county staff to provide shelter staffing and feeding.**

**2 Shelter are located on University of West Florida- Suggested solution is to use county staff to provide shelter staffing and feeding.**

**Red Cross commented that they could possible help with the transportation of meals for some of the shelters without kitchen facilities.**

**Committee of the Whole**

7.

**Meeting Date:** 03/14/2019

**Issue:** County Administrator Search

**From:** AMY LOVOY, Interim County Administrator

---

**Information**

**Recommendation:**

County Administrator Search

(Amy Lovoy - 15 min)

A. Board Discussion

B. Board Direction

---

**Attachments**

*No file(s) attached.*

---
