



AGENDA

COMMITTEE OF THE WHOLE WORKSHOP BOARD OF COUNTY COMMISSIONERS

Board Chambers
Suite 100
Ernie Lee Magaha Government Building - First Floor
221 Palafox Place

April 11, 2019
9:00 a.m.

Escambia County is committed to making our website accessible. If you use assistive technology, for example a screen reader, and have difficulty accessing information in this agenda online, please contact our ADA Coordinator at ADA@myescambia.com or 850-595-1637.

Notice: This meeting is televised live on ECTV and recorded for rebroadcast on the same channel. Refer to your cable provider's channel lineup to find ECTV.

1. Call to Order

(PLEASE TURN YOUR CELL PHONE TO THE SILENCE OR OFF SETTING.)
2. Was the meeting properly advertised?
3. County Administrator's Search
(Amy Lovoy - 60 min)
 - A. Board Discussion
 - B. Board Direction
4. Tourist Development Council
(Shirley Cronley - 30 min)
 - A. Board Discussion
 - B. Board Direction
5. Fees on Rosamond Johnson Beach
(Commissioner Underhill - 10 min)
 - A. Board Discussion
 - B. Board Direction

6. Portable Storage Containers
(Tim Day/Tim Tolbert/Griffin Vickery - 15 min)
 - A. Board Discussion
 - B. Board Direction

7. Alcohol Sales Measurement
(Horace Jones/Andrew Holmer - 15 min)
 - A. Board Discussion
 - B. Board Direction

8. Amending Resolution R2018-133 Establishing the Escambia County Youth Commission
(Commissioner Bergosh - 15 minutes)
 - A. Board Discussion
 - B. Board Direction

9. New Escambia County Correctional Facility Progress Report
(Steve Jernigan, Bay Design/Bob Dye, Facilities Management - 15 min)
 - A. Board Discussion
 - B. Board Direction

10. Fire Service January 19, 2019, ISO Briefing
(Michael Tucker, Superintendent/Bureau Chief, Florida State Fire College/Bureau of Fire Standards & Training; Julius Halas, Division Director, Florida State Fire Marshal's Office; and Kyle Biles, ISO Representative - 60 min)
 - A. Board Discussion
 - B. Board Direction

11. Adjourn

Committee of the Whole

3.

Meeting Date: 04/11/2019

Issue: County Administrator's Search

From: AMY LOVOY, Interim County Administrator

Information

Recommendation:

County Administrator's Search

(Amy Lovoy - 60 min)

A. Board Discussion

B. Board Direction

Attachments

No file(s) attached.

Committee of the Whole

4.

Meeting Date: 04/11/2019

Issue: Tourist Development Council

From: AMY LOVOY, Interim County Administrator

Information

Recommendation:

Tourist Development Council
(Shirley Cronley - 30 min)

- A. Board Discussion
 - B. Board Direction
-

Attachments

No file(s) attached.

Committee of the Whole

5.

Meeting Date: 04/11/2019

Issue: Fees on Rosamond Johnson Beach

From: AMY LOVOY, Interim County Administrator

Information

Recommendation:

Fees on Rosamond Johnson Beach
(Commissioner Underhill - 10 min)

- A. Board Discussion
 - B. Board Direction
-

Attachments


Rosamond Johnson Beach


Rosamond Johnson Beach

At Perdido Key Area

Gulf Islands National Seashore

National Park Service | U.S. Department of the Interior

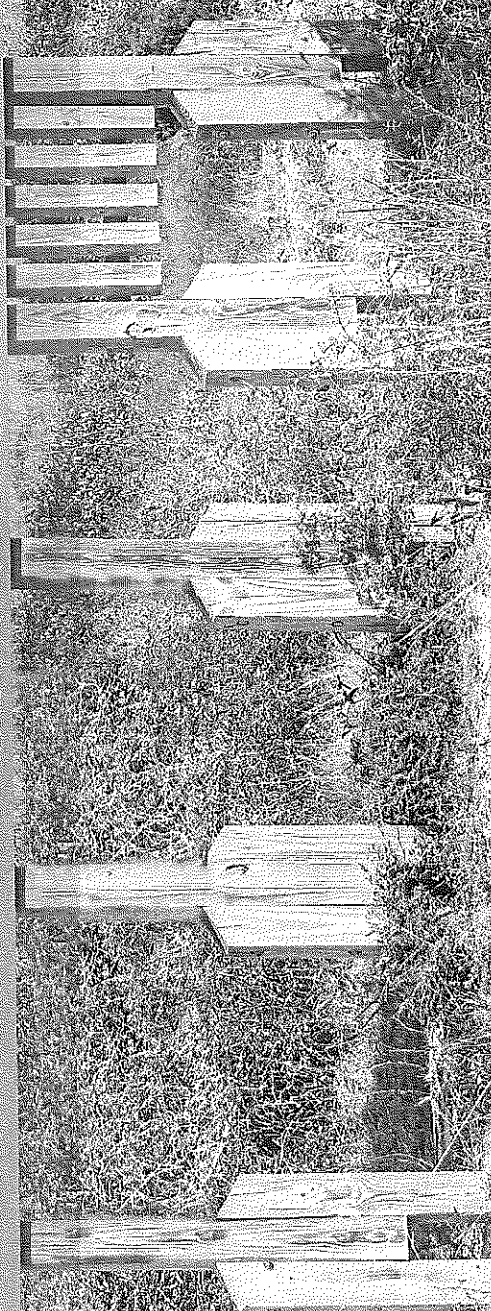

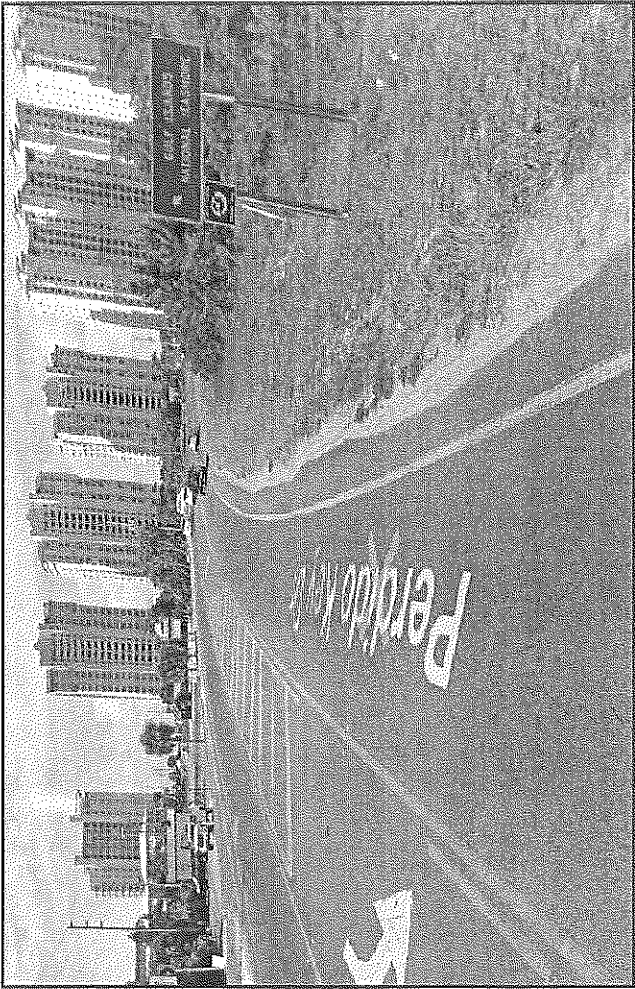

Gulf Islands National Seashore



Perdido Key

Rosamond Johnson Beach



Rosamond Johnson Memorial - May 5, 2018

The Promise of Liberty

On behalf of the National Park Service and the staff of Gulf Islands National Seashore, welcome to Rosamond Johnson Beach within the Perdido Key Area.

I want to take this opportunity to first thank the Johnson family for keeping the memory of Rosamond alive. I'd also like to thank our partners Eugene Franklin, President and CEO of the Florida Black Chamber of Commerce, the Johnson Beach Society, and Alison Davenport and all those at the Perdido Key Chamber of Commerce who have worked so hard to make this event happen.

For the last several years, I have attended and participated in this event providing the official National Park Service welcome, and I'm honored to expand upon that role this year to share a few more words.

Every now and then in life you come upon something that just strikes you as being the right thing to do. I don't remember when I first learned about the name of this beach or the story behind how it came to be named after Rosamond Johnson. It may have been from Joe Herring, whose smile, warmth and enthusiasm is infectious. It may have been when I was exploring the beach and its facilities one day after my arrival here at Gulf Islands in 2010, and stumbled upon the granite memorial marker placed in a somewhat

inconspicuous location behind the restrooms. The story of Rosamond, still a teenager, getting permission from his parents so he could serve his country in the military; his heroic acts during the Korean War to save his fellow soldiers while under fire, and his ultimate sacrifice, giving his life - it was a compelling story, one that people needed to know about. It was not until later that I learned the connection with naming this particular beach after Rosamond – that it was one of the few beaches that Rosamond and his family, friends, and community could come to and enjoy at that time when facilities including beaches were segregated. My two daughters simply cannot imagine a time when their friends – all of their friends – could not go to the same beach with them. That story also needed to be told.

When I attended this memorial ceremony during my first year here as Superintendent, in May 2011, the National Park Service was a spectator. We issued a special use permit for this event to occur in the park, the same mechanism we use to permit weddings and pavilion rentals for family gatherings, but we played no active role. I couldn't help but be struck by the strong impression, the strong desire, that we needed to do more. This was one of those special stories that we needed to help tell. And there were things we could actively do, and needed to do.

I began by asking our staff to work with our partners and the Johnson family to make this ceremony a National Park Service event on par with other events we plan and conduct to share critically important stories of the national seashore. This led to other changes to

recognize Rosamond Johnson's service and sacrifice. We relocated the memorial marker to a more suitable and prominent location – the primary pathway from the parking lot to the beach. We created a new interpretive exhibit panel to help tell this story, placing that exhibit next to the memorial marker. We later expanded the story on that exhibit panel to include the story of Rosamond's military unit, the all-black 24th Infantry Regiment, and the posthumous award of the Purple Heart for Rosamond. Somewhere I learned that there used to be a sign at the entrance to the area designating it as Rosamond Johnson Beach. As I shared last year, when the National Park Service acquired the easternmost seven miles of Perdido Key as part of Gulf Islands National Seashore, like we always do, we gave this area a name that seemed to make sense based on its geographic location – Perdido Key Area. But in doing so the National Park Service failed to fully understand and to recognize that the area already had a name given to it by the local community – Rosamond Johnson Beach. In doing so we may have unwittingly separated a part of the community – the African American community - from the only beach they had been allowed to use for many years. We made an effort to correct that by adding “Rosamond Johnson Beach” to the bottom of our existing sign. It eventually dawned on me – and please forgive me for not seeing or understanding it sooner - but even that effort fell short of what was really the most appropriate and the right thing to do. So last August, and I hope you noticed it when you drove in, we replaced the official entrance sign with a brand new sign that correctly and fully identifies this area as “Rosamond Johnson Beach at Perdido Key”. For the past more than 50 years and now into the future the name of this beach will continue to be “Rosamond Johnson Beach.”

This work continues not just through recognizing Rosamond, but also by recommitting ourselves to this area through dedicated staff. We recently hired and assigned a maintenance employee to this area to keep the facilities in good shape. I hope that you have started to see the fruits of this effort. And we will soon be hiring an additional park ranger duty stationed here – at Rosamond Johnson Beach. I can promise there will be more to come in the future. I share all of these things to point out that the National Park Service is committed to this area, this event, and to the memory of Rosamond Johnson.

When I come to this beach, I am constantly reminded of a question that has always puzzled me. Why would someone sacrifice, give of their time and effort, fight, and even potentially die for their country, demonstrating what must be a deep love for their country, when that country has often failed to love them back?

On a recent trip to the Pacific Northwest, I had the opportunity to visit Bainbridge Island. This is a wonderful island in Puget Sound west of Seattle, a beautiful place to visit and to live. The community on Bainbridge Island is made up of diverse residents, including Japanese-Americans many of whom are second and third generation, and now even fourth and fifth generation Americans. Japanese immigration to Bainbridge Island started in 1883. However, sixty years later as the United States entered World War II following the attack on Pearl Harbor, Japanese-Americans were forcibly removed from this island. In fact, they were the very first Japanese-Americans in the United States to be sent to internment camps in 1942.

During World War II, approximately 120,000 people of Japanese descent were relocated under an executive order to internment camps – for the duration of the war to be held literally as prisoners in their own country. Most were in fact U.S. citizens. They were allowed to bring only the clothes on their backs and one suitcase. They were forced to give up their homes, their property, their businesses and livelihoods, virtually everything that constituted their lives. Following the end of the war, many communities passed laws preventing their return. Thankfully for the citizens of Bainbridge Island, many were welcomed back, but they returned with the conviction to never forget or let a similar incident happen again.

Through their efforts, and the efforts of the generations that followed, a memorial was constructed and is now part of the National Park System – Minedoka National Historic Site. During my visit, I was moved by the personal stories of the people removed from the island. What I found most incredible was that although their entire community was forcibly removed from their homes, 66 men and two women of Japanese descent from Bainbridge Island served in the U.S. Armed Forces during World War II. I guess I knew that Japanese-Americans had served during the war, but I was particularly moved by the following quote one father told his son on the eve of their removal from the island:

“I don’t know what will happen to us. I don’t know where they’re going to take us. I don’t know whether we will ever be able to come back here. But always remember, this is your country and you must act accordingly.”

What an incredibly powerful and honorable thing to say in that moment. As I read that quote, I couldn’t help but think of the story of Rosamond Johnson. Rosamond actually comes from a long line of African Americans who served their country in time of war.

- At least 5,000 African Americans fought for our new nation during the Revolutionary War, and when the British finally surrendered to George Washington at Yorktown in 1781, about ¼ of the American Army was black.
- At the Battle of New Orleans during the War of 1812, Andrew Jackson incorporated two battalions of Free Men of Color into the fray, and the overwhelming American victory began when the British Commanding General was shot – by one of these free black troops.
- Many are familiar with the U.S. Colored Troops during the Civil War, and the 54th Massachusetts regiment made famous by the movie “Glory” with Morgan Freeman and Denzel Washington. But the first engagement by Black U.S. Army regulars during the Civil War against Confederate troops was not far from here at Pascagoula, Mississippi in April 1863.

I was recently tapped to temporarily serve as the Park Superintendent overseeing Tuskegee Institute and Tuskegee Airman national historic sites, and the Selma to Montgomery National Historic Trail until a new superintendent is hired (I might add, while still serving as Superintendent here at Gulf Islands – needless to say it is keeping me very busy going back and forth). Each of these park areas contributes to helping us understand the struggle of African Americans for equality in our country. And next week I will join others from the National Park Service hosting an open house in Biloxi, Mississippi to consider the feasibility of declaring as a new national historic site at the office of Dr. Gilbert Mason, a civil rights leader who organized and led “wade-ins” at white’s only Biloxi beaches during the Civil Rights Movement. Isn’t that fitting for this area? I knew of lunch counter sit-ins, and bus boycotts, but only here along the Gulf Coast would we have “wade-ins.” So stay tuned, maybe that will become a new unit of our National Park System.

Before returning home to Gulf Islands from Tuskegee last week, I spent some time at the Tuskegee Airman site. It is an absolutely fascinating story – if you haven’t been there, you should go. The field of aviation was closed to African Americans before WWII, including military aviation. Yet in July 1941, 13 young African American men arrived at Tuskegee Institute to begin training as Army Air Corps pilots. They faced incredible resistance. The idea that they could meet the high standards of military aviation generated the fiercest resistance of all. Nearly 1,000 eventually earned their pilot wings, however, in the newly established, and segregated, 99th Pursuit Squadron, and 17,000

men and women served in the Army Air Corps as mechanics, armament specialists, and air traffic controllers – all considered Tuskegee Airmen.

Sixty six (66) Tuskegee Airmen were killed in action during the war, yet they proved their skills and their courage, downing 12 German planes in two days, and in bomber escort missions not losing a single bomber in 180 missions. By war's end, the Tuskegee Airmen had flown more than 15,500 sorties and completed 1,578 combat missions destroying more than 260 enemy aircraft, numerous enemy ground installations, and even an enemy destroyer. As they had done so many times before, when finally given the opportunity, African Americans proved they were equal to the task. Their service, bravery, and professionalism earned them the highest military honors including the Distinguished Flying Cross, Legion of Merit, Silver Star, and Purple Heart. They had clearly demonstrated to all Americans that African Americans were wholly capable and deserving members of the U.S. military, and in 1948 President Harry S Truman issued Executive Order 9981 officially desegregating the U.S. Armed Forces. And finally, in 2007, the Tuskegee Airmen received the highest civilian award bestowed by our nation, the Congressional Gold Medal.

I can't help but come back to my perplexing question: Why would people sacrifice, give of their time and effort, fight, and even die for their country, demonstrating what must be a deep love for their country, when that country has often failed to love them back?

I think the answer may lie with the very founding of our country, starting with the Declaration of Independence. Most of you can quote these words: “We hold these truths to be self-evident, that all men are created equal, that they are endowed by their Creator with certain unalienable rights, that among these are... (say them with me)... Life, Liberty, and the pursuit of Happiness.”

Two weeks ago as I walked along the trail on Bainbridge Island commemorating the Japanese American internment, one particular exhibit panel stood out to me. It contained a quote from one of those individuals who was forcibly removed. The thing that struck me was that although he and his family had lost virtually everything they had, he said that the most valuable thing he lost, the thing that mattered the most, was his loss of liberty. Think about it. It is one of our unalienable rights. Our country was founded on it. The statue in New York Harbor is called the Statue of (what?) – Liberty.

When we think of what makes America distinct from other countries we typically think of two things: democracy and liberty. They are not the same thing. Benjamin Franklin, one of our founding fathers, understood the difference. When asked how you distinguish between democracy and liberty, he explained it this way: “Democracy is two wolves and a lamb voting on what to have for lunch. Liberty is a well-armed lamb contesting the vote.” That may be an overly vivid comparison, but it describes how critically important and cherished liberty was and is – something to fight for and defend. And it is something that only those who have been deprived of liberty can value and understand best. The

dictionary defines liberty as: “Freedom from oppression, tyranny, or harsh domination; Freedom from confinement or slavery; Freedom of thought or action; Exemption from forms of compulsion or indignity, regarded as a human right.”

So why would so many of those who’ve been made to suffer indignities or been deprived of liberty in various ways fight and defend a country that falls short of its founding principles? I think it can only be explained by one thing – promise; the promise of liberty; that hope and desire within us to finally overcome our own human failings and fulfill that promise – fully and for everyone. Unfortunately that liberty allowed us individually and collectively to make mistakes, sometimes horrific mistakes, but fortunately it also enabled us to work toward correcting those mistakes.

For us, at Gulf Islands National Seashore, we know that this beach will continue to serve as a place where we can remember Private Rosamond Johnson’s life, understand the injustice of segregation, and learn for the future of our nation. As the Superintendent of this incredible national seashore, I can assure you that the National Park Service will strive to preserve this wonderful beach, support this event, and keep the memory of Rosamond Johnson alive.

Sacrifice Honored

On June 27, 1950 President Harry S. Truman authorized United States military forces to assist with a United Nations operation to oppose the invasion of South Korea by North Korea. Less than a month later, on July 26, Army Private Rosamond Johnson, Jr. became the first Escambia County resident killed during the conflict. On the day he was killed, Johnson, a member of the 24th U.S. Infantry, carried two wounded soldiers to safety. He was fatally wounded by the enemy while attempting to save a third wounded man.

Rosamond Johnson, Jr. Beach
Shortly after the Korean Conflict, the Sunsets Biking Club Inc. suggested renaming this beach in honor of Private Johnson's sacrifice. In 1973, the beach became part of Gulf Islands National Seashore, and the name was retained.

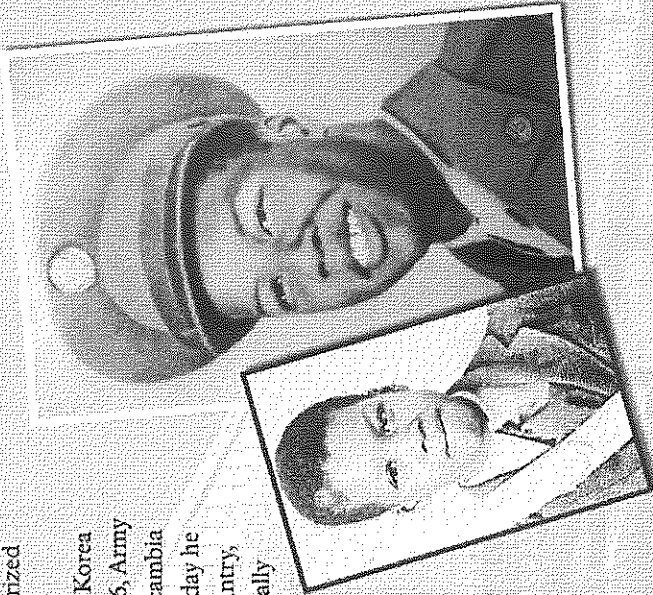


Photo: Rosamond Johnson at age 10. Painting: Portrait of Johnson in his U.S. Army uniform.


Purple Heart

This medal was originally established by General George Washington during the American Revolution as the Badge of Military Merit. The modern version was adopted by the War Department in 1932 and is presented to members of the U.S. military, "being wounded or killed in any action against an enemy of the United States or as a result of an act of any such enemy or opposing armed force." Private Johnson was posthumously awarded the Purple Heart on August 21, 1950.




Jim Crow

The 13th, 14th, and 15th Amendments to the United States Constitution provided all citizens with equal rights by law. However, local and state laws, known collectively as Jim Crow laws, were passed to impede or prevent African Americans from fully realizing their rights. These included segregation, which was applied to all beaches in Escambia County at the time of Private Johnson's death. Jim Crow laws were made illegal through the federal Civil Rights Act of 1964.



Visitors enjoy Johnson Beach in the 1960s.



Korean War

Following the end of World War II, the Korean peninsula was divided along the 38th parallel. A communist government was established in the north, and a democratic government was formed in the south. On June 25, 1950, North Korean forces invaded South Korea. The fighting lasted for over three years and resulted in the Korean Armistice Agreement, which is still in place today. Over 36,000 Americans, including Private Johnson, sacrificed their lives during the conflict.



United States Department of the Interior



National Park Service
Gulf Islands National Seashore
1801 Gulf Breeze Parkway
Gulf Breeze, Florida 32563

F5419 (GUIS)

Memorandum

To: Regional Director, Southeast Region

Through: Acting Fee Program Manager, Southeast Region

From: Superintendent, Gulf Islands National Seashore *Daniel R. Brown*

Subject: Partial Day Fee Suspension for GUIS – Rosamond Johnson Memorial Event

GUIS requests approval for a waiver of entrance fees for May 4, 2019, from 9:00 a.m. to 12:00 p.m. for the Rosemond Johnson Memorial event. Rosamond Johnson Beach at the Perdido Key Area of Gulf Islands National Seashore was named after a 17 year old African American youth who was the first Pensacola resident to die during the Korean Conflict. On the day he was killed, Private Johnson carried two wounded soldiers to safety, and was fatally wounded by the enemy while attempting to save a third wounded man. Private Johnson was posthumously awarded the Purple Heart on August 21, 1950. During segregation, this beach at Perdido Key was the only place that the African American community was allowed to use. Shortly after the Korean Conflict, the community named this beach in honor of Private Johnson's sacrifice. In 1973, the beach became part of Gulf Islands National Seashore, and the name was retained.

The park is conducting a memorial ceremony on May 4, 2019, to commemorate Rosamond Johnson in cooperation with the Perdido Key Chamber of Commerce, the Florida Black Chamber of Commerce, and the Johnson Beach Society. The Johnson family, local officials, and the public are invited to this ceremony. The Escambia County Board of County Commissioners has issued a resolution proclaiming the first Saturday in May as Rosamond Johnson Beach Day in honor and memory of Private Rosamond Johnson, who made the ultimate sacrifice for our freedom.

In support of the Rosamond Johnson Memorial event, the park requests a waiver of entrance fees from 9:00 am to 12:00 pm on May 4, 2019. The park estimates that it will lose approximately \$6,500 in entrance fee money during the temporary suspension. This represents about 1/2 of one percent of GUIS park entrance fees collected annually which will have negligible effect on the accomplishment of the approved projects for 2019 in the park's Comprehensive Fee Plan. In 2018, GUIS exceeded its deferred maintenance target for 80% fee funds by \$346,719.

Thank you for your consideration of this request. If you need additional information please contact me at 850-934-2613.

Approved _____

Date _____

Not Approved _____

Date _____



Committee of the Whole

6.

Meeting Date: 04/11/2019

Issue: Portable Storage Containers

From: AMY LOVOY, Interim County Administrator

Information

Recommendation:

Portable Storage Containers

(Tim Day/Tim Tolbert/Griffin Vickery - 15 min)

A. Board Discussion

B. Board Direction

Attachments

No file(s) attached.

Committee of the Whole

7.

Meeting Date: 04/11/2019

Issue: Alcohol Sales Measurement

From: HORACE JONES, Director

Information

Recommendation:

Alcohol Sales Measurement

(Horace Jones/Andrew Holmer - 15 min)

A. Board Discussion

B. Board Direction

Attachments

Alcohol Sales Measurement



Alcohol Sales Measurement

Sec. 4-7.5 Alcoholic beverage sales.


(b) Measurement. The distance required between the place of business selling alcoholic beverages and a place of worship, child care facility, or K-12 educational facility shall be measured along the shortest route of ordinary pedestrian travel within public rights-of-way, from the main entrance of the place of business to the main entrance of the place of worship or child care facility; or for an educational facility, to the nearest point of the grounds in use as part of the facility.



Alcohol Sales	Within 1000' of a school	Within 1000' of a day care	Within 1000' of a place of worship
Off-premise wine and/or beer	Allowed	Allowed	Allowed
On-premise consumption	Prohibited	Cond. Use	Cond. Use
Off-premise liquor	Prohibited	Cond. Use	Cond. Use




Current Measurement

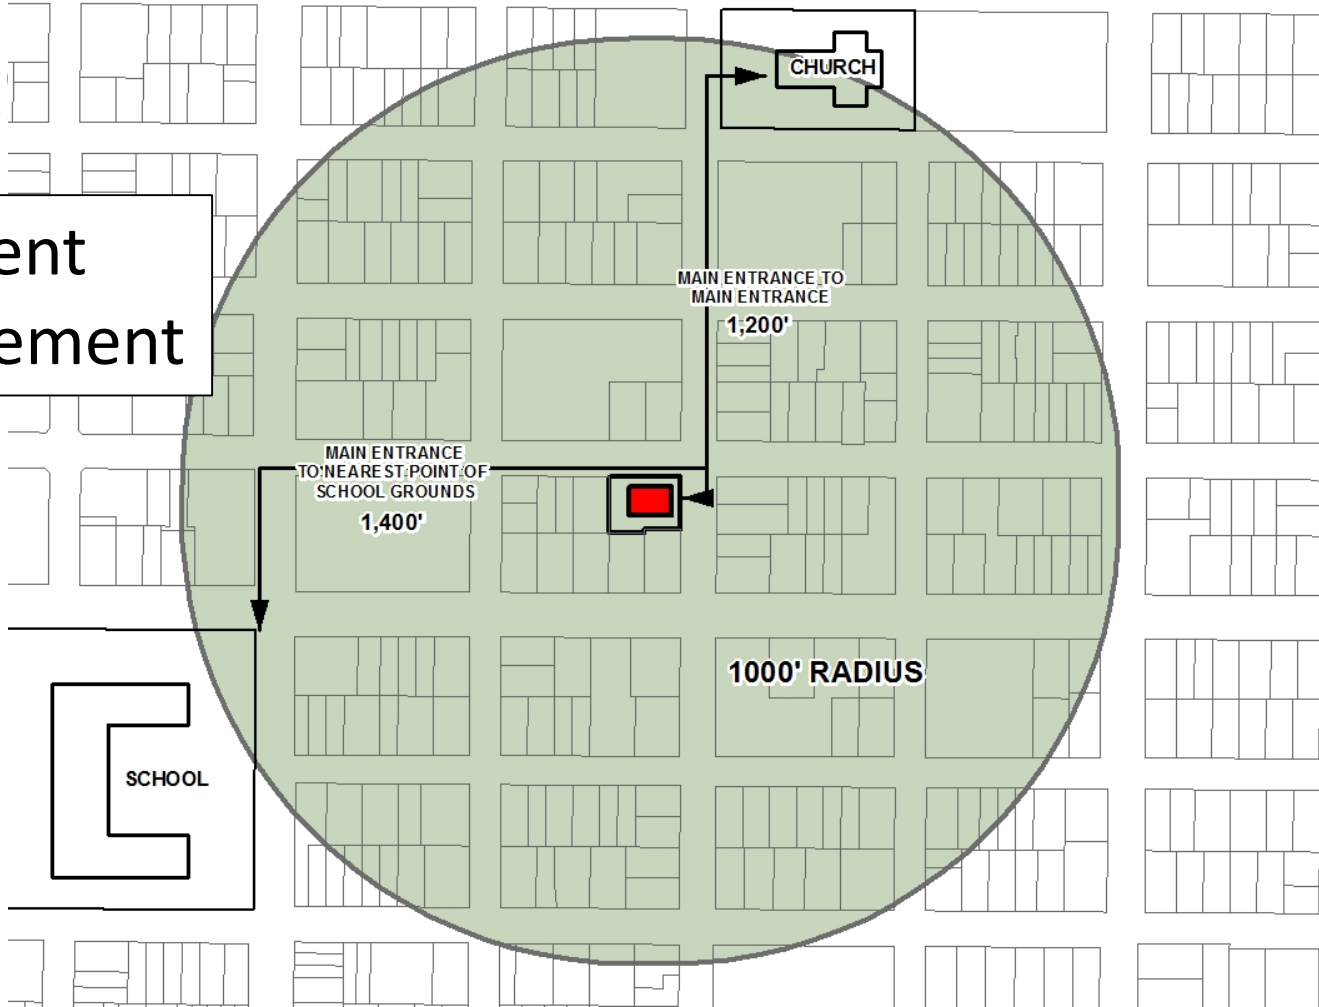



Previous Measurement

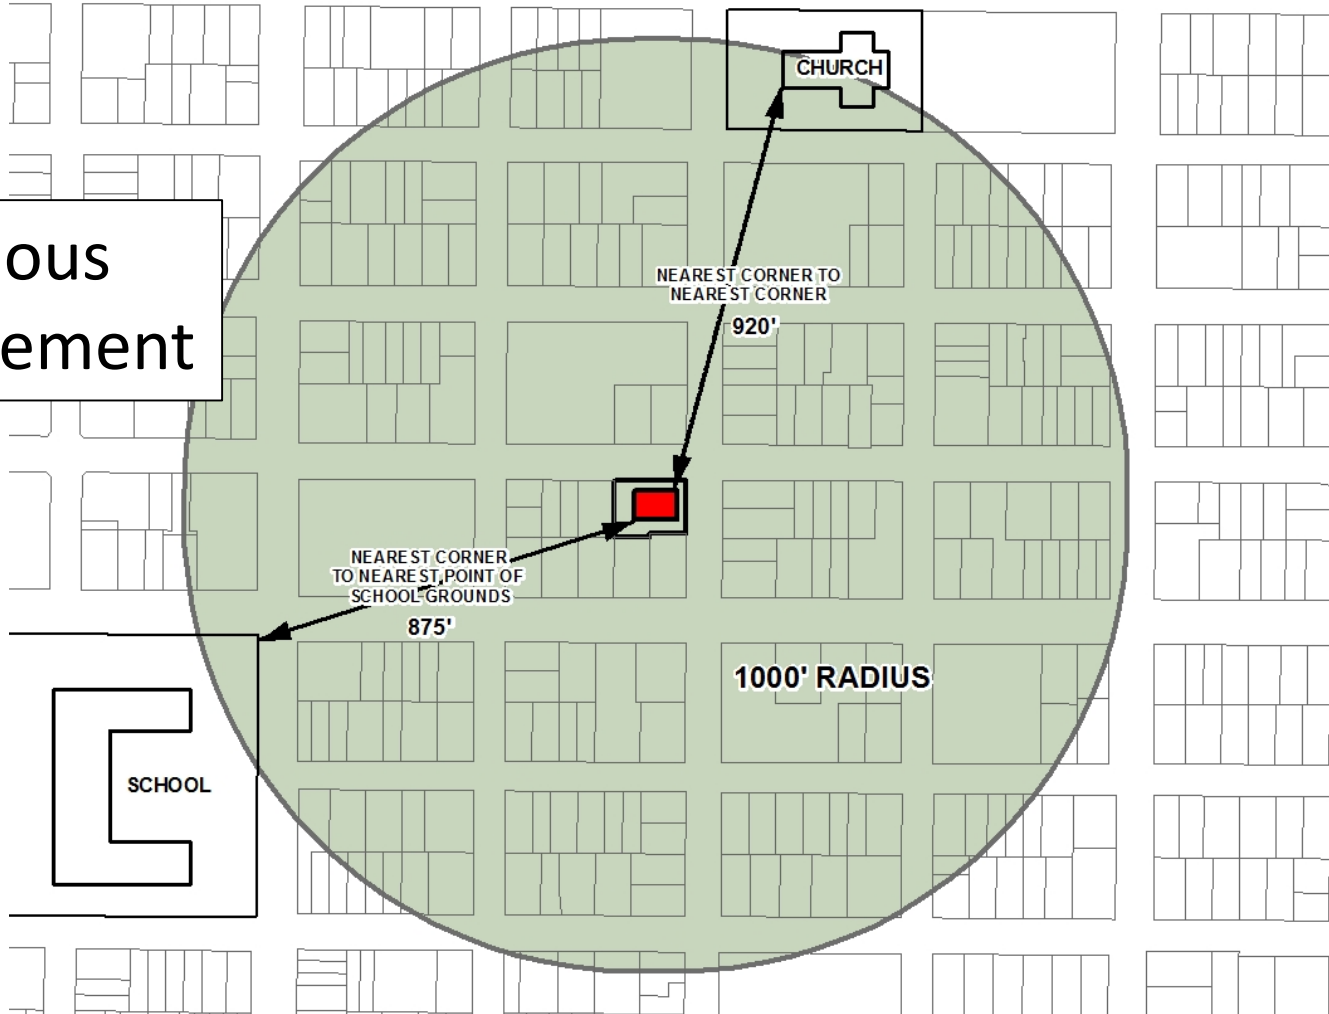



Measurement method prior to Ord. 2011-38

B. *Measurement.* The distance as set out above, shall be measured by radial spacing as follows: In the case of a place of worship, by measuring from the nearest corner of the applicant's business to the nearest corner of the place of worship, excluding projections, eaves, or overhangs. In the case of an educational facility, by measuring from the nearest corner of the applicant's business, excluding projections, eaves, or overhangs, to the nearest point of the school grounds in use as part of the school facilities. Measurements concerning child care and day care facilities shall be taken in the same manner as for educational facilities.



Santa Rosa County

Required distance is 2500'

Distance measurements. The distance as set forth in subpart A above shall be measured by following the shortest route of ordinary pedestrian travel along the public thoroughfare from the main entrance of said place of business to the main entrance of the church or, in the case of a school, to the nearest point of the school grounds in use as part of the school facilities.



City of Pensacola

Required distance is 500' or 300' depending on location

The city engineer shall determine distances by measuring a radius from the property line of the place or establishment. If any portion of a parcel of land in use as church or school facilities lies within said radius, whether or not the property is located within the corporate limits of the city, then the church or school shall be deemed to be within said distance.

You  .com / EscambiaCountyTV

 @ *my* escambia



my escambia.com

Committee of the Whole

8.

Meeting Date: 04/11/2019

Issue: Amended Resolution - Escambia County Youth Commission

From: KIA JOHNSON, Assistant County Attorney

Information

Recommendation:

Amending Resolution R2018-133 Establishing the Escambia County Youth Commission
(Commissioner Bergosh - 15 minutes)

A. Board Discussion

B. Board Direction

Attachments

Resolution

RESOLUTION R2019-_____

A RESOLUTION ESTABLISHING THE ESCAMBIA COUNTY YOUTH COMMISSION; PROVIDING FOR APPOINTMENT OF MEMBERS; AND PROVIDING FOR AN EFFECTIVE DATE.

WHEREAS, Escambia County needs young leaders who are familiar with the local government process and want to serve their commission districts on behalf of their peers; and,

WHEREAS, the Escambia County Board of County Commissioners would like to give Escambia youth a vehicle to participate in the process of County government; and

WHEREAS, this leadership and service-oriented program will give Escambia youth the opportunity to interact with politicians on the local and state level, help local government better understand the issues facing youth, plan community events, participate in volunteer projects, and speak out on behalf of all Escambia County youth; and

WHEREAS, youth involvement in the process of county government will encourage leadership and self-empowerment; develop critical thinking and public speaking skills; teach participants the functions of government and legislative processes; and teach participants advocacy and decision-making skills that will apply to their communities.

NOW, THEREFORE, BE IT RESOLVED BY THE BOARD OF COUNTY COMMISSIONERS OF ESCAMBIA COUNTY, FLORIDA, AS FOLLOWS:

SECTION 1. RECITALS.

That the whereas clauses are true and correct and are incorporated by reference herein.

SECTION 2. ESTABLISHMENT.

The Escambia County Board of County Commissioners hereby establishes the Escambia County Youth Commission.

SECTION 3. COMPOSITION AND QUALIFICATIONS.

The composition of the Escambia County Youth Commission will be as follows:

- A. The Commission will consist of five members during the Commission's first year of establishment.

- B. In each subsequent year, the total number of Youth Commissioners will range between five and ten members.
- C. If the application pool for each academic year will allow, each Escambia County Commissioner shall have the ability to select two Youth Commissioners who reside in his respective District.
- D. Each applicant for the position of Youth Commissioner:
 - 1. Shall be a resident of Escambia County;
 - 2. Shall attend school in Escambia County (Escambia County Public Schools, Private, Charter or Home School);
 - 3. Must be in the 10th through 11th grade during the 2019-2020 academic year; and
 - 4. Must submit a completed application and any required attachments.
- E. Each Youth Commissioner will receive, at no cost to the student, an embroidered polo-style shirt to wear to official events and ceremonies.

SECTION 4. COMMISSION COORDINATOR.

A staff member appointed by the County Administrator will be the Coordinator for the Youth Commission. All communications and activities will be coordinated through that individual/department.

SECTION 5. REGULAR MEETINGS.

The Youth Commission will meet monthly, except that the Commission will not meet during the months of June, July, and August.

SECTION 6. BYLAWS AND RULES OF PROCEDURE.

The Youth Commission will establish its own Bylaws. The Commission shall conduct its meetings in accordance with the current edition of Robert's Rules of Order, except to the extent that the provision thereof is inconsistent with this Resolution.

SECTION 7. SUNSHINE LAW.

The Youth Commission shall be subject to and each member shall be responsible for compliance with the Florida Sunshine Law and the Florida Public Records Act.

SECTION 8. MINUTES.

Minutes shall be kept at each Youth Commission meeting. The written summary of each meeting shall be submitted for approval of the members at the next regular meeting. Each written summary shall reflect the persons in attendance, items discussed, each action taken at the meeting, and the vote of the members on each item presented at the meeting. Upon acceptance of the previous meeting minutes by the Commission, a copy of these minutes shall immediately be forwarded to the Escambia County staff member assigned to facilitate the meetings of this committee.

SECTION 9. NOTICE OF PUBLIC MEETING.

Notice of regular or special meetings of the Youth Commission and the time and location of each meeting shall be published to the public.

SECTION 10. EFFECTIVE DATE.

That this Resolution shall become effective immediately upon adoption by the Board of County Commissioners.

ADOPTED this ___ day of April, 2019.

BOARD OF COUNTY COMMISSIONERS
ESCAMBIA COUNTY, FLORIDA

By: _____
Lumon J. May, Chairman

ATTEST: Pam Childers
Clerk of the Circuit Court

**Approved as to form and legal
sufficiency.**

By: _____
Deputy Clerk

By: Kia M. Johnson

Date: 4/3/2019

(SEAL)

Committee of the Whole

9.

Meeting Date: 04/11/2019

Issue: Progress Report on New Correctional Facility

From: AMY LOVOY, Interim County Administrator

Information

Recommendation:

New Escambia County Correctional Facility Progress Report
(Steve Jernigan, Bay Design/Bob Dye, Facilities Management - 15 min)

A. Board Discussion

B. Board Direction

Attachments

presentation

DBE progress report



New Escambia County Correctional Facility Progress update

Steve Jernigan – Bay Design

Bob Dye – Facilities Management



Key Points

Construction:

- Rebar and concrete placed for Area D, elevation 115 for sequence 2 & 3.
- Concrete poured at level 2 of the corridor and part of level 3 of the corridor.
- The remaining two pile caps and beam piers were reinforced and poured at the connector.
- Concrete was poured at Stair A.



Key points continued

- Sitework continued excavating for the storm pond at the old JJC Parking lot
- Electrical work - temporary lighting at the second level , and electrical rough-in of level 2 of the corridor. Conduit roughed-in in the topping slab at Area C, Level 3 and Level 4.



- Schedule update:
 - March schedule reflects a positive trend for the time line.
 - Substantial completion now projected to be April 20, 2020.
 - Weather and facility equipment installation dependent.
- RFP conformance review completed 2-3 April
 - Division by Division review to insure RFP compliance



Retainage

- Existing contract language
 - 10% until 50% completion is reached
 - Reduces to 5% for subsequent Pay applications
 - No mention of return of excess retainage
- Local Government Prompt Payment Act, §§218.70 et seq., Florida Statutes
 - Contracts in excess of 200K
 - after 50% completion, the County is required to reduce the retainage to 5% of the gross amount of each payment unless the payment is the subject of a dispute.
 - Upon 50% completion, a contractor may request the release of up to 50% of the retainage currently held by the County



New Escambia County Correctional Facility

PD 16-17.004

**Monthly Project Report
March 2019**

Table of Contents

1.0 Progress Summary	3
2.0 Construction Progress.....	4
3.0 Design Build Entity Schedule	4
4.0 Design Status	5
5.0 Subcontractor Procurement.....	6
6.0 Design-Build Entity's Safety Program	6
7.0 Disputes and Claims.....	6
8.0 Look Ahead Task List.....	6
9.0 Daily Log.....	6

1.0 Progress Summary

ITEM	Description	COMMENTS
Original Contract Sum	\$132,445,243.00	
Change Order 1:	(-\$455,530.50)	ODP Change Order deduct for auger cast pile grout.
Change Order 2:	(\$-360.00)	Mathematical error with Alternate Number 5.
Change Order 3:	(-\$147,455.28)	ODP Change Order deduct for auger cast pile rebar.
Change Order 4:	(-\$28,769.30)	ODP Change Order deduct for additional auger cast pile rebar.
Change Order 5:	(-\$2,092,095.52)	ODP Change Order deduct for CIP Concrete and Rebar, Laundry Equipment, and Bi-Folding Doors.
Change Order 6:	(-\$463,697.91)	ODP Change Order deduct for Site Utility Piping and Structures.
Change Order 7:	(-\$32,731.48)	ODP Change Order deduct for Underground Electrical Raceways.
Change Order 8:	(-\$48,746.02)	ODP Change Order deduct for additional auger cast pile grout.
Change Order 9:	(-\$169,758.74)	ODP Change Order deduct for asphalt paving and corrections to existing POs.
Change Order 10:	(-\$9,005,200.12)	ODP Change Order deduct for structural steel, cell walls, hollow metal doors, door hardware and plumbing materials.
Change Order 11:	(-\$47,141.00)	ODP Change Order deduct for additional plumbing materials.
Change Order 12:	(-\$4,380,132.83)	ODP Change Order deduct for mechanical equipment, commercial HM and hardware, security glazing, and security electronics.
Change Order 13:	(-\$5,000,000.00)	Lump Sum ODP Deduct.
Change Order 14:	(-\$5,000,000.00)	Lump Sum ODP Deduct
Adjusted Contract Sum	\$105,573,624.30	
Pending Change Order Request/Claims	NONE	
Original Date of Substantial Completion	May 28, 2020	
Forecast Date of Substantial Completion	April 12, 2020	Positive 27 Days

2.0 Construction Progress

Bayside Structures installed rebar and placed concrete for Area D, elevation 115 for sequence 2 and sequence 3. They also installed reinforcing and poured concrete at level 2 of the corridor from 3-line to 50-line and part of level 3 of the corridor. Bayside excavated, reinforced and poured the remaining two pile caps and beam piers at the connector. They also poured concrete at Stair A.

EAA Sitework continued excavating for the storm pond at the old JJC Parking lot, and they placed fill onsite outside of the building footprint to get close to grade. They also began demolition of the remaining asphalt in the existing site entrance to allow for storm structures and pipe installation.

A&B Electric installed temporary lighting at the second level, and they did electrical rough-in of level 2 of the corridor. They also roughed-in conduit in the topping slab at Area C, Level 3 and Level 4.

Emmons Steel Erectors completed erecting railings, stringers and landings at Stairwell A, and they erected the remaining structural steel and decking at Area D, elevation 115. They also erected structural steel in Area D, elevation 102 and elevation 137.

Tindall erected the exterior precast panels in the first phase of Area D, and they erected precast at the corridor from elevation 115 to elevation 137, 14-line to 50-line. They then moved to Area A to continue erecting precast columns and double tees.

Chavers Construction installed the meter vault, backflow preventers, and domestic water and fire main piping at Fairfield Avenue, and they performed the hot tap to the existing line at Fairfield Avenue. They also installed storm piping and structures from S-23 to S-24 and to the outlet at the storm pond.

Nash installed pipe hangers and prefabricated pipe at the Corridor, and they installed underground plumbing rough-in in Area A and Area C. They also performed layout of sleeves, block-outs, and drains this week on the fourth level of Area C, and they cored penetrations in walls at level 1 and in the topping slab at level 4 of Area C.

3.0 Design Build Entity Schedule

See attached Progress Schedule.

4.0 Design Status

Summary:

The document submittal set for permitting is scheduled as follows:

- WGI/Caddell issued the Underground Permitting documents to the County Permitting Office for review on October 02, 2018.
- WGI/Caddell issued the Architectural, Structural, Fire Suppression and Life Safety Permitting documents to the County Permitting Office for review on October 10, 2018.
- WGI/Caddell issued the Mechanical, Plumbing, Telecommunications, Electrical, Fire Alarm, Security Electronics and Food Service Permitting documents to the County Permitting Office for review on November 07, 2018.
- WGI/Caddell received approved permitting documents for Underground, Architectural, Structural, FFE and Precast drawings on December 6, 2018.
- WGI/Caddell received approved Fire Suppression, Telecommunications and Plumbing permitting documents on January 10, 2019.
- WGI/Caddell received the Electrical, Security Electronics, Fire Alarm and Food Service Permitting documents on February 01, 2019.
- WGI/Caddell received the HVAC Permitting documents on March 01, 2019.

Contract Deliverables:

- Supplemental Instruction 011-Issued March 11, 2019
- Supplemental Instruction 012-Issued March 22, 2019
- Electronic Copy of the Conformed Issue Documents
 - Drawings Uploaded to Newforma-March 27, 2019
 - Specifications Uploaded to Newforma-March 28, 2019

Areas of Concern:

- NONE

Actions and Approvals Needed:

- NONE

Recommendations:

- NONE

5.0 Subcontractor Procurement

- Dannix Painting
- ABG Caulking Contractors, Inc.
- Wilson Floor Covering
- Santa Rosa Insulation and Fireproofing

6.0 Design-Build Entity's Safety Program

No incidents were recorded for the month of March 2019.

7.0 Disputes and Claims

No disputes or claims were filed in the month of March 2019.

8.0 Look Ahead Task List

See attached 90-day Look Ahead Schedule.

9.0 Daily Log

See attached Daily Logs for the month of March 2019.

Activity ID	Activity Name	Orig Dur	Rem Dur	Pct%	Early Start	Early Finish	Total Float	2019											
								Apr			May			Jun			Jul		
PRECONSTRUCTION																			
MILESTONES																			
009999	OBTAIN LICENSES, FEES, PERMITS	0	0	0%		30-Mar-19	144	◆ OBTAIN LICENSES, FEES, PERMITS											
800018	QUARTERLY TOWN HALL PROGRESS MEETING (COC) 1ST WED OF QTR	0	0	0%		03-Apr-19*	0	◆ QUARTERLY TOWN HALL PROGRESS MEETING (COC) 1ST WED OF QTR											
000629	APPROVE CONSTRUCTION SCHEDULE	0	0	0%		19-Apr-19	237	◆ APPROVE CONSTRUCTION SCHEDULE											
800019	PFRR BOARD MEETING - BCC RECOMMENDATION PUBLIC Q&A	0	0	0%		01-May-19*	0	◆ PFRR BOARD MEETING - BCC RECOMMENDATION PUBLIC Q&A											
800020	PFRR PRESENT RECOMMENDATIONS TO THE BOARD OF COUNTY COMMISSIONERS	0	0	0%		03-Jun-19*	0	◆ PFRR PRESENT RECOMMENDATIONS TO THE BOARD OF COUNTY COMMISSIONERS											
119999	OTHER UTILITIES AVAILABLE	0	0	0%		24-Jun-19	183	◆ OTHER UTILITIES AVAILABLE											
WEATHER																			
890018	ANTICIPATED ADVERSE WEATHER - OCT19	3	3	0%	01-Apr-19	03-Apr-19	260	[Green Bar] ANTICIPATED ADVERSE WEATHER - OCT19											
890019	ANTICIPATED ADVERSE WEATHER - NOV19	4	4	0%	04-Apr-19	09-Apr-19	260	[Green Bar] ANTICIPATED ADVERSE WEATHER - NOV19											
890020	ANTICIPATED ADVERSE WEATHER - DEC19	5	5	0%	10-Apr-19	16-Apr-19	260	[Green Bar] ANTICIPATED ADVERSE WEATHER - DEC19											
890021	ANTICIPATED ADVERSE WEATHER - JAN20	5	5	0%	17-Apr-19	23-Apr-19	260	[Green Bar] ANTICIPATED ADVERSE WEATHER - JAN20											
890022	ANTICIPATED ADVERSE WEATHER - FEB20	5	5	0%	24-Apr-19	30-Apr-19	260	[Green Bar] ANTICIPATED ADVERSE WEATHER - FEB20											
890023	ANTICIPATED ADVERSE WEATHER - MAR20	5	5	0%	01-May-19	07-May-19	260	[Green Bar] ANTICIPATED ADVERSE WEATHER - MAR20											
890024	ANTICIPATED ADVERSE WEATHER - APR20	3	3	0%	08-May-19	10-May-19	260	[Green Bar] ANTICIPATED ADVERSE WEATHER - APR20											
890025	ANTICIPATED ADVERSE WEATHER - MAY20	3	3	0%	13-May-19	15-May-19	260	[Green Bar] ANTICIPATED ADVERSE WEATHER - MAY20											
DESIGN																			
004000	DESIGN BUILD SERVICES - CORNERSTONE DETENTION	1	1	95%	15-Oct-18A	01-Apr-19	43	[Blue Bar] DESIGN BUILD SERVICES - CORNERSTONE DETENTION											
PRECONSTRUCTION SUBMITTALS																			
000600	SUBMIT LOD 300/400 FEDERATED MODEL	20	20	90%	07-Nov-18A	18-Apr-19	259	[Green Bar] SUBMIT LOD 300/400 FEDERATED MODEL											
000625	APPROVE FINAL BASELINE DESIGN/CONSTRUCTION SCHEDULE	21	21	0%	30-Mar-19	19-Apr-19	237	[Green Bar] APPROVE FINAL BASELINE DESIGN/CONSTRUCTION SCHEDULE											
PROCUREMENT																			
010000	PROCUREMENT OF LONG-LEAD ITEMS	450	49	65%	02-Jan-18A	17-May-19	138	[Green Bar] PROCUREMENT OF LONG-LEAD ITEMS											
010031	PRECAST PROCUREMENT (MATERIAL COST)	1	1	95%	26-Sep-18A	30-Mar-19	247	[Green Bar] PRECAST PROCUREMENT (MATERIAL COST)											
010061	STEEL PROCUREMENT (STR & MISC) - MATERIAL COST	210	1	59%	07-Nov-18A	30-Mar-19	123	[Green Bar] STEEL PROCUREMENT (STR & MISC) - MATERIAL COST											
011130	OWNER DIRECT PURCHASE MATERIAL (ODP) DETENTION 1/4	1	1	15%	01-Jan-19A	28-Jun-19	169	[Green Bar] OWNER DIRECT PURCHASE MATERIAL (ODP) DETENTION 1/4											
011140	OWNER DIRECT PURCHASE ORDER ADMINISTRATION DETENTION 1/4	1	1	11%	01-Jan-19A	28-Jun-19	169	[Green Bar] OWNER DIRECT PURCHASE ORDER ADMINISTRATION DETENTION 1/4											
011150	OWNER DIRECT PURCHASE MATERIAL (ODP) - PLUMBING	1	1	3%	01-Jan-19A	29-Apr-19	212	[Green Bar] OWNER DIRECT PURCHASE MATERIAL (ODP) - PLUMBING											
011160	OWNER DIRECT PURCHASE MATERIAL (ODP) - HVAC	1	1	7%	01-Jan-19A	18-Apr-19	182	[Green Bar] OWNER DIRECT PURCHASE MATERIAL (ODP) - HVAC											
011260	OWNER DIRECT PURCHASE MATERIAL (ODP) - ELECTRICAL	1	1	5%	01-Jan-19A	01-Apr-19	292	[Green Bar] OWNER DIRECT PURCHASE MATERIAL (ODP) - ELECTRICAL											
010220	FAB/DELV WALL PANELS	30	30	40%	06-Mar-19A	28-Apr-19	310	[Green Bar] FAB/DELV WALL PANELS											
010250	FAB/DELV SECURITY HOLLOW METAL	30	30	25%	12-Mar-19A	28-Apr-19	310	[Green Bar] FAB/DELV SECURITY HOLLOW METAL											
010340	FAB/DELV COMMERCIAL HOLLOW METAL	30	30	4%	30-Mar-19A	28-Apr-19	310	[Green Bar] FAB/DELV COMMERCIAL HOLLOW METAL											
010440	SUBMIT SECURITY FURNITURE & ACCESSORIES	30	30	0%	30-Mar-19	28-Apr-19	250	[Green Bar] SUBMIT SECURITY FURNITURE & ACCESSORIES											
010470	SUBMIT WIRE MESH	30	30	0%	30-Mar-19	28-Apr-19	250	[Green Bar] SUBMIT WIRE MESH											
010500	SUBMIT SECURITY ELECTRONICS PRODUCT DATA	30	30	0%	30-Mar-19	28-Apr-19	214	[Green Bar] SUBMIT SECURITY ELECTRONICS PRODUCT DATA											
010530	SUBMIT SECURITY ELECTRONICS SHOP DRAWINGS	30	30	0%	30-Mar-19	28-Apr-19	214	[Green Bar] SUBMIT SECURITY ELECTRONICS SHOP DRAWINGS											
010560	SUBMIT SECURITY ELECTRONIC TOUCHSCREEN	30	30	0%	30-Mar-19	28-Apr-19	214	[Green Bar] SUBMIT SECURITY ELECTRONIC TOUCHSCREEN											
010280	FAB/DELV GLASS	30	30	0%	30-Mar-19	28-Apr-19	310	[Green Bar] FAB/DELV GLASS											
010310	FAB/DELV SECURITY HARDWARE	30	30	0%	30-Mar-19	28-Apr-19	310	[Green Bar] FAB/DELV SECURITY HARDWARE											
010370	FAB/DELV COMMERCIAL HARDWARE	30	30	0%	30-Mar-19	28-Apr-19	310	[Green Bar] FAB/DELV COMMERCIAL HARDWARE											
010400	FAB/DELV SECURITY CEILING	30	30	0%	30-Mar-19	28-Apr-19	310	[Green Bar] FAB/DELV SECURITY CEILING											
011170	SUBMIT MAIN SWITCHBOARDS - MSB1/MSB2	30	30	0%	30-Mar-19	28-Apr-19	132	[Green Bar] SUBMIT MAIN SWITCHBOARDS - MSB1/MSB2											

Activity ID	Activity Name	Orig Dur	Rem Dur	Pct%	Early Start	Early Finish	Total Float	2019																
								Apr	May	Jun	Jul	Aug	Sep	Oct	Nov	Dec	Jan	Feb	Mar					
011200	SUBMIT SERVICE ENTRANCEATS-1/ATS-2 3000AMP SWITCHES	30	30	0%	30-Mar-19	28-Apr-19	164																	
011230	SUBMIT GENERATOR #1/#2 ENGINES/PLATFORMS/ENCLOSURES	30	30	0%	30-Mar-19	28-Apr-19	171																	
010140	APPROVE FIRE SPRINKLER SHOP DRAWINGS	30	30	0%	02-Apr-19	01-May-19	61																	
010170	APPROVE FIRE PUMP	30	30	0%	02-Apr-19	01-May-19	112																	
010450	APPROVE SECURITY FURNITURE & ACCESSORIES	30	30	0%	29-Apr-19	28-May-19	250																	
010480	APPROVE WIRE MESH	30	30	0%	29-Apr-19	28-May-19	250																	
010510	APPROVE SECURITY ELECTRONICS PRODUCT DATA	30	30	0%	29-Apr-19	28-May-19	214																	
010540	APPROVE SECURITY ELECTRONICS SHOP DRAWINGS	30	30	0%	29-Apr-19	28-May-19	214																	
010570	APPROVE SECURITY ELECTRONICS TOUCHSCREEN	30	30	0%	29-Apr-19	28-May-19	214																	
011180	APPROVE MAIN SWITCHBOARDS - MSB1/MSB2	30	30	0%	29-Apr-19	28-May-19	132																	
011210	APPROVE SERVICE ENTRANCEATS-1/ATS-2 3000AMP SWITCHES	30	30	0%	29-Apr-19	28-May-19	164																	
011240	APPROVE GENERATOR #1/#2 ENGINES/PLATFORMS/ENCLOSURES	30	30	0%	29-Apr-19	28-May-19	171																	
010180	FAB/DELV FIRE PUMP	42	42	0%	02-May-19	12-Jun-19	112																	
010181	FIRE PROTECTION MATERIAL	1	1	0%	02-May-19	02-May-19	292																	
010460	FAB/DELV SECURITY FURNITURE & ACCESSORIES	30	30	0%	29-May-19	27-Jun-19	250																	
010490	FAB/DELV WIRE MESH	30	30	0%	29-May-19	27-Jun-19	250																	
010550	FAB/DELV SECURITY ELECTRONICS	30	30	0%	29-May-19	27-Jun-19	214																	
010580	FAB/DELV SECURITY ELECTRONICSTOUCHSCREEN	30	30	0%	29-May-19	27-Jun-19	214																	
011190	FAB/DELV MAIN SWITCHBOARDS - MSB1/MSB2	120	120	0%	29-May-19	25-Sep-19	132																	
011220	FAB/DELV SERVICE ENTRANCEATS-1/ATS-2 3000AMP SWITCHES	88	88	0%	29-May-19	24-Aug-19	164																	
011250	FAB/DELV GENERATOR #1/#2 ENGINES/PLATFORMS/ENCLOSURES	187	187	0%	29-May-19	01-Dec-19	171																	
CORRECTIONAL FACILITY																								
000950	TEMPORARY POWER	15	10	33%	04-Mar-19A	12-Apr-19	283																	
CONSTRUCTION																								
ADMINISTRATION																								
700001	BUILDING & SITE DEMOLITION	56	10	0%	11-Jun-18 A	12-Apr-19	27																	
700002	CAST-IN-PLACE CONCRETE	271	118	0%	11-Jun-18 A	16-Sep-19	27																	
700003	PRECAST CONCRETE	281	69	0%	11-Jun-18 A	08-Jul-19	101																	
700004	MASONRY	138	145	0%	11-Jun-18 A	24-Oct-19	37																	
700005	METALS	233	145	0%	11-Jun-18 A	24-Oct-19	95																	
700006	ROUGH CARPENTRY	388	186	0%	11-Jun-18 A	24-Dec-19	36																	
700007	FINISH CARPENTRY & CASEWORK	388	186	0%	11-Jun-18 A	24-Dec-19	36																	
700008	WATERPROOFING, JOINT SEALANTS, AIR BARRIER, EXP. JTS.	273	218	0%	11-Jun-18 A	11-Feb-20	32																	
700009	ROOFING & INSULATED METAL PANELS	101	108	0%	11-Jun-18 A	30-Aug-19	37																	
700010	STEEL DOORS & FRAMES, WOOD DOORS, HARDWARE	137	176	0%	11-Jun-18 A	10-Dec-19	55																	
700011	ALUMINUM ENTRANCES, DOORS, FRAMES, GLASS & GLAZING	0	87	0%	11-Jun-18 A	01-Aug-19	133																	
700012	OVERHEAD COILING DOORS, VEHICLE SALLYPORT DOORS	107	176	0%	11-Jun-18 A	10-Dec-19	55																	
700013	GYPSUM BOARD, METAL FRAMING, ACOUSTICAL TREATMENTS	176	191	0%	11-Jun-18 A	02-Jan-20	40																	
700014	FLOORING & PAINTING	161	190	0%	11-Jun-18 A	31-Dec-19	40																	
700015	SPECIALTIES	210	223	0%	11-Jun-18 A	19-Feb-20	27																	
700016	FOOD SERVICE & LAUNDRY EQUIPMENT	26	170	0%	11-Jun-18 A	02-Dec-19	63																	
700017	MISCELLANEOUS EQUIPMENT	51	166	0%	11-Jun-18 A	25-Nov-19	85																	
700018	DETENTION HOLLOW METAL DOORS, FRAMES, GLAZING	207	186	0%	11-Jun-18 A	24-Dec-19	37																	
700019	MODULAR STEEL CELLS, STEEL PANELS, DETENTION CEILING	182	176	0%	11-Jun-18 A	10-Dec-19	54																	

■ Actual Work
■ Remaining Work
■ Critical Remaining Work
◆ Milestone

D/B New Escambia County Correctional Facility
Pensacola, FL

ECCF18 ECCF18-MAR3 30Mar19 DBS Schedule Update

* 90-Day Schedule 11x17

Page 2 of 16
03-Apr-19 10:36

Data Date: 30-Mar-19

Caddell - WGI

#1054

Activity ID	Activity Name	Orig Dur	Rem Dur	Pct%	Early Start	Early Finish	Total Float	2019																
								Apr			May			Jun			Jul							
700020	DETENTION FURNISHINGS & EQUIPMENT	135	190	0%	11-Jun-18 A	31-Dec-19	46																	
700021	FURNISHINGS	5	176	0%	11-Jun-18 A	10-Dec-19	75																	
700022	SPECIAL CONSTRUCTION	516	266	0%	11-Jun-18 A	20-Apr-20	27																	
700023	CONVEYING SYSTEMS	84	180	0%	11-Jun-18 A	16-Dec-19	56																	
700024	FIRE SUPPRESSION	121	170	0%	11-Jun-18 A	02-Dec-19	52																	
700025	PLUMBING	516	266	0%	11-Jun-18 A	20-Apr-20	27																	
700026	HEATING, VENTILATING, AND AIR CONDITIONING	516	266	0%	11-Jun-18 A	20-Apr-20	27																	
700027	ELECTRICAL	516	266	0%	11-Jun-18 A	20-Apr-20	27																	
700028	COMMUNICATIONS	516	266	0%	11-Jun-18 A	20-Apr-20	27																	
700029	ELECTRONIC SECURITY SYSTEMS	409	216	0%	11-Jun-18 A	07-Feb-20	27																	
700031	EXTERIOR IMPROVEMENTS	409	210	0%	11-Jun-18 A	30-Jan-20	33																	
700032	UTILITIES	103	60	0%	11-Jun-18 A	24-Jun-19	183																UTILITIES	
401000	ALTERNATE 01 - FULL EMERGENCY POWER	516	266	0%	11-Jun-18 A	20-Apr-20	27																	
402000	ALTERNATE 02 - DOMESTIC HOT WATER, CHILLED WATER, & HEATING	516	266	0%	11-Jun-18 A	20-Apr-20	27																	
403000	ALTERNATE 03 - INMATE PLUMBING CONTROL SYSTEM	516	266	0%	11-Jun-18 A	20-Apr-20	27																	
405000	ALTERNATE 05 - FULL OPERABLE SLIDER DOORS	516	266	0%	11-Jun-18 A	20-Apr-20	27																	
409000	ALTERNATE 09 - EXACQ VISION VMS	516	266	0%	11-Jun-18 A	20-Apr-20	27																	
410000	ALTERNATE 10 - PERVIOUS CONCRETE PAVING	516	266	0%	11-Jun-18 A	20-Apr-20	27																	
414000	ALTERNATE 14 - SECOND BUNK FOR CELLS	516	266	0%	11-Jun-18 A	20-Apr-20	27																	
700030	EARTHWORK	366	167	0%	20-Aug-18 A	26-Nov-19	72																	
DESIGN																								
003000	A/E CONSTRUCTION ADMINISTRATION SERVICES (25 MONTHS)	25	18	28%	05-Sep-18 A	16-Apr-19	408																	
MODIFICATIONS / CHANGE ORDERS																								
900006	CHANGE ORDER NO.6	1	1	31%	01-Dec-18 A	01-Apr-19	292																	
900008	CHANGE ORDER NO.8	1	1	2%	28-Feb-19 A	01-Apr-19	292																	
900009	CHANGE ORDER NO.9	1	1	0%	01-Apr-19	01-Apr-19	292																	
900010	CHANGE ORDER NO.10	1	1	0%	01-Apr-19	01-Apr-19	292																	
SITWORK																								
100002	MAINTAIN EROSION CONTROLS (25 MONTHS)	25	16	36%	16-Jul-18 A	22-Apr-19	182																	
101400	ELECTRICAL DEMOLITION - CONNECTOR/CORRIDOR	15	2	90%	13-Sep-18 A	16-Apr-19	35																	
112300	SITE UTILITIES - U/G ELECTRICAL FOR SITE LIGHTING WEST	15	15	3%	22-Oct-18 A	17-May-19	33																	
100100	SITE GRADING - STORMWATER POND (EXIST SE JUV PLOT)	10	1	90%	21-Jan-19 A	01-Apr-19	56																	
112000	SITE UTILITIES - WATER WEST/NORTH (INCL CONNECTOR/CORRIDOR)	10	1	90%	09-Feb-19 A	13-May-19	97																	
112360	SITE UTILITIES - COMMUNICATION DUCTBANK TO ST MARY	60	36	40%	04-Mar-19 A	21-May-19	206																	
112370	SITE UTILITIES - ELECTRICAL POWER DUCTBANK TO ST MARY	60	36	40%	04-Mar-19 A	21-May-19	206																	
110000	SITE UTILITIES - STORMWATER POND	10	6	40%	11-Mar-19 A	09-Apr-19	56																	
101200	SITE & UTILITY DEMOLITION - REMAINING SITE	10	10	0%	01-Apr-19	12-Apr-19	27																	
101110	SITE & UTILITY DEMOLITION - EXISTING SE JUVENILE PARKING LOT 2 OF 2 (DELETE)	0	0	0%	01-Apr-19	01-Apr-19	293																	
100110	SITE GRADING - STORMWATER POND (EXIST SE JUV PLOT) 2 OF 2 (DELETE)	0	0	0%	01-Apr-19	01-Apr-19	293																	
112330	SITE UTILITIES - UNDERSLAB ELECTRICAL MAIN SWITCHGEAR	26	26	0%	01-Apr-19	06-May-19	267																	
112340	SITE UTILITIES - UNDERSLAB ELECTRICAL DISTRIBUTION FEEDERS	26	26	0%	01-Apr-19	06-May-19	267																	
112360	SITE UTILITIES - U/G ELECTRICAL UTILITY YARD SERVICES	14	14	0%	01-Apr-19	18-Apr-19	279																	
151010	GRAVEL - STORMWATER POND	5	5	0%	10-Apr-19	16-Apr-19	176																	
100200	SITE GRADING - REMAINING SITE	10	10	0%	15-Apr-19	26-Apr-19	27																	

■ Actual Work
■ Remaining Work
■ Critical Remaining Work
◆ ◆ Milestone

D/B New Escambia County Correctional Facility
Pensacola, FL

ECCF18 ECCF18-MAR3 30Mar19 DBS Schedule Update

* 90-Day Schedule 11x17

Page 3 of 16
03-Apr-19 10:36

Data Date: 30-Mar-19

Caddell - WGI

#1054

Activity ID	Activity Name	Orig Dur	Rem Dur	Pct%	Early Start	Early Finish	Total Float	2019														
								Apr	May	Jun	Jul	Aug	Sep	Oct	Nov	Dec	Jan	Feb	Mar			
152000	DECORATIVE FENCE/GATE - RETENTION POND	10	10	0%	17-Apr-19	30-Apr-19	176															
112420	SITE UTILITIES - ELECTRICAL RELOCATION CONNECTOR/CORRIDOR	15	15	0%	17-Apr-19	07-May-19	216															
159300	LANDSCAPING - NE JUVENILE PARKING LOT	5	5	0%	23-Apr-19	29-Apr-19	242															
100400	SITE GRADING - CONNECTOR/CORRIDOR AREA	10	10	0%	29-Apr-19	10-May-19	27															
151200	SITE CONCRETE - NORTHEAST SITE/UTILITY YARD/LOADING DOCK	10	10	0%	29-Apr-19	10-May-19	169															
151300	SITE CONCRETE - STAFF PARKING	10	10	0%	29-Apr-19	10-May-19	53															
111000	SITE UTILITIES - SANITARY SOUTH	10	10	0%	29-Apr-19	10-May-19	38															
110010	SITE UTILITIES - STORM SOUTH 1 OF 2	10	10	0%	29-Apr-19	10-May-19	43															
113000	SITE UTILITIES - GAS EAST	10	10	0%	29-Apr-19	10-May-19	213															
112440	SITE UTILITIES - HYDRONICS	30	30	0%	29-Apr-19	10-Jun-19	153															
112450	WATER LEAD-IN	2	2	0%	29-Apr-19	30-Apr-19	123															
151100	CONCRETE PADS - COOLING TOWERS	6	6	0%	13-May-19	20-May-19	169															
112400	SITE UTILITIES - COMMUNICATION DUCTBANK TO EXISTING JAIL (1/2)	15	15	0%	13-May-19	03-Jun-19	188															
151150	CONCRETE PADS - GENERATORS	6	6	0%	13-May-19	20-May-19	202															
112380	SITE UTILITIES - U/G ELECTRIC NORTH (BY GULF POWER)	20	20	0%	13-May-19	10-Jun-19	27															
151400	SITE CONCRETE - PUBLIC PARKING/ENTRANCE AREA	15	15	0%	13-May-19	03-Jun-19	53															
158000	FRP CANTILEVER WALL - ROADS/DRIVES SITE NORTH	15	15	0%	13-May-19	03-Jun-19	93															
110015	SITE UTILITIES - STORM SOUTH 2 OF 2	10	10	0%	13-May-19	24-May-19	43															
111010	SITE UTILITIES - SANITARY EAST	15	15	0%	13-May-19	03-Jun-19	38															
111020	SITE UTILITIES - SANITARY LATERALS NORTH (CONNECTOR/CORRIDOR)	5	5	0%	13-May-19	17-May-19	93															
112310	SITE UTILITIES - U/G ELECTRICAL FOR SITE LIGHTING EAST	15	15	0%	20-May-19	10-Jun-19	33															
151000	GRAVEL - UTILITY YARD	5	5	0%	21-May-19	28-May-19	202															
112460	COOLING TOWER	15	15	0%	21-May-19	11-Jun-19	169															
153001	PULL DETENTION SYSTEM CABLES SITE	10	10	0%	22-May-19	05-Jun-19	216															
110020	SITE UTILITIES - STORM NORTH (INCL CONNECTOR/CORRIDOR) 1 OF 2	10	10	0%	28-May-19	10-Jun-19	68															
151500	SITE CONCRETE - FACILITY VEHICLE PARKING	10	10	0%	04-Jun-19	17-Jun-19	73															
150090	FLAGPOLES	2	2	0%	04-Jun-19	05-Jun-19	196															
150092	BIKE RACK	2	2	0%	04-Jun-19	05-Jun-19	196															
158200	FRP CONC GRAVITY WALL - ROAD SITE WEST	15	15	0%	04-Jun-19	24-Jun-19	93															
112410	SITE UTILITIES - COMMUNICATION DUCTBANK TO EXISTING JAIL (2/2)	10	10	0%	04-Jun-19	17-Jun-19	188															
153000	INSTALL DETENTION DEVICES SITE	10	10	0%	06-Jun-19	19-Jun-19	216															
112390	SITE UTILITIES - BLDG & FIRE PUMP TRANSFORMERS (BY GULF POWER)	10	10	0%	11-Jun-19	24-Jun-19	27															
150200	CURB & GUTTER - STAFF PARKING LOT	10	10	0%	11-Jun-19	24-Jun-19	33															
110025	SITE UTILITIES - STORM NORTH (INCL CONNECTOR/CORRIDOR) 2 OF 2	10	10	0%	11-Jun-19	24-Jun-19	68															
112480	NEW PIPING EXISTING BUILDING PLANT	20	20	0%	11-Jun-19	09-Jul-19	153															
150080	SITE BOLLARDS	5	5	0%	18-Jun-19	24-Jun-19	183															
150300	CURB & GUTTER - PUBLIC PARKING LOT	10	10	0%	25-Jun-19	09-Jul-19	38															
150250	ASPHALT - STAFF PARKING LOT	15	15	0%	25-Jun-19	16-Jul-19	33															
CORRECTIONAL FACILITY																						
200420	UNDER SLAB SANITARY/STORM B (1/2)	10	8	0%	17-Dec-18A	10-Apr-19	112															
200400	UNDER SLAB SANITARY/STORM A (1/2)	10	6	40%	07-Jan-19A	24-Jun-19	45															
200455	UNDER SLAB SANITARY/STORM C (2/2)	10	2	80%	11-Feb-19A	02-Apr-19	88															
200785	TOPPING SLAB C 4TH LVL	10	3	70%	01-Mar-19A	09-Apr-19	51															
201085	IN-SLAB PLUMBING C 4TH LVL	5	1	80%	26-Mar-19A	04-Apr-19	49															

■ Actual Work
■ Remaining Work
■ Critical Remaining Work
◆ Milestone

D/B New Escambia County Correctional Facility
Pensacola, FL

ECCF18 ECCF18-MAR3 30Mar19 DBS Schedule Update

* 90-Day Schedule 11x17





Page 4 of 16
03-Apr-19 10:36

Data Date: 30-Mar-19

Caddell - WGI

#1054

Activity ID	Activity Name	Orig Dur	Rem Dur	Pct%	Early Start	Early Finish	Total Float	2019															
								Apr	May	Jun	Jul	Aug	Sep	Oct	Nov	Dec	Jan	Feb	Mar				
211094	TOPPING SLAB CENTER CORRIDOR LVL 3	4	2	50%	26-Mar-19A	25-Apr-19	161																
210280	DETAIL STRUCTURAL STEELD ELEV 137	9	1	90%	27-Mar-19A	01-Apr-19	40																
201090	IN-SLAB PLUMBING C ROOF	5	3	40%	27-Mar-19A	03-Apr-19	49																
201280	IN-SLAB ELECTRICAL C 3RD LVL	4	2	50%	28-Mar-19A	03-Apr-19	55																
201290	IN-SLAB ELECTRICAL C ROOF	4	1	75%	28-Mar-19A	01-Apr-19	54																
220000	EXTERIOR BUILDING FINISHES (PCST/MTL PNL/C,WALL) (DELETE)	1	1	0%	01-Apr-19	01-Apr-19	292																
270000	MEPS & INTERIOR FINISHES C4 (DELETE)	0	0	0%	01-Apr-19	01-Apr-19	293																
271000	MEPS & INTERIOR FINISHES D1 (DELETE)	0	0	0%	01-Apr-19	01-Apr-19	293																
272000	MEPS & INTERIOR FINISHES A4 (DELETE)	0	0	0%	01-Apr-19	01-Apr-19	293																
273000	MEPS & INTERIOR FINISHES B1 (DELETE)	0	0	0%	01-Apr-19	01-Apr-19	293																
270200	MEPS & INTERIOR FINISHES C3 (DELETE)	0	0	0%	01-Apr-19	01-Apr-19	293																
270400	MEPS & INTERIOR FINISHES C2 (DELETE)	0	0	0%	01-Apr-19	01-Apr-19	293																
270600	MEPS & INTERIOR FINISHES C1 (DELETE)	0	0	0%	01-Apr-19	01-Apr-19	293																
271200	MEPS & INTERIOR FINISHES D2 (DELETE)	0	0	0%	01-Apr-19	01-Apr-19	293																
271400	MEPS & INTERIOR FINISHES D3 (DELETE)	0	0	0%	01-Apr-19	01-Apr-19	293																
271600	MEPS & INTERIOR FINISHES D4 (DELETE)	0	0	0%	01-Apr-19	01-Apr-19	293																
272200	MEPS & INTERIOR FINISHES A3 (DELETE)	0	0	0%	01-Apr-19	01-Apr-19	293																
272400	MEPS & INTERIOR FINISHES A2 (DELETE)	0	0	0%	01-Apr-19	01-Apr-19	293																
272600	MEPS & INTERIOR FINISHES A1 (DELETE)	0	0	0%	01-Apr-19	01-Apr-19	293																
273200	MEPS & INTERIOR FINISHES B2 (DELETE)	0	0	0%	01-Apr-19	01-Apr-19	293																
273400	MEPS & INTERIOR FINISHES B3 (DELETE)	0	0	0%	01-Apr-19	01-Apr-19	293																
273600	MEPS & INTERIOR FINISHES B4 (DELETE)	0	0	0%	01-Apr-19	01-Apr-19	293																
200550	SLAB ON GRADE C (1/2)	10	10	0%	01-Apr-19	12-Apr-19	80																
210300	SWITCHBACK STAIRS C	15	15	0%	01-Apr-19	19-Apr-19	160																
210330	SWITCHBACK STAIRS A	15	15	0%	01-Apr-19	19-Apr-19	138																
200470	UNDER SLAB SANITARY/STORM D (1/2)	10	10	0%	01-Apr-19	12-Apr-19	69																
201040	IN-SLAB PLUMBING D 4TH LVL & HIGH ROOF	5	5	0%	01-Apr-19	05-Apr-19	92																
201050	IN-SLAB PLUMBING D LOW ROOF CL 14-29	5	5	0%	01-Apr-19	05-Apr-19	63																
201130	IN-SLAB PLUMBING A ROOF LVL	5	5	0%	01-Apr-19	05-Apr-19	37																
200480	UNDER SLAB ELECTRICAL D (1/2)	7	7	0%	01-Apr-19	09-Apr-19	72																
200465	UNDER SLAB ELECTRICAL C (2/2)	7	7	0%	01-Apr-19	09-Apr-19	83																
200430	UNDER SLAB ELECTRICAL B	14	14	0%	01-Apr-19	18-Apr-19	116																
201240	IN-SLAB ELECTRICAL D 4TH LVL & HIGH ROOF	2	2	0%	01-Apr-19	02-Apr-19	95																
201250	IN-SLAB ELECTRICAL D LOW ROOF CL 14-29	2	2	0%	01-Apr-19	02-Apr-19	69																
201330	IN-SLAB ELECTRICAL A ROOF LVL	4	4	0%	01-Apr-19	04-Apr-19	38																
200490	UNDER SLAB ELECTRICAL CC CL3-14	14	14	0%	01-Apr-19	18-Apr-19	124																
244395	INSTALL SECURITY/COMMERCIAL FRAMES - PRECAST D3	5	5	0%	01-Apr-19	05-Apr-19	202																
240871	INSTALL SECURITY/COMMERCIAL FRAMES - PRECAST C4 POD H	8	8	0%	01-Apr-19	10-Apr-19	144																
241266	INSTALL PRECAST WINDOW FRAMES D2 JUVENILE POD M	8	8	0%	01-Apr-19	10-Apr-19	151																
244415	INSTALL SECURITY/COMMERCIAL FRAMES - PRECAST D2 COMMON AREA	5	5	0%	01-Apr-19	05-Apr-19	194																
211071	PRECAST D EXTERIOR WALLS (2/2)	4	4	0%	01-Apr-19	04-Apr-19	27																
210161	DETAIL STRUCTURAL STEELD LOW ROOF 102 (2/3)	5	5	0%	01-Apr-19	05-Apr-19	41																
200890	SLAB ON DECK D ELEV 137 - 4TH LVL	3	3	0%	02-Apr-19	04-Apr-19	40																
201260	IN-SLAB ELECTRICAL D LOW ROOF CL 29-50	2	2	0%	03-Apr-19	04-Apr-19	69																

 Actual Work
 Remaining Work
 Critical Remaining Work
 Milestone

D/B New Escambia County Correctional Facility
Pensacola, FL

ECCF18 ECCF18-MAR3 30Mar19 DBS Schedule Update
* 90-Day Schedule 11x17

Page 5 of 16
03-Apr-19 10:36
Data Date: 30-Mar-19

Caddell - WGI
#1054

Activity ID	Activity Name	Orig Dur	Rem Dur	Pct%	Early Start	Early Finish	Total Float	2019														
								Apr			May			Jun			Jul					
282600	UNDER SLAB SANITARY/STORM SP	13	13	0%	03-Apr-19	19-Apr-19	190															
200790	TOPPING SLAB C ROOF	10	10	0%	04-Apr-19	17-Apr-19	52															
201270	IN-SLAB ELECTRICAL C 2ND LVL	4	4	0%	04-Apr-19	09-Apr-19	66															
211096	TOPPING SLAB CENTER CORRIDOR LVL 4	4	4	0%	04-Apr-19	09-Apr-19	180															
261400	CMU WALLS D3	11	11	0%	05-Apr-19	19-Apr-19	106															
211080	PRECAST D ELEV 156	4	4	0%	05-Apr-19	10-Apr-19	40															
201080	IN-SLAB PLUMBING C 3RD LVL	5	5	0%	05-Apr-19	11-Apr-19	49															
201320	IN-SLAB ELECTRICAL A 4TH LVL	4	4	0%	05-Apr-19	10-Apr-19	44															
251430	HVAC CONTROLS - ROUGH-IN D3	4	4	0%	05-Apr-19	10-Apr-19	192															
251445	PLUMBING CONTROLS - ROUGH-IN D3	1	1	0%	05-Apr-19	05-Apr-19	196															
251810	ELECTRICAL ROUGH-IN IN-WALL D3 (1/2)	8	8	0%	05-Apr-19	16-Apr-19	202															
251830	ELECTRICAL ROUGH-IN OVERHEAD D3 (1/4)	11	11	0%	05-Apr-19	19-Apr-19	155															
244400	INSTALL SECURITY/COMMERCIAL FRAMES - MASONRY D3	5	5	0%	05-Apr-19	11-Apr-19	198															
210021	PRECAST A (4/5)	4	4	0%	05-Apr-19	10-Apr-19	27															
244710	INSTALL SECURITY/COMMERCIAL FRAMES - PRECAST D1	5	5	0%	05-Apr-19	11-Apr-19	181															
200830	TOPPING SLAB A ROOF LVL	10	10	0%	08-Apr-19	19-Apr-19	37															
201060	IN-SLAB PLUMBING D LOW ROOF CL 29-50	5	5	0%	08-Apr-19	12-Apr-19	63															
201120	IN-SLAB PLUMBING A 4TH LVL	5	5	0%	08-Apr-19	12-Apr-19	42															
251447	PLUMBING CONTROLS - ROUGH-IN D3M	2	2	0%	08-Apr-19	09-Apr-19	196															
244416	GROUT & CONNECT R/I SECURITY/COMMERCIAL FRAMES - PRECAST D2 COMMON AREA	10	10	0%	08-Apr-19	19-Apr-19	194															
244396	GROUT & CONNECT R/I SECURITY/COMMERCIAL FRAMES - PRECAST D3	10	10	0%	08-Apr-19	19-Apr-19	202															
283150	INTERIOR JOINT SEALANT D	15	15	0%	08-Apr-19	26-Apr-19	231															
200485	UNDER SLAB ELECTRICAL D (2/2)	7	7	0%	10-Apr-19	18-Apr-19	75															
201310	IN-SLAB ELECTRICAL A 3RD LVL	4	4	0%	11-Apr-19	16-Apr-19	67															
200425	UNDER SLAB SANITARY/STORM B (2/2)	10	10	0%	11-Apr-19	24-Apr-19	112															
251432	HVAC CONTROLS - ROUGH-IN D3M	3	3	0%	11-Apr-19	15-Apr-19	192															
244405	INSTALL SECURITY/COMMERCIAL FRAMES - PRECAST D4	5	5	0%	11-Apr-19	17-Apr-19	198															
241071	INSTALL SECURITY/COMMERCIAL FRAMES - PRECAST C4 POD I	8	8	0%	11-Apr-19	22-Apr-19	144															
241336	INSTALL PRECAST WINDOW FRAMES D2 JUVENILE POD N	20	20	0%	11-Apr-19	08-May-19	151															
210152	STRUCTURAL STEEL D LOW ROOF 102 (3/3)	4	4	0%	11-Apr-19	16-Apr-19	34															
211091	PRECAST CENTER CORRIDOR CL 14-50 / PRECAST D ELEV 154	6	6	0%	11-Apr-19	18-Apr-19	27															
240873	GROUT & CONNECT R/I SECURITY/COMMERCIAL FRAMES - PRECAST C4 POD H	4	4	0%	11-Apr-19	16-Apr-19	194															
283100	INTERIOR JOINT SEALANT C	15	15	0%	11-Apr-19	01-May-19	228															
200780	TOPPING SLAB C 3RD LVL	10	10	0%	12-Apr-19	25-Apr-19	49															
201070	IN-SLAB PLUMBING C 2ND LVL	5	5	0%	12-Apr-19	18-Apr-19	59															
244365	INSTALL SECURITY SLIDERS D3	2	2	0%	12-Apr-19	15-Apr-19	225															
244370	INSTALL SECURITY DOORS D3	3	3	0%	12-Apr-19	16-Apr-19	212															
211101	TOPPING SLAB CENTER CORRIDOR ROOF	4	4	0%	12-Apr-19	17-Apr-19	182															
244711	GROUT & CONNECT R/I SECURITY/COMMERCIAL FRAMES - PRECAST D1	3	3	0%	12-Apr-19	16-Apr-19	188															
200560	SLAB ON GRADE C (2/2)	10	10	0%	15-Apr-19	26-Apr-19	80															
200475	UNDER SLAB SANITARY/STORM D (2/2)	10	10	0%	15-Apr-19	26-Apr-19	69															
201110	IN-SLAB PLUMBING A 3RD LVL	5	5	0%	15-Apr-19	19-Apr-19	64															
251405	DOMESTIC WATER D3	5	5	0%	15-Apr-19	19-Apr-19	186															
201300	IN-SLAB ELECTRICAL A 2ND LVL	4	4	0%	17-Apr-19	22-Apr-19	73															

■ Actual Work
■ Remaining Work
■ Critical Remaining Work
◆ Milestone

D/B New Escambia County Correctional Facility
Pensacola, FL

ECCF18 ECCF18-MAR3 30Mar19 DBS Schedule Update
* 90-Day Schedule 11x17

Page 6 of 16
03-Apr-19 10:36
Data Date: 30-Mar-19

Caddell - WGI
#1054

Activity ID	Activity Name	Orig Dur	Rem Dur	Pct%	Early Start	Early Finish	Total Float	2019														
								Apr			May			Jun			Jul					
251811	ELECTRICAL ROUGH-IN IN-WALL D3 (2/2)	8	8	0%	17-Apr-19	26-Apr-19	202															
210162	DETAIL STRUCTURAL STEEL D LOW ROOF 102 (3/3)	5	5	0%	17-Apr-19	23-Apr-19	34															
260000	CMU WALLS C4 (1/2)	10	10	0%	18-Apr-19	01-May-19	63															
230000	ROOF SYSTEM C - INSULATION OR LWIC	7	7	0%	18-Apr-19	26-Apr-19	53															
282530	DUCTWORK CC4M	7	7	0%	18-Apr-19	26-Apr-19	182															
250017	DUCTWORK C4M (1/2)	8	8	0%	18-Apr-19	29-Apr-19	65															
250003	AG SANITARY/STORM C4M (1/2)	5	5	0%	18-Apr-19	24-Apr-19	68															
244406	GROUT & CONNECT R/I SECURITY/COMMERCIAL FRAMES - PRECAST D4	10	10	0%	18-Apr-19	01-May-19	198															
210030	PRECAST ELEVATOR SHAFTS B	7	7	0%	19-Apr-19	29-Apr-19	27															
210380	PRECAST STAIR SHAFT B C	7	7	0%	19-Apr-19	29-Apr-19	27															
200485	UNDER SLAB ELECTRICAL CC CL14-50	14	14	0%	19-Apr-19	08-May-19	124															
200820	TOPPING SLAB A 4TH LVL	10	10	0%	22-Apr-19	03-May-19	37															
210320	MEZZANINE STAIR C	6	6	0%	22-Apr-19	29-Apr-19	160															
210340	MECHANICAL STAIRSA	10	10	0%	22-Apr-19	03-May-19	138															
232000	ROOF SYSTEM A - INSULATION OR LWIC	7	7	0%	22-Apr-19	30-Apr-19	133															
201100	IN-SLAB PLUMBING A 2ND LVL	5	5	0%	22-Apr-19	26-Apr-19	69															
200940	POUR SWITCHBACK STAIRS C	3	3	0%	22-Apr-19	24-Apr-19	168															
200970	POUR SWITCHBACK STAIRS A	3	3	0%	22-Apr-19	24-Apr-19	163															
261720	FRAME GYPSUM WALLS D3	5	5	0%	22-Apr-19	26-Apr-19	168															
251410	HYDRONIC PIPING D3	10	10	0%	22-Apr-19	03-May-19	172															
251415	DUCTWORK D3	10	10	0%	22-Apr-19	03-May-19	172															
251420	MECH EQUIPMENT D3	2	2	0%	22-Apr-19	23-Apr-19	199															
251460	PLUMBING INSULATION D3	3	3	0%	22-Apr-19	24-Apr-19	189															
251407	DOMESTIC WATER D3M	4	4	0%	22-Apr-19	25-Apr-19	186															
244385	WIRE MESH @ BREAKROOM D3	2	2	0%	22-Apr-19	23-Apr-19	234															
251831	ELECTRICAL ROUGH-IN OVERHEAD D3 (2/4)	11	11	0%	22-Apr-19	06-May-19	155															
244600	WIRE MESH @ STOREFRONT WINDOWS D3	5	5	0%	22-Apr-19	26-Apr-19	231															
240471	INSTALL SECURITY/COMMERCIAL FRAMES - PRECAST C3 POD C	8	8	0%	23-Apr-19	02-May-19	144															
241073	GROUT & CONNECT R/I SECURITY/COMMERCIAL FRAMES - PRECAST C4 POD I	4	4	0%	23-Apr-19	26-Apr-19	186															
200900	SLAB ON DECK D ELEV 102 - 2ND LVL (LOW ROOF)	6	6	0%	24-Apr-19	01-May-19	56															
210200	STRUCTURAL STEEL B SEQ1	11	11	0%	24-Apr-19	08-May-19	34															
251425	PLUMBING FIXTURES D3	3	3	0%	25-Apr-19	29-Apr-19	212															
260200	CMU WALLS C3 (1/2)	8	8	0%	26-Apr-19	07-May-19	135															
200770	TOPPING SLAB C 2ND LVL	10	10	0%	26-Apr-19	09-May-19	54															
282330	DUCTWORK CC3M	7	7	0%	26-Apr-19	06-May-19	168															
250202	AG SANITARY/STORM C3M (1/2)	7	7	0%	26-Apr-19	06-May-19	50															
250217	DUCTWORK C3M (1/2)	8	8	0%	26-Apr-19	07-May-19	49															
251462	PLUMBING INSULATION D3M	2	2	0%	26-Apr-19	29-Apr-19	186															
252227	DUCTWORK A3M (1/2)	7	7	0%	26-Apr-19	06-May-19	87															
282410	DOMESTIC WATER CC4	3	3	0%	29-Apr-19	01-May-19	189															
282500	CONDENSATE/DRAINAGE CC4M	2	2	0%	29-Apr-19	30-Apr-19	188															
282510	DOMESTIC WATER CC4M	5	5	0%	29-Apr-19	03-May-19	185															
282520	HYDRONIC PIPING CC4M	5	5	0%	29-Apr-19	03-May-19	186															
282590	DUCTWORK INSULATION CC4M	5	5	0%	29-Apr-19	03-May-19	205															

■ Actual Work
■ Remaining Work
■ Critical Remaining Work
◆ Milestone

D/B New Escambia County Correctional Facility
Pensacola, FL

ECCF18 ECCF18-MAR3 30Mar19 DBS Schedule Update
* 90-Day Schedule 11x17

Page 7 of 16
03-Apr-19 10:36
Data Date: 30-Mar-19

Caddell - WGI
#1054

Activity ID	Activity Name	Orig Dur	Rem Dur	Pct%	Early Start	Early Finish	Total Float	2019														
								Apr			May			Jun			Jul					
261730	HANG GYPSUM WALLS D3	5	5	0%	29-Apr-19	03-May-19	168															
230010	ROOF SYSTEM C - SBS/NAILER	15	15	0%	29-Apr-19	17-May-19	143															
210420	PAN STAIRS B C	5	5	0%	30-Apr-19	06-May-19	164															
211085	STRUCTURAL STEEL D ELEV 154	4	4	0%	30-Apr-19	03-May-19	27															
200960	POUR MEZZANINE STAIR C	3	3	0%	30-Apr-19	02-May-19	162															
282400	CONDENSATE/DRAINAGE CC4	3	3	0%	01-May-19	03-May-19	188															
232010	ROOF SYSTEM A - SBS/NAILER	15	15	0%	01-May-19	21-May-19	133															
261200	CMU WALLS D2 (1/2)	5	5	0%	02-May-19	08-May-19	149															
200575	SLAB ON GRADE D (1/2)	10	10	0%	02-May-19	15-May-19	56															
251215	DUCTWORK D2 (1/2)	13	13	0%	02-May-19	20-May-19	79															
250700	FIRE SPRINKLER PIPING C4M CELL BLOCK H	6	6	0%	02-May-19	09-May-19	57															
250740	FIRE SPRINKLER PIPING C3M CELL BLOCK C	6	6	0%	02-May-19	09-May-19	47															
251710	FIRE SPRINKLER PIPING D3	2	2	0%	02-May-19	03-May-19	178															
251720	FIRE SPRINKLER PIPING D2 (1/2)	5	5	0%	02-May-19	08-May-19	87															
282700	FIRE SPRINKLER PIPING CC4	10	10	0%	02-May-19	15-May-19	182															
251805	ELECTRICAL ROUGH-IN IN-WALL D2 (1/3)	8	8	0%	02-May-19	13-May-19	156															
240671	INSTALL SECURITY/COMMERCIAL FRAMES - PRECAST C3 POD D	8	8	0%	03-May-19	14-May-19	144															
240473	GROUT & CONNECT R/I SECURITY/COMMERCIAL FRAMES - PRECAST C3 POD C	4	4	0%	03-May-19	08-May-19	178															
262000	CMU WALLS A4 (1/2)	9	9	0%	06-May-19	16-May-19	37															
210350	MAIN ACCESS STAIRS A	15	15	0%	06-May-19	24-May-19	138															
211120	DETAIL STRUCTURAL STEEL D ELEV 154	5	5	0%	06-May-19	10-May-19	67															
200980	POUR MECHANICAL STAIRS A	3	3	0%	06-May-19	08-May-19	153															
282540	HVAC CONTROLS - ROUGH-IN CC4M	2	2	0%	06-May-19	07-May-19	186															
282570	PLUMBING INSULATION CC4M	2	2	0%	06-May-19	07-May-19	185															
282580	HYDRONIC PIPING INSULATION CC4M	2	2	0%	06-May-19	07-May-19	188															
261740	FINISH GYPSUM WALLS D3	10	10	0%	06-May-19	17-May-19	168															
251465	DUCTWORK INSULATION D3	5	5	0%	06-May-19	10-May-19	177															
251470	HYDRONIC PIPING INSULATION D3	5	5	0%	06-May-19	10-May-19	172															
251417	DUCTWORK D3M	7	7	0%	06-May-19	14-May-19	172															
251422	MECH EQUIPMENT D3M	2	2	0%	06-May-19	07-May-19	202															
252002	AG SANITARY/STORM A4M (1/2)	5	5	0%	06-May-19	10-May-19	41															
252027	DUCTWORK A4M (1/2)	7	7	0%	06-May-19	14-May-19	39															
252700	FIRE SPRINKLER PIPING CELL A4M BLOCK L	6	6	0%	06-May-19	13-May-19	40															
253915	ELECTRICAL ROUGH-IN IN-WALL A1 (1/2)	8	8	0%	06-May-19	15-May-19	140															
210022	PRECAST A (5/5)	9	9	0%	06-May-19	16-May-19	27															
282928	GRD INSTALLATION CC4M	1	1	0%	06-May-19	06-May-19	205															
200930	POUR PAN STAIRS B C	3	3	0%	07-May-19	09-May-19	164															
282230	DUCTWORK CC3	8	8	0%	07-May-19	16-May-19	168															
282300	CONDENSATE/DRAINAGE CC3M	2	2	0%	07-May-19	08-May-19	177															
282310	DOMESTIC WATER CC3M	7	7	0%	07-May-19	15-May-19	175															
282320	HYDRONIC PIPING CC3M	3	3	0%	07-May-19	09-May-19	173															
282390	DUCTWORK INSULATION CC3M	5	5	0%	07-May-19	13-May-19	179															
251832	ELECTRICAL ROUGH-IN OVERHEAD D3 (3/4)	11	11	0%	07-May-19	21-May-19	155															
282440	HVAC CONTROLS - ROUGH-IN CC4	2	2	0%	08-May-19	09-May-19	186															

■ Actual Work
■ Remaining Work
■ Critical Remaining Work
◆ Milestone

D/B New Escambia County Correctional Facility
Pensacola, FL

ECCF18 ECCF18-MAR3 30Mar19 DBS Schedule Update

* 90-Day Schedule 11x17

Page 8 of 16
03-Apr-19 10:36

Data Date: 30-Mar-19

Caddell - WGI

#1054

Activity ID	Activity Name	Orig Dur	Rem Dur	Pct%	Early Start	Early Finish	Total Float	2019															
								Apr			May			Jun			Jul						
282470	PLUMBING INSULATION CC4	3	3	0%	08-May-19	10-May-19	185																
282550	HVAC CONTROLS - PULL/TERMINATE CONTROL WIRE CC4M	2	2	0%	08-May-19	09-May-19	194																
210210	STRUCTURAL STEEL B SEQ2	9	9	0%	09-May-19	21-May-19	37																
210220	DETAIL STRUCTURAL STEEL B SEQ1	12	12	0%	09-May-19	24-May-19	34																
261205	CMU WALLS D2 (2/3)	6	6	0%	09-May-19	16-May-19	149																
251230	HVAC CONTROLS - ROUGH-IN D2	10	10	0%	09-May-19	22-May-19	151																
251245	PLUMBING CONTROLS - ROUGH-IN D2	5	5	0%	09-May-19	15-May-19	156																
251605	DOMESTIC WATER D4	8	8	0%	09-May-19	20-May-19	175																
241264	INSTALL SECURITY CEILING @ MULTI-PURPOSE RM D2 JUVENILE POD M	4	4	0%	09-May-19	14-May-19	193																
241406	INSTALL PRECAST WINDOW FRAMES D2 JUVENILE POD O	20	20	0%	09-May-19	06-Jun-19	151																
244420	INSTALL SECURITY/COMMERCIAL FRAMES - MASONRY D2 COMMON AREA	5	5	0%	09-May-19	15-May-19	166																
241211	INSTALL SECURITY CEILING D2 JUVENILE POD M	15	15	0%	09-May-19	30-May-19	188																
260400	CMU WALLS C2	6	6	0%	10-May-19	17-May-19	171																
260600	CMU WALLS C1 (1/2)	13	13	0%	10-May-19	29-May-19	129																
240400	INSTALL STEEL CELL WALL PANELS C3 POD C EAST	10	10	0%	10-May-19	23-May-19	47																
240800	INSTALL STEEL CELL WALL PANELS C4 POD H EAST	10	10	0%	10-May-19	23-May-19	57																
282030	DUCTWORK CC1	25	25	0%	10-May-19	14-Jun-19	123																
282130	DUCTWORK CC2	13	13	0%	10-May-19	29-May-19	151																
282380	HYDRONIC PIPING INSULATION CC3M	3	3	0%	10-May-19	14-May-19	178																
282560	HVAC CONTROLS - CONTROLS CHECKOUT/POINT-TO-POINT CHECK CC4M	2	2	0%	10-May-19	13-May-19	200																
250415	DUCTWORK C2	17	17	0%	10-May-19	04-Jun-19	54																
250430	HVAC CONTROLS - ROUGH-IN C2	7	7	0%	10-May-19	20-May-19	189																
250445	PLUMBING CONTROLS - ROUGH-IN C2	2	2	0%	10-May-19	13-May-19	196																
250705	FIRE SPRINKLER PIPING C4M CELL BLOCK I	6	6	0%	10-May-19	17-May-19	71																
250745	FIRE SPRINKLER PIPING C3M CELL BLOCK D	6	6	0%	10-May-19	17-May-19	61																
250780	FIRE SPRINKLER PIPING C2M CELL BLOCK A	6	6	0%	10-May-19	17-May-19	65																
261600	CMU WALLS D4	6	6	0%	13-May-19	20-May-19	89																
200905	SLAB ON DECK D ELEV 154 ROOF LVL	3	3	0%	13-May-19	15-May-19	123																
220010	EXTERIOR FRAMING D3M JUVENILE POP-UP 1	8	8	0%	13-May-19	22-May-19	67																
251630	HVAC CONTROLS - ROUGH-IN D4	4	4	0%	13-May-19	16-May-19	181																
251645	PLUMBING CONTROLS - ROUGH-IN D4	1	1	0%	13-May-19	13-May-19	184																
251815	ELECTRICAL ROUGH-IN IN-WALL D4 (1/2)	8	8	0%	13-May-19	22-May-19	169																
251835	ELECTRICAL ROUGH-IN OVERHEAD D4 (1/4)	11	11	0%	13-May-19	28-May-19	149																
244410	INSTALL SECURITY/COMMERCIAL FRAMES - MASONRY D4	5	5	0%	13-May-19	17-May-19	176																
282922	GRD INSTALLATION D3	1	1	0%	13-May-19	13-May-19	197																
251472	HYDRONIC PIPING INSULATION D3M	5	5	0%	13-May-19	17-May-19	172																
250450	PLUMBING CONTROLS - PULL/TERMINATE CONTROL WIRE C2	2	2	0%	14-May-19	15-May-19	196																
252705	FIRE SPRINKLER PIPING CELLA4M BLOCK K	6	6	0%	14-May-19	21-May-19	56																
251806	ELECTRICAL ROUGH-IN IN-WALL D2 (2/3)	8	8	0%	14-May-19	23-May-19	156																
282927	GRD INSTALLATION CC3M	1	1	0%	14-May-19	14-May-19	199																
251467	DUCTWORK INSULATION D3M	3	3	0%	15-May-19	17-May-19	172																
240071	INSTALL SECURITY/COMMERCIAL FRAMES - PRECAST C1 POD A	5	5	0%	15-May-19	21-May-19	144																
240673	GROUT & CONNECT R1 SECURITY/COMMERCIAL FRAMES - PRECAST C3 POD D	4	4	0%	15-May-19	20-May-19	170																
200585	SLAB ON GRADE D (2/2)	10	10	0%	16-May-19	30-May-19	56																

■ Actual Work
■ Remaining Work
■ Critical Remaining Work
◆ Milestone

D/B New Escambia County Correctional Facility
Pensacola, FL

ECCF18 ECCF18-MAR3 30Mar19 DBS Schedule Update
* 90-Day Schedule 11x17

Page 9 of 16
03-Apr-19 10:36
Data Date: 30-Mar-19

Caddell - WGI
#1054

Activity ID	Activity Name	Orig Dur	Rem Dur	Pct%	Early Start	Early Finish	Total Float	2019															
								Apr			May			Jun			Jul						
282340	HVAC CONTROLS - ROUGH-IN CC3M	2	2	0%	16-May-19	17-May-19	177																
282370	PLUMBING INSULATION CC3M	5	5	0%	16-May-19	22-May-19	175																
250455	PLUMBING CONTROLS - CONTROLS CHECKOUT/POINT-TO-POINT CHECK C2	2	2	0%	16-May-19	17-May-19	196																
253916	ELECTRICAL ROUGH-IN IN-WALLA1 (2/2)	8	8	0%	16-May-19	28-May-19	140																
282790	CEILING GRID CC4	5	5	0%	16-May-19	22-May-19	182																
244431	INSTALL SECURITY SLIDERS D2	2	2	0%	16-May-19	17-May-19	201																
200810	TOPPING SLABA 3RD LVL	10	10	0%	17-May-19	31-May-19	45																
210360	PRECAST STAIR SHAFT B B	4	4	0%	17-May-19	22-May-19	27																
282200	CONDENSATE/DRAINAGE CC3	7	7	0%	17-May-19	28-May-19	171																
282210	DOMESTIC WATER CC3	3	3	0%	17-May-19	21-May-19	175																
282220	HYDRONIC PIPING CC3	8	8	0%	17-May-19	29-May-19	168																
282230	DUCTWORK INSULATION CC3	5	5	0%	17-May-19	23-May-19	176																
282720	FIRE SPRINKLER PIPING CC3	10	10	0%	17-May-19	31-May-19	171																
241980	INSTALL MINI DORM CELL FRONTS A4 POD L	7	7	0%	17-May-19	28-May-19	37																
261215	CMU WALLS D2 (3/3)	6	6	0%	17-May-19	24-May-19	149																
241334	INSTALL SECURITY CEILING @ MULTI-PURPOSE RM D2 JUVENILE POD N	4	4	0%	17-May-19	22-May-19	191																
241281	INSTALL SECURITY CEILINGS D2 JUVENILE POD N	15	15	0%	17-May-19	07-Jun-19	182																
267140	CEILING GRID D3	3	3	0%	20-May-19	22-May-19	178																
282350	HVAC CONTROLS - PULL/TERMINATE CONTROL WIRE CC3M	2	2	0%	20-May-19	21-May-19	186																
250785	FIRE SPRINKLER PIPING C2M CELL BLOCK B	6	6	0%	20-May-19	28-May-19	79																
250790	FIRE SPRINKLER PIPING C2 CELL BLOCK A	5	5	0%	20-May-19	24-May-19	188																
244330	INSTALL SECURITY SLIDERS D4	2	2	0%	20-May-19	21-May-19	199																
244335	INSTALL SECURITY DOORS D4	3	3	0%	20-May-19	22-May-19	190																
244360	INSTALL SECURITY CEILINGS D3	2	2	0%	20-May-19	21-May-19	190																
244560	WIRE MESH @ STAIR E C2	20	20	0%	20-May-19	17-Jun-19	196																
270410	PRIME & 1ST COAT PAINT C2	10	10	0%	20-May-19	03-Jun-19	171																
230020	ROOF SYSTEM C - COPING/BRAKE METAL	6	6	0%	20-May-19	28-May-19	209																
282333	MECHANICAL EQUIPMENT C ROOF	1	1	0%	20-May-19	20-May-19	194																
250435	HVAC CONTROLS - PULL/TERMINATE CONTROL WIRE C2	4	4	0%	21-May-19	24-May-19	189																
251610	HYDRONIC PIPING D4	10	10	0%	21-May-19	04-Jun-19	164																
251615	DUCTWORK D4	10	10	0%	21-May-19	04-Jun-19	164																
251620	MECH EQUIPMENT D4	2	2	0%	21-May-19	22-May-19	180																
251660	PLUMBING INSULATION D4	4	4	0%	21-May-19	24-May-19	175																
251700	FIRE SPRINKLER PIPING D4	2	2	0%	21-May-19	22-May-19	177																
244325	INSTALL SECURITY CEILINGS D4	2	2	0%	21-May-19	22-May-19	193																
244350	WIRE MESH @ BREAKROOM D4	2	2	0%	21-May-19	22-May-19	213																
244595	WIRE MESH @ STOREFRONT WINDOWS D4	5	5	0%	21-May-19	28-May-19	210																
282360	HVAC CONTROLS - CONTROLS CHECKOUT/POINT-TO-POINT CHECK CC3M	2	2	0%	22-May-19	23-May-19	192																
252710	FIRE SPRINKLER PIPING CELLA4M BLOCK J	6	6	0%	22-May-19	30-May-19	72																
251833	ELECTRICAL ROUGH-IN OVERHEAD D3 (4/4)	11	11	0%	22-May-19	06-Jun-19	155																
240271	INSTALL SECURITY/COMMERCIAL FRAMES - PRECAST C1 POD B	5	5	0%	22-May-19	29-May-19	144																
232020	ROOF SYSTEM A - COPING/BRAKE METAL	9	9	0%	22-May-19	04-Jun-19	204																
240073	GROUT & CONNECT R1 SECURITY/COMMERCIAL FRAMES - PRECAST C1 POD A	10	10	0%	22-May-19	05-Jun-19	149																
282331	MECHANICAL EQUIPMENT A ROOF	1	1	0%	22-May-19	22-May-19	193																

■ Actual Work
■ Remaining Work
■ Critical Remaining Work
◆ Milestone

D/B New Escambia County Correctional Facility
Pensacola, FL

ECCF18 ECCF18-MAR3 30Mar19 DBS Schedule Update

* 90-Day Schedule 11x17

Page 10 of 16
03-Apr-19 10:36

Data Date: 30-Mar-19





Caddell - WGI

#1054

Activity ID	Activity Name	Orig Dur	Rem Dur	Pct%	Early Start	Early Finish	Total Float	2019														
								Apr			May			Jun			Jul					
262400	CMU WALLSA2	6	6	0%	17-Jun-19	24-Jun-19	67															
200410	UNDER SLAB ELECTRICALA	14	14	0%	17-Jun-19	05-Jul-19	47															
282000	CONDENSATE DRAINAGE CC1	10	10	0%	17-Jun-19	28-Jun-19	143															
282010	DOMESTIC WATER CC1	21	21	0%	17-Jun-19	16-Jul-19	123															
282020	HYDRONIC PIPING CC1	25	25	0%	17-Jun-19	22-Jul-19	123															
282090	DUCTWORK INSULATION CC1	17	17	0%	17-Jun-19	10-Jul-19	144															
282260	HVAC CONTROLS - CONTROLS CHECKOUT/POINT-TO-POINT CHECK CC3	2	2	0%	17-Jun-19	18-Jun-19	174															
252405	AG SANITARY/STORM IN-WALLA2	7	7	0%	17-Jun-19	25-Jun-19	172															
252415	DOMESTIC WATER IN-WALLA2	8	8	0%	17-Jun-19	26-Jun-19	124															
252445	HVAC CONTROLS - ROUGH-IN IN-WALLA2	4	4	0%	17-Jun-19	20-Jun-19	166															
252465	PLUMBING CONTROLS - ROUGH-IN IN-WALLA2	3	3	0%	17-Jun-19	19-Jun-19	169															
282760	FIRE SPRINKLER PIPING CC1	10	10	0%	17-Jun-19	28-Jun-19	151															
253910	ELECTRICAL ROUGH-IN IN-WALLA2 (1/2)	8	8	0%	17-Jun-19	26-Jun-19	124															
251821	ELECTRICAL ROUGH-IN OVERHEAD D1 (2/4)	11	11	0%	17-Jun-19	01-Jul-19	58															
251880	ELECTRICAL TRIMOUT OVERHEAD D4 (1/3)	10	10	0%	17-Jun-19	28-Jun-19	169															
251881	ELECTRICAL TRIMOUT OVERHEAD D4 (2/3)	10	10	0%	17-Jun-19	28-Jun-19	169															
241402	WIRE MESH @ REC CEILING D2 JUVENILE POD O	7	7	0%	17-Jun-19	25-Jun-19	190															
244515	INSTALL SECURITY/COMMERCIAL FRAMES - MASONRY A2	5	5	0%	17-Jun-19	21-Jun-19	147															
267170	CEILING TILE D4	3	3	0%	17-Jun-19	19-Jun-19	174															
282912	GRD INSTALLATION C2	2	2	0%	17-Jun-19	18-Jun-19	175															
282140	HVAC CONTROLS - ROUGH-IN CC2	7	7	0%	18-Jun-19	26-Jun-19	154															
282180	HYDRONIC PIPING INSULATION CC2	10	10	0%	18-Jun-19	01-Jul-19	151															
251635	HVAC CONTROLS - PULL/TERMINATE CONTROL WIRE D4	2	2	0%	18-Jun-19	19-Jun-19	173															
251650	PLUMBING CONTROLS - PULL/TERMINATE CONTROL WIRE D4	1	1	0%	18-Jun-19	18-Jun-19	176															
244390	INSTALL SECURITY FURNITURE & ACCESSORIES D3	9	9	0%	18-Jun-19	28-Jun-19	172															
271601	INSTALL COMMERCIAL DOORS/HARDWARE/GLASS D4	5	5	0%	18-Jun-19	24-Jun-19	171															
271615	FINAL PAINT D4	15	15	0%	18-Jun-19	09-Jul-19	166															
271620	SEAL/HARDEN CONCRETE FLOOR D4	5	5	0%	18-Jun-19	24-Jun-19	166															
271630	VCT FLOORING D4	10	10	0%	18-Jun-19	01-Jul-19	166															
271670	RESILIENT BASE D4	10	10	0%	18-Jun-19	01-Jul-19	166															
271675	CASEWORK & COUNTERTOPS D4	15	15	0%	18-Jun-19	09-Jul-19	166															
271685	INSTALL DIVISION 10'12 ITEMS D4	15	15	0%	18-Jun-19	09-Jul-19	166															
261010	CMU WALLS D1 (3/3)	7	7	0%	19-Jun-19	27-Jun-19	82															
261770	FINISH GYPSUM CEILINGS D3	6	6	0%	19-Jun-19	26-Jun-19	155															
220050	EXTERIOR FRAMING D3M JUVENILE POP-UP 3	8	8	0%	19-Jun-19	28-Jun-19	67															
251655	PLUMBING CONTROLS - CONTROLS CHECKOUT/POINT-TO-POINT CHECK D4	1	1	0%	19-Jun-19	19-Jun-19	176															
252715	FIRE SPRINKLER PIPING CELLA4M BLOCK L	5	5	0%	19-Jun-19	25-Jun-19	160															
252730	FIRE SPRINKLER DROPS CELLA4M BLOCK L	2	2	0%	19-Jun-19	20-Jun-19	165															
252760	FIRE SPRINKLER PIPING CELLA3M BLOCK E	6	6	0%	19-Jun-19	26-Jun-19	159															
242030	INSTALL PRIVACY PARTITIONS A4M POD L	12	12	0%	19-Jun-19	05-Jul-19	155															
242035	INSTALL MINI DORM CELL FRONTS A4 POD K	7	7	0%	19-Jun-19	27-Jun-19	37															
220310	TRUSSES D3M JUVENILE POP-UP 2	3	3	0%	19-Jun-19	21-Jun-19	80															
240480	INSTALL STEEL CELL WALL PANELS C3M POD C EAST	10	10	0%	20-Jun-19	03-Jul-19	67															
240880	INSTALL STEEL CELL WALL PANELS C4M POD H EAST	10	10	0%	20-Jun-19	03-Jul-19	77															

Activity ID	Activity Name	Orig Dur	Rem Dur	Pct%	Early Start	Early Finish	Total Float	2019														
								Apr			May			Jun			Jul					
253911	ELECTRICAL ROUGH-IN IN-WALLA2 (2/2)	8	8	0%	27-Jun-19	09-Jul-19	126															
251876	ELECTRICAL TRIMOUT OVERHEAD D3 (2/3)	10	10	0%	27-Jun-19	11-Jul-19	191															
244100	INSTALL SECURITY CEILINGS @ DORM CELLSA3 & A3M POD F	15	15	0%	27-Jun-19	18-Jul-19	141															
200814	FRP SODA3 POD G	5	5	0%	27-Jun-19	03-Jul-19	61															
271401	INSTALL COMMERCIAL DOORS/HARDWARE/GLASS D3	5	5	0%	27-Jun-19	03-Jul-19	164															
271415	FINAL PAINT D3	15	15	0%	27-Jun-19	18-Jul-19	155															
271420	SEAL/HARDEN CONCRETE FLOOR D3	5	5	0%	27-Jun-19	03-Jul-19	155															
271430	VCT FLOORING D3	10	10	0%	27-Jun-19	11-Jul-19	155															
271470	RESILIENT BASE D3	10	10	0%	27-Jun-19	11-Jul-19	155															
271475	CASEWORK & COUNTERTOPS D3	15	15	0%	27-Jun-19	18-Jul-19	155															
271485	INSTALL DIVISION 10/12 ITEMS D3	15	15	0%	27-Jun-19	18-Jul-19	155															
282870	SEAL/HARDEN CONCRETE FLOOR CC3	5	5	0%	27-Jun-19	03-Jul-19	184															
TESTING & CLOSEOUT																						
CORRECTIONAL FACILITY																						
291405	AIR SIDE EQUIPMENT START-UP D3M	2	2	0%	08-May-19	09-May-19	202															

 AIR SIDE EQUIPMENT START-UP D3M

-  Actual Work
-  Remaining Work
-  Critical Remaining Work
-  Milestone

D/B New Escambia County Correctional Facility
Pensacola, FL

ECCF18 ECCF18-MAR3 30Mar19 DBS Schedule Update

* 90-Day Schedule 11x17

Page 16 of 16
03-Apr-19 10:36

Data Date: 30-Mar-19

Caddell - WGI

#1054

Activity ID	Activity Name	Orig Dur	Rem Dur	Prev Pct%	New Pct %	Actual Start	Actual Finish	Total Float	Early Start	Early Finish	Budgeted Cost	This Period Cost	Cost to Complete
ECCF18-MAR3 30Mar19 DBS Schedule Update		627	286			02-Jan-18		49	02-Jan-18 A	18-May-20	\$12,549,205.31	\$3,544,394.50	\$7,745,846.28
Progress this Period		564	64			02-Jan-18		99	02-Jan-18 A	28-Jun-19	\$16,799,280.31	\$3,544,394.50	\$11,995,921.28
PRECONSTRUCTION		564	64			02-Jan-18		99	02-Jan-18 A	28-Jun-19	\$28,400,534.00	\$4,227,314.08	\$22,194,445.92
MILESTONES		6	0			01-Mar-19	25-Mar-19		01-Mar-19 A	25-Mar-19 A	\$0.00	\$0.00	\$0.00
001599	DESIGN COMPLETE	0	0	0%	100%		25-Mar-19			25-Mar-19 A	\$0.00	\$0.00	\$0.00
800017	PFRR BOARD MEETING - BCC RECOMMENDATION DEVELOPMENT WORKSHOP	0	0	0%	100%		01-Mar-19			01-Mar-19 A	\$0.00	\$0.00	\$0.00
WEATHER		5	0			01-Mar-19	29-Mar-19		01-Mar-19 A	29-Mar-19 A	\$0.00	\$0.00	\$0.00
890011	ANTICIPATED ADVERSE WEATHER - MAR19	5	0	0%	100%	01-Mar-19	29-Mar-19		01-Mar-19 A	29-Mar-19 A	\$0.00	\$0.00	\$0.00
DESIGN		243	1			25-Jul-18		43	25-Jul-18 A	01-Apr-19	\$443,000.00	\$375,850.00	\$19,650.00
001171	SITE/CIVIL DESIGN - FENCING/MISC. SITE ITEMS	30	0	95%	100%	25-Jul-18	25-Mar-19		25-Jul-18 A	25-Mar-19 A	\$50,000.00	\$2,500.00	\$0.00
001420	EC REVIEW - FF&E DESIGN (100% DESIGN)	14	0	95%	100%	10-Oct-18	07-Nov-18		10-Oct-18 A	07-Nov-18 A	\$0.00	\$0.00	\$0.00
001500	CONSOLIDATED CONSTRUCTION SET (100% CD)	60	0	0%	100%	25-Mar-19	25-Mar-19		25-Mar-19 A	25-Mar-19 A	\$0.00	\$0.00	\$0.00
004000	DESIGN BUILD SERVICES - CORNERSTONE DETENTION	1	1		95%	15-Oct-18		43	15-Oct-18 A	01-Apr-19	\$393,000.00	\$373,350.00	\$19,650.00
PERMITS		60	0			13-Mar-18	15-Mar-19		13-Mar-18 A	15-Mar-19 A	\$10,000.00	\$1,000.00	\$0.00
009020	PERMITS - BUILDING	60	0	90%	100%	13-Mar-18	15-Mar-19		13-Mar-18 A	15-Mar-19 A	\$10,000.00	\$1,000.00	\$0.00
PRECONSTRUCTION SUBMITTALS		205	20			30-Jan-18		259	30-Jan-18 A	18-Apr-19	\$0.00	\$0.00	\$0.00
000600	SUBMIT LOD 300/400 FEDERATED MODEL	20	20	0%	90%	07-Nov-18		259	07-Nov-18 A	18-Apr-19	\$0.00	\$0.00	\$0.00
000620	SUBMIT FINAL BASELINE DESIGN/CONSTRUCTION SCHEDULE	90	0	0%	100%	30-Jan-18	29-Mar-19		30-Jan-18 A	29-Mar-19 A	\$0.00	\$0.00	\$0.00
PROCUREMENT		376	64			02-Jan-18		229	02-Jan-18 A	28-Jun-19	\$27,572,534.00	\$3,726,714.08	\$21,923,545.92
010000	PROCUREMENT OF LONG-LEAD ITEMS	450	49	40%	65%	02-Jan-18		138	02-Jan-18 A	17-May-19	\$0.00	\$0.00	\$0.00
010061	STEEL PROCUREMENT (STR & MISC) - MATERIAL COST	210	1	40%	59%	07-Nov-18		123	07-Nov-18 A	30-Mar-19	\$4,805,685.00	\$913,080.15	\$1,970,330.85
010130	SUBMIT FIRE SPRINKLER SHOP DRAWINGS	30	0		100%	22-Mar-19	22-Mar-19		22-Mar-19 A	22-Mar-19 A	\$0.00	\$0.00	\$0.00
010160	SUBMIT FIRE PUMP	30	0		100%	22-Mar-19	22-Mar-19		22-Mar-19 A	22-Mar-19 A	\$0.00	\$0.00	\$0.00
010200	SUBMIT WALL PANEL	30	0		100%	07-Jun-18	20-Feb-19		07-Jun-18 A	20-Feb-19 A	\$400,000.00	\$400,000.00	\$0.00
010210	APPROVE WALL PANELS	30	0		100%	29-Jun-18	06-Mar-19		29-Jun-18 A	06-Mar-19 A	\$0.00	\$0.00	\$0.00
010220	FAB/DELV WALL PANELS	30	30		40%	06-Mar-19		310	06-Mar-19 A	28-Apr-19	\$0.00	\$0.00	\$0.00
010230	SUBMIT SECURITY HOLLOW METAL	30	0		100%	19-Dec-18	06-Mar-19		19-Dec-18 A	06-Mar-19 A	\$102,000.00	\$102,000.00	\$0.00

Activity ID	Activity Name	Orig Dur	Rem Dur	Prev Pct%	New Pct %	Actual Start	Actual Finish	Total Float	Early Start	Early Finish	Budgeted Cost	This Period Cost	Cost to Complete
010240	APPROVE SECURITY HOLLOW METAL	30	0		100%	02-Jan-19	12-Mar-19		02-Jan-19 A	12-Mar-19 A	\$0.00	\$0.00	\$0.00
010250	FAB/DELV SECURITY HOLLOW METAL	30	30		25%	12-Mar-19		310	12-Mar-19 A	28-Apr-19	\$0.00	\$0.00	\$0.00
010260	SUBMIT GLASS	30	0		100%	12-Jun-18	09-Jan-19		12-Jun-18 A	09-Jan-19 A	\$10,000.00	\$10,000.00	\$0.00
010270	APPROVE GLASS	30	0		100%	12-Jul-18	30-Jan-19		12-Jul-18 A	30-Jan-19 A	\$0.00	\$0.00	\$0.00
010290	SUBMIT SECURITY HARDWARE	30	0		100%	12-Jun-18	07-Dec-18		12-Jun-18 A	07-Dec-18 A	\$45,000.00	\$45,000.00	\$0.00
010300	APPROVE SECURITY HARDWARE	30	0		100%	09-Jul-18	14-Jan-19		09-Jul-18 A	14-Jan-19 A	\$0.00	\$0.00	\$0.00
010320	SUBMIT COMMERCIAL HOLLOW METAL	30	0		100%	19-Dec-18	06-Mar-19		19-Dec-18 A	06-Mar-19 A	\$15,000.00	\$15,000.00	\$0.00
010330	APPROVE COMMERCIAL HOLLOW METAL	30	0		100%	18-Jan-19	12-Mar-19		18-Jan-19 A	12-Mar-19 A	\$0.00	\$0.00	\$0.00
010340	FAB/DELV COMMERCIAL HOLLOW METAL	30	30		4%	30-Mar-19		310	30-Mar-19 A	28-Apr-19	\$0.00	\$0.00	\$0.00
010350	SUBMIT COMMERCIAL HARDWARE	30	0		100%	21-Dec-18	21-Dec-18		21-Dec-18 A	21-Dec-18 A	\$15,000.00	\$15,000.00	\$0.00
010360	APPROVE COMMERCIAL HARDWARE	30	0		100%	24-Jan-19	24-Jan-19		24-Jan-19 A	24-Jan-19 A	\$0.00	\$0.00	\$0.00
010380	SUBMIT SECURITY CEILING	30	0		100%	03-Aug-18	01-Feb-19		03-Aug-18 A	01-Feb-19 A	\$221,258.00	\$221,258.00	\$0.00
010390	APPROVE SECURITY CEILING	30	0		100%	05-Mar-19	05-Mar-19		05-Mar-19 A	05-Mar-19 A	\$0.00	\$0.00	\$0.00
011130	OWNER DIRECT PURCHASE MATERIAL (ODP) DETENTION 1/4	1	1		15%	01-Jan-19		169	01-Jan-19 A	28-Jun-19	\$6,846,688.00	\$1,027,003.20	\$5,819,684.80
011140	OWNER DIRECT PURCHASE ORDER ADMINISTRATION DETENTION 1/4	1	1		11%	01-Jan-19		169	01-Jan-19 A	28-Jun-19	\$2,000,000.00	\$220,000.00	\$1,780,000.00
011150	OWNER DIRECT PURCHASE MATERIAL (ODP) - PLUMBING	1	1		3%	01-Jan-19		212	01-Jan-19 A	29-Apr-19	\$876,472.00	\$26,294.16	\$850,177.84
011160	OWNER DIRECT PURCHASE MATERIAL (ODP) - HVAC	1	1		7%	01-Jan-19		182	01-Jan-19 A	18-Apr-19	\$6,015,351.00	\$421,074.57	\$5,594,276.43
011260	OWNER DIRECT PURCHASE MATERIAL (ODP) - ELECTRICAL	1	1		5%	01-Jan-19		292	01-Jan-19 A	01-Apr-19	\$6,220,080.00	\$311,004.00	\$5,909,076.00
CORRECTIONAL FACILITY		15	10			04-Mar-19		283	04-Mar-19 A	12-Apr-19	\$375,000.00	\$123,750.00	\$251,250.00
000950	TEMPORARY POWER	15	10		33%	04-Mar-19		283	04-Mar-19 A	12-Apr-19	\$375,000.00	\$123,750.00	\$251,250.00
CONSTRUCTION		383	60			16-Jul-18		233	16-Jul-18 A	24-Jun-19	\$11,601,253.69	(\$682,919.58)	(\$10,198,524.64)
MODIFICATIONS / CHANGE ORDERS		313	1			01-Dec-18		292	01-Dec-18 A	01-Apr-19	\$13,555,091.69	(\$1,922,594.48)	(\$10,623,251.74)
900006	CHANGE ORDER NO.6	1	1	11%	31%	01-Dec-18		292	01-Dec-18 A	01-Apr-19	(\$9,174,958.86)	(\$1,834,991.82)	(\$6,330,721.57)
900008	CHANGE ORDER NO.8	1	1	0%	2%	28-Feb-19		292	28-Feb-19 A	01-Apr-19	(\$4,380,132.83)	(\$87,602.66)	(\$4,292,530.17)
SITWORK		255	37			16-Jul-18		206	16-Jul-18 A	21-May-19	\$681,295.00	\$173,429.50	\$288,429.50
100002	MAINTAIN EROSION CONTROLS (25 MONTHS)	25	16	32%	36%	16-Jul-18		182	16-Jul-18 A	22-Apr-19	\$70,000.00	\$2,800.00	\$44,800.00

Activity ID	Activity Name	Orig Dur	Rem Dur	Prev Pct%	New Pct %	Actual Start	Actual Finish	Total Float	Early Start	Early Finish	Budgeted Cost	This Period Cost	Cost to Complete
100100	SITE GRADING - STORMWATER POND (EXIST SE JUV P.LOT)	10	1	80%	90%	21-Jan-19		56	21-Jan-19 A	01-Apr-19	\$220,000.00	\$22,000.00	\$22,000.00
110000	SITE UTILITIES - STORMWATER POND	10	6	0%	40%	11-Mar-19		56	11-Mar-19 A	09-Apr-19	\$25,000.00	\$10,000.00	\$15,000.00
112000	SITE UTILITIES - WATER WEST/NORTH (INCL CONNECTOR/CORRIDOR)	10	1	80%	90%	09-Feb-19		97	09-Feb-19 A	13-May-19	\$26,295.00	\$2,629.50	\$2,629.50
112360	SITE UTILITIES - COMMUNICATION DUCTBANK TO ST MARY	60	36		40%	04-Mar-19		206	04-Mar-19 A	21-May-19	\$170,000.00	\$68,000.00	\$102,000.00
112370	SITE UTILITIES - ELECTRICAL POWER DUCTBANK TO ST MARY	60	36		40%	04-Mar-19		206	04-Mar-19 A	21-May-19	\$170,000.00	\$68,000.00	\$102,000.00
CORRECTIONAL FACILITY		93	60			07-Jan-19		121	07-Jan-19 A	24-Jun-19	\$1,272,543.00	\$1,066,245.40	\$136,297.60
200290	ELEVATOR PIT WATERPROOFING	3	0		100%	04-Feb-19	08-Feb-19		04-Feb-19 A	08-Feb-19 A	\$30,000.00	\$30,000.00	\$0.00
200400	UNDER SLAB SANITARY/STORM A (1/2)	10	6	20%	40%	07-Jan-19		45	07-Jan-19 A	24-Jun-19	\$50,000.00	\$10,000.00	\$30,000.00
200455	UNDER SLAB SANITARY/STORM C (2/2)	10	2	50%	80%	11-Feb-19		88	11-Feb-19 A	02-Apr-19	\$50,000.00	\$15,000.00	\$10,000.00
200701	SLAB ON DECK D ELEV 115 - 3RD LVL (2/2)	6	0	66%	100%	25-Feb-19	01-Mar-19		25-Feb-19 A	01-Mar-19 A	\$0.00	\$0.00	\$0.00
200785	TOPPING SLAB C 4TH LVL	10	3	0%	70%	01-Mar-19		51	01-Mar-19 A	09-Apr-19	\$100,000.00	\$70,000.00	\$30,000.00
200950	POUR LARGE STAIR C A	3	0	0%	100%	11-Mar-19	12-Mar-19		11-Mar-19 A	12-Mar-19 A	\$3,555.00	\$3,555.00	\$0.00
201085	IN-SLAB PLUMBING C 4TH LVL	5	1		80%	26-Mar-19		49	26-Mar-19 A	04-Apr-19	\$13,988.00	\$11,190.40	\$2,797.60
201090	IN-SLAB PLUMBING C ROOF	5	3	0%	40%	27-Mar-19		49	27-Mar-19 A	03-Apr-19	\$50,000.00	\$20,000.00	\$30,000.00
201280	IN-SLAB ELECTRICAL C 3RD LVL	4	2	0%	50%	28-Mar-19		55	28-Mar-19 A	03-Apr-19	\$35,000.00	\$17,500.00	\$17,500.00
201285	IN-SLAB ELECTRICAL C 4TH LVL	4	0		100%	22-Mar-19	27-Mar-19		22-Mar-19 A	27-Mar-19 A	\$10,000.00	\$10,000.00	\$0.00
201290	IN-SLAB ELECTRICAL C ROOF	4	1	0%	75%	28-Mar-19		54	28-Mar-19 A	01-Apr-19	\$10,000.00	\$7,500.00	\$2,500.00
210020	PRECAST A (3/5)	9	0	0%	100%	14-Mar-19	28-Mar-19		14-Mar-19 A	28-Mar-19 A	\$200,000.00	\$200,000.00	\$0.00
210121	STRUCTURAL STEEL D ELEV 115 (2/2)	9	0		100%	26-Feb-19	26-Feb-19		26-Feb-19 A	26-Feb-19 A	\$0.00	\$0.00	\$0.00
210150	STRUCTURAL STEEL D LOW ROOF 102 (1/3)	4	0	0%	100%	18-Mar-19	21-Mar-19		18-Mar-19 A	21-Mar-19 A	\$50,000.00	\$50,000.00	\$0.00
210151	STRUCTURAL STEEL D LOW ROOF 102 (2/3)	4	0	0%	100%	25-Mar-19	29-Mar-19		25-Mar-19 A	29-Mar-19 A	\$0.00	\$0.00	\$0.00
210160	DETAIL STRUCTURAL STEEL D LOW ROOF 102 (1/3)	5	0	0%	100%	25-Mar-19	29-Mar-19		25-Mar-19 A	29-Mar-19 A	\$10,000.00	\$10,000.00	\$0.00
210270	STRUCTURAL STEEL D ELEV 137	3	0	0%	100%	22-Mar-19	26-Mar-19		22-Mar-19 A	26-Mar-19 A	\$50,000.00	\$50,000.00	\$0.00
210280	DETAIL STRUCTURAL STEEL D ELEV 137	9	1	0%	90%	27-Mar-19		40	27-Mar-19 A	01-Apr-19	\$10,000.00	\$9,000.00	\$1,000.00
211061	PRECAST D ELEV 100 (2/2)	5	0		100%	15-Jan-19	30-Jan-19		15-Jan-19 A	30-Jan-19 A	\$0.00	\$0.00	\$0.00

D/B New Correctional Facility
Escambia Co., FL #1054

ECCF18-MAR3 30Mar19 DBS Schedule Update

ECCF18

* Progress This Period: 30-Mar-19

Page 3 of 6
03-Apr-19 10:54

Data Date: 30-Mar-19

Activity ID	Activity Name	Orig Dur	Rem Dur	Prev Pct%	New Pct %	Actual Start	Actual Finish	Total Float	Early Start	Early Finish	Budgeted Cost	This Period Cost	Cost to Complete
211070	PRECAST D EXTERIOR WALLS (1/2)	5	0	20%	100%	28-Feb-19	08-Mar-19		28-Feb-19 A	08-Mar-19 A	\$175,000.00	\$140,000.00	\$0.00
211090	PRECAST CENTER CORRIDOR CL 14-50	6	0	0%	100%	11-Mar-19	16-Mar-19		11-Mar-19 A	16-Mar-19 A	\$200,000.00	\$200,000.00	\$0.00
211092	TOPPING SLAB CENTER CORRIDOR LVL 2	4	0		100%	21-Mar-19	26-Mar-19		21-Mar-19 A	26-Mar-19 A	\$25,000.00	\$25,000.00	\$0.00
211094	TOPPING SLAB CENTER CORRIDOR LVL 3	4	2		50%	26-Mar-19		161	26-Mar-19 A	25-Apr-19	\$25,000.00	\$12,500.00	\$12,500.00
211110	PRECAST D ELEV 115-137	6	0	0%	100%	09-Mar-19	14-Mar-19		09-Mar-19 A	14-Mar-19 A	\$175,000.00	\$175,000.00	\$0.00
Change Original Duration		60	60					27	23-Oct-19	21-Jan-20	\$696,170.00	\$0.00	\$696,170.00
CONSTRUCTION		60	60					27	23-Oct-19	21-Jan-20	\$696,170.00	\$0.00	\$696,170.00
CORRECTIONAL FACILITY		60	60					27	23-Oct-19	21-Jan-20	\$696,170.00	\$0.00	\$696,170.00
221200	ALUMINUM CURTAINWALL PLAN SOUTH ELEV (TRUE WEST)	60	60		0%			27	23-Oct-19	21-Jan-20	\$696,170.00	\$0.00	\$696,170.00
Logic Change		551	286			11-Jun-18		49	11-Jun-18 A	18-May-20	\$53,755.00	\$0.00	\$53,755.00
PRECONSTRUCTION		286	286					49	01-Apr-19	18-May-20	\$0.00	\$0.00	\$0.00
MILESTONES		50	50					49	09-Mar-20	18-May-20	\$0.00	\$0.00	\$0.00
289999	** SUBSTANTIAL COMPLETION (28May20) **	0	0	0%	0%			38		20-Apr-20*	\$0.00	\$0.00	\$0.00
999995	COMPLETE CONSTRUCTION	0	0	0%	0%			27		09-Mar-20	\$0.00	\$0.00	\$0.00
999996	COMPLETION OF WORK	0	0	0%	0%			27		09-Mar-20	\$0.00	\$0.00	\$0.00
999998	COMPLETE DEMOBILIZATION	0	0	0%	0%			49		18-May-20	\$0.00	\$0.00	\$0.00
WEATHER		33	33					260	01-Apr-19	15-May-19	\$0.00	\$0.00	\$0.00
890018	ANTICIPATED ADVERSE WEATHER - OCT19	3	3	0%	0%			260	01-Apr-19	03-Apr-19	\$0.00	\$0.00	\$0.00
890019	ANTICIPATED ADVERSE WEATHER - NOV19	4	4	0%	0%			260	04-Apr-19	09-Apr-19	\$0.00	\$0.00	\$0.00
890020	ANTICIPATED ADVERSE WEATHER - DEC19	5	5	0%	0%			260	10-Apr-19	16-Apr-19	\$0.00	\$0.00	\$0.00
890021	ANTICIPATED ADVERSE WEATHER - JAN20	5	5	0%	0%			260	17-Apr-19	23-Apr-19	\$0.00	\$0.00	\$0.00
890022	ANTICIPATED ADVERSE WEATHER - FEB20	5	5	0%	0%			260	24-Apr-19	30-Apr-19	\$0.00	\$0.00	\$0.00
890023	ANTICIPATED ADVERSE WEATHER - MAR20	5	5	0%	0%			260	01-May-19	07-May-19	\$0.00	\$0.00	\$0.00
890024	ANTICIPATED ADVERSE WEATHER - APR20	3	3	0%	0%			260	08-May-19	10-May-19	\$0.00	\$0.00	\$0.00
890025	ANTICIPATED ADVERSE WEATHER - MAY20	3	3	0%	0%			260	13-May-19	15-May-19	\$0.00	\$0.00	\$0.00
CONSTRUCTION		551	266			11-Jun-18		27	11-Jun-18 A	20-Apr-20	\$50,000.00	\$0.00	\$50,000.00
ADMINISTRATION		551	266			11-Jun-18		27	11-Jun-18 A	20-Apr-20	\$50,000.00	\$0.00	\$50,000.00

Activity ID	Activity Name	Orig Dur	Rem Dur	Prev Pct%	New Pct %	Actual Start	Actual Finish	Total Float	Early Start	Early Finish	Budgeted Cost	This Period Cost	Cost to Complete
700001	BUILDING & SITE DEMOLITION	56	10	0%	0%	11-Jun-18		27	11-Jun-18 A	12-Apr-19	\$0.00	\$0.00	\$0.00
700002	CAST-IN-PLACE CONCRETE	271	118	0%	0%	11-Jun-18		27	11-Jun-18 A	16-Sep-19	\$0.00	\$0.00	\$0.00
700003	PRECAST CONCRETE	281	69	0%	0%	11-Jun-18		101	11-Jun-18 A	08-Jul-19	\$0.00	\$0.00	\$0.00
700004	MASONRY	138	145	0%	0%	11-Jun-18		37	11-Jun-18 A	24-Oct-19	\$0.00	\$0.00	\$0.00
700005	METALS	233	145	0%	0%	11-Jun-18		95	11-Jun-18 A	24-Oct-19	\$0.00	\$0.00	\$0.00
700006	ROUGH CARPENTRY	388	186	0%	0%	11-Jun-18		36	11-Jun-18 A	24-Dec-19	\$50,000.00	\$0.00	\$50,000.00
700007	FINISH CARPENTRY & CASEWORK	388	186	0%	0%	11-Jun-18		36	11-Jun-18 A	24-Dec-19	\$0.00	\$0.00	\$0.00
700008	WATERPROOFING, JOINT SEALANTS, AIR BARRIER, EXP. JTS.	273	218	0%	0%	11-Jun-18		32	11-Jun-18 A	11-Feb-20	\$0.00	\$0.00	\$0.00
700009	ROOFING & INSULATED METAL PANELS	101	108	0%	0%	11-Jun-18		37	11-Jun-18 A	30-Aug-19	\$0.00	\$0.00	\$0.00
700010	STEEL DOORS & FRAMES, WOOD DOORS, HARDWARE	137	176	0%	0%	11-Jun-18		55	11-Jun-18 A	10-Dec-19	\$0.00	\$0.00	\$0.00
700011	ALUMINUM ENTRANCES, DOORS, FRAMES, GLASS & GLAZING	0	87	0%	0%	11-Jun-18		133	11-Jun-18 A	01-Aug-19	\$0.00	\$0.00	\$0.00
700012	OVERHEAD COILING DOORS, VEHICLE SALLYPORT DOORS	107	176	0%	0%	11-Jun-18		55	11-Jun-18 A	10-Dec-19	\$0.00	\$0.00	\$0.00
700013	GYPSUM BOARD, METAL FRAMING, ACOUSTICAL TREATMENTS	176	191	0%	0%	11-Jun-18		40	11-Jun-18 A	02-Jan-20	\$0.00	\$0.00	\$0.00
700014	FLOORING & PAINTING	161	190	0%	0%	11-Jun-18		40	11-Jun-18 A	31-Dec-19	\$0.00	\$0.00	\$0.00
700015	SPECIALTIES	210	223	0%	0%	11-Jun-18		27	11-Jun-18 A	19-Feb-20	\$0.00	\$0.00	\$0.00
700016	FOOD SERVICE & LAUNDRY EQUIPMENT	26	170	0%	0%	11-Jun-18		63	11-Jun-18 A	02-Dec-19	\$0.00	\$0.00	\$0.00
700017	MISCELLANEOUS EQUIPMENT	51	166	0%	0%	11-Jun-18		85	11-Jun-18 A	25-Nov-19	\$0.00	\$0.00	\$0.00
700018	DETENTION HOLLOW METAL DOORS, FRAMES, GLAZING	207	186	0%	0%	11-Jun-18		37	11-Jun-18 A	24-Dec-19	\$0.00	\$0.00	\$0.00
700019	MODULAR STEEL CELLS, STEEL PANELS, DETENTION CEILINGS	182	176	0%	0%	11-Jun-18		54	11-Jun-18 A	10-Dec-19	\$0.00	\$0.00	\$0.00
700020	DETENTION FURNISHINGS & EQUIPMENT	135	190	0%	0%	11-Jun-18		46	11-Jun-18 A	31-Dec-19	\$0.00	\$0.00	\$0.00
700021	FURNISHINGS	5	176	0%	0%	11-Jun-18		75	11-Jun-18 A	10-Dec-19	\$0.00	\$0.00	\$0.00
700022	SPECIAL CONSTRUCTION	516	266	0%	0%	11-Jun-18		27	11-Jun-18 A	20-Apr-20	\$0.00	\$0.00	\$0.00
700023	CONVEYING SYSTEMS	84	180	0%	0%	11-Jun-18		56	11-Jun-18 A	16-Dec-19	\$0.00	\$0.00	\$0.00
700024	FIRE SUPPRESSION	121	170	0%	0%	11-Jun-18		52	11-Jun-18 A	02-Dec-19	\$0.00	\$0.00	\$0.00

Activity ID	Activity Name	Orig Dur	Rem Dur	Prev Pct%	New Pct %	Actual Start	Actual Finish	Total Float	Early Start	Early Finish	Budgeted Cost	This Period Cost	Cost to Complete
700025	PLUMBING	516	266	0%	0%	11-Jun-18		27	11-Jun-18 A	20-Apr-20	\$0.00	\$0.00	\$0.00
700026	HEATING, VENTILATING, AND AIR CONDITIONING	516	266	0%	0%	11-Jun-18		27	11-Jun-18 A	20-Apr-20	\$0.00	\$0.00	\$0.00
700027	ELECTRICAL	516	266	0%	0%	11-Jun-18		27	11-Jun-18 A	20-Apr-20	\$0.00	\$0.00	\$0.00
700028	COMMUNICATIONS	516	266	0%	0%	11-Jun-18		27	11-Jun-18 A	20-Apr-20	\$0.00	\$0.00	\$0.00
700029	ELECTRONIC SECURITY SYSTEMS	409	216	0%	0%	11-Jun-18		27	11-Jun-18 A	07-Feb-20	\$0.00	\$0.00	\$0.00
700030	EARTHWORK	366	167	0%	0%	20-Aug-18		72	20-Aug-18 A	26-Nov-19	\$0.00	\$0.00	\$0.00
700031	EXTERIOR IMPROVEMENTS	409	210	0%	0%	11-Jun-18		33	11-Jun-18 A	30-Jan-20	\$0.00	\$0.00	\$0.00
700032	UTILITIES	103	60	0%	0%	11-Jun-18		183	11-Jun-18 A	24-Jun-19	\$0.00	\$0.00	\$0.00
TESTING & CLOSEOUT		52	52					60	20-Feb-20	01-May-20	\$3,755.00	\$0.00	\$3,755.00
MOBILIZATION		2	2					60	30-Apr-20	01-May-20	\$3,755.00	\$0.00	\$3,755.00
000991	DEMOBILIZATION - ROOFING	2	2		0%			60	30-Apr-20	01-May-20	\$3,755.00	\$0.00	\$3,755.00
CORRECTIONAL FACILITY		50	50					60	20-Feb-20	29-Apr-20	\$0.00	\$0.00	\$0.00
294500	PREPARE & COMPLETE ROOF/EXTERIOR PUNCHLIST	10	10		0%			27	20-Feb-20	04-Mar-20	\$0.00	\$0.00	\$0.00
294510	PREPARE OWNER ROOF/EXTERIOR PUNCHLIST	3	3		0%			27	05-Mar-20	09-Mar-20	\$0.00	\$0.00	\$0.00
294520	COMPLETE OWNER ROOF/EXTERIOR PUNCHLIST	7	7		0%			60	21-Apr-20	29-Apr-20	\$0.00	\$0.00	\$0.00
Added Activity This Period / Modifications		1	1					292	01-Apr-19	01-Apr-19	(\$5,000,000.00)	\$0.00	(\$5,000,000.00)
CONSTRUCTION		1	1					292	01-Apr-19	01-Apr-19	(\$5,000,000.00)	\$0.00	(\$5,000,000.00)
MODIFICATIONS / CHANGE ORDERS		1	1					292	01-Apr-19	01-Apr-19	(\$5,000,000.00)	\$0.00	(\$5,000,000.00)
900010	CHANGE ORDER NO.10	1	1		0%			292	01-Apr-19	01-Apr-19	(\$5,000,000.00)	\$0.00	(\$5,000,000.00)



Daily Log: Friday 3/1/2019

Daily Log Completed
 The Daily Log was completed by Donald Shelton on Mon Mar 4, 2019 at 11:39 am CST.

WEATHER REPORT

Temperature			Precipitation Since			Humidity				Windspeed		
Low	High	Avg	Midnight	2 Days Ago	3 Days Ago	Low	Avg	High	Dew	Avg	Max	Gust
61°F	76°F	67°F	0.08 in.	0.43 in.	0.80 in.	69%	89%	100%	63°F	4.6 mph	8 mph	13 mph

DAILY SNAPSHOT

06:00 AM	09:00 AM	12:00 PM	03:00 PM	06:00 PM	09:00 PM
cloudy 62°F	partly-cloudy-day 67°F	partly-cloudy-day 74°F	partly-cloudy-day 75°F	clear-night 69°F	partly-cloudy-night 64°F

OBSERVED WEATHER CONDITIONS

No.	Weather Delay	Sky	Temp	Average	Precipitation	Wind	Ground/Sea
1	No						
2	No	Cloudy	Mild	67	0	Light Wind	Dry

MANPOWER LOG

45 Workers | 392.0 Man Hours

No.	Contact/Company	Cost Code	Workers	# Hours	Man Hours	Location
1	EAA Site Contractors LLC		3	8.0	24.0	Site
Notes: Total man hours 24. EAA continued to dig retention pond today. Ramp into section D is complete with structural fill.						
2	A&B Electric Co., Inc.		6	10.0	60.0	Building
Notes: Working on temporary power packs and temporary lights, pull homeruns to lights and power packs (yellow turtles) and Have outage on temporary power to terminate homerun circuits.						
3	Bayside Structures, LLC		9	8.0	72.0	Building>D
Notes: Poured 8 yards at supplemental GB H.7/37. Place W.W.M. at elevation 115 Area D between center line 28/37. Installed bulk head 3' North of center line 37. Installed 3' #4 over beams and 12' #4 over GB. at elevation 115 in Area D.						
4	Caddell Construction Co. (DE), LLC		9	10.0	90.0	Site
Notes: WGI/Caddell supervision, quality control and safety onsite.						
5	Chavers Construction Inc.		3	9.0	27.0	Site
Notes: Installed 8" D.D.C. Back flow for Fire Main						

MANPOWER LOG

45 Workers | 392.0 Man Hours

No.	Contact/Company	Cost Code	Workers	# Hours	Man Hours	Location
6	Ed Emmons Steel Erectors, Inc.		1	8.0	8.0	Building>C
Notes: Installed two landings and two stringers in Stairwell A.						
7	Larry M. Jacobs & Associates, Inc.		1	1.0	1.0	Building>D
Notes: Conducted test for concrete pour.						
8	Nash Plumbing and Mechanical, LLC		10	8.0	80.0	Building
Notes: Mechanical- Installed anchors for pipe hangers and staging pipe. Plumbing- Installed anchors for pipe hangers.						
9	Tindall Corporation		3	10.0	30.0	Building>C
Notes: **Patching in area C. **Install rat line on roof for access to alternate connection installs						
			45		392.0	

Manpower Log's Attachments:

2. A&B Electric Co., Inc.



[Daily Construction Report -- 3_1_19.pdf](#)

3. Bayside Structures, LLC



[Bayside Daily 3-1-2019.PDF](#)

5. Chavers Construction Inc.

[Chaver Daily 3-1-2019.PDF](#)

6. Ed Emmons Steel Erectors, Inc.

[New Doc 2019-03-01 15.17.30.pdf](#)

8. Nash Plumbing and Mechanical, LLC

[Nash Daily 3-1-2019.xlsx](#)

9. Tindall Corporation

[Tindall Escambia daily 3-1-19.xlsx](#)

EQUIPMENT LOG

No.	Equipment Name	Cost Code	Hrs Operating	Hrs Idle	Inspected?	Inspection Time	Location
1	Volvo 330 Excavator				No	07:00 AM	Site>Stormwater Pond
	Notes:						
2	Komatsu 320 PT Loader				No	07:00 AM	Site>Stormwater Pond
	Notes:						
3	John Deere 750 Dozer				No	07:00 AM	Site>Stormwater Pond
	Notes:						
4	Terex Articulated Dump Truck				No	07:00 AM	Site>Stormwater Pond
	Notes:						
5	Sky Power Lift 600AJ				No	07:00 AM	Building>C
	Notes:						

EQUIPMENT LOG

No.	Equipment Name	Cost Code	Hrs Operating	Hrs Idle	Inspected?	Inspection Time	Location
6	Grove Crane AT700D				No	07:35 AM	Building>C
	Notes:						
7	Bobcat Miniexcavator				No	07:00 AM	Building>C
	Notes:						
8	John Deere 85G Excavator				No	07:00 AM	Site
	Notes:						
9	JLG Skytrak Telehandler				No	07:00 AM	Site
	Notes:						
10	JLG Skytrak Telehandler				No	07:00 AM	Site
	Notes:						

By

Date

Copies To



Whitesell Green / Caddell, a Joint Venture
 2700 Lagoon Park Drive
 Montgomery, Alabama 36109
 P: (334) 272-7723
 F: (334) 394-0193

Project: 1054 - Escambia County Correctional Facility
 3080 N. Pace Boulevard
 Pensacola, Florida 32501

Daily Log: Saturday 3/2/2019

Daily Log Completed
 The Daily Log was completed by Donald Shelton on Mon Mar 4, 2019 at 11:23 am CST.

WEATHER REPORT

Temperature			Precipitation Since			Humidity				Windspeed		
Low	High	Avg	Midnight	2 Days Ago	3 Days Ago	Low	Avg	High	Dew	Avg	Max	Gust
63°F	77°F	69°F	0.03 in.	0.11 in.	0.45 in.	74%	91%	100%	66°F	2.7 mph	6 mph	9 mph

DAILY SNAPSHOT

06:00 AM	09:00 AM	12:00 PM	03:00 PM	06:00 PM	09:00 PM
cloudy 66°F	partly-cloudy-day 70°F	partly-cloudy-day 77°F	cloudy 75°F	partly-cloudy-night 70°F	partly-cloudy-night 66°F

OBSERVED WEATHER CONDITIONS

No.	Weather Delay	Sky	Temp	Average	Precipitation	Wind	Ground/Sea
1	No	Cloudy	Mild	69	0	Light Wind	Wet/Muddy

MANPOWER LOG

4 Workers | 22.0 Man Hours

No.	Contact/Company	Cost Code	Workers	# Hours	Man Hours	Location
1	Caddell Construction Co. (DE), LLC		1	5.5	5.5	Site
Notes: WGI/Caddell supervision, quality control and safety onsite.						
2	Chavers Construction Inc.		3	5.5	16.5	Site
Notes: Continued installing existing water main to new. Raised new water main to be able to reach plumbing meter vault.						
			4	22.0		

Manpower Log's Attachments:

2. Chavers Construction Inc.

[Chaver Daily 3-2-2019.PDF](#)

EQUIPMENT LOG

No.	Equipment Name	Cost Code	Hrs Operating	Hrs Idle	Inspected?	Inspection Time	Location
1	John Deere 300G Excavator				No	07:00 AM	Site
Notes:							

By _____

Date _____

Copies To _____



Whitesell Green / Caddell, a Joint Venture
 2700 Lagoon Park Drive
 Montgomery, Alabama 36109
 P: (334) 272-7723
 F: (334) 394-0193

Project: 1054 - Escambia County Correctional
Facility
 3080 N. Pace Boulevard
 Pensacola, Florida 32501

Daily Log: Sunday 3/3/2019

WEATHER REPORT

Temperature			Precipitation Since			Humidity				Windspeed		
Low	High	Avg	Midnight	2 Days Ago	3 Days Ago	Low	Avg	High	Dew	Avg	Max	Gust
49°F	77°F	65°F	0.34 in.	0.37 in.	0.45 in.	79%	92%	100%	63°F	8.5 mph	15 mph	33 mph

DAILY SNAPSHOT

06:00 AM	09:00 AM	12:00 PM	03:00 PM	06:00 PM	09:00 PM
cloudy 63°F	cloudy 70°F	cloudy 76°F	partly-cloudy-day 76°F	cloudy 64°F	partly-cloudy-night 56°F

OBSERVED WEATHER CONDITIONS

No.	Weather Delay	Sky	Temp	Average	Precipitation	Wind	Ground/Sea
1	No						

By _____

Date _____

Copies To _____



Daily Log: Monday 3/4/2019

Daily Log Completed
 The Daily Log was completed by Donald Shelton on Mon Mar 11, 2019 at 09:50 am CDT.

WEATHER REPORT

Temperature			Precipitation Since			Humidity				Windspeed		
Low	High	Avg	Midnight	2 Days Ago	3 Days Ago	Low	Avg	High	Dew	Avg	Max	Gust
39°F	48°F	43°F	0.02 in.	0.36 in.	0.39 in.	60%	76%	89%	36°F	9.7 mph	13 mph	22 mph

DAILY SNAPSHOT

06:00 AM	09:00 AM	12:00 PM	03:00 PM	06:00 PM	09:00 PM
cloudy 40°F	partly-cloudy-day 43°F	partly-cloudy-day 47°F	partly-cloudy-day 48°F	partly-cloudy-night 42°F	partly-cloudy-night 40°F

OBSERVED WEATHER CONDITIONS

No.	Weather Delay	Sky	Temp	Average	Precipitation	Wind	Ground/Sea
1	No	Overcast	Cold	43	0	Light Wind	Dry

MANPOWER LOG

70 Workers | 646.0 Man Hours

No.	Contact/Company	Cost Code	Workers	# Hours	Man Hours	Location
1	A&B Electric Co., Inc.		8	10.0	80.0	Building
Notes: Working on temporary lights 2nd floor, Working on power pack 1st floor, Working on temporary lights, Replace cords and check for right voltage connection. Building print tables.						
2	Bayside Structures, LLC		8	9.0	72.0	Building>D
Notes: Finish rebar for Area D sequence two elevation 115. Installed remaining embeds in Area D elevation 115 on G.7 to G. Worked on moving rebar and cleanup.						
3	Caddell Construction Co. (DE), LLC		9	10.0	90.0	Site
Notes: WGI/Caddell supervision, quality control and safety onsite.						
4	Chavers Construction Inc.		4	10.0	40.0	Site
Notes: Installed 7'x11' meter vault Started plumbing Hauled off two loads of asphalt						
5	Ed Emmons Steel Erectors, Inc.		8	8.0	64.0	Building>C
Notes: Continued installing stingers and landings in stairwell A elevation 115.						


MANPOWER LOG

70 Workers | 646.0 Man Hours

No.	Contact/Company	Cost Code	Workers	# Hours	Man Hours	Location
6	Nash Plumbing and Mechanical, LLC		11	8.0	88.0	Building
<p>Notes: Mechanical- installed pipe hangers and prefabricated pipe in fab shop. Plumbing- laid out for precast wall penetrations.</p>						
7	Tindall Corporation		18	10.0	180.0	Building
<p>Notes: **Crane move into area D, two hours **Patching in area C and corridor between B and D at ground level. **Erecting in are D near dock 195 Total Man Hours</p>						
8	EAA Site Contractors LLC		4	8.0	32.0	Site
<p>Notes: Total man hours 33. EAA continued to dig retention pond today. Established the toe of the pond at the south east corner today</p>						
			70		646.0	


Manpower Log's Attachments:

- 1. A&B Electric Co., Inc.

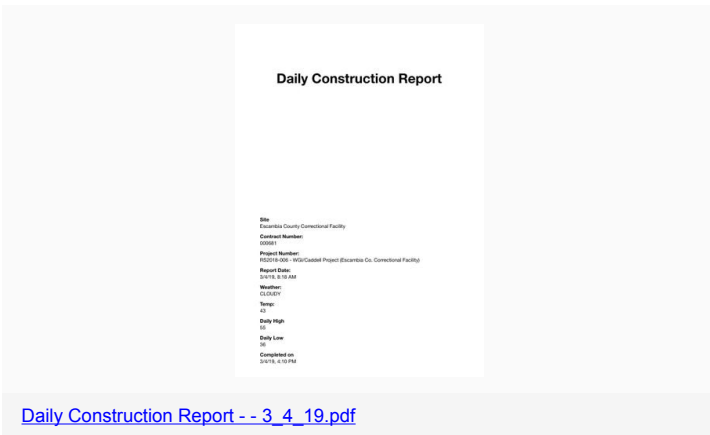

[Daily Construction Report -- 3_4_19.pdf](#)

- 2. Bayside Structures, LLC

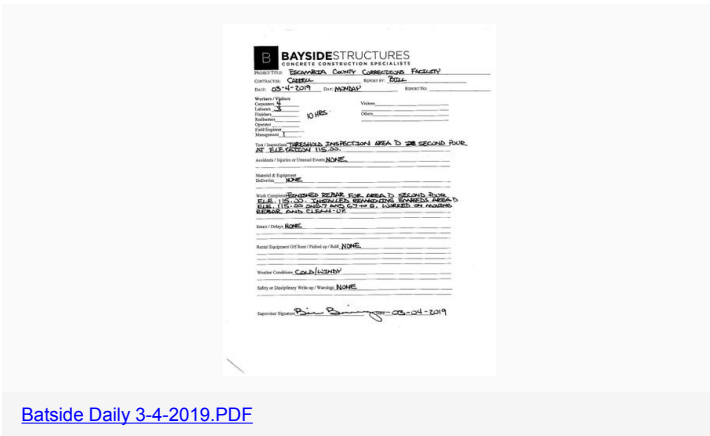

[Batside Daily 3-4-2019.PDF](#)

4. Chavers Construction Inc.

[Chaver Daily 3-4-2019.PDF](#)

5. Ed Emmons Steel Erectors, Inc.

[New Doc 2019-03-04 16.57.08.pdf](#)

6. Nash Plumbing and Mechanical, LLC

[Nash Daily 3-4-2019.xlsx](#)

7. Tindall Corporation

[Tindall Escambia Daily 3-4-2019.xlsx](#)

EQUIPMENT LOG

No.	Equipment Name	Cost Code	Hrs Operating	Hrs Idle	Inspected?	Inspection Time	Location
1	John Deere 750 Dozer				No	07:00 AM	Building>B
	Notes:						
2	Grove Crane AT700D				No	07:00 AM	Building>C
	Notes:						
3	Kobelco Crane CKE2500				No	07:00 AM	Building>D
	Notes:						
4	JLG Lift 660SJ				No	07:00 AM	Building>D
	Notes:						
5	JLG Lift 660SJ				No	07:00 AM	Building>D
	Notes:						
6	Scissor Lift				No	07:00 AM	Building>D
	Notes:						

EQUIPMENT LOG

No.	Equipment Name	Cost Code	Hrs Operating	Hrs Idle	Inspected?	Inspection Time	Location
7	Scissor Lift				No	07:00 AM	Building>D
	Notes:						
8	Scissor Lift				No	07:00 AM	Building
	Notes:						
9	Scissor Lift				No	07:00 AM	Building
	Notes:						
10	Scissor Lift				No	07:00 AM	Building
	Notes:						
11	JLG Skytrak Telehandler				No	07:00 AM	Site
	Notes:						
12	JLG Skytrak Telehandler				No	07:00 AM	Site
	Notes:						
13	Volvo 330 Excavator				No	07:00 AM	Site>Stormwater Pond
	Notes:						
14	Komatsu 320 PT Loader				No	07:00 AM	Site>Stormwater Pond
	Notes:						
15	Terex Articulated Dump Truck				No	07:00 AM	Site>Stormwater Pond
	Notes:						

INSPECTION LOG

No.	Start Time	End Time	Inspection Type	Inspecting Entity	Inspector Name	Location	Area
1	11:30 AM	01:30 PM	Third Party	Mott MacDonald	Mike Tugwell	Building>D	
	Comments: Threshold inspection Area D sequence two at elevation 115.						

By _____

Date _____

Copies To _____



Daily Log: Tuesday 3/5/2019

Daily Log Completed
 The Daily Log was completed by Donald Shelton on Mon Mar 11, 2019 at 09:51 am CDT.

WEATHER REPORT

Temperature			Precipitation Since			Humidity				Windspeed		
Low	High	Avg	Midnight	2 Days Ago	3 Days Ago	Low	Avg	High	Dew	Avg	Max	Gust
34°F	54°F	42°F	0.03 in.	0.04 in.	0.39 in.	28%	60%	97%	27°F	9.1 mph	12 mph	20 mph

DAILY SNAPSHOT

06:00 AM	09:00 AM	12:00 PM	03:00 PM	06:00 PM	09:00 PM
partly-cloudy-night 34°F	clear-day 40°F	clear-day 50°F	clear-day 54°F	clear-night 47°F	clear-night 40°F

OBSERVED WEATHER CONDITIONS

No.	Weather Delay	Sky	Temp	Average	Precipitation	Wind	Ground/Sea
1	No	Cloudy	Cold	42	0	Light Wind	Dry



MANPOWER LOG

81 Workers | 744.0 Man Hours

No.	Contact/Company	Cost Code	Workers	# Hours	Man Hours	Location
1	A&B Electric Co., Inc.		8	10.0	80.0	Building
Notes: Relocate temporary lights on 1st floor corridor, Extend Conduit for bulk Hoist (Material Lift)Have outage to pull jet line, to be ready to pull feeder.						
2	Bayside Structures, LLC		21	9.0	189.0	Building>D
Notes: Poured sequence two in Area D at elevation 115. Worked on removing forms in connector area at stem wall and grade beams. Erected forms at supplemental grade beams H/37 and back filled in 12 inches lift.						
3	Caddell Construction Co. (DE), LLC		9	10.0	90.0	Site
Notes: WGI/Caddell supervision, quality control and safety onsite.						
4	Chavers Construction Inc.		4	9.75	39.0	Site
Notes: Plumb meter vault. Hauled off 1 load of asphalt Cleaned job site.						
5	Ed Emmons Steel Erectors, Inc.		6	8.0	48.0	Building>C
Notes: Continued installing stringers and landing in Stairwell A.						


MANPOWER LOG

81 Workers | 744.0 Man Hours

No.	Contact/Company	Cost Code	Workers	# Hours	Man Hours	Location
6	Larry M. Jacobs & Associates, Inc.		1	2.0	2.0	Building>D
	Notes: Conducted Density Test					
7	Nash Plumbing and Mechanical, LLC		9	8.0	72.0	Building 
	Notes: Mechanical- installed pipe hangers, load test, and prefabricated pipe for corridor. Plumbing- underground rough-in and repair broken pipe.					
8	Tindall Corporation		20	10.0	200.0	Building 
	Notes: **Brush blasting to even panels and remove soils on white product east side of area C. **Patching in area C and D. **Erecting in are D near dock **Grouting and welding 215 Total Man Hours					
9	EAA Site Contractors LLC		3	8.0	24.0	Site
	Notes: Total man hours 30. EAA continued to dig retention pond today. Placed dirt around the outside of section A and B.					
			81		744.0	


Manpower Log's Attachments:

- 1. A&B Electric Co., Inc.

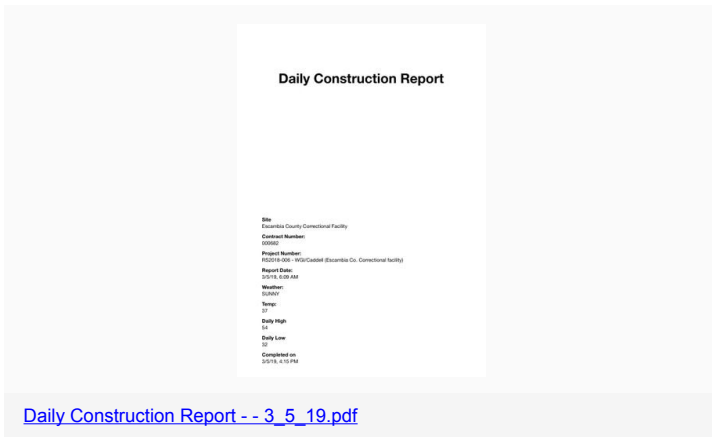

[Daily Construction Report -- 3_5_19.pdf](#)

- 2. Bayside Structures, LLC

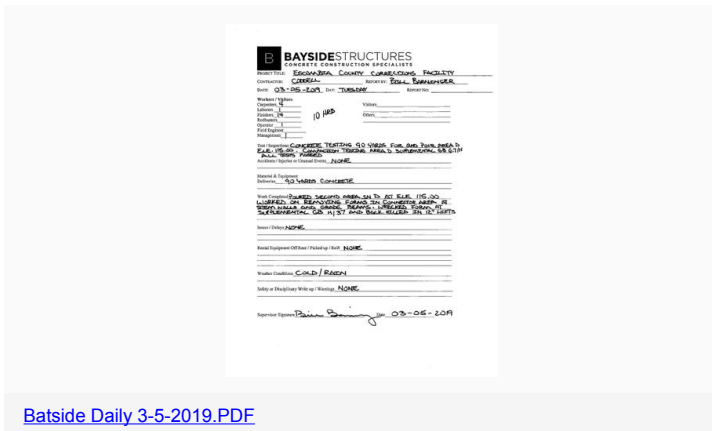

[Batside Daily 3-5-2019.PDF](#)

4. Chavers Construction Inc.

[Chaver Daily 3-5-2019.PDF](#)

5. Ed Emmons Steel Erectors, Inc.

[New Doc 2019-03-05 14.29.02.pdf](#)

7. Nash Plumbing and Mechanical, LLC

[Nash Daily 3-5-2019.xlsx](#)

8. Tindall Corporation

[Tindall Escambia daily 3-5-19.xlsx](#)

EQUIPMENT LOG

No.	Equipment Name	Cost Code	Hrs Operating	Hrs Idle	Inspected?	Inspection Time	Location
1	John Deere 50G Miniexcavator				No	07:00 AM	Building>A
	Notes:						
2	Sky Power Lift 600AJ				No	07:00 AM	Building>C
	Notes:						
3	Grove Crane AT700D				No	07:00 AM	Building>D
	Notes:						
4	Kobelco Crane CKE2500				No	07:00 AM	Building>D
	Notes:						
5	Genie Lift S85				No	07:00 AM	Building>D
	Notes:						

EQUIPMENT LOG

No.	Equipment Name	Cost Code	Hrs Operating	Hrs Idle	Inspected?	Inspection Time	Location
6	JLG Lift 660SJ				No	07:00 AM	Building>D
	Notes:						
7	Bobcat Miniexcavator				No	07:00 AM	Building>D
	Notes:						
8	John Deere 85G Excavator				No	07:00 AM	Site
	Notes:						
9	JLG Skytrak Telehandler				No	07:00 AM	Site
	Notes:						
10	JLG Skytrak Telehandler				No	07:00 AM	Site
	Notes:						
11	Kubota Skidsteer				No	07:00 AM	Site
	Notes:						
12	Volvo 330 Excavator				No	07:00 AM	Site>Stormwater Pond
	Notes:						
13	Daewoo 220 Excavator				No	07:00 AM	Site>Stormwater Pond
	Notes:						
14	John Deere 300G Excavator				No	07:00 AM	Site
	Notes:						

By _____

Date _____

Copies To _____



Daily Log: Wednesday 3/6/2019

Daily Log Completed
 The Daily Log was completed by Donald Shelton on Mon Mar 11, 2019 at 09:52 am CDT.

WEATHER REPORT

Temperature			Precipitation Since			Humidity				Windspeed		
Low	High	Avg	Midnight	2 Days Ago	3 Days Ago	Low	Avg	High	Dew	Avg	Max	Gust
29°F	56°F	42°F	0.00 in.	0.03 in.	0.05 in.	24%	49%	95%	22°F	5.5 mph	10 mph	25 mph

DAILY SNAPSHOT

06:00 AM	09:00 AM	12:00 PM	03:00 PM	06:00 PM	09:00 PM
clear-night 30°F	clear-day 41°F	clear-day 50°F	clear-day 56°F	partly-cloudy-night 51°F	clear-night 40°F

OBSERVED WEATHER CONDITIONS

No.	Weather Delay	Sky	Temp	Average	Precipitation	Wind	Ground/Sea
1	No	Clear	Cold	42	0	Light Wind	Dry




MANPOWER LOG

67 Workers | 620.0 Man Hours

No.	Contact/Company	Cost Code	Workers	# Hours	Man Hours	Location	
1	A&B Electric Co., Inc.		7	10.0	70.0	Building	
Notes: Working on feeder for bulk Hoist, Working on 120volt Power for bulk Hoist, Working on temporary power 1st. Floor, Working on layout of normal & Emergency lighting circuits, Running conduit for lighting circuits on 1st floor corridor.							
2	Bayside Structures, LLC		6	10.0	60.0	Site	
Notes: Excavated two 3P-65 Pile Caps on new jail side. Tied 4 Pile Caps mats for 3P-65's. Finished form removal at connector and stem wall.							
3	Caddell Construction Co. (DE), LLC		9	10.0	90.0	Site	
Notes: WGI/Caddell supervision, quality control and safety onsite.							
4	Chavers Construction Inc.		4	9.75	39.0	Site	
Notes: Set back flow for water line back-fill county right of way with rock for DOT set up safety fence.							

MANPOWER LOG

67 Workers | 620.0 Man Hours

No.	Contact/Company	Cost Code	Workers	# Hours	Man Hours	Location	
5	Ed Emmons Steel Erectors, Inc.		7	8.0	56.0	Building>A	
Notes: Continued erecting Stairwell A.							
6	Larry M. Jacobs & Associates, Inc.		1	1.0	1.0	Building>D	
Notes: Conducted Density Test							
7	Nash Plumbing and Mechanical, LLC		9	8.0	72.0	Building	
Notes: Mechanical- installed pipe hangers and prefabricated pipe for corridor. Plumbing- underground rough-in and repairs to broken pipe.							
8	Tindall Corporation		20	10.0	200.0	Building	
Notes: **Brush blasting to even panels and remove soils on white product east side of area C. **Patching in area C and D. **Erecting in are D near dock **Grouting and welding 215 Total Man Hours							
9	EAA Site Contractors LLC		4	8.0	32.0	Site	
Notes: Total man hours 38. EAA continued to dig retention pond today. Moved dirt and topsoil off site.							
			67		620.0		

Manpower Log's Attachments:

- 1. A&B Electric Co., Inc.



[Daily Construction Report -- 3_6_19.pdf](#)

EQUIPMENT LOG

No.	Equipment Name	Cost Code	Hrs Operating	Hrs Idle	Inspected?	Inspection Time	Location
1	John Deere 50G Miniexcavator				No	07:00 AM	Building>A
	Notes:						
2	JLG Lift 860SJ				No	07:00 AM	Building>C
	Notes:						
3	Grove Crane AT700D				No	07:00 AM	Building>C
	Notes:						
4	Kobelco Crane CKE2500				No	07:00 AM	Building>D
	Notes:						
5	Genie Lift S85				No	07:00 AM	Building>D
	Notes:						
6	JLG Lift 660SJ				No	07:00 AM	Building>D
	Notes:						
7	Bobcat Miniexcavator				No	07:00 AM	Building>D
	Notes:						
8	Scissor Lift				No	07:00 AM	Building
	Notes:						
9	Scissor Lift				No	07:00 AM	Building
	Notes:						
10	Scissor Lift				No	07:00 AM	Building
	Notes:						
11	Scissor Lift				No	07:00 AM	Building
	Notes:						
12	Scissor Lift				No	07:00 AM	Building
	Notes:						
13	JLG Skytrak Telehandler				No	07:00 AM	Site
	Notes:						
14	JLG Skytrak Telehandler				No	07:00 AM	Site
	Notes:						
15	Kubota Skidsteer				No	07:00 AM	Site
	Notes:						
16	John Deere 85G Excavator				No	07:00 AM	Site
	Notes:						
17	Volvo 330 Excavator				No	07:00 AM	Site>Stormwater Pond
	Notes:						
18	Daewoo 220 Excavator				No	07:00 AM	Site>Stormwater Pond
	Notes:						

By _____

Date _____

Copies To _____



Daily Log: Thursday 3/7/2019

Daily Log Completed
 The Daily Log was completed by Donald Shelton on Mon Mar 11, 2019 at 09:53 am CDT.

WEATHER REPORT

Temperature			Precipitation Since			Humidity				Windspeed		
Low	High	Avg	Midnight	2 Days Ago	3 Days Ago	Low	Avg	High	Dew	Avg	Max	Gust
32°F	63°F	50°F	0.00 in.	0.00 in.	0.03 in.	41%	66%	95%	38°F	5.3 mph	9 mph	13 mph

DAILY SNAPSHOT

06:00 AM	09:00 AM	12:00 PM	03:00 PM	06:00 PM	09:00 PM
clear-night 33°F	clear-day 53°F	clear-day 62°F	partly-cloudy-day 62°F	cloudy 57°F	cloudy 55°F

OBSERVED WEATHER CONDITIONS

No.	Weather Delay	Sky	Temp	Average	Precipitation	Wind	Ground/Sea
1	No	Clear	Mild	50	0	Light Wind	Dry

MANPOWER LOG

71 Workers | 672.24 Man Hours

No.	Contact/Company	Cost Code	Workers	# Hours	Man Hours	Location
1	A&B Electric Co., Inc.		7	10.0	70.0	Building
Notes: Rough in normal & Emergency lighting conduit in 1st floor corridor						
2	Bayside Structures, LLC		9	10.0	90.0	Site
Notes: Formed and installed rebar for two pile caps at connector next to new jail on center line T. Worked on general cleanup.						
3	Caddell Construction Co. (DE), LLC		9	10.66	95.94	Site
Notes: WGI/Caddell supervision, quality control and safety onsite.						
4	Chavers Construction Inc.		5	10.66	53.3	Site
Notes: Install 40' of domestic water main 8". Laid 60' of firewater main. Poured concrete kicker for back flow. Poured 1 sq.yd. concrete for sidewalk 12'x6'x5 Thick.						
5	Ed Emmons Steel Erectors, Inc.		8	8.0	64.0	Building>A
Notes: Continued working on Stairwell A.						
6	Larry M. Jacobs & Associates, Inc.		1	7.0	7.0	Building>A
Notes: Inspecting welds in Stairwell A						

MANPOWER LOG

71 Workers | 672.24 Man Hours

No.	Contact/Company	Cost Code	Workers	# Hours	Man Hours	Location
7	Nash Plumbing and Mechanical, LLC		9	8.0	72.0	Building
Notes: Mechanical- installed pipe hangers and prefabricated pipe for corridor. Plumbing- underground rough-in.						
8	Tindall Corporation		18	10.0	180.0	Building
Notes: **White panels being touched up **Patching in area C and D. **Erecting along line T in area D. **Grouting and welding						
9	EAA Site Contractors LLC		5	8.0	40.0	Site
Notes: Total man hours 50. EAA continued to dig retention pond today. Moved dirt off site. Regraded pad for crane outside of section D. Also graded and compacted area near connector for concrete truck						
			71		672.24	

Manpower Log's Attachments:

1. A&B Electric Co., Inc.



[Daily Construction Report -- 3_7_19.pdf](#)

2. Bayside Structures, LLC



[Bayside Daily 3-7-2019.PDF](#)

4. Chavers Construction Inc.

[Chaver Daily 3-7-2019.PDF](#)

5. Ed Emmons Steel Erectors, Inc.

[New Doc 2019-03-07 14.49.34.pdf](#)

7. Nash Plumbing and Mechanical, LLC

[Nash Daily 3-7-2019.xlsx](#)

8. Tindall Corporation

[Tindall Escambia daily 3-7-19.xlsx](#)

EQUIPMENT LOG

No.	Equipment Name	Cost Code	Hrs Operating	Hrs Idle	Inspected?	Inspection Time	Location
1	John Deere 85G Excavator				No	07:00 AM	Building>A
	Notes:						
2	Komatsu 320 PT Loader				No	07:00 AM	Building>A
	Notes:						
3	JLG Lift 860SJ				No	07:00 AM	Building>C
	Notes:						
4	Grove Crane AT700D				No	07:00 AM	Building>C
	Notes:						
5	Kobelco Crane CKE2500				No	07:00 AM	Building>D
	Notes:						
6	Genie Lift S85				No	07:00 AM	Building>D
	Notes:						

EQUIPMENT LOG

No.	Equipment Name	Cost Code	Hrs Operating	Hrs Idle	Inspected?	Inspection Time	Location
7	JLG Lift 660SJ				No	07:00 AM	Building>D
	Notes:						
8	Scissor Lift				No	07:00 AM	Building>D
	Notes:						
9	Scissor Lift				No	07:00 AM	Building>D
	Notes:						
10	Scissor Lift				No	07:00 AM	Building>D
	Notes:						
11	Scissor Lift				No	07:00 AM	Building>D
	Notes:						
12	Scissor Lift				No	07:00 AM	Building>D
	Notes:						
13	Kubota Skidsteer				No	07:00 AM	Site
	Notes:						
14	JLG Skytrak Telehandler				No	07:00 AM	Site
	Notes:						
15	JLG Skytrak Telehandler				No	07:00 AM	Site
	Notes:						
16	Daewoo 220 Excavator				No	07:00 AM	Site>Stormwater Pond
	Notes:						
17	Volvo 330 Excavator				No	07:00 AM	Site>Stormwater Pond
	Notes:						
18	John Deere 750 Dozer				No	07:00 AM	Site>Stormwater Pond
	Notes:						
19	Bobcat Miniexcavator				No	07:00 AM	Site
	Notes:						

By _____

Date _____

Copies To _____



Daily Log: Friday 3/8/2019

Daily Log Completed
 The Daily Log was completed by Donald Shelton on Mon Mar 11, 2019 at 08:53 am CDT.

WEATHER REPORT

Temperature			Precipitation Since			Humidity				Windspeed		
Low	High	Avg	Midnight	2 Days Ago	3 Days Ago	Low	Avg	High	Dew	Avg	Max	Gust
57°F	73°F	65°F	0.00 in.	0.00 in.	0.01 in.	56%	76%	94%	57°F	7.2 mph	11 mph	17 mph

DAILY SNAPSHOT

06:00 AM	09:00 AM	12:00 PM	03:00 PM	06:00 PM	09:00 PM
cloudy 59°F	cloudy 69°F	partly-cloudy-day 74°F	partly-cloudy-day 72°F	partly-cloudy-night 68°F	partly-cloudy-night 64°F

OBSERVED WEATHER CONDITIONS

No.	Weather Delay	Sky	Temp	Average	Precipitation	Wind	Ground/Sea
1	No	Cloudy	Mild	65	0	Light Wind	Dry



MANPOWER LOG

68 Workers | 611.62 Man Hours

No.	Contact/Company	Cost Code	Workers	# Hours	Man Hours	Location
1	EAA Site Contractors LLC		3	8.0	24.0	Site
Notes: Total man hours 17. EAA continued to dig retention pond today. Hauled dirt off site						
2	A&B Electric Co., Inc.		6	10.0	60.0	Building
Notes: Working on 120 volt Power for Bulk Hoist & 480 volt power for bulk Hoist, Working on normal and Emergency lighting conduit on 1st floor corridor.						
3	Bayside Structures, LLC		9	7.0	63.0	Building
Notes: Poured 18 sq. yd. at connector P3-65T pile caps at T line. Moved rebar for Tindall at Line 50. Erected bulkhead at center line 37 elevation 115 Area D. Erected embed forms at elevation 115 from second pour worked on cleanup at connector.						
4	Caddell Construction Co. (DE), LLC		9	10.33	92.97	Site
Notes: WGI/Caddell supervision, quality control and safety onsite.						
5	Chavers Construction Inc.		5	10.33	51.65	Site
Notes: Mobilized for 36" pipe between boxes 23 and 24. Back-filled and compacted trench for water and fire main. Cleaned right of way.						
6	Ed Emmons Steel Erectors, Inc.		7	8.0	56.0	Building>C
Notes: Topped and welded out, ready for concrete in Stairwell A. All connections to stringers are 100% welded.						

MANPOWER LOG

68 Workers | 611.62 Man Hours

No.	Contact/Company	Cost Code	Workers	# Hours	Man Hours	Location
7	Larry M. Jacobs & Associates, Inc.		1	6.0	6.0	Site
Notes: Conduct density test and checked weld on structural steel and precast.						
8	Nash Plumbing and Mechanical, LLC		11	8.0	88.0	Building 
Notes: Mechanical- Installed hangers for chw, hhw pipe and prefabricated pipe for corridor. Plumbing- Underground rough-in in Area A.						
9	Tindall Corporation		17	10.0	170.0	Building>D 
Notes: **Patching in area D. **Erecting in D along line 50 **Grouting and welding 177.5 Total Man Hours						
			68	611.62		

Manpower Log's Attachments:

2. A&B Electric Co., Inc.



[Daily Construction Report -- 3_8_19.pdf](#)

3. Bayside Structures, LLC



[Bayside Daily 3-8-2019.PDF](#)

5. Chavers Construction Inc.

[Chaver Daily 3-8-2019.PDF](#)

6. Ed Emmons Steel Erectors, Inc.

[New Doc 2019-03-08 14.50.33.pdf](#)

8. Nash Plumbing and Mechanical, LLC

[Nash Daily 3-8-2019.xlsx](#)

9. Tindall Corporation

[Tindall Escambia Daily 3-8-2019.xlsx](#)

EQUIPMENT LOG

No.	Equipment Name	Cost Code	Hrs Operating	Hrs Idle	Inspected?	Inspection Time	Location
1	John Deere 50G Miniexcavator				No	07:00 AM	Building>A
Notes:							
2	JLG Lift 660SJ				No	07:00 AM	Building>A
Notes:							
3	Grove Crane AT700D				No	07:00 AM	Building>C
Notes:							
4	Kobelco Crane CKE2500				No	07:00 AM	Building>D
Notes:							
5	Genie Lift S85				No	07:00 AM	Building>D
Notes:							

EQUIPMENT LOG

No.	Equipment Name	Cost Code	Hrs Operating	Hrs Idle	Inspected?	Inspection Time	Location
6	JLG Lift 660SJ				No	07:00 AM	Building>D
	Notes:						
7	JLG Lift 660SJ				No	07:00 AM	Building>D
	Notes:						
8	Scissor Lift				No	07:00 AM	Building
	Notes:						
9	Scissor Lift				No	07:00 AM	Building
	Notes:						
10	Scissor Lift				No	07:00 AM	Building
	Notes:						
11	Scissor Lift				No	07:00 AM	Building
	Notes:						
12	Scissor Lift				No	07:00 AM	Building
	Notes:						
13	Bobcat Miniexcavator				No	07:00 AM	Site
	Notes:						
14	Kubota Skidsteer				No	07:00 AM	Site
	Notes:						
15	John Deere 85G Excavator				No	07:00 AM	Site
	Notes:						
16	Daewoo 220 Excavator				No	07:00 AM	Site>Stormwater Pond
	Notes:						
17	Volvo 330 Excavator				No	07:00 AM	Site>Stormwater Pond
	Notes:						
18	John Deere 300G Excavator				No	07:00 AM	Site>Stormwater Pond
	Notes:						

By _____

Date _____

Copies To _____



Whitesell Green / Caddell, a Joint Venture
 2700 Lagoon Park Drive
 Montgomery, Alabama 36109
 P: (334) 272-7723
 F: (334) 394-0193

Project: 1054 - Escambia County Correctional Facility
 3080 N. Pace Boulevard
 Pensacola, Florida 32501

Daily Log: Saturday 3/9/2019

Daily Log Completed
 The Daily Log was completed by Donald Shelton on Mon Mar 11, 2019 at 09:48 am CDT.

WEATHER REPORT

Temperature			Precipitation Since			Humidity				Windspeed		
Low	High	Avg	Midnight	2 Days Ago	3 Days Ago	Low	Avg	High	Dew	Avg	Max	Gust
61°F	76°F	68°F	0.00 in.	0.01 in.	0.01 in.	67%	89%	100%	64°F	8.6 mph	15 mph	22 mph

DAILY SNAPSHOT

06:00 AM	09:00 AM	12:00 PM	03:00 PM	06:00 PM	09:00 PM
partly-cloudy-night 65°F	partly-cloudy-day 72°F	partly-cloudy-day 77°F	partly-cloudy-day 72°F	partly-cloudy-night 68°F	clear-night 66°F

OBSERVED WEATHER CONDITIONS

No.	Weather Delay	Sky	Temp	Average	Precipitation	Wind	Ground/Sea
1	No	Cloudy	Mild	68	0	Light Wind	Dry

MANPOWER LOG

19 Workers | 184.0 Man Hours

No.	Contact/Company	Cost Code	Workers	# Hours	Man Hours	Location
1	Caddell Construction Co. (DE), LLC		1	10.0	10.0	Site
Notes: WGI/Caddell supervision, quality control and safety onsite.						
2	Chavers Construction Inc.		3	8.0	24.0	Site>Stormwater Pond
Notes: Excavated for storm pipe. Install silt fence.						
3	Tindall Corporation		15	10.0	150.0	Building
Notes: **Move crane from D to B to continue corridor **Erecting on G and G.7 lines **Grouting and welding						
			19	184.0		

Manpower Log's Attachments:

2. Chavers Construction Inc.

Chavers Construction, Inc.
Daily Report

Date: 3/9/2019
Location: Whitesell Green / Caddell

Equipment: Kobelco Crane CKE2500, Genie Lift S85, JLG Lift 660SJ, JLG Skytrak Telehandler, John Deere 300G Excavator

Notes: Wash site fence

[Chaver Daily 3-9-2019.PDF](#)

3. Tindall Corporation

[Tindall Escambia daily 3-9-19.xlsx](#)

EQUIPMENT LOG

No.	Equipment Name	Cost Code	Hrs Operating	Hrs Idle	Inspected?	Inspection Time	Location
1	Kobelco Crane CKE2500				No	07:00 AM	Building
	Notes:						
2	Genie Lift S85				No	07:00 AM	Building
	Notes:						
3	JLG Lift 660SJ				No	07:00 AM	Building
	Notes:						
4	JLG Skytrak Telehandler				No	07:00 AM	Site
	Notes:						
5	John Deere 300G Excavator				No	07:00 AM	Site>Stormwater Pond
	Notes:						

By _____

Date _____

Copies To _____



Whitesell Green / Caddell, a Joint Venture
 2700 Lagoon Park Drive
 Montgomery, Alabama 36109
 P: (334) 272-7723
 F: (334) 394-0193

Project: 1054 - Escambia County Correctional
Facility
 3080 N. Pace Boulevard
 Pensacola, Florida 32501

Daily Log: Sunday 3/10/2019

WEATHER REPORT

Temperature			Precipitation Since			Humidity				Windspeed		
Low	High	Avg	Midnight	2 Days Ago	3 Days Ago	Low	Avg	High	Dew	Avg	Max	Gust
65°F	75°F	70°F	0.10 in.	0.10 in.	0.11 in.	74%	89%	100%	66°F	5.8 mph	7 mph	11 mph

DAILY SNAPSHOT

07:00 AM	10:00 AM	01:00 PM	04:00 PM	07:00 PM	10:00 PM
cloudy 68°F	partly-cloudy-day 71°F	partly-cloudy-day 75°F	partly-cloudy-day 76°F	partly-cloudy-night 70°F	partly-cloudy-night 67°F

OBSERVED WEATHER CONDITIONS

No.	Weather Delay	Sky	Temp	Average	Precipitation	Wind	Ground/Sea
1	No						

By _____

Date _____

Copies To _____



Daily Log: Monday 3/11/2019

Daily Log Completed
 The Daily Log was completed by Donald Shelton on Mon Mar 18, 2019 at 09:00 am CDT.

WEATHER REPORT

Temperature			Precipitation Since			Humidity				Windspeed		
Low	High	Avg	Midnight	2 Days Ago	3 Days Ago	Low	Avg	High	Dew	Avg	Max	Gust
60°F	82°F	70°F	0.04 in.	0.14 in.	0.14 in.	71%	90%	100%	67°F	5.1 mph	9 mph	21 mph

DAILY SNAPSHOT

06:00 AM	09:00 AM	12:00 PM	03:00 PM	06:00 PM	09:00 PM
fog 67°F	fog 70°F	partly-cloudy-day 79°F	partly-cloudy-day 83°F	partly-cloudy-day 71°F	partly-cloudy-night 64°F

OBSERVED WEATHER CONDITIONS

No.	Weather Delay	Sky	Temp	Average	Precipitation	Wind	Ground/Sea
1	No	Cloudy	Mild	70	0	Light Wind	Dry




MANPOWER LOG

72 Workers | 685.0 Man Hours

No.	Contact/Company	Cost Code	Workers	# Hours	Man Hours	Location
1	EAA Site Contractors LLC		3	8.0	24.0	Site
Notes: Total man hours 30. EAA continued to dig retention pond today. Dirt was hauled off site.						
2	A&B Electric Co., Inc.		9	9.0	81.0	Building
Notes: Started running conduit for em. and normal power lighting in corridor on 2nd floor, started studying and laying out in slab and overhead conduit runs. Installed temp lights in stair case A.						
3	Bayside Structures, LLC		8	10.0	80.0	Building
Notes: Moved all materials stored in the corridor area at elevation 115.00 so Tindall can set panels. Continued removing bad forms from the job site. Placed W.W.M in all landings in stairwell A. for tomorrow's pour. Removed forms from P.2 65T pile caps in the connector at T line. Backfilled at pile caps in one foot lifts and compacted.						
4	Caddell Construction Co. (DE), LLC		9	10.0	90.0	Site
Notes: WGI/Caddell supervision, quality control and safety onsite.						
5	Chavers Construction Inc.		4	10.0	40.0	Site>Stormwater Pond
Notes: Worked on Storm water between Boxes 23 and 24.						

MANPOWER LOG

72 Workers | 685.0 Man Hours

No.	Contact/Company	Cost Code	Workers	# Hours	Man Hours	Location	
6	Ed Emmons Steel Erectors, Inc.		7	10.0	70.0	Building	
<p>Notes: Moved crane, punch list, and worked on Stairwell A. Started elevation 115 steel at south end.</p>							
7	Nash Plumbing and Mechanical, LLC		10	8.0	80.0	Building	
<p>Notes: Mechanical- Install pipe hangers Mechanical- Prefabricated piping for corridor Plumbing- Underground rough-in in Area C</p>							
8	Tindall Corporation		22	10.0	220.0	Building	
<p>Notes: **Touching up white panels in area D. **Erecting on G and G.7 lines **Grouting and welding **Patching in area D 230 Total Man Hours</p>							
			72		685.0		

Manpower Log's Attachments:

2. A&B Electric Co., Inc.

Daily Construction Report

Site
 Escambia County Correctional Facility
 Contract Number
 00001
 Project Number
 00-000-0001
 Report Date
 3/11/19, 4:53 PM
 Weather
 82/60°
 Type
 77
 Study High
 78
 Study Low
 68
 Completed on
 3/11/19, 4:11 PM

[Daily Construction Report -- 3_11_19.pdf](#)

3. Bayside Structures, LLC

 [Bayside Daily 3-11-2019.docx](#)

5. Chavers Construction Inc.

[Chaver Daily 3-11-2019.PDF](#)

6. Ed Emmons Steel Erectors, Inc.

[New Doc 2019-03-11 18.53.51.pdf](#)

7. Nash Plumbing and Mechanical, LLC

[Nash Daily 3-11-2019.xlsx](#)

8. Tindall Corporation

[Tindall Escambia daily 3-11-19.xlsx](#)

EQUIPMENT LOG

No.	Equipment Name	Cost Code	Hrs Operating	Hrs Idle	Inspected?	Inspection Time	Location
1	JLG Lift 660SJ				No	07:00 AM	Building>A
	Notes:						
2	Kobelco Crane CKE2500				No	07:00 AM	Building>B
	Notes:						
3	JLG Lift 660SJ				No	07:00 AM	Building>B
	Notes:						
4	Genie Lift S85				No	07:00 AM	Building>B
	Notes:						
5	John Deere 50G Miniexcavator				No	07:00 AM	Building>C
	Notes:						

EQUIPMENT LOG

No.	Equipment Name	Cost Code	Hrs Operating	Hrs Idle	Inspected?	Inspection Time	Location
6	JLG Lift 860SJ				No	07:00 AM	Building>D
	Notes:						
7	Grove Crane AT700D				No	07:00 AM	Building>D
	Notes:						
8	Sky Power Lift 600AJ				No	07:00 AM	Building>D
	Notes:						
9	John Deere 300G Excavator				No	07:00 AM	Site>Stormwater Pond
	Notes:						
10	Doosan Loader				No	07:00 AM	Site>Stormwater Pond
	Notes:						
11	Kubota Skidsteer				No	07:00 AM	Site>Stormwater Pond
	Notes:						
12	Volvo 330 Excavator				No	07:00 AM	Site>Stormwater Pond
	Notes:						
13	John Deere 750 Dozer				No	07:00 AM	Site>Stormwater Pond
	Notes:						
14	Komatsu 320 PT Loader				No	07:00 AM	Site>Stormwater Pond
	Notes:						
15	JLG Skytrak Telehandler				No	07:00 AM	Site
	Notes:						
16	JLG Skytrak Telehandler				No	07:00 AM	Site
	Notes:						
17	JLG Skytrak Telehandler				No	07:00 AM	Site
	Notes:						
18	Cat Telehandler				No	07:00 AM	Site
	Notes:						
19	Bobcat Miniexcavator				No	07:00 AM	Site
	Notes:						

By _____

Date _____

Copies To _____



Daily Log: Tuesday 3/12/2019

Daily Log Completed
 The Daily Log was completed by Donald Shelton on Mon Mar 18, 2019 at 09:35 am CDT.

WEATHER REPORT

Temperature			Precipitation Since			Humidity				Windspeed		
Low	High	Avg	Midnight	2 Days Ago	3 Days Ago	Low	Avg	High	Dew	Avg	Max	Gust
53°F	75°F	62°F	0.00 in.	0.04 in.	0.14 in.	48%	78%	100%	54°F	5.6 mph	8 mph	12 mph

DAILY SNAPSHOT

06:00 AM	09:00 AM	12:00 PM	03:00 PM	06:00 PM	09:00 PM
partly-cloudy-night 54°F	partly-cloudy-day 60°F	partly-cloudy-day 71°F	partly-cloudy-day 75°F	partly-cloudy-day 69°F	partly-cloudy-night 61°F

OBSERVED WEATHER CONDITIONS

No.	Weather Delay	Sky	Temp	Average	Precipitation	Wind	Ground/Sea
1	No	Cloudy	Mild	62	0	Light Wind	Dry

MANPOWER LOG

80 Workers | 748.0 Man Hours

No.	Contact/Company	Cost Code	Workers	# Hours	Man Hours	Location
1	EAA Site Contractors LLC		4	8.0	32.0	Site
Notes: Total man hours 40. EAA continued to dig retention pond today. We also took out the topsoil and concrete in the island of old entrance off ST Mary. Replaced with crushed concrete. Also started removing the topsoil on the south side of the bldg. This will be replaced with structural fill.						
2	A&B Electric Co., Inc.		9	10.0	90.0	Building
Notes: Rough in on 2nd floor corridor, Running conduit for normal & Emergency lighting circuits.						
3	Bayside Structures, LLC		15	10.0	150.0	Site
Notes: Poured stairwell A from top to bottom. Laid out and formed four piers over P2 pile caps for grade beam over easement at connector. Tied rebar for four piers at connector. Laid out and started drilling for dowels connecting grade beam on T line to grade beam at connector. Started cleaning precast in corridor at elevation 100.00 from 3 line to 14 line.						
4	Caddell Construction Co. (DE), LLC		9	10.0	90.0	Site
Notes: WGI/Caddell supervision, quality control and safety onsite.						
5	Chavers Construction Inc.		4	10.0	40.0	Site>Stormwater Pond
Notes: Installed 3 sticks of 36" storm pipe. Mud pipe to box 24.						

MANPOWER LOG

80 Workers | 748.0 Man Hours

No.	Contact/Company	Cost Code	Workers	# Hours	Man Hours	Location
6	Ed Emmons Steel Erectors, Inc.		8	7.0	56.0	Building>D
Notes: Hung out and decked to elevation 115 at south end. Set up stud generator and welder and moved crane.						
7	Nash Plumbing and Mechanical, LLC		10	8.0	80.0	Building
Notes: Installed hangers for piping Prefab piping for corridor Underground rough-in Area C						
8	Tindall Corporation		21	10.0	210.0	Building
Notes: **Touching up white panels in area D. **Erecting on G and G.7 lines **Grouting and welding **Patching in area D 218 Total Man Hours						
			80		748.0	

Manpower Log's Attachments:

2. A&B Electric Co., Inc.




[Daily Construction Report -- 3_12_19.pdf](#)

3. Bayside Structures, LLC


[Bayside Daily 3-12-2019.docx](#)

5. Chavers Construction Inc.



[Chaver Daily 3-12-2019.PDF](#)

6. Ed Emmons Steel Erectors, Inc.



[New Doc 2019-03-12 19.15.10.pdf](#)

7. Nash Plumbing and Mechanical, LLC

[Nash Daily 3-12-2019.xlsx](#)

8. Tindall Corporation

[Tindall Escambia daily 3-12-19.xlsx](#)

EQUIPMENT LOG

No.	Equipment Name	Cost Code	Hrs Operating	Hrs Idle	Inspected?	Inspection Time	Location
1	Kobelco Crane CKE2500				No	07:00 AM	Building>B
	Notes:						
2	Genie Lift S85				No	07:00 AM	Building>B
	Notes:						
3	JLG Lift 660SJ				No	07:00 AM	Building>B
	Notes:						
4	John Deere 50G Miniexcavator				No	07:00 AM	Building>C
	Notes:						
5	Grove Crane AT700D				No	07:00 AM	Building>D
	Notes:						
6	JLG Lift 860SJ				No	07:30 AM	Building>D
	Notes:						
7	Sky Power Lift 600AJ				No	07:00 AM	Building>D
	Notes:						
8	JLG Skytrak Telehandler				No	07:00 AM	Site
	Notes:						
9	JLG Skytrak Telehandler				No	07:00 AM	Site
	Notes:						
10	JLG Skytrak Telehandler				No	07:00 AM	Site
	Notes:						
11	Cat Telehandler				No	07:00 AM	Site
	Notes:						

EQUIPMENT LOG

No.	Equipment Name	Cost Code	Hrs Operating	Hrs Idle	Inspected?	Inspection Time	Location
12	John Deere 300G Excavator				No	07:00 AM	Site>Stormwater Pond
Notes:							
13	Kubota Skidsteer				No	07:00 AM	Site>Stormwater Pond
Notes:							
14	Volvo 330 Excavator				No	07:00 AM	Site>Stormwater Pond
Notes:							
15	Komatsu 320 PT Loader				No	07:00 AM	Site>Stormwater Pond
Notes:							
16	John Deere 750 Dozer				No	07:00 AM	Site>Stormwater Pond
Notes:							

By

Date

Copies To



Daily Log: Wednesday 3/13/2019

Daily Log Completed
 The Daily Log was completed by Donald Shelton on Mon Mar 18, 2019 at 09:49 am CDT.

WEATHER REPORT

Temperature			Precipitation Since			Humidity				Windspeed		
Low	High	Avg	Midnight	2 Days Ago	3 Days Ago	Low	Avg	High	Dew	Avg	Max	Gust
58°F	74°F	66°F	0.02 in.	0.02 in.	0.06 in.	72%	88%	100%	63°F	12.6 mph	17 mph	29 mph

DAILY SNAPSHOT

06:00 AM	09:00 AM	12:00 PM	03:00 PM	06:00 PM	09:00 PM
partly-cloudy-night 64°F	cloudy 67°F	wind 71°F	cloudy 74°F	cloudy 70°F	wind 68°F

OBSERVED WEATHER CONDITIONS

No.	Weather Delay	Sky	Temp	Average	Precipitation	Wind	Ground/Sea
1	No	Overcast	Mild	66	0	Light Wind	Dry

MANPOWER LOG

75 Workers | 698.0 Man Hours

No.	Contact/Company	Cost Code	Workers	# Hours	Man Hours	Location
1	EAA Site Contractors LLC		4	8.0	32.0	Site
Notes: Total man hours 40. EAA continued to dig retention pond today. We also completed the removal of most of the topsoil along the south side of bldg. We started replacing the topsoil with structural fill.						
2	A&B Electric Co., Inc.		10	10.0	100.0	Building
Notes: Rough In Electrical conduits for Emergency and Normal lighting circuits, Rework Electrical feeder conduit for bulk Hoist, (Dirt contractor removing all top soil dirt that was put in)						
3	Bayside Structures, LLC		9	10.0	90.0	Building
Notes: We installed all 6x6 W.W.M in corridor at elevation 100.00' in area A from column line 3 to column line 14. We installed all #5 rebar for topping slab in corridor on elevation 100.00. Started cleaning stair pans in stairwell A. Worked on piers at connector for grade beam at easement . Continued working on trash and removing unusable forms.						
4	Caddell Construction Co. (DE), LLC		9	10.0	90.0	Site
Notes: WGI/Caddell supervision, quality control and safety onsite.						
5	Chavers Construction Inc.		4	10.0	40.0	Site>Stormwater Pond
Notes: Set Box 24. Installed 24' of 36" RCP						

MANPOWER LOG

75 Workers | 698.0 Man Hours

No.	Contact/Company	Cost Code	Workers	# Hours	Man Hours	Location
6	Ed Emmons Steel Erectors, Inc.		8	7.0	56.0	Building>D
Notes: Studs and closures at elevation 115 south deck. Received and unloaded one load of columns and beams.						
7	Nash Plumbing and Mechanical, LLC		10	8.0	80.0	Building
Notes: Installed pipe hangers Prefab pipe for corridors Underground rough-in						
8	Tindall Corporation		21	10.0	210.0	Building
Notes: **Continue touching up white panels in area D. **Erecting on G and G.7 lines **Grouting and welding **Patching in area D @ elevation 115. 218 Total Man Hours						
			75		698.0	

Manpower Log's Attachments:

2. A&B Electric Co., Inc.




[Daily Construction Report -- 3_13_19.pdf](#)

3. Bayside Structures, LLC


[Bayside Daily 3-13-2019.docx](#)

5. Chavers Construction Inc.



[Chaver Daily 3-13-2019.PDF](#)

6. Ed Emmons Steel Erectors, Inc.



[New Doc 2019-03-13 14.59.03.pdf](#)

7. Nash Plumbing and Mechanical, LLC

[Nash Daily 3-13-2019.xlsx](#)

8. Tindall Corporation

[Tindall Escambia daily 3-13-19.xlsx](#)

EQUIPMENT LOG

No.	Equipment Name	Cost Code	Hrs Operating	Hrs Idle	Inspected?	Inspection Time	Location
1	JLG Lift 660SJ				No	07:00 AM	Building>A
	Notes:						
2	Kobelco Crane CKE2500				No	07:00 AM	Building>B
	Notes:						
3	Genie Lift S85				No	07:00 AM	Building>B
	Notes:						
4	JLG Lift 660SJ				No	07:00 AM	Building>B
	Notes:						
5	CAT 303.5E2 Excavator				No	07:00 AM	Building>C
	Notes:						
6	Grove Crane AT700D				No	07:00 AM	Building>D
	Notes:						
7	JLG Lift 660SJ				No	07:00 AM	Building>D
	Notes:						
8	JLG Skytrak Telehandler				No	07:00 AM	Site
	Notes:						
9	JLG Skytrak Telehandler				No	07:00 AM	Site
	Notes:						
10	JLG Skytrak Telehandler				No	07:00 AM	Site
	Notes:						
11	Cat Telehandler				No	07:00 AM	Site
	Notes:						

EQUIPMENT LOG

No.	Equipment Name	Cost Code	Hrs Operating	Hrs Idle	Inspected?	Inspection Time	Location
12	John Deere 750 Dozer				No	07:00 AM	Site>Stormwater Pond
	Notes:						
13	Volvo 330 Excavator				No	07:00 AM	Site>Stormwater Pond
	Notes:						
14	Komatsu 320 PT Loader				No	07:00 AM	Site>Stormwater Pond
	Notes:						
15	John Deere 300G Excavator				No	07:00 AM	Site>Stormwater Pond
	Notes:						

By

Date

Copies To



Daily Log: Thursday 3/14/2019

Daily Log Completed
 The Daily Log was completed by Donald Shelton on Mon Mar 18, 2019 at 12:10 pm CDT.

WEATHER REPORT

Temperature			Precipitation Since			Humidity				Windspeed		
Low	High	Avg	Midnight	2 Days Ago	3 Days Ago	Low	Avg	High	Dew	Avg	Max	Gust
67°F	76°F	71°F	0.07 in.	0.09 in.	0.09 in.	75%	87%	97%	67°F	12.6 mph	15 mph	26 mph

DAILY SNAPSHOT

06:00 AM	09:00 AM	12:00 PM	03:00 PM	06:00 PM	09:00 PM
partly-cloudy-night 67°F	cloudy 71°F	cloudy 77°F	cloudy 75°F	partly-cloudy-day 73°F	partly-cloudy-night 70°F

OBSERVED WEATHER CONDITIONS

No.	Weather Delay	Sky	Temp	Average	Precipitation	Wind	Ground/Sea
1	No	Cloudy	Mild	71	0	Light Wind	Dry

MANPOWER LOG

50 Workers | 440.0 Man Hours

No.	Contact/Company	Cost Code	Workers	# Hours	Man Hours	Location
1	EAA Site Contractors LLC		5	8.0	40.0	Site
Notes: Total man hours 50. EAA continued to dig retention pond today. Dirt was placed on south side of bldg where the topsoil had been removed.						
2	A&B Electric Co., Inc.		9	10.0	90.0	Building
Notes: Finish 2nd floor rough in of normal & Emergency lighting circuits, Fix boxes installed incorrectly in precast and dig out styrofoam for rough in of precast, Unload Bulk order of material from Mayer and sort in rental property.						
3	Bayside Structures, LLC		1	8.0	8.0	Building
Notes: Poured 18 yards of 3,500 psi topping slab in area A corridor at elevation 100.00 from column line 3 to 14. Placed all 4x4 WWM in area D from column line 37 to 50. Started placing #4 rebar over girders and beams. Placed rebar at block outs and floor drains.						
4	Caddell Construction Co. (DE), LLC		9	10.0	90.0	Site
Notes: WGI/Caddell supervision, quality control and safety onsite.						
5	Chavers Construction Inc.		4	10.0	40.0	Site>Stormwater Pond
Notes: Worked on storm water between Boxes 23 and 24. Moved storm pipe for EAA. Cleaned job site						

MANPOWER LOG

50 Workers | 440.0 Man Hours

No.	Contact/Company	Cost Code	Workers	# Hours	Man Hours	Location
6	Ed Emmons Steel Erectors, Inc.		8	8.0	64.0	Building>D
Notes: Finished elevation 115 deck. Stood columns for elevation 102 steel.						
7	Larry M. Jacobs & Associates, Inc.		2	4.0	8.0	Site
Notes: Conducted test for concrete pour. Steel Inspection (welds, embeds, and bolts)						
8	Nash Plumbing and Mechanical, LLC		10	8.0	80.0	Building
Notes: Installed hangers for piping Prefab piping for corridor Underground rough-in, testing						
9	Tindall Corporation		2	10.0	20.0	Building
Notes: **Patching various.						
			50		440.0	

Manpower Log's Attachments:

2. A&B Electric Co., Inc.




[Daily Construction Report -- 3_14_19.pdf](#)

3. Bayside Structures, LLC


[Bayside Daily 3-14-2019.docx](#)

5. Chavers Construction Inc.



[Chaver Daily 3-14-2019.PDF](#)

6. Ed Emmons Steel Erectors, Inc.

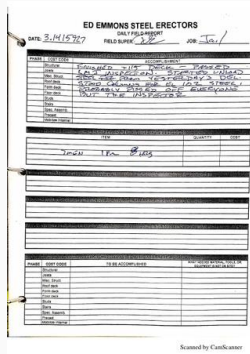

[New Doc 2019-03-14 16.23.06.pdf](#)

8. Nash Plumbing and Mechanical, LLC

[Nash Daily 3-14-2019.xlsx](#)

9. Tindall Corporation

[Tindall Escambia daily 3-14-19.xlsx](#)

EQUIPMENT LOG

No.	Equipment Name	Cost Code	Hrs Operating	Hrs Idle	Inspected?	Inspection Time	Location
1	Kobelco Crane CKE2500				No	11:05 AM	Building>A
	Notes:						
2	JLG Lift 860SJ				No	11:05 AM	Building>A
	Notes:						
3	Genie Lift S85				No	11:05 AM	Building>A
	Notes:						
4	CAT 303.5E2 Excavator				No	11:05 AM	Building>C
	Notes:						
5	Sky Power Lift 600AJ				No	11:05 AM	Building>D
	Notes:						
6	Kobelco Crane CKE2500				No	11:05 AM	Building>D
	Notes:						
7	JLG Lift 660SJ				No	11:05 AM	Building>D
	Notes:						
8	Scissor Lift				No	11:05 AM	Building
	Notes:						
9	Scissor Lift				No	11:05 AM	Building
	Notes:						
10	Scissor Lift				No	11:05 AM	Building
	Notes:						
11	Scissor Lift				No	11:05 AM	Building
	Notes:						

EQUIPMENT LOG

No.	Equipment Name	Cost Code	Hrs Operating	Hrs Idle	Inspected?	Inspection Time	Location
12	Scissor Lift				No	11:05 AM	Building
	Notes:						
13	JLG Skytrak Telehandler				No	11:05 AM	Site
	Notes:						
14	JLG Skytrak Telehandler				No	11:05 AM	Site
	Notes:						
15	JLG Skytrak Telehandler				No	11:05 AM	Site
	Notes:						
16	Cat Telehandler				No	11:05 AM	Site
	Notes:						

By _____

Date _____

Copies To _____



Daily Log: Friday 3/15/2019

WEATHER REPORT

Temperature			Precipitation Since			Humidity				Windspeed		
Low	High	Avg	Midnight	2 Days Ago	3 Days Ago	Low	Avg	High	Dew	Avg	Max	Gust
59°F	72°F	67°F	0.02 in.	0.09 in.	0.11 in.	52%	74%	100%	58°F	9.3 mph	13 mph	25 mph

DAILY SNAPSHOT

06:00 AM	09:00 AM	12:00 PM	03:00 PM	06:00 PM	09:00 PM
cloudy 70°F	partly-cloudy-day 67°F	partly-cloudy-day 71°F	partly-cloudy-day 71°F	partly-cloudy-day 65°F	partly-cloudy-night 62°F

OBSERVED WEATHER CONDITIONS

No.	Weather Delay	Sky	Temp	Average	Precipitation	Wind	Ground/Sea
1	No	Cloudy	Mild	67	0	Light Wind	Dry

MANPOWER LOG

40 Workers | 374.0 Man Hours

No.	Contact/Company	Cost Code	Workers	# Hours	Man Hours	Location
1	A&B Electric Co., Inc.		5	8.0	40.0	Building
Notes: Started overhead conduit layout and install in section D first floor for VAV units, finished organizing and storing bulk materials in warehouse, started lighting conduit layout in section D 1st floor. 45 Total Man Hours						
2	Bayside Structures, LLC		10	8.0	80.0	Building
Notes: Excavated the 10x15 x15" pad for the buck hoist placed the two #5 rebar mats 10" on center. Poured buck hoist pad. Continued working on the third pour in area D at elevation 115.00 from column line 37 to 50. We continued to work on rebar for third pour on elevation 115.00 in area D.						
3	Caddell Construction Co. (DE), LLC		9	12.5	112.5	Site
Notes: WGI/Caddell supervision, quality control and safety onsite.						
4	Chavers Construction Inc.		3	12.5	37.5	Site>Stormwater Pond
Notes: Covered stovepipe between boxes 23 and 24.						
5	Larry M. Jacobs & Associates, Inc.		1	4.0	4.0	Site
Notes: Conducted Density test in Area C and Concrete test on site.						
6	Nash Plumbing and Mechanical, LLC		10	8.0	80.0	Building
Notes: Installed hangers for piping in main corridor 83' el. Prefab piping for corridor Underground plumbing inspection, backfill						

MANPOWER LOG

40 Workers | 374.0 Man Hours

No.	Contact/Company	Cost Code	Workers	# Hours	Man Hours	Location
7	Tindall Corporation		2	10.0	20.0	Building
Notes: **Patching various.						
			40		374.0	

Manpower Log's Attachments:

1. A&B Electric Co., Inc.




[Daily Construction Report - - 3_15_19.pdf](#)

2. Bayside Structures, LLC

[Bayside Daily 3-15-2019.docx](#)

4. Chavers Construction Inc.

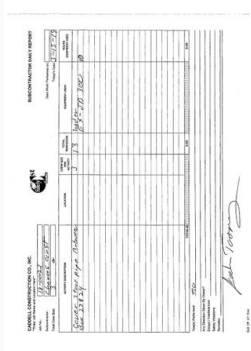

[Chaver Daily 3-15-2019.PDF](#)

6. Nash Plumbing and Mechanical, LLC

[Nash Daily 3-15-2019.xlsx](#)

7. Tindall Corporation

[Tindall Escambia daily 3-15-19.xlsx](#)

EQUIPMENT LOG

No.	Equipment Name	Cost Code	Hrs Operating	Hrs Idle	Inspected?	Inspection Time	Location
1	CAT 303.5E2 Excavator				No	07:00 AM	Building>C
	Notes:						
2	Scissor Lift				No	07:00 AM	Building
	Notes:						
3	Scissor Lift				No	07:00 AM	Building
	Notes:						
4	Scissor Lift				No	07:00 AM	Building
	Notes:						
5	JLG Skytrak Telehandler				No	07:00 AM	Site
	Notes:						
6	Bobcat Telehandler				No	07:00 AM	Site
	Notes:						
7	Doosan Loader				No	07:00 AM	Site
	Notes:						
8	John Deere 300G Excavator				No	07:00 AM	Site
	Notes:						

By

Date

Copies To



Whitesell Green / Caddell, a Joint Venture
 2700 Lagoon Park Drive
 Montgomery, Alabama 36109
 P: (334) 272-7723
 F: (334) 394-0193

Project: 1054 - Escambia County Correctional
Facility
 3080 N. Pace Boulevard
 Pensacola, Florida 32501

Daily Log: Saturday 3/16/2019

WEATHER REPORT

Temperature			Precipitation Since			Humidity				Windspeed		
Low	High	Avg	Midnight	2 Days Ago	3 Days Ago	Low	Avg	High	Dew	Avg	Max	Gust
49°F	57°F	52°F	0.03 in.	0.05 in.	0.12 in.	50%	68%	89%	42°F	7.6 mph	11 mph	22 mph

DAILY SNAPSHOT

06:00 AM	09:00 AM	12:00 PM	03:00 PM	06:00 PM	09:00 PM
partly-cloudy-night 51°F	cloudy 52°F	partly-cloudy-day 53°F	cloudy 57°F	cloudy 54°F	partly-cloudy-night 50°F

OBSERVED WEATHER CONDITIONS

No.	Weather Delay	Sky	Temp	Average	Precipitation	Wind	Ground/Sea
1	No						

By _____

Date _____

Copies To _____



Whitesell Green / Caddell, a Joint Venture
 2700 Lagoon Park Drive
 Montgomery, Alabama 36109
 P: (334) 272-7723
 F: (334) 394-0193

Project: 1054 - Escambia County Correctional
Facility
 3080 N. Pace Boulevard
 Pensacola, Florida 32501

Daily Log: Sunday 3/17/2019

WEATHER REPORT

Temperature			Precipitation Since			Humidity				Windspeed		
Low	High	Avg	Midnight	2 Days Ago	3 Days Ago	Low	Avg	High	Dew	Avg	Max	Gust
45°F	65°F	53°F	0.00 in.	0.03 in.	0.05 in.	27%	52%	69%	35°F	6.0 mph	8 mph	13 mph

DAILY SNAPSHOT

06:00 AM	09:00 AM	12:00 PM	03:00 PM	06:00 PM	09:00 PM
partly-cloudy-night 46°F	partly-cloudy-day 50°F	cloudy 59°F	clear-day 66°F	partly-cloudy-day 62°F	partly-cloudy-night 53°F

OBSERVED WEATHER CONDITIONS

No.	Weather Delay	Sky	Temp	Average	Precipitation	Wind	Ground/Sea
1	No						

By _____

Date _____

Copies To _____



Daily Log: Monday 3/18/2019

Daily Log Completed
 The Daily Log was completed by Donald Shelton on Fri Mar 22, 2019 at 11:21 am CDT.

WEATHER REPORT

Temperature			Precipitation Since			Humidity				Windspeed		
Low	High	Avg	Midnight	2 Days Ago	3 Days Ago	Low	Avg	High	Dew	Avg	Max	Gust
43°F	67°F	56°F	0.00 in.	0.00 in.	0.04 in.	27%	48%	75%	35°F	8.4 mph	11 mph	23 mph

DAILY SNAPSHOT

06:00 AM	09:00 AM	12:00 PM	03:00 PM	06:00 PM	09:00 PM
clear-night 44°F	partly-cloudy-day 54°F	partly-cloudy-day 65°F	partly-cloudy-day 67°F	partly-cloudy-day 65°F	cloudy 60°F

OBSERVED WEATHER CONDITIONS

No.	Weather Delay	Sky	Temp	Average	Precipitation	Wind	Ground/Sea
1	No	Cloudy	Mild	56	0	Light Wind	Dry



MANPOWER LOG

69 Workers | 664.0 Man Hours

No.	Contact/Company	Cost Code	Workers	# Hours	Man Hours	Location
1	A&B Electric Co., Inc.		12	10.0	120.0	Building
Notes: Rough in of overhead Electrical conduits in section "D" first floor, Temporary lighting on 2nd Floor in section "A", Rework boxes in precast and dig out styrofoam in precast for rough in of conduits 2nd & 3rd Floor.						
2	Bayside Structures, LLC		9	10.0	90.0	Building>D
Notes: We completed W.W.M.. and rebar for pour in area D elevation 115.00 between column line 37 and 50. We installed 32 embeds at the clear story for Emmons steel work. We sealed all openings and cracks in deck to help prevent concrete from leaking to floor below.						
3	Caddell Construction Co. (DE), LLC		9	10.0	90.0	Site
Notes: WGI/Caddell supervision, quality control and safety onsite.						
4	Chavers Construction Inc.		3	8.0	24.0	Site>Stormwater Pond
Notes: Continued covering pipe between boxes 23 and 24.						
5	Ed Emmons Steel Erectors, Inc.		6	10.0	60.0	Building>D
Notes: Hung elevation 102 steel at true south end of Area C. Moved crane to east side at loading deck to work around issue at precast openings.						

MANPOWER LOG

69 Workers | 664.0 Man Hours

No.	Contact/Company	Cost Code	Workers	# Hours	Man Hours	Location
6	Nash Plumbing and Mechanical, LLC		9	8.0	72.0	Building 
Notes: Installed hangers for piping Prefab pipe for corridor Installed hangers for piping						
7	Tindall Corporation		19	10.0	190.0	Building>A 
Notes: **Erecting in area A. **Welding and grouting **Patching in stair A						
8	EAA Site Contractors LLC		2	9.0	18.0	Site
Notes: Total man hours 20. EAA did not dig in the retention pond today. Instead we worked on removing the topsoil along the current construction entrance. This is where the new entrance will be located.						
			69		664.0	

Manpower Log's Attachments:

1. A&B Electric Co., Inc.




[Daily Construction Report -- 3_18_19.pdf](#)

2. Bayside Structures, LLC

 [Bayside Daily 3-18-2019.docx](#)

5. Ed Emmons Steel Erectors, Inc.



[New Doc 2019-03-18 17.42.33.pdf](#)

6. Nash Plumbing and Mechanical, LLC

[Nash Daily 3-18-2019.xlsx](#)

7. Tindall Corporation

[Tindall Escambia Daily 3-18-2019.xlsx](#)

EQUIPMENT LOG

No.	Equipment Name	Cost Code	Hrs Operating	Hrs Idle	Inspected?	Inspection Time	Location
1	JLG Lift 660SJ				No	07:00 AM	Building>A
	Notes:						
2	JLG Lift 660SJ				No	07:00 AM	Building>A
	Notes:						
3	JLG Lift 860SJ				No	07:00 AM	Building>B
	Notes:						
4	CAT 303.5E2 Excavator				No	07:00 AM	Building>C
	Notes:						
5	Grove Crane AT700D				No	07:00 AM	Building>D
	Notes:						
6	Kobelco Crane CKE2500				No	07:00 AM	Building>A
	Notes:						
7	JLG Skytrak Telehandler				No	07:00 AM	Site
	Notes:						
8	JLG Skytrak Telehandler				No	07:00 AM	Site
	Notes:						
9	JLG Skytrak Telehandler				No	07:00 AM	Site
	Notes:						
10	John Deere 300G Excavator				No	07:00 AM	Site>Stormwater Pond
	Notes:						
11	Doosan Excavator				No	07:00 AM	Site>Stormwater Pond
	Notes:						
12	Kawasaki 652 V Loader				No	07:00 AM	Site>Stormwater Pond
	Notes:						
13	Excavator				No	07:00 AM	Site>Stormwater Pond
	Notes:						

PHOTOS



[DJI_0390.jpg](#)



[DJI_0392.jpg](#)



[DJI_0403.jpg](#)



[DJI_0394.jpg](#)



[DJI_0400.jpg](#)



[DJI_0402.jpg](#)



[DJI_0393.jpg](#)



[DJI_0395.jpg](#)



[DJI_0399.jpg](#)



[DJI_0404.jpg](#)



[DJI_0401.jpg](#)



[DJI_0398.jpg](#)



[DJI_0409.jpg](#)



[DJI_0407.jpg](#)



[DJI_0406.jpg](#)



[DJI_0410.jpg](#)



DJI_0408.jpg



DJI_0405.jpg



DJI_0391.jpg



DJI_0414.jpg



DJI_0411.jpg



DJI_0415.jpg



DJI_0413.jpg



DJI_0416.jpg



DJI_0421.jpg



DJI_0417.jpg



DJI_0419.jpg



DJI_0427.jpg



DJI_0382.jpg



DJI_0384.jpg



DJI_0383.jpg



DJI_0386.jpg



[DJI_0388.jpg](#)



[DJI_0387.jpg](#)



[DJI_0389.jpg](#)



[DJI_0418.jpg](#)



[DJI_0426.jpg](#)



[DJI_0385.jpg](#)

By

Date

Copies To



Daily Log: Tuesday 3/19/2019

Daily Log Completed
 The Daily Log was completed by Donald Shelton on Fri Mar 22, 2019 at 09:03 am CDT.

WEATHER REPORT

Temperature			Precipitation Since			Humidity				Windspeed		
Low	High	Avg	Midnight	2 Days Ago	3 Days Ago	Low	Avg	High	Dew	Avg	Max	Gust
45°F	66°F	54°F	0.00 in.	0.01 in.	0.01 in.	21%	42%	78%	30°F	5.9 mph	9 mph	22 mph

DAILY SNAPSHOT

06:00 AM	09:00 AM	12:00 PM	03:00 PM	06:00 PM	09:00 PM
partly-cloudy-night 48°F	partly-cloudy-day 51°F	partly-cloudy-day 61°F	partly-cloudy-day 65°F	clear-day 65°F	clear-night 51°F

OBSERVED WEATHER CONDITIONS

No.	Weather Delay	Sky	Temp	Average	Precipitation	Wind	Ground/Sea
1	No	Cloudy	Cold	54	0	Light Wind	Dry

MANPOWER LOG

68 Workers | 618.0 Man Hours

No.	Contact/Company	Cost Code	Workers	# Hours	Man Hours	Location
1	EAA Site Contractors LLC		2	8.0	16.0	Site
Notes: Total man hours 20. EAA did not dig in the retention pond today. We continued to prepare the new entrance off ST Mary						
2	A&B Electric Co., Inc.		11	10.0	110.0	Building
Notes: Rough in of overhead conduit in "D" section on first floor for Emergency & normal lights, Have outage on temporary power to pull feeder for bulk Hoist Elevator, Get cable an lights to 4th floor to get ready to install temporary lighting on 4th floor in "C" section.						
3	Bayside Structures, LLC		9	10.0	90.0	Building
Notes: We placed 103 yards of concrete in area D at elevation 115.00 between column line 37 and 50. After concrete was placed we machine float finished. We made rebar corrections to four beam piers at the connector. Quality Control Manager Tim Smith inspected and we passed. I ordered concrete and we poured all four. We pulled all snap tie cones from stem walls at the connector and patched for back fill between walls.						
4	Caddell Construction Co. (DE), LLC		9	10.0	90.0	Site
Notes: WGI/Caddell supervision, quality control and safety onsite.						
5	Ed Emmons Steel Erectors, Inc.		8	10.0	80.0	Building>D
Notes: Continued erecting elevation 102 steel connected to landing dock south wall.						

MANPOWER LOG

68 Workers | 618.0 Man Hours

No.	Contact/Company	Cost Code	Workers	# Hours	Man Hours	Location
6	Nash Plumbing and Mechanical, LLC		9	8.0	72.0	Building
Notes: Mechanical-installed hangers for piping Mechanical- began setting pipe in hangers on south end Plumbing- prefabbing hangers for corridor						
7	Tindall Corporation		19	8.0	152.0	Building
Notes: **Erecting in area A. **Welding and grouting **Patching 168 Total Man Hours						
8	Larry M. Jacobs & Associates, Inc.		1	8.0	8.0	Site
Notes: Conducted test for concrete pour.						
			68		618.0	

Manpower Log's Attachments:

2. A&B Electric Co., Inc.




[Daily Construction Report - - 3_19_19.pdf](#)

3. Bayside Structures, LLC

[Bayside Daily 3-20-2019.docx](#)

5. Ed Emmons Steel Erectors, Inc.



[New Doc 2019-03-19 19.32.37.pdf](#)

6. Nash Plumbing and Mechanical, LLC

[Nash Daily 3-19-2019.xlsx](#)

7. Tindall Corporation

[Tindall Escambia daily 3-18 and 3-19-19.xlsx](#)

EQUIPMENT LOG

No.	Equipment Name	Cost Code	Hrs Operating	Hrs Idle	Inspected?	Inspection Time	Location
1	Kobelco Crane CKE2500				No	07:00 AM	Building>A
	Notes:						
2	JLG Lift 660SJ				No	07:00 AM	Building>A
	Notes:						
3	JLG Lift 860SJ				No	07:00 AM	Building>A
	Notes:						
4	Genie Lift S85				No	07:00 AM	Building>B
	Notes:						
5	Grove Crane AT700D				No	07:00 AM	Building>D
	Notes:						
6	JLG Lift 660SJ				No	07:00 AM	Building>D
	Notes:						
7	Scissor Lift				No	07:00 AM	Building
	Notes:						
8	Scissor Lift				No	07:00 AM	Building
	Notes:						
9	Scissor Lift				No	07:00 AM	Building
	Notes:						
10	Scissor Lift				No	07:00 AM	Building
	Notes:						
11	Bobcat Miniexcavator				No	07:00 AM	Site
	Notes:						
12	Cat Telehandler				No	07:00 AM	Site
	Notes:						
13	JLG Skytrak Telehandler				No	07:00 AM	Site
	Notes:						
14	JLG Skytrak Telehandler				No	07:00 AM	Site
	Notes:						
15	Volvo 330 Excavator				No	07:00 AM	Site>Stormwater Pond
	Notes:						
16	Kawasaki 652 V Loader				No	07:00 AM	Site>Stormwater Pond
	Notes:						
17	John Deere 750 Dozer				No	07:00 AM	Site>Stormwater Pond
	Notes:						

By _____

Date _____

Copies To _____



Daily Log: Wednesday 3/20/2019

Daily Log Completed
 The Daily Log was completed by Donald Shelton on Fri Mar 22, 2019 at 09:31 am CDT.

WEATHER REPORT

Temperature			Precipitation Since			Humidity				Windspeed		
Low	High	Avg	Midnight	2 Days Ago	3 Days Ago	Low	Avg	High	Dew	Avg	Max	Gust
40°F	68°F	54°F	0.00 in.	0.00 in.	0.01 in.	35%	61%	88%	40°F	5.5 mph	9 mph	15 mph

DAILY SNAPSHOT

06:00 AM	09:00 AM	12:00 PM	03:00 PM	06:00 PM	09:00 PM
clear-night 45°F	clear-day 54°F	clear-day 65°F	clear-day 68°F	clear-day 65°F	clear-night 55°F

OBSERVED WEATHER CONDITIONS

No.	Weather Delay	Sky	Temp	Average	Precipitation	Wind	Ground/Sea
1	No	Clear	Cold	54	0	Light Wind	Dry

MANPOWER LOG

68 Workers | 650.0 Man Hours

No.	Contact/Company	Cost Code	Workers	# Hours	Man Hours	Location
1	EAA Site Contractors LLC		6	8.0	48.0	Site
Notes: Total man hours 42. EAA conducted limited digging in the retention pond. Dirt was placed in the connector. The first lift passed density test.						
2	A&B Electric Co., Inc.		6	10.0	60.0	Building>C
Notes: Installing temporary lights on 4th floor section "C", Layout of walls on 4th floor of Section "C", Haul material to 4th floor, Section "C" for rough in of Electrical conduits for Electrical, Security etc.						
3	Bayside Structures, LLC		11	10.0	110.0	Building>D
Notes: We placed continued to excavate and form column isolation block outs in area D at elevation 83.00. We poured twenty column isolations in area D. We finished stripping snap tie cones and patching the outside of the steam walls at the connector. We stripped the forms from the four piers at the connector from yesterdays pour. Grading and compacting for the beam that sets on the piers at connector was started.						
4	Caddell Construction Co. (DE), LLC		9	10.0	90.0	Site
Notes: WGI/Caddell supervision, quality control and safety onsite.						
5	Ed Emmons Steel Erectors, Inc.		8	10.0	80.0	Building>D
Notes: Hung beams at elevation 102. Placed bolts in same location. Punched list welds at deck support angle bottoms to embeds, 95% complete.						

MANPOWER LOG

68 Workers | 650.0 Man Hours

No.	Contact/Company	Cost Code	Workers	# Hours	Man Hours	Location
6	Nash Plumbing and Mechanical, LLC		9	8.0	72.0	Building
Notes: Cored drilling holes in precast walls for pipe penetrations elevation 83'. Installed hydronic piping and hangers elevation 83'. Laid out holes for pipe penetrations elevation 137'.						
7	Tindall Corporation		19	10.0	190.0	Building
Notes: **Erecting in area A. **Welding and grouting **Patching						
			68		650.0	

Manpower Log's Attachments:

2. A&B Electric Co., Inc.




[Daily Construction Report -- 3_20_19.pdf](#)

3. Bayside Structures, LLC

[Bayside Daily 3-20-2019.docx](#)

5. Ed Emmons Steel Erectors, Inc.



[New Doc 2019-03-20 19.24.19.pdf](#)

6. Nash Plumbing and Mechanical, LLC

[Nash Daily 3-20-2019.xlsx](#)

[Tindall Escambia daily 3-20-19.xlsx](#)

EQUIPMENT LOG

No.	Equipment Name	Cost Code	Hrs Operating	Hrs Idle	Inspected?	Inspection Time	Location
1	Kobelco Crane CKE2500				No	07:00 AM	Building>A
	Notes:						
2	JLG Lift 660SJ				No	07:00 AM	Building>A
	Notes:						
3	Genie Lift S85				No	07:00 AM	Building>B
	Notes:						
4	Sky Power Lift 600AJ				No	07:00 AM	Building>C
	Notes:						
5	Grove Crane AT700D				No	07:00 AM	Building>D
	Notes:						
6	Genie Lift S80				No	07:00 AM	Building>D
	Notes:						
7	Bobcat Miniexcavator				No	07:00 AM	Building>D
	Notes:						
8	Scissor Lift				No	07:00 PM	Building
	Notes:						
9	Scissor Lift				No	07:00 AM	Building
	Notes:						
10	Scissor Lift				No	07:00 AM	Building
	Notes:						
11	Scissor Lift				No	07:00 AM	Building
	Notes:						
12	JLG Skytrak Telehandler				No	07:00 AM	Site
	Notes:						
13	JLG Skytrak Telehandler				No	07:00 AM	Site
	Notes:						
14	Cat Telehandler				No	07:00 AM	Site
	Notes:						
15	Volvo 330 Excavator				No	07:00 AM	Site>Stormwater Pond
	Notes:						
16	Komatsu 320 PT Loader				No	07:00 AM	Site>Stormwater Pond
	Notes:						
17	Vibratory Roller				No	07:00 AM	Site
	Notes:						
18	John Deere 50G Miniexcavator				No	07:00 AM	Site
	Notes:						

By _____

Date _____

Copies To _____



Daily Log: Thursday 3/21/2019

Daily Log Completed
 The Daily Log was completed by Donald Shelton on Fri Mar 22, 2019 at 11:19 am CDT.

WEATHER REPORT

Temperature			Precipitation Since			Humidity				Windspeed		
Low	High	Avg	Midnight	2 Days Ago	3 Days Ago	Low	Avg	High	Dew	Avg	Max	Gust
48°F	72°F	58°F	0.00 in.	0.00 in.	0.00 in.	28%	62%	91%	43°F	7.4 mph	11 mph	19 mph

DAILY SNAPSHOT

06:00 AM	09:00 AM	12:00 PM	03:00 PM	06:00 PM	09:00 PM
partly-cloudy-night 49°F	clear-day 54°F	clear-day 65°F	clear-day 72°F	clear-day 69°F	clear-night 57°F

OBSERVED WEATHER CONDITIONS

No.	Weather Delay	Sky	Temp	Average	Precipitation	Wind	Ground/Sea
1	No	Clear	Mild	58	0	Light Wind	Dry



MANPOWER LOG

61 Workers | 556.0 Man Hours

No.	Contact/Company	Cost Code	Workers	# Hours	Man Hours	Location
1	EAA Site Contractors LLC		4	8.0	32.0	Site
Notes: Total man hours 39. EAA started demo of old construction entrance. Removed the remaining topsoil and started asphalt removal. Placed dirt for the second lift in the connector but the density test failed.						
2	A&B Electric Co., Inc.		6	10.0	60.0	Building>C
Notes: Rough in of Electrical conduits in Section "C" 4th Floor slab, (Electrical, Security, etc)						
3	Bayside Structures, LLC		9	10.0	90.0	Building>D
Notes: We worked on excavating and forming column Isolated in area D at elevation 83.00. We wrecked all isolation forms from Wednesday's pour.						
4	Caddell Construction Co. (DE), LLC		9	10.0	90.0	Site
Notes: WGI/Caddell supervision, quality control and safety onsite.						
5	Ed Emmons Steel Erectors, Inc.		7	7.0	49.0	Building>D
Notes: Erected beams south end in Area D at elevation 102. 51 Total man Hours						
6	Larry M. Jacobs & Associates, Inc.		1	1.0	1.0	Site
Notes: Conducted Density Test in Connector Area.						

MANPOWER LOG

61 Workers | 556.0 Man Hours

No.	Contact/Company	Cost Code	Workers	# Hours	Man Hours	Location
7	Nash Plumbing and Mechanical, LLC		8	8.0	64.0	Building 
Notes: Installed piping and hangers Cored drilling holes in precast walls for pipe penetrations Laid out holes for plumbing penetrations 137' el.						
8	Tindall Corporation		17	10.0	170.0	Building>A 
Notes: **Erecting in area A. **Welding and grouting **Patching						
			61		556.0	

Manpower Log's Attachments:

2. A&B Electric Co., Inc.




[Daily Construction Report -- 3_21_19.pdf](#)

3. Bayside Structures, LLC

 [Bayside Daily 3-21-2019.docx](#)

5. Ed Emmons Steel Erectors, Inc.



[New Doc 2019-03-21 18.01.09.pdf](#)

7. Nash Plumbing and Mechanical, LLC

 [Nash Daily 3-21-2019.xlsx](#)

[Tindall Escambia daily 3-21-19.xlsx](#)

EQUIPMENT LOG

No.	Equipment Name	Cost Code	Hrs Operating	Hrs Idle	Inspected?	Inspection Time	Location
1	Kobelco Crane CKE2500				No	07:00 AM	Building>A
	Notes:						
2	JLG Lift 660SJ				No	07:00 AM	Building>A
	Notes:						
3	JLG Lift 860SJ				No	07:00 AM	Building>A
	Notes:						
4	Genie Lift S85				No	07:00 AM	Building>B
	Notes:						
5	Sky Power Lift 600AJ				No	07:00 AM	Building>C
	Notes:						
6	Grove Crane AT700D				No	07:00 AM	Building>D
	Notes:						
7	Genie Lift S80				No	07:00 AM	Building>D
	Notes:						
8	Bobcat Miniexcavator				No	07:00 AM	Building>D
	Notes:						
9	Scissor Lift				No	07:00 AM	Building
	Notes:						
10	Scissor Lift				No	07:00 AM	Building
	Notes:						
11	Scissor Lift				No	07:00 AM	Building
	Notes:						
12	Scissor Lift				No	07:00 AM	Building
	Notes:						
13	JLG Skytrak Telehandler				No	07:00 AM	Site
	Notes:						
14	JLG Skytrak Telehandler				No	07:00 AM	Site
	Notes:						
15	Cat Telehandler				No	07:00 AM	Site
	Notes:						
16	Water Truck				No	07:00 AM	Site
	Notes:						
17	John Deere 50G Miniexcavator				No	07:00 AM	Site
	Notes:						
18	Vibratory Roller				No	07:00 AM	Site
	Notes:						

By _____

Date _____

Copies To _____



Daily Log: Friday 3/22/2019

Daily Log Completed
 The Daily Log was completed by Donald Shelton on Mon Mar 25, 2019 at 09:21 am CDT.

WEATHER REPORT

Temperature			Precipitation Since			Humidity				Windspeed		
Low	High	Avg	Midnight	2 Days Ago	3 Days Ago	Low	Avg	High	Dew	Avg	Max	Gust
43°F	73°F	57°F	0.00 in.	0.00 in.	0.00 in.	23%	56%	93%	39°F	5.9 mph	8 mph	15 mph

DAILY SNAPSHOT

06:00 AM	09:00 AM	12:00 PM	03:00 PM	06:00 PM	09:00 PM
clear-night 44°F	clear-day 52°F	clear-day 65°F	clear-day 73°F	clear-day 70°F	clear-night 59°F

OBSERVED WEATHER CONDITIONS

No.	Weather Delay	Sky	Temp	Average	Precipitation	Wind	Ground/Sea
1	No	Clear	Mild	57	0	Light Wind	Dry

MANPOWER LOG

52 Workers | 451.0 Man Hours

No.	Contact/Company	Cost Code	Workers	# Hours	Man Hours	Location
1	A&B Electric Co., Inc.		6	10.0	60.0	Building>C
Notes: Rough in of Electrical conduits in 4th Floor slab of "C" area. (Electrical,Security,Fire alarm,etc)						
2	Bayside Structures, LLC		12	8.0	96.0	Building
Notes: ___ We cleaned and installed ice and water shield over all joints in the floor in the corridor on the second floor between column lines 17 and 50. We placed wire mesh in the corridor on second floor between column lines 17 and 50. We cleaned and installed ice and water shield in the corridor on the third floor between column lines 13 and 16. We installed wire mesh on the third floor in the corridor between column lines 13 and 16. We worked on installing ice and water shield on the fourth floor in area C. We poured 19 more isolation block outs in area D at elevation 83.00						
3	Caddell Construction Co. (DE), LLC		1	8.0	8.0	Site
Notes: WGI/Caddell supervision, quality control and safety onsite.						
4	Ed Emmons Steel Erectors, Inc.		7	8.0	56.0	Building>D
Notes: Weld out beams connection to elevation 102. Competed, hung columns, brace beams at elevation 135.						
5	Larry M. Jacobs & Associates, Inc.		1	1.0	1.0	Site
Notes: Conducted a Density Test in the Connector Area						

MANPOWER LOG

52 Workers | 451.0 Man Hours

No.	Contact/Company	Cost Code	Workers	# Hours	Man Hours	Location
6	Nash Plumbing and Mechanical, LLC		7	8.0	56.0	Building
Notes: Welded 8" piping in main corridor at elevation 83. Core drilling holes for plumbing penetrations in Area C at elevation 137. Oversaw core drilling operations in Area C at elevation 137.						
7	Tindall Corporation		17	10.0	170.0	Building
Notes: **Erecting in area A. **Welding and grouting						
8	EAA Site Contractors LLC		1	4.0	4.0	Site
Notes: Total man hours 4. EAA continued work on backfill of the connector. The second lift density retest passed today. Placed third lift in connector.						
			52		451.0	

Manpower Log's Attachments:

1. A&B Electric Co., Inc.




[Daily Construction Report -- 3_22_19.pdf](#)

2. Bayside Structures, LLC

[Bayside Daily 3-22-2019.docx](#)

4. Ed Emmons Steel Erectors, Inc.



[New Doc 2019-03-22 16.28.22.pdf](#)

6. Nash Plumbing and Mechanical, LLC

7. Tindall Corporation

EQUIPMENT LOG

No.	Equipment Name	Cost Code	Hrs Operating	Hrs Idle	Inspected?	Inspection Time	Location
1	Kobelco Crane CKE2500				No	07:00 AM	Building>A
	Notes:						
2	JLG Lift 860SJ				No	07:00 AM	Building>A
	Notes:						
3	JLG Lift 660SJ				No	07:00 AM	Building>A
	Notes:						
4	Genie Lift S85				No	07:00 AM	Building>B
	Notes:						
5	Grove Crane AT700D				No	07:00 AM	Building>D
	Notes:						
6	JLG Lift 660SJ				No	07:00 AM	Building>D
	Notes:						
7	Scissor Lift				No	07:00 AM	Building
	Notes:						
8	Scissor Lift				No	07:00 AM	Building
	Notes:						
9	Scissor Lift				No	07:00 AM	Building
	Notes:						
10	Scissor Lift				No	07:00 AM	Building
	Notes:						
11	Bobcat Miniexcavator				No	07:00 AM	Building
	Notes:						
12	JLG Skytrak Telehandler				No	07:00 AM	Site
	Notes:						
13	JLG Skytrak Telehandler				No	07:00 AM	Site
	Notes:						
14	Cat Telehandler				No	07:00 AM	Site
	Notes:						
15	Vibratory Roller				No	07:00 AM	Site
	Notes:						
16	John Deere 50G Miniexcavator				No	07:00 AM	Site
	Notes:						

By _____ Date _____ Copies To _____



Daily Log: Saturday 3/23/2019

Daily Log Completed
 The Daily Log was completed by Donald Shelton on Mon Mar 25, 2019 at 09:19 am CDT.

WEATHER REPORT

Temperature			Precipitation Since			Humidity				Windspeed		
Low	High	Avg	Midnight	2 Days Ago	3 Days Ago	Low	Avg	High	Dew	Avg	Max	Gust
38°F	72°F	56°F	0.00 in.	0.00 in.	0.00 in.	26%	67%	100%	42°F	4.5 mph	12 mph	16 mph

DAILY SNAPSHOT

06:00 AM	09:00 AM	12:00 PM	03:00 PM	06:00 PM	09:00 PM
partly-cloudy-night 41°F	clear-day 57°F	clear-day 71°F	clear-day 72°F	clear-day 67°F	clear-night 54°F

OBSERVED WEATHER CONDITIONS

No.	Weather Delay	Sky	Temp	Average	Precipitation	Wind	Ground/Sea
1	No	Clear	Mild	56	0	Light Wind	Dry

MANPOWER LOG

19 Workers | 152.0 Man Hours

No.	Contact/Company	Cost Code	Workers	# Hours	Man Hours	Location
1	Caddell Construction Co. (DE), LLC		3	8.0	24.0	Site
Notes: WGI/Caddell supervision, quality control and safety onsite.						
2	Tindall Corporation		16	8.0	128.0	Building>A
Notes: **Erecting in area A. **Welding and grouting						
			19	152.0		

2. Tindall Corporation

[Tindasll Escambia Daily 3-23-2019.xlsx](#)

EQUIPMENT LOG

No.	Equipment Name	Cost Code	Hrs Operating	Hrs Idle	Inspected?	Inspection Time	Location
1	Kobelco Crane CKE2500				No	07:00 AM	Building>A
Notes:							
2	JLG Lift 860SJ				No	07:00 AM	Building>A
Notes:							

EQUIPMENT LOG

No.	Equipment Name	Cost Code	Hrs Operating	Hrs Idle	Inspected?	Inspection Time	Location
3	JLG Lift 660SJ				No	07:00 AM	Building>A
Notes:							
4	JLG Skytrak Telehandler				No	07:00 AM	Site
Notes:							

By

Date

Copies To



Whitesell Green / Caddell, a Joint Venture
 2700 Lagoon Park Drive
 Montgomery, Alabama 36109
 P: (334) 272-7723
 F: (334) 394-0193

Project: 1054 - Escambia County Correctional
Facility
 3080 N. Pace Boulevard
 Pensacola, Florida 32501

Daily Log: Sunday 3/24/2019

WEATHER REPORT

Temperature			Precipitation Since			Humidity				Windspeed		
Low	High	Avg	Midnight	2 Days Ago	3 Days Ago	Low	Avg	High	Dew	Avg	Max	Gust
41°F	71°F	57°F	0.00 in.	0.00 in.	0.00 in.	52%	79%	100%	50°F	4.2 mph	8 mph	13 mph

DAILY SNAPSHOT

06:00 AM	09:00 AM	12:00 PM	03:00 PM	06:00 PM	09:00 PM
clear-night 42°F	clear-day 59°F	clear-day 71°F	clear-day 72°F	clear-day 68°F	clear-night 58°F

OBSERVED WEATHER CONDITIONS

No.	Weather Delay	Sky	Temp	Average	Precipitation	Wind	Ground/Sea
1	No						

By _____

Date _____

Copies To _____



Daily Log: Monday 3/25/2019

Daily Log Completed
 The Daily Log was completed by Donald Shelton on Thu Mar 28, 2019 at 02:54 pm CDT.

WEATHER REPORT

Temperature			Precipitation Since			Humidity				Windspeed		
Low	High	Avg	Midnight	2 Days Ago	3 Days Ago	Low	Avg	High	Dew	Avg	Max	Gust
48°F	77°F	64°F	0.06 in.	0.06 in.	0.06 in.	55%	81%	100%	57°F	6.4 mph	12 mph	21 mph

DAILY SNAPSHOT

06:00 AM	09:00 AM	12:00 PM	03:00 PM	06:00 PM	09:00 PM
clear-night 52°F	partly-cloudy-day 67°F	partly-cloudy-day 75°F	partly-cloudy-day 77°F	clear-day 72°F	clear-night 66°F

OBSERVED WEATHER CONDITIONS

No.	Weather Delay	Sky	Temp	Average	Precipitation	Wind	Ground/Sea
1	No	Clear	Mild	63	0	Light Wind	Dry

MANPOWER LOG

88 Workers | 770.0 Man Hours

No.	Contact/Company	Cost Code	Workers	# Hours	Man Hours	Location
1	A&B Electric Co., Inc.		13	10.0	130.0	Building
Notes: Working on rough in of 4th floor slab of Section "C"(Electrical,Security,etc,) Fab rigid 90 for rough in (Fab area), Rough in of Overhead conduits in Section "D"(Electrical lighting conduits).						
2	Bayside Structures, LLC		21	8.0	168.0	Building
Notes: We worked on clean -up and wrecking the isolation forms in area D. We worked on the sealing of the floor in area C on the fourth floor. We placed W.W.M in the corridor on the second floor elevation 100.00 from column line 15 to 50. We placed rebar in the same location. We placed a bulk head at column line 17 due to Caddell not having the expansion joint on site to install. We installed WWM on the third floor at elevation 115.00 from column line 3 to 15. We also installed rebar and a bulk head.						
3	Caddell Construction Co. (DE), LLC		9	10.0	90.0	Site
Notes: WGI/Caddell supervision, quality control and safety onsite.						
4	Ed Emmons Steel Erectors, Inc.		10	8.0	80.0	Building>D
Notes: Install deck support angle at elevation 102. Began installing weld-in, field verify beams near south wall, bolted up all 102 beams that are hung elevation 137- all beams are hung, started deck support angle at same time.						
5	Larry M. Jacobs & Associates, Inc.		2	1.0	2.0	Site
Notes: Conducted Density Test in Connector Area.						

6. Nash Plumbing and Mechanical, LLC

[Nash Daily 3-25-2019.xlsx](#)

7. Tindall Corporation

[Tindall Escambia daily 3-25-19.xlsx](#)

EQUIPMENT LOG

No.	Equipment Name	Cost Code	Hrs Operating	Hrs Idle	Inspected?	Inspection Time	Location
1	Kobelco Crane CKE2500				No	07:00 AM	Building>A
	Notes:						
2	Genie Lift S85				No	07:00 AM	Building>A
	Notes:						
3	JLG Lift 860SJ				No	07:00 AM	Building>A
	Notes:						
4	Sky Power Lift 600AJ				No	07:00 AM	Building>C
	Notes:						
5	Grove Crane AT700D				No	07:00 AM	Building>D
	Notes:						
6	Genie Lift S80				No	07:00 AM	Building>D
	Notes:						
7	Scissor Lift				No	07:00 AM	Building
	Notes:						
8	Scissor Lift				No	07:00 AM	Building
	Notes:						
9	Scissor Lift				No	07:00 AM	Building
	Notes:						
10	JLG Skytrak Telehandler				No	07:00 AM	Site
	Notes:						
11	JLG Skytrak Telehandler				No	07:00 AM	Site
	Notes:						
12	Vibratory Roller				No	07:00 AM	Site
	Notes:						
13	John Deere 750 Dozer				No	07:00 AM	Site
	Notes:						
14	Volvo 330 Excavator				No	07:00 AM	Site>Stormwater Pond
	Notes:						

INSPECTION LOG

No.	Start Time	End Time	Inspection Type	Inspecting Entity	Inspector Name	Location	Area
1	02:00 PM	03:30 PM	Third Party	Mott MacDonald	Mike Tugwell	Building	
	Comments: Threshold inspection in second and third level of corridor.						

By _____

Date _____

Copies To _____



Daily Log: Tuesday 3/26/2019

Daily Log Completed
 The Daily Log was completed by Donald Shelton on Thu Mar 28, 2019 at 02:53 pm CDT.

WEATHER REPORT

Temperature			Precipitation Since			Humidity				Windspeed		
Low	High	Avg	Midnight	2 Days Ago	3 Days Ago	Low	Avg	High	Dew	Avg	Max	Gust
48°F	68°F	59°F	0.00 in.	0.06 in.	0.06 in.	48%	72%	94%	50°F	7.6 mph	11 mph	22 mph

DAILY SNAPSHOT

06:00 AM	09:00 AM	12:00 PM	03:00 PM	06:00 PM	09:00 PM
clear-night 55°F	clear-day 58°F	partly-cloudy-day 68°F	partly-cloudy-day 68°F	partly-cloudy-day 60°F	clear-night 52°F

OBSERVED WEATHER CONDITIONS

No.	Weather Delay	Sky	Temp	Average	Precipitation	Wind	Ground/Sea
1	No	Cloudy	Mild	59	0	Light Wind	Dry

MANPOWER LOG

88 Workers | 782.0 Man Hours

No.	Contact/Company	Cost Code	Workers	# Hours	Man Hours	Location
1	EAA Site Contractors LLC		4	8.0	32.0	Site
	Notes: Total man hours 31. EAA continued to dig retention pond today. The dirt was placed on the north side of the bldg. We also rolled and compacted the dirt.					
2	A&B Electric Co., Inc.		13	10.0	130.0	Building
	Notes: Working on rough in of 4th floor slab of Section "C"(Electrical,Security,etc,) Fab rigid 90 for rough in (Fab area), Rough in of Overhead conduits in Section "D"(Electrical lighting conduits).					
3	Bayside Structures, LLC		23	8.0	184.0	Building
	Notes: We poured the topping slab in the corridor on the second floor from column line 15 to 50 265' twenty-seven yards. We poured the topping slab on the third floor from column line 3 to 15 150' eighteen yards. We worked on excavating and forming column isolations in area D at elevation 83.00.					
4	Caddell Construction Co. (DE), LLC		9	10.0	90.0	Site
	Notes: WGI/Caddell supervision, quality control and safety onsite.					
5	Ed Emmons Steel Erectors, Inc.		10	8.0	80.0	Building>D
	Notes: Elevation 135: X brace and bolt-up completed, Edge angle 50% complete, and started deck. Elevation 102: Bolt-up completed, field verify beams 100%, bent plate at same location 90% complete, and started decking.					


MANPOWER LOG

88 Workers | 782.0 Man Hours

No.	Contact/Company	Cost Code	Workers	# Hours	Man Hours	Location
6	Nash Plumbing and Mechanical, LLC		9	8.0	72.0	Building
Notes: installed hydronic piping; laid out holes for hydronic piping in precast walls; and installed drains, trap primers.						
7	Ruben Surveying		2	8.0	16.0	Building
Notes: Set control point						
8	Tindall Corporation		17	10.0	170.0	Building
Notes: **Erecting in area A. **Welding and grouting **Patching 4th level of C						
9	Larry M. Jacobs & Associates, Inc.		1	8.0	8.0	Building
Notes: Conducted concrete tests.						
			88		782.0	

Manpower Log's Attachments:

2. A&B Electric Co., Inc.

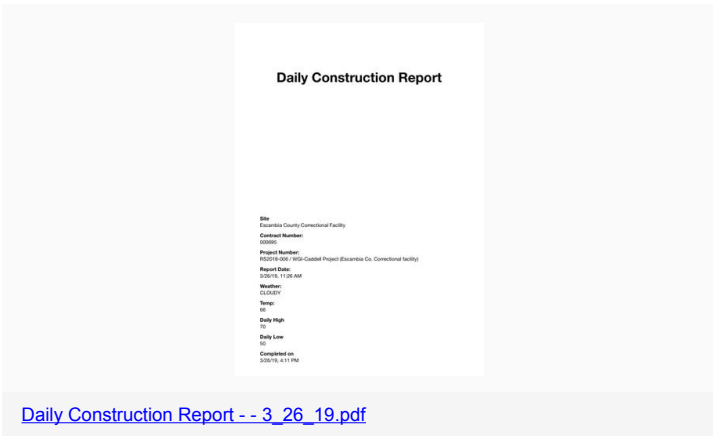


[Daily Construction Report -- 3_26_19.pdf](#)

3. Bayside Structures, LLC



5. Ed Emmons Steel Erectors, Inc.

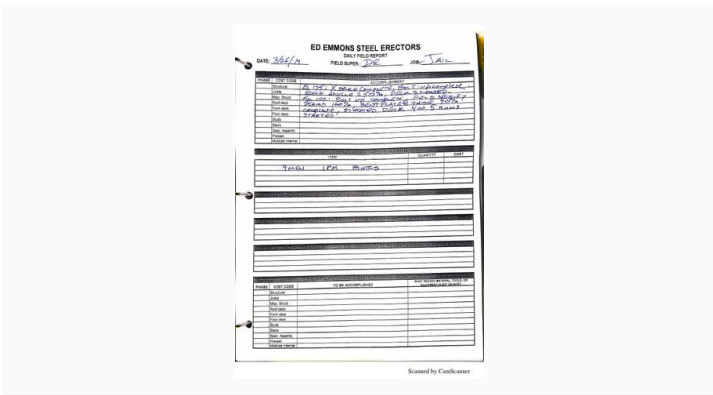

[New Doc 2019-03-26 15.39.59.pdf](#)

6. Nash Plumbing and Mechanical, LLC

[Nash Daily 3-26-2019.xlsx](#)

8. Tindall Corporation

[Tindall Escambai Daily 3-26-2019.xlsx](#)

EQUIPMENT LOG

No.	Equipment Name	Cost Code	Hrs Operating	Hrs Idle	Inspected?	Inspection Time	Location
1	Kobelco Crane CKE2500				No	07:00 AM	Building>A
	Notes:						
2	Genie Lift S85				No	07:00 AM	Building>A
	Notes:						
3	JLG Lift 660SJ				No	07:00 AM	Building>A
	Notes:						
4	Grove Crane AT700D				No	07:00 AM	Building>D
	Notes:						
5	Genie Lift S80				No	07:00 AM	Building>D
	Notes:						
6	Scissor Lift				No	07:00 AM	Building
	Notes:						
7	Scissor Lift				No	07:00 AM	Building
	Notes:						
8	Scissor Lift				No	07:00 AM	Building
	Notes:						
9	Scissor Lift				No	07:00 AM	Building
	Notes:						
10	Bobcat Telehandler				No	07:00 AM	Site
	Notes:						
11	JLG Skytrak Telehandler				No	07:00 AM	Site
	Notes:						
12	JLG Skytrak Telehandler				No	07:00 AM	Site
	Notes:						
13	Bobcat Miniexcavator				No	07:00 AM	Site
	Notes:						
14	Volvo 330 Excavator				No	07:00 PM	Site>Stormwater Pond
	Notes:						
15	Vibratory Roller				No	07:00 AM	Site
	Notes:						
16	John Deere 50G Miniexcavator				No	07:00 AM	Site
	Notes:						

PHOTOS



[20190326_091725.jpg](#)



[20190326_091753.jpg](#)



[20190326_093939.jpg](#)

By

Date

Copies To



Daily Log: Wednesday 3/27/2019

Daily Log Completed
 The Daily Log was completed by Donald Shelton on Fri Mar 29, 2019 at 12:44 pm CDT.

WEATHER REPORT

Temperature			Precipitation Since			Humidity				Windspeed		
Low	High	Avg	Midnight	2 Days Ago	3 Days Ago	Low	Avg	High	Dew	Avg	Max	Gust
46°F	71°F	58°F	0.00 in.	0.00 in.	0.06 in.	43%	71%	98%	47°F	5.3 mph	10 mph	21 mph

DAILY SNAPSHOT

06:00 AM	09:00 AM	12:00 PM	03:00 PM	06:00 PM	09:00 PM
clear-night 48°F	clear-day 57°F	clear-day 69°F	clear-day 72°F	clear-day 69°F	clear-night 56°F

OBSERVED WEATHER CONDITIONS

No.	Weather Delay	Sky	Temp	Average	Precipitation	Wind	Ground/Sea
1	No	Clear	Mild	58	0	Light Wind	Dry

MANPOWER LOG

73 Workers | 682.0 Man Hours

No.	Contact/Company	Cost Code	Workers	# Hours	Man Hours	Location
1	EAA Site Contractors LLC		5	8.0	40.0	Site
Notes: Total man hours 40. EAA did not dig in the retention pond today. We continued to compact the dirt on the north side of bldg. We also placed clay on the drive path along this area. We also rough graded the new construction entrance off ST Mary. EAA will pull off site after today. We are waiting for Chavers to complete more storm drain installation.						
2	A&B Electric Co., Inc.		13	10.0	130.0	Building
Notes: Rough in of Electrical conduits for 4th Floor slab Section "C", Rough in of overhead Electrical conduits in Section "D", Fab 90 and conduits for rough in (Fab area)						
3	Bayside Structures, LLC		11	10.0	110.0	Building>C
Notes: We worked on cleaning the floor in area C at fourth floor elevation so we could place peel and stick to help keep floor topping from leaking through to floor below. Started placing rebar and WWM on fourth floor area C. We saw cut all control joints in corridors that we poured yesterday. We started cleaning third floor in area C and started placing peel and stick. We cleaned the entire second floor. We do not have proper concrete coverage in the flat slab areas Pete Johnson with Caddell has been notified.						
4	Caddell Construction Co. (DE), LLC		9	10.0	90.0	Site
Notes: WGI/Caddell supervision, quality control and safety onsite.						
5	Ed Emmons Steel Erectors, Inc.		10	8.0	80.0	Building>D
Notes: Deck support complete at elevation 135 Area D. Deck is 75% complete in same area. Continued deck support and deck at elevation 102.						


MANPOWER LOG

73 Workers | 682.0 Man Hours

No.	Contact/Company	Cost Code	Workers	# Hours	Man Hours	Location
6	Nash Plumbing and Mechanical, LLC		9	8.0	72.0	Building
Notes: Installed hydronic piping, laid out pipe penetrations for hydronic piping, laid out pipe penetrations plumbing, cored drilling holes for plumbing						
7	Tindall Corporation		16	10.0	160.0	Building
Notes: **Erecting in area A. **Welding and grouting						
			73	682.0		

Manpower Log's Attachments:

2. A&B Electric Co., Inc.

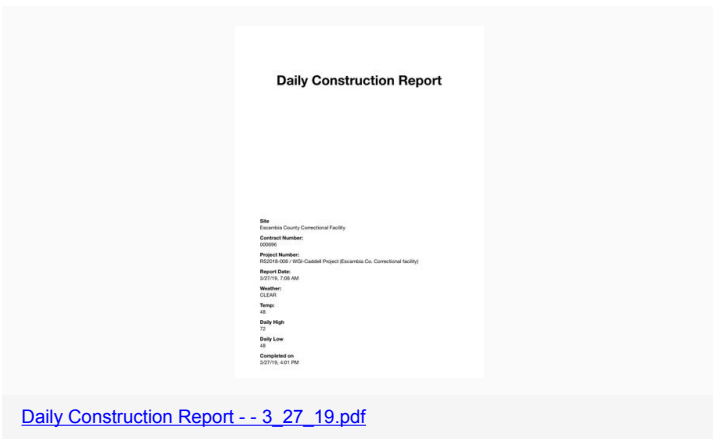


[Daily Construction Report -- 3_27_19.pdf](#)

3. Bayside Structures, LLC

[Bayside Daily 3-27-2019.docx](#)

5. Ed Emmons Steel Erectors, Inc.

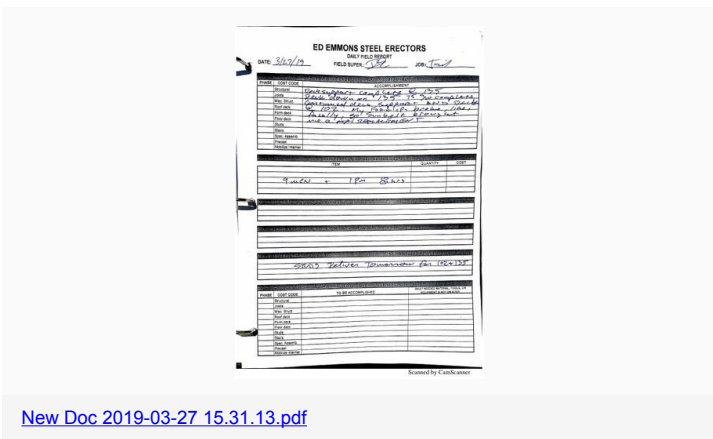

[New Doc 2019-03-27 15.31.13.pdf](#)

6. Nash Plumbing and Mechanical, LLC

[Nash Daily 3-27-2019.xlsx](#)

[Tindall Escambia daily 3-27-19.xlsx](#)

EQUIPMENT LOG

No.	Equipment Name	Cost Code	Hrs Operating	Hrs Idle	Inspected?	Inspection Time	Location
1	Kobelco Crane CKE2500				No	07:00 AM	Building>A
	Notes:						
2	Genie Lift S85				No	07:00 AM	Building>A
	Notes:						
3	JLG Lift 660SJ				No	07:00 AM	Building>A
	Notes:						
4	Grove Crane AT700D				No	07:00 AM	Building>D
	Notes:						
5	Scissor Lift				No	07:00 AM	Building
	Notes:						
6	Scissor Lift				No	07:00 AM	Building
	Notes:						
7	Scissor Lift				No	07:00 AM	Building
	Notes:						
8	Bobcat Miniexcavator				No	07:00 AM	Site
	Notes:						
9	JLG Skytrak Telehandler				No	07:00 AM	Site
	Notes:						
10	JLG Skytrak Telehandler				No	07:00 AM	Site
	Notes:						
11	Vibratory Roller				No	07:00 AM	Site
	Notes:						
12	John Deere 50G Miniexcavator				No	07:00 AM	Site
	Notes:						
13	John Deere 750 Dozer				No	07:00 AM	Site
	Notes:						

PHOTOS



[DJI_0452.jpg](#)



[DJI_0453.jpg](#)



[DJI_0454.jpg](#)



[DJI_0455.jpg](#)



[DJI_0456.jpg](#)



[DJI_0457.jpg](#)



[DJI_0458.jpg](#)



[DJI_0459.jpg](#)



[DJI_0460.jpg](#)



[DJI_0462.jpg](#)



[DJI_0463.jpg](#)



[DJI_0464.jpg](#)



[DJI_0465.jpg](#)



[DJI_0466.jpg](#)



[DJI_0467.jpg](#)



[DJI_0468.jpg](#)



[DJI_0469.jpg](#)



[DJI_0470.jpg](#)



[DJI_0471.jpg](#)



[DJI_0479.jpg](#)



[DJI_0480.jpg](#)

By _____

Date _____

Copies To _____



Daily Log: Thursday 3/28/2019

Daily Log Completed
 The Daily Log was completed by Donald Shelton on Mon Apr 1, 2019 at 08:39 am CDT.

WEATHER REPORT

Temperature			Precipitation Since			Humidity				Windspeed		
Low	High	Avg	Midnight	2 Days Ago	3 Days Ago	Low	Avg	High	Dew	Avg	Max	Gust
42°F	73°F	58°F	0.00 in.	0.00 in.	0.00 in.	34%	64%	100%	44°F	4.6 mph	8 mph	10 mph

DAILY SNAPSHOT

06:00 AM	09:00 AM	12:00 PM	03:00 PM	06:00 PM	09:00 PM
clear-night 42°F	clear-day 58°F	clear-day 69°F	clear-day 74°F	partly-cloudy-day 68°F	clear-night 58°F

OBSERVED WEATHER CONDITIONS

No.	Weather Delay	Sky	Temp	Average	Precipitation	Wind	Ground/Sea
1	No	Clear	Mild	58	0	High Wind	Dry

MANPOWER LOG

55 Workers | 506.0 Man Hours

No.	Contact/Company	Cost Code	Workers	# Hours	Man Hours	Location
1	A&B Electric Co., Inc.		13	10.0	130.0	Building
Notes: Working on rough in of 4th floor slab (Section C). Working on rough in of lightning protection on 4th floor roof (Section C). Working on temporary lights on 3rd Floor (Section C). Working on Layout of 3rd. Floor rough in (Section C). Start Electrical rough in on 3rd Floor (Section C). Rough in overhead conduits in 1st floor (Section D) Lighting Emergency & Normal, VAV, Exhaust fans.						
2	Bayside Structures, LLC		11	10.0	110.0	Building>C
Notes: We continued to work on placing WWM and rebar on the fourth floor in area C. We built edge forms at all shaft openings and at the leading edge of the building where necessary.						
3	Caddell Construction Co. (DE), LLC		9	10.0	90.0	Site
Notes: WGI/Caddell supervision, quality control and safety onsite.						
4	Ed Emmons Steel Erectors, Inc.		11	8.0	88.0	Building>D
Notes: Erected columns and beams at elevation 102.						
5	Nash Plumbing and Mechanical, LLC		9	8.0	72.0	Building
Notes: Installed hydronic piping, laid out holes for piping,						

MANPOWER LOG

55 Workers | 506.0 Man Hours

No.	Contact/Company	Cost Code	Workers	# Hours	Man Hours	Location
	laid out holes for plumbing, and drilled holes for plumbing					
6	Ruben Surveying		2	8.0	16.0	Building
	Notes: Set control points					
			55		506.0	

Manpower Log's Attachments:

1. A&B Electric Co., Inc.




[Daily Construction Report - - 3_28_19.pdf](#)

2. Bayside Structures, LLC

[Bayside Daily 3-28-2019.docx](#)

4. Ed Emmons Steel Erectors, Inc.



[New Doc 2019-03-28 15.47.44.pdf](#)

5. Nash Plumbing and Mechanical, LLC

[Nash Daily 3-28-2019.xlsx](#)

EQUIPMENT LOG

No.	Equipment Name	Cost Code	Hrs Operating	Hrs Idle	Inspected?	Inspection Time	Location
1	Sky Power Lift 600AJ				No	07:00 AM	Building>C
	Notes:						

EQUIPMENT LOG

No.	Equipment Name	Cost Code	Hrs Operating	Hrs Idle	Inspected?	Inspection Time	Location
2	Grove Crane AT700D				No	07:00 AM	Building>D
	Notes:						
3	Scissor Lift				No	07:00 AM	Building
	Notes:						
4	Scissor Lift				No	07:00 AM	Building
	Notes:						
5	Scissor Lift				No	07:00 AM	Building
	Notes:						
6	JLG Skytrak Telehandler				No	07:00 AM	Site
	Notes:						
7	JLG Skytrak Telehandler				No	07:00 AM	Site
	Notes:						
8	Cat Telehandler				No	07:00 AM	Site
	Notes:						
9	Kobelco Crane CKE2500				No	07:00 AM	Building>A
	Notes:						

By

Date

Copies To



Daily Log: Friday 3/29/2019

Daily Log Completed
 The Daily Log was completed by Donald Shelton on Mon Apr 1, 2019 at 08:40 am CDT.

WEATHER REPORT

Temperature			Precipitation Since			Humidity				Windspeed		
Low	High	Avg	Midnight	2 Days Ago	3 Days Ago	Low	Avg	High	Dew	Avg	Max	Gust
45°F	75°F	61°F	0.00 in.	0.00 in.	0.00 in.	46%	80%	100%	53°F	5.6 mph	10 mph	13 mph

DAILY SNAPSHOT

06:00 AM	09:00 AM	12:00 PM	03:00 PM	06:00 PM	09:00 PM
partly-cloudy-night 48°F	partly-cloudy-day 61°F	clear-day 74°F	partly-cloudy-day 75°F	partly-cloudy-day 70°F	partly-cloudy-night 63°F

OBSERVED WEATHER CONDITIONS

No.	Weather Delay	Sky	Temp	Average	Precipitation	Wind	Ground/Sea
1	No	Cloudy	Mild	61	0	Light Wind	Dry

MANPOWER LOG

51 Workers | 439.0 Man Hours

No.	Contact/Company	Cost Code	Workers	# Hours	Man Hours	Location
1	A&B Electric Co., Inc.		13	9.0	117.0	Building
Notes: Support conduits roughed in on 4th floor Section "C" after steel wire installed, Rough in conduits on 3rd Floor Section "C", Rough in overhead Electrical conduits on 1st floor Section "D"(Emergency & Normal Lighting and VAV Power) Fab conduits and 90 for rough in. (Fab area).						
2	Bayside Structures, LLC		8	8.0	64.0	Building>C
Notes: We continued to work on placing WWM and rebar on the fourth floor in area C. We built edge forms at all shaft openings and at the leading edge of the building where necessary.						
3	Caddell Construction Co. (DE), LLC		9	10.0	90.0	Site
Notes: WGI/Caddell supervision, quality control and safety onsite.						
4	Ed Emmons Steel Erectors, Inc.		12	8.0	96.0	Building>D
Notes: Continued erecting deck support angle and decking at elevation 102 and 135 in Area D.						
5	Nash Plumbing and Mechanical, LLC		9	8.0	72.0	Building
Notes: Installed piping, laid out holes for pipe penetrations outside precast walls, laid out holes in double tees area, and						

MANPOWER LOG

51 Workers | 439.0 Man Hours

No. Contact/Company	Cost Code	Workers	# Hours	Man Hours	Location
cored holes in precast slabs					
		51		439.0	

Manpower Log's Attachments:

1. A&B Electric Co., Inc.




[Daily Construction Report -- 3_29_19.pdf](#)

2. Bayside Structures, LLC

[Bayside Daily 3-29-2019.docx](#)

4. Ed Emmons Steel Erectors, Inc.



[New Doc 2019-03-29 15.53.40.pdf](#)

5. Nash Plumbing and Mechanical, LLC

[Nash Daily 3-29-2019.xlsx](#)

EQUIPMENT LOG

No.	Equipment Name	Cost Code	Hrs Operating	Hrs Idle	Inspected?	Inspection Time	Location
1	Sky Power Lift 600AJ				No	07:00 AM	Building>C
	Notes:						
2	Grove Crane AT700D				No	07:00 AM	Building>D
	Notes:						

EQUIPMENT LOG

No.	Equipment Name	Cost Code	Hrs Operating	Hrs Idle	Inspected?	Inspection Time	Location
3	Scissor Lift				No	07:00 AM	Building
	Notes:						
4	Scissor Lift				No	07:00 AM	Building
	Notes:						
5	Scissor Lift				No	07:00 AM	Building
	Notes:						
6	JLG Skytrak Telehandler				No	07:00 AM	Site
	Notes:						
7	JLG Skytrak Telehandler				No	07:00 AM	Site
	Notes:						
8	Cat Telehandler				No	07:00 AM	Site
	Notes:						

By

Date

Copies To



Whitesell Green / Caddell, a Joint Venture
 2700 Lagoon Park Drive
 Montgomery, Alabama 36109
 P: (334) 272-7723
 F: (334) 394-0193

Project: 1054 - Escambia County Correctional Facility
 3080 N. Pace Boulevard
 Pensacola, Florida 32501

Daily Log: Saturday 3/30/2019

Daily Log Completed
 The Daily Log was completed by Donald Shelton on Mon Apr 1, 2019 at 08:40 am CDT.

WEATHER REPORT

Temperature			Precipitation Since			Humidity				Windspeed		
Low	High	Avg	Midnight	2 Days Ago	3 Days Ago	Low	Avg	High	Dew	Avg	Max	Gust
54°F	76°F	66°F	0.00 in.	0.00 in.	0.00 in.	56%	81%	100%	60°F	7.0 mph	13 mph	20 mph

DAILY SNAPSHOT

06:00 AM	09:00 AM	12:00 PM	03:00 PM	06:00 PM	09:00 PM
clear-night 55°F	partly-cloudy-day 70°F	partly-cloudy-day 75°F	partly-cloudy-day 76°F	partly-cloudy-day 71°F	partly-cloudy-night 65°F

OBSERVED WEATHER CONDITIONS

No.	Weather Delay	Sky	Temp	Average	Precipitation	Wind	Ground/Sea
1	No	Cloudy	Mild	66	0	Light Wind	Dry

MANPOWER LOG

4 Workers | 28.0 Man Hours

No.	Contact/Company	Cost Code	Workers	# Hours	Man Hours	Location
1	Caddell Construction Co. (DE), LLC		1	7.0	7.0	Site
Notes: WGI/Caddell supervision, quality control and safety onsite.						
2	Chavers Construction Inc.		3	7.0	21.0	Site>Stormwater Pond
Notes: Continued installing and back filling Manhole S24.						
			4	28.0		

EQUIPMENT LOG

No.	Equipment Name	Cost Code	Hrs Operating	Hrs Idle	Inspected?	Inspection Time	Location
1	Volvo 330 Excavator				No	07:00 AM	Site>Stormwater Pond
Notes:							

By _____ Date _____ Copies To _____



Whitesell Green / Caddell, a Joint Venture
 2700 Lagoon Park Drive
 Montgomery, Alabama 36109
 P: (334) 272-7723
 F: (334) 394-0193

Project: 1054 - Escambia County Correctional
Facility
 3080 N. Pace Boulevard
 Pensacola, Florida 32501

Daily Log: Sunday 3/31/2019

WEATHER REPORT

Temperature			Precipitation Since			Humidity				Windspeed		
Low	High	Avg	Midnight	2 Days Ago	3 Days Ago	Low	Avg	High	Dew	Avg	Max	Gust
47°F	66°F	55°F	0.02 in.	0.02 in.	0.02 in.	68%	83%	100%	50°F	9.8 mph	13 mph	22 mph

DAILY SNAPSHOT

06:00 AM	09:00 AM	12:00 PM	03:00 PM	06:00 PM	09:00 PM
partly-cloudy-night 57°F	partly-cloudy-day 56°F	cloudy 53°F	cloudy 51°F	partly-cloudy-day 53°F	partly-cloudy-night 50°F

OBSERVED WEATHER CONDITIONS

No.	Weather Delay	Sky	Temp	Average	Precipitation	Wind	Ground/Sea
1	No						

By _____

Date _____

Copies To _____

Committee of the Whole

10.

Meeting Date: 04/11/2019

Issue: Fire Service January 19, 2019, ISO Briefing

From: AMY LOVOY, Interim County Administrator

Information

Recommendation:

Fire Service January 19, 2019, ISO Briefing

(Michael Tucker, Superintendent/Bureau Chief, Florida State Fire College/Bureau of Fire Standards & Training; Julius Halas, Division Director, Florida State Fire Marshal's Office; and Kyle Biles, ISO Representative - 60 min)

A. Board Discussion

B. Board Direction

Attachments

Fire Service ISO Briefing



Special Workshop
Presented To
The Board of County Commissioners
Escambia County
April 11, 2019



Fire Service and Community Risk Reduction Overview

Jimmy Patronis, CFO/Florida State Fire Marshal

Julius Halas, Division Director

Mike Tucker, Bureau Chief

Kyle Biles, ISO, Senior Field Representative
Community Hazard Mitigation Services



Small County Coalition of Florida



- The Small County Coalition, Insurance Service Office, and Division of State Fire Marshal in conjunction with the local Fire Chief has presented information to local elected officials concerning the ISO Rating Schedule.
- Highlights of this information are contained in this presentation.



Goal of the Presentation



The primary focus of this program is to review:

- Considerations of local elected officials and fire service leadership;
- Providing increased “level of service” to enhance local fire protection and prevention;
- How the local ISO Rating can be improved through “Community Risk Reduction”.



State Fire Marshal Authority



- Shall adopt the most recent edition of the National Fire Prevention Association (NFPA) Fire Code (NFPA 1) and Life Safety Code (NFPA 101) by rule every three (3) years pursuant to s. 633.202, Florida Statutes.
- Shall provide cost effective training programs for the certification of firefighters and other fire related fields pursuant to s. 633.128, Florida Statutes.
- May issue, when requested by any substantially affected person or AHJ, a declaratory statement interpreting the Florida Fire Prevention Code pursuant to s. 633.104, Florida Statutes.



Escambia County is a Fire Service Provider



- Which includes (633.120 F.S.)
 - Municipality
 - County
 - Special District
 - State
 - Organizations under contract or other agreement with such entity to provide such services
- What it is not included
 - Private Fire Departments
 - 501(c)3 corporations not under contract with Holmes County
 - Associations serving as volunteer fire departments not under contract with Holmes County



Fire Service Providers



Employ firefighters or uses volunteer firefighters to provide:

- Fire extinguishment, or
- Fire prevention services for the protection of life and property.



Persons Employed by Fire Service Providers



- Authorized to enforce laws and rules of State Fire Marshal:
 - Chiefs of county, municipal and special-district fire service providers;
 - Other fire service provider personnel designated by their respective chiefs;
 - Personnel designated by local governments having no organized fire service providers.



Fire Service Provider Responsibilities



- Properly Trained Personnel (633.416 F.S.)
 - Trained Commensurate to Duty
 - Volunteer Firefighters (I)
 - Firefighters with Certificate of Compliance (II)
- Proper Recordkeeping (633.502 – 536 F.S.)
 - Fire Department Rosters
 - Firefighter Training
 - Firefighter Injuries
 - Medical Evaluations



Fire Service Provider Responsibilities (cont.)



- Safe Working Environment
 - Fire Stations (FAC 69A-62)
 - Presence of toxic substances
 - Safety Committee / Safety Coordinator (FAC 69A-62)
- Safe Equipment
 - Self Contained Breathing Apparatus
 - Annual fit testing
 - Personal Protective Equipment



Responsibilities of the Authority Having Jurisdiction (AHJ)



Section 125.01, Florida Statutes states that the legislative and governing body of a county shall have the power to carry on county government and that this power includes the power to:

“**provide fire protection**, including the enforcement of the Florida Fire Prevention Code, as provided in 633.206 and 633.208, Florida Statutes and adopt and enforce local technical amendments to the Florida Fire Prevention Code as provided in those sections and pursuant to 633.202, Florida Statutes.”



Responsibilities of the AHJ



633.208, Florida Statutes mandates that “each municipality, county, and special district with firesafety responsibilities shall enforce the Florida Fire Prevention Code” (FFPC)





Responsibilities Within FFPC



NFPA 1:1.6 states that the code “shall be administered and enforced by the AHJ designated by the governing authority.”

NFPA 1:1.7.6.1 authorizes the AHJ to “inspect, at all reasonable times, any building or premises for dangerous or hazardous conditions or materials”

NFPA 1:1.7.12.1 also authorizes the AHJ to inspect construction and installation work

Insurance Service Office (ISO)

Is a Verisk Business (Nasdaq:VRSK), providing statistical, actuarial, underwriting, and claims data to the property/casualty insurance industry, helping their customers compete effectively.




ISO Fire Suppression Rating Schedule

- **FSRS** reviews the firefighting capabilities of individual communities, to provide the insurance industry with information on a community's ability to suppress and limit fire losses.
- A numerical grading scale, ISO's Public Protection Classification (**PPC™**)



The revised schedule continues to evaluate three major categories of fire suppression:


- ✘ Fire department (50 points)
- ✘ Emergency communications (10 points)
- ✘ Water supply (40 points)
- ✘ Community Risk Reduction (5.5 points)

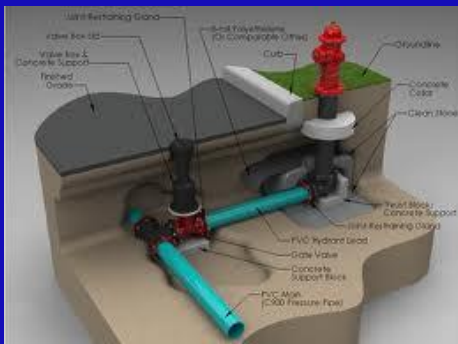

FSRS Classes 1 to 10

90.00	to	100 + Points	=	Class	1
80.00	to	89.99 Points	=	Class	2
70.00	to	79.99 Points	=	Class	3
60.00	to	69.99 Points	=	Class	4
50.00	to	59.99 Points	=	Class	5
40.00	to	49.99 Points	=	Class	6
30.00	to	39.99 Points	=	Class	7
20.00	to	29.99 Points	=	Class	8
10.00	to	19.99 Points	=	Class	9
00.00	to	9.99 Points	=	Class	10

TIME vs. PRODUCTS of COMBUSTION

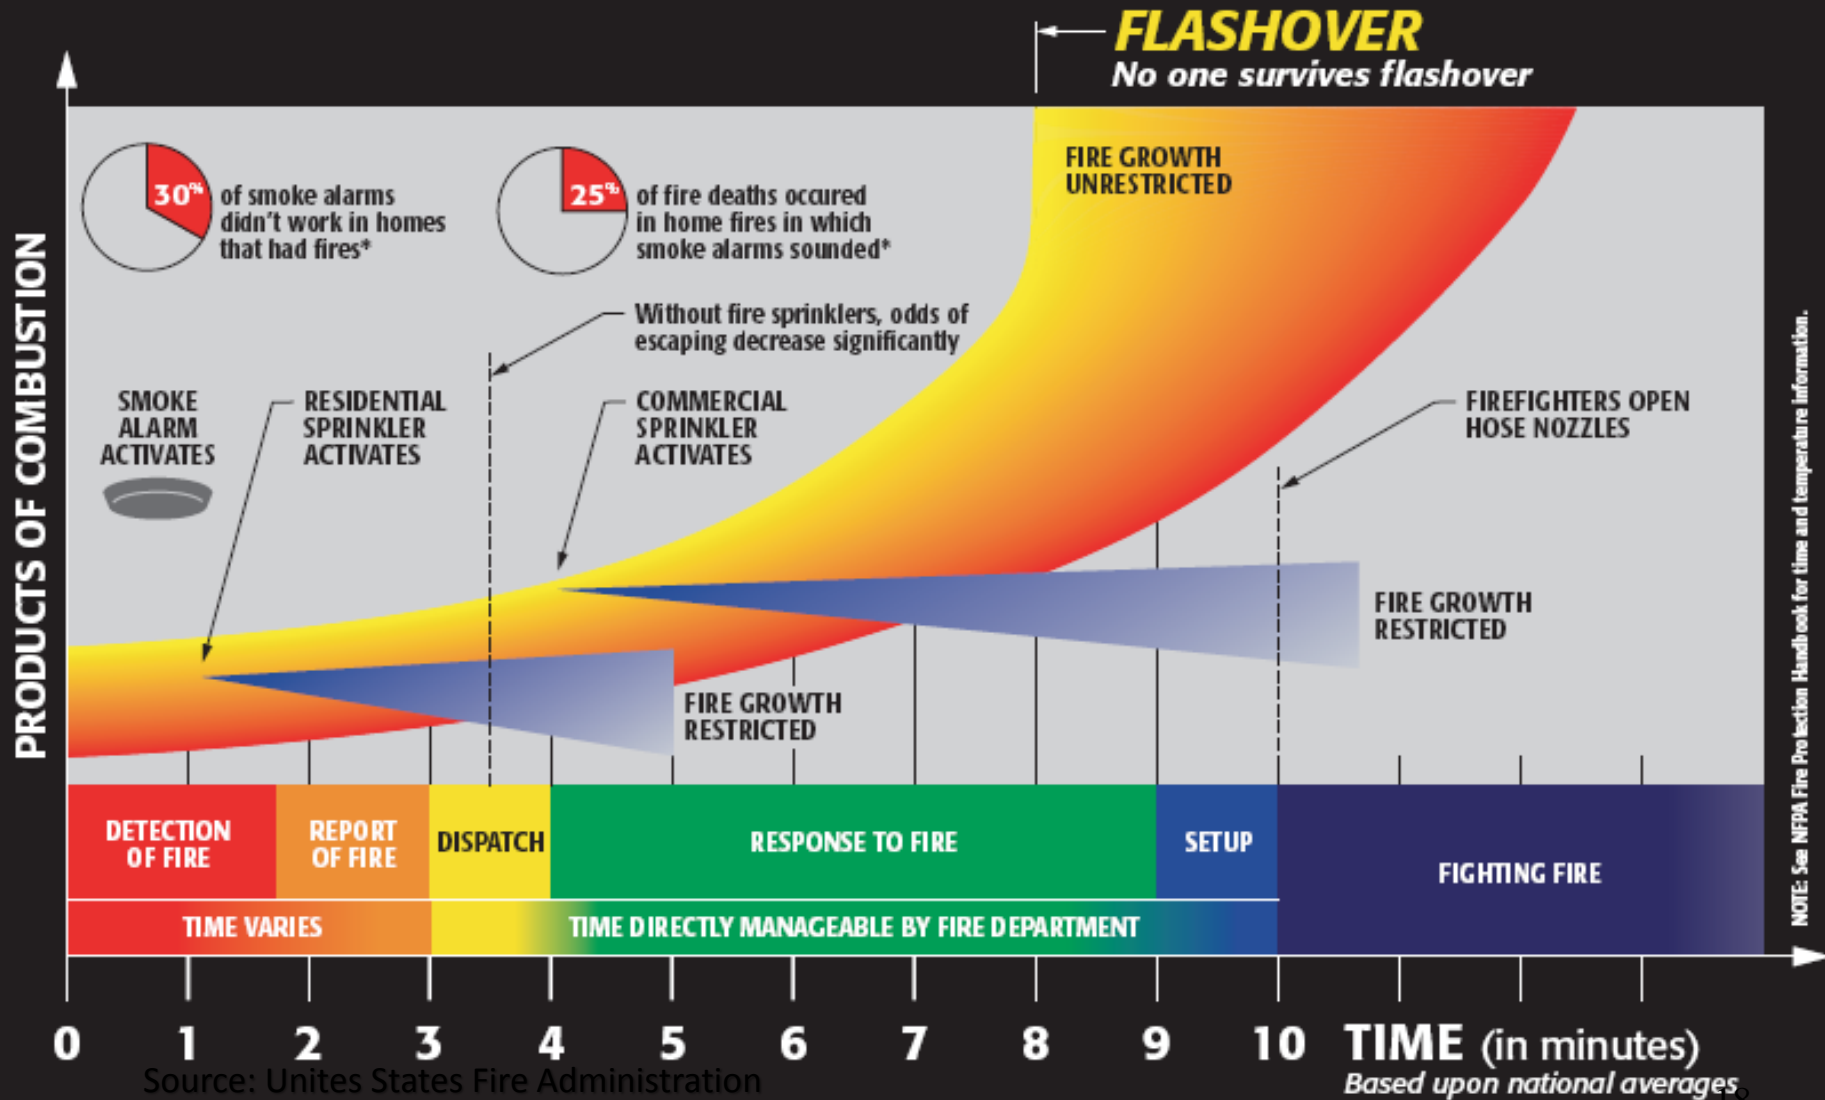

A Community's PPC Depends on an Evaluation of:

Emergency
communication systems,
including 911 systems,
wireless capabilities,
VOIP, staffing with
associated training, and
dispatching systems



A Community's PPC Depends on an Evaluation of:

The fire department, including equipment, staffing, training, and geographic distribution of fire companies



A Community's PPC Depends on an Evaluation of:

The water supply system, including the condition, inspection, and maintenance of hydrants, and the amount of available water compared with the amount needed to suppress fires



Community Risk Reduction

The new **Community Risk Reduction** section that recognizes community efforts to reduce losses through **fire prevention, public fire safety education, and fire investigation.**



The Community Risk Reduction section has a weight of 5.5 points, resulting in a revised 105.5+ available points.

Community Risk Reduction

Fire Prevention Code Adoption / Enforcement (2.2 points)

- Code adoption
- Code regulations
- Staffing
- Training / certification
- Frequency
- Continuing education
- Plan review
- Quality-Assurance
- Pre-fire planning



Community Risk Reduction


Public Fire Safety Education (2.2 points)

- Educator qualifications / training
- Continuing education
- Fire safety programs
- Juvenile fire setter intervention programs
- Program for occupancies having large loss potential



Community Risk Reduction Education

Public Fire & Life Safety Educator certification is available through the Division of State Fire Marshal




Community Risk Reduction Education

Fire Investigation (1.1 points)

- Fire investigation organization
- Fire investigation staffing
- Fire investigator certification
- Fire investigator continuing education
- Use of the National Fire Incident Reporting System




Countrywide Summary January 2018

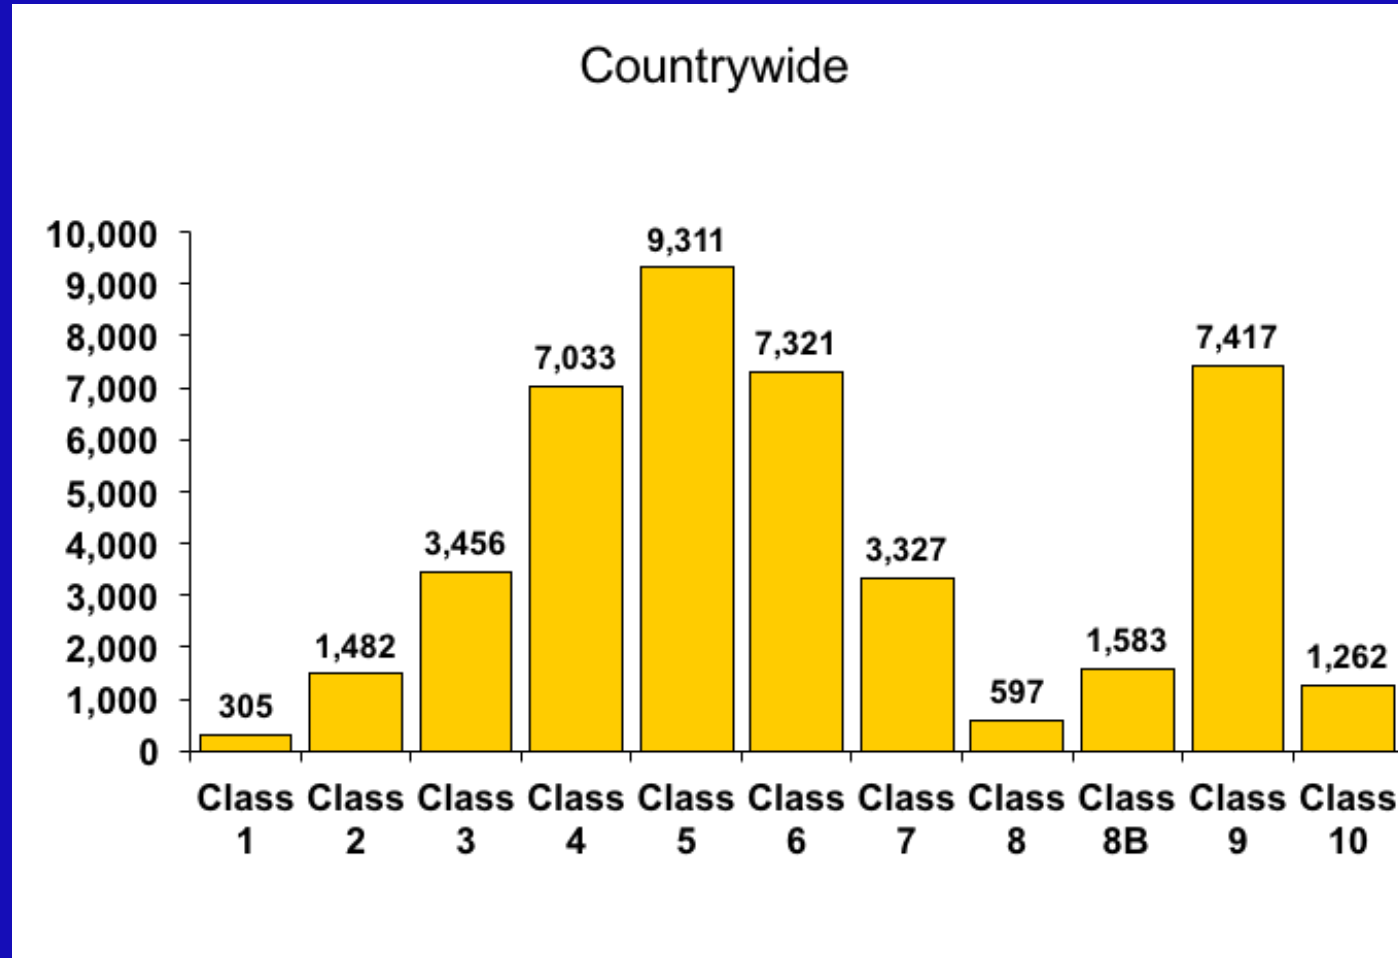

Florida

January 2018

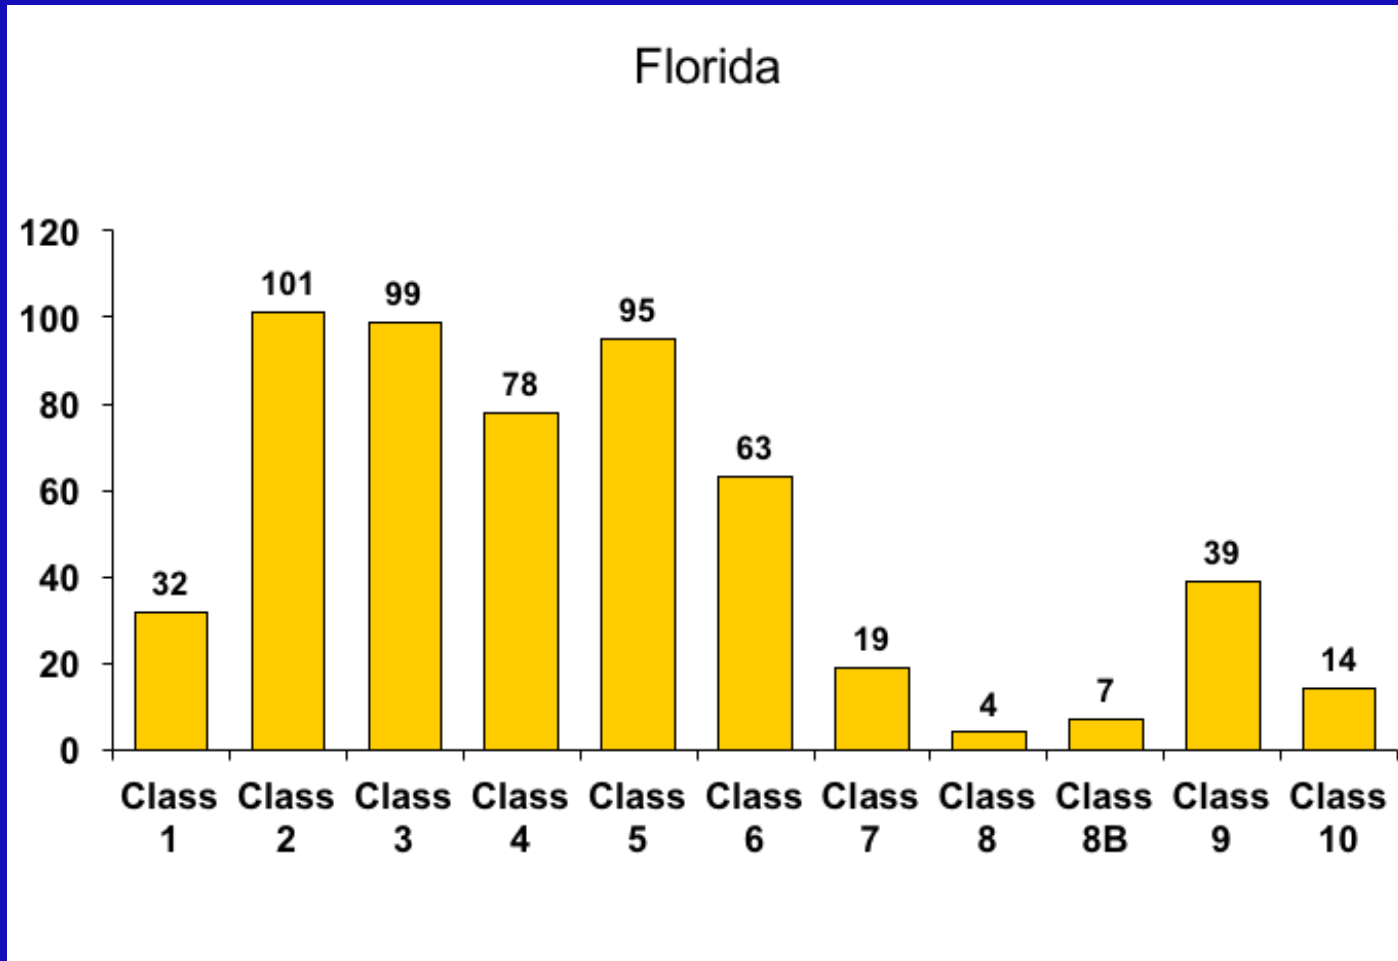



Fire Prevention Code Regulation



AHJ adopts and enforces the latest edition of the model code:

633.202 Florida Fire Prevention Code

(2) The State Fire Marshal shall adopt the current edition of the National Fire Protection Association's Standard 1, Fire Prevention Code but may not adopt a building, mechanical, or plumbing code. The State Fire Marshal shall adopt the current edition of the Life Safety Code, NFPA 101, current editions, by reference.



Fire Prevention Programs



Plan Review

- §553.79 (2), Florida Statutes states that “an enforcing agency may not issue any permit for construction, erection, alteration, modification, repair, or demolition of any building until the appropriate firesafety inspector certified pursuant to s. 633.216 has reviewed the plans and specifications required by the Florida Building Code, or local amendment thereto, for such proposal and found that the plans comply with the Florida Fire Prevention Code and the Life Safety Code.”



Benefits of an Effective Fire Prevention Program



Fire inspections identify and correct hazards that may exist and could cause a fire, contribute to fire spread, or affect occupant safety

Reduces fire risks due to conformance with fire codes and increases public awareness of risks

Consistency of enforcement and safety for all commercial properties through consistent and systematic inspections

Helps to maintain **ISO ratings by credit for Community Risk Reduction**, such as effective fire prevention practices



National (Florida) Fire Incident Reporting System



- Participation is voluntary but may be required for grant eligibility.
- Reported annually at a minimum.





Reported Information



This information is needed to develop Rules, Codes and Standards and to accurately communicate the “fire problem”.


For a copy of the 2018 Annual Report:

<https://www.myfloridacfo.com/Division/SFM/FFIRS/>






Civilian Fire Deaths 2017

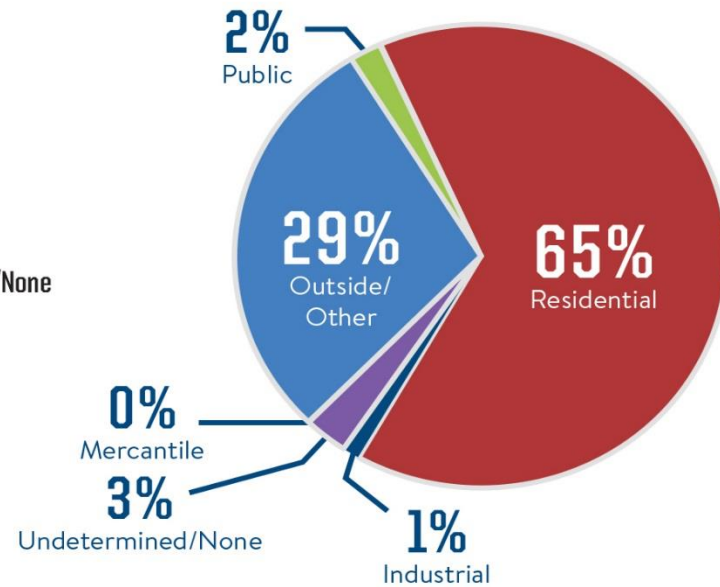




FIRE DEATHS BY AGE / GENDER

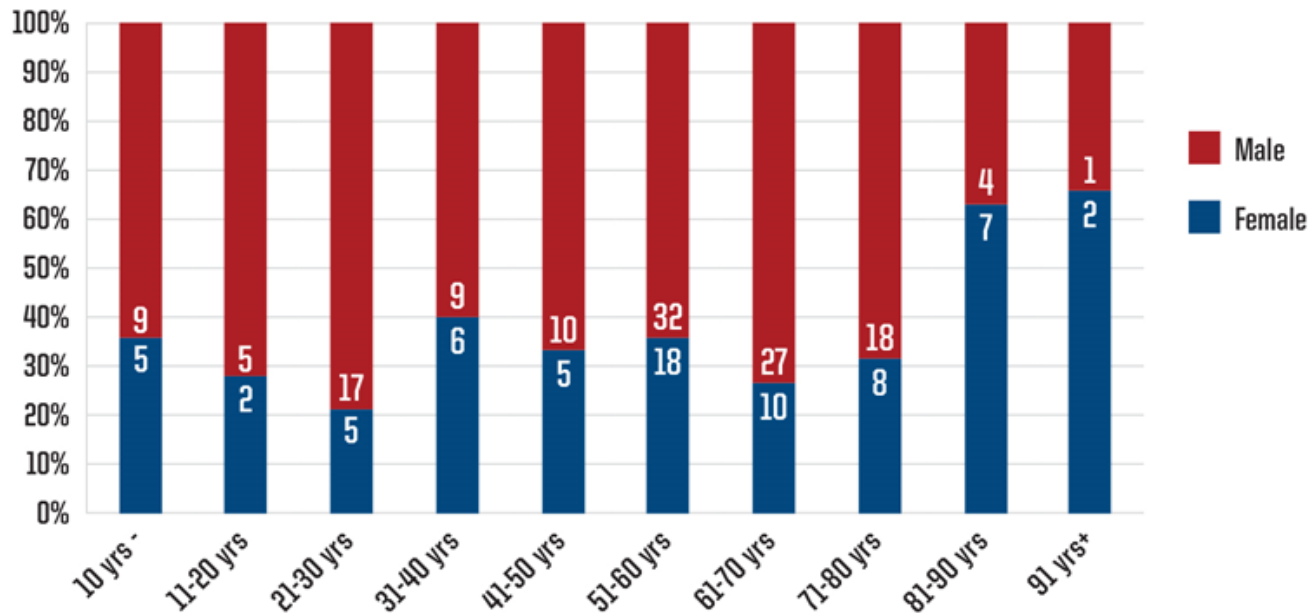



2017 State Incident Summary

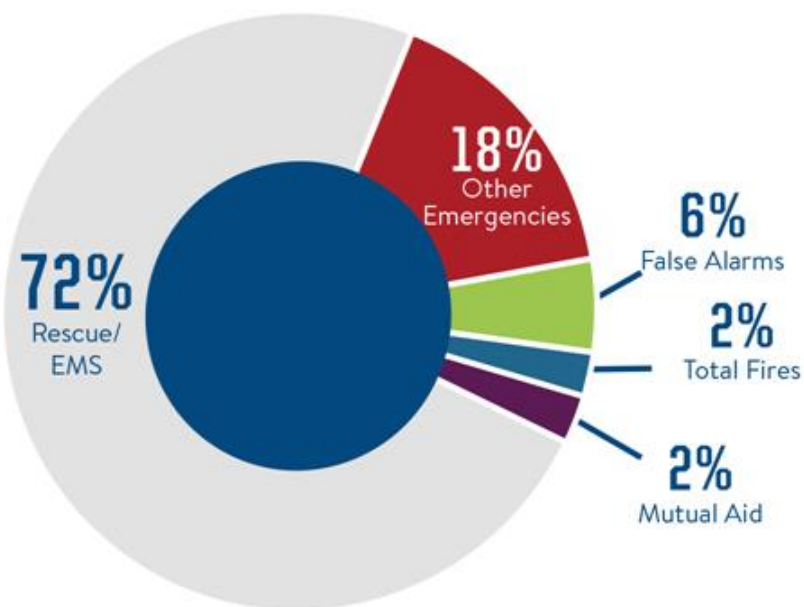


2017 State Incident Summary

Structure Fires	14,056
Vehicle Fires	9,317
Other Fires	28,825
Exposures Fires	697
Total Fire Incidents	52,895
Rescue/EMS	2,042,876
Other Emergencies	519,824
False Alarms	160,372
Total Non-Fire Incidents	2,723,072
Mutual Aid Given	66,572
*Total Incidents <u>plus</u> Mutual Aid Given	2,842,539



2017 Fires By Property Use

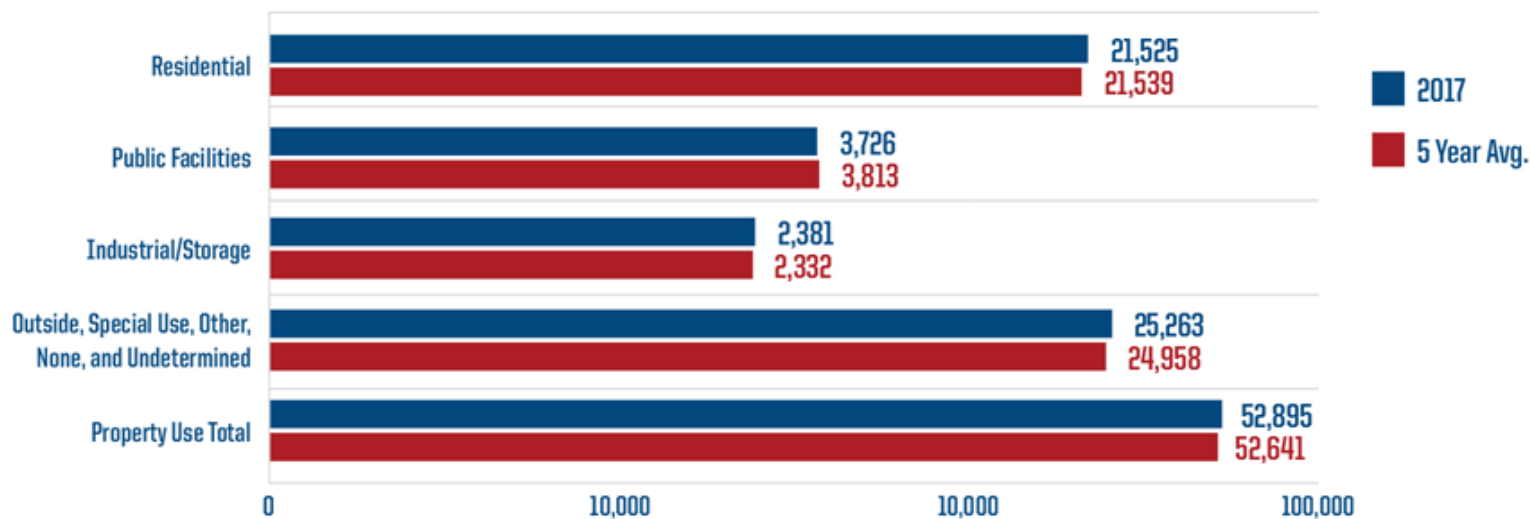



Florida Firefighter Assistance Grant



- Volunteer and combination departments
- Grant provides for
 - Personal Protective Equipment
 - Self-Contained Breathing Apparatus
 - Fire Engines / Tankers (First Award)
 - Training
- State Volunteer Fire Coordinator
 - Charlie Frank
 - 352-369-2830 (Office)

Closing



- Questions?
- Comments?

Thank you for your time
